

PALM BEACH COUNTY  
BOARD OF COUNTY COMMISSIONERS  
AGENDA ITEM SUMMARY

Meeting Date: March 11, 2014 Consent [X] Regular [ ]  
Public Hearing [ ]

Department: Water Utilities Department

I. EXECUTIVE BRIEF

**Motion and Title:** Staff recommends motion to approve: A) Change Order No. 1 to the Contract with JCC Enterprises Labor, Inc. (R2013-0160) for the City of Pahokee Inflow & Infiltration Improvements - Phase III Project; and B) Final payment to JCC Enterprises Labor, Inc. (R2013-0160) in the amount of \$56,885.85.

**Summary:** On February 5, 2013, the Palm Beach County Board of County Commissioners approved the Water Utilities Department Construction Contract for the City of Pahokee Inflow & Infiltration Improvements - Phase III (R2013-0160) with JCC Enterprises Labor, Inc. Change Order No. 1 includes a final adjustment of quantities resulting in a net decrease of \$36,450.70 and provides JCC Enterprises Labor, Inc. with an 82 calendar day time extension for delays due to extensive rain and surcharged conditions in the sanitary sewer system. JCC Enterprises Labor, Inc. has satisfactorily completed all of the work associated with this project, and final payment in the amount of \$56,885.85 is due. This project is funded by the State of Florida Department of Economic Opportunity (DEO) through the Disaster Recovery Initiative Program (DRI). The prime contractor is MWBE (100% minority and 0% female participation). JCC Enterprises Labor, Inc. is not a Palm Beach County company. (WUD Project No. 12-049) District 6 (JM)

**Background and Justification:** The State of Florida DEO has appropriated funds for the rehabilitation of the City of Pahokee's wastewater infrastructure through the DRI. This final change order will reconcile all contract issues associated with this project.

**Attachments:**

- 1. Location Map
- 2. Two (2) Original Change Order No. 1
- 3. Two (2) Original Final Payment

Recommended By:  2/25/14  
Department Director Date

Approved By:  3/10/14  
Assistant County Administrator Date

**II. FISCAL IMPACT ANALYSIS**

**A. Five Year Summary of Fiscal Impact:**

Fiscal Years	2014	2015	2016	2017	2018
Capital Expenditures	(\$36,451)	0	0	0	0
External Revenues	<u>36,451</u>	0	0	0	0
Program Income (County)	0	0	0	0	0
In-Kind Match County	0	0	0	0	0
<b>NET FISCAL IMPACT</b>	<u>0</u>	0	0	0	0
<b># ADDITIONAL FTE POSITIONS (Cumulative)</b>	0	0	0	0	0

**Budget Account No.:**

Fund 4011 Dept 721 Unit W040 Object 6546

Is Item Included in Current Budget? Yes  No

Reporting Category N/A

**B. Recommended Sources of Funds/Summary of Fiscal Impact:**

This project is funded by the State of Florida DEO through the DRI.

**C. Department Fiscal Review:** Debra M West

**III. REVIEW COMMENTS**

**A. OFMB Fiscal and/or Contract Development and Control Comments:**

OFMB  
2/26/14  
[Signature]

Contract Development and Control  
3-5-14  
[Signature]

**B. Legal Sufficiency:**

Assistant County Attorney  
3/7/14  
[Signature]


**C. Other Department Review:**

\_\_\_\_\_  
Department Director



Palm Beach County  
Water Utilities  
Department  
Service Area (SA) and  
Major Facilities

Attachment 1

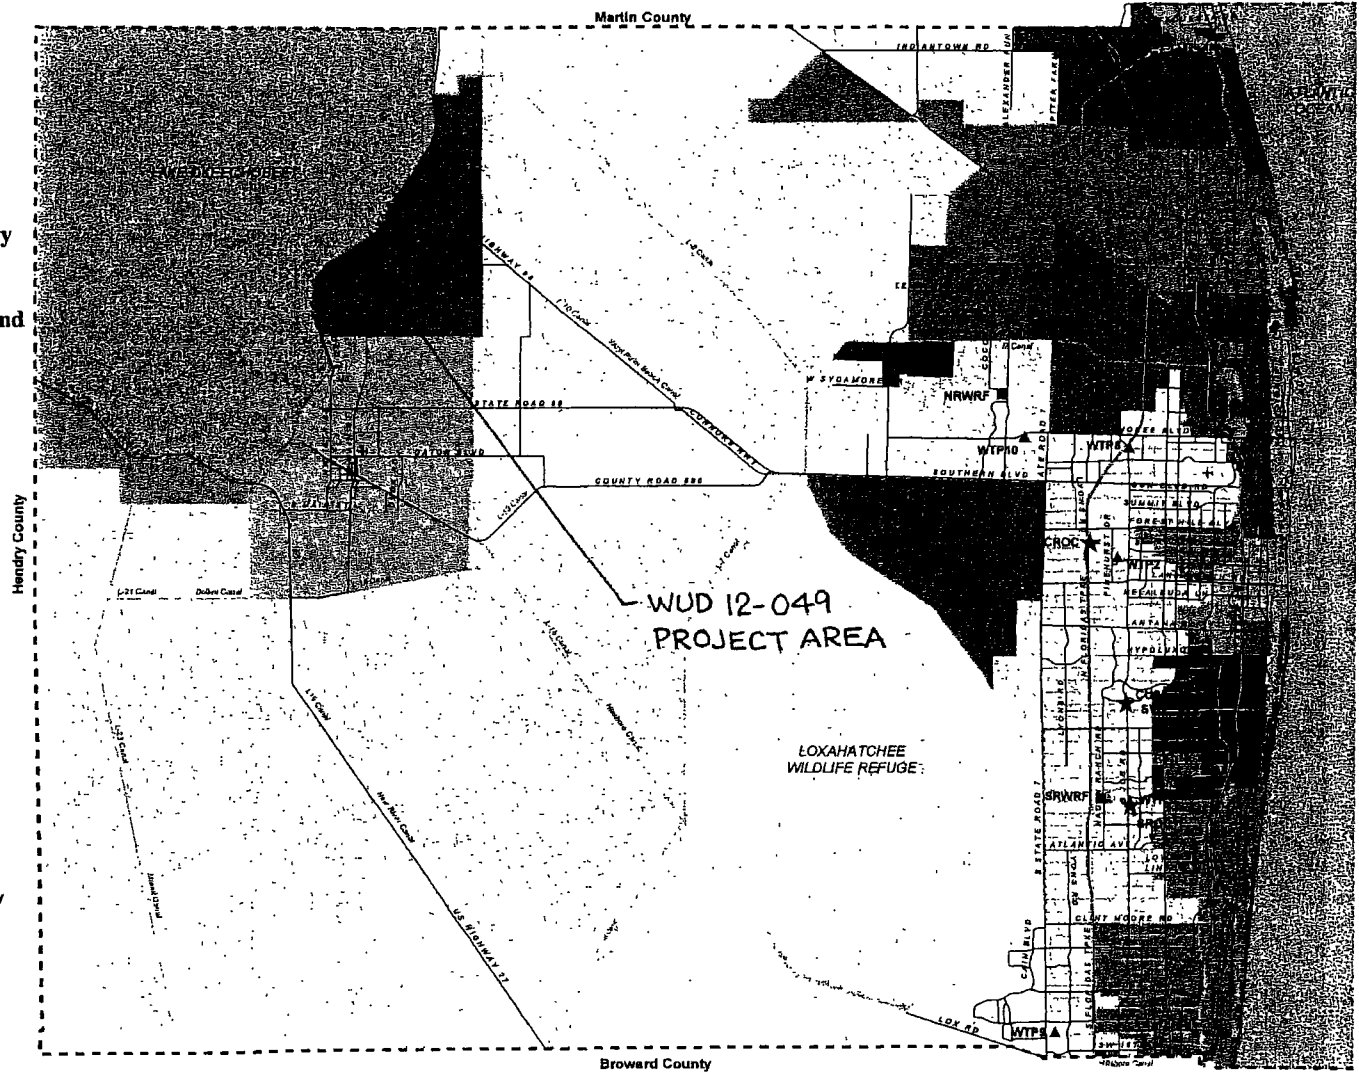

- Legend**
- P.B.C.W.U.D. SA
  - Mandatory Reclaimed SA
  - Palm Beach County Limits
  - Administration
  - Water Reclamation Facility
  - Water Treatment Facility
  - Wetlands



CHANGE ORDER

---

**PROJECT: City of Pahokee Inflow and Infiltration Improvements - Phase III**  
**WUD PROJECT NO. WUD 12-049**  
**DISTRICT NO. 6**  
**CHANGE ORDER NO: 1**

**TO:**  
**JCC Enterprises Labor, Inc.**  
**1800 S Ocean Dr. Suite 4304**  
**Hallandale, Fl. 33009**

**DOCUMENT NO. R2013-0160**  
**CONTRACT DATE: February 5, 2013**  
**NOTICE TO PROCEED: March 18, 2013**  
**BUDGET LINE ITEM: 4011-721-W040-6546**

**You are directed to make the following changes in this contract:**

1.1 Final contract adjustment	-	\$36,450.70	
	Total	-	\$36,450.70

City of Pahokee Inflow and Infiltration Improvements- Phase III  
 Project No. WUD 12-049  
 District Number 6  
 Contract No. R2013-0160  
 Change Order No. 1

NOT VALID UNTIL SIGNED BY BOTH OWNER AND ENGINEER. SIGNATURE OF THE CONTRACTOR INDICATES HIS CONTRACT HEREWITH INCLUDING ANY ADJUSTMENT IN THE CONTRACT SUM OR CONTRACT TIME, AND NO ADDITIONAL COST OR TIME INDICATED HEREIN WILL BE RELATED TO THIS CHANGE

The Original Contract Sum was.....	\$ 248,650.00
Net Change by previous Change Orders .....	\$ 0.00
The Contract Sum prior to this Change Order was .....	\$ 248,650.00
The Contract Sum will be <b>decreased</b> by this Change Order.....	\$ -\$36,450.70
The New Contract Sum indicating this Change Order will be...	\$ 212,199.30
The Contract Time will be <b>changed</b> by	<b>82 Days</b>
The Date of Substantial Compl. including this Change Order:	<b>November 5, 2013</b>
The Date of Final Completion including this Change Order:	<b>December 5, 2013</b>


Execution of this change order acknowledges final settlement of, and releases, all claims for costs and time associated, directly or indirectly, with the above stated modification(s), including all claims for cumulative delays or disruptions resulting from, caused by, or incident to such modification(s), and including any claim that the above stated modification(s) constitutes, in whole or part, a cardinal change to the contract.


Palm Beach County Water  
 Utilities Department  
**ENGINEER**  
 P.O. Box 16097  
 W. Palm Beach, Fl.33416  
 Address

JCC Enterprises, Labor, Inc.  
**CONTRACTOR**  
 2441 NW 93 Ave. Ste 103  
 Doral, Fl. 33172  
 Address

Palm Beach County Board of  
 County Comm.  
**OWNER**  
 Box 16097  
 W. Palm Beach, Fl. 33416  
 Address

  
 Signature  
 Jackie Michels , P.E.

  
 Signature  
 Jenny McGregor Cudd

  
 Signature  
 Priscilla A. Taylor, Mayor

DATE 1/27/14

DATE 1/22/14

DATE \_\_\_\_\_

Approved as to Form and Legal Sufficiency

By: \_\_\_\_\_  
 County Attorney

Attest: Sharon R. Brock, Clerk and Comptroller

By: \_\_\_\_\_  
 Deputy Clerk

City of Pahokee Inflow and Infiltration Improvements- Phase III  
Project No. WUD 12-049  
District Number 6  
Contract No. R2013-0160  
Change Order No. 1

**CHANGE ORDER CATEGORIZATION**

OWNER INITIATED

QUANTITY OVERRUNS/UNDER-RUNS

DIFFERING SITE CONDITIONS

REQUEST BY ANOTHER AGENCY/OUTSIDE

ZONING/CODE/ORDINANCE CHANGES

A. REIMBURSABLE

ERRORS/OMISSIONS/IN DESIGN

B. NON-REIMBURSABLE

---

City of Pahokee Inflow and Infiltration Improvements- Phase III  
Project No. WUD 12-049  
District Number 6  
Contract No. R2013-0160  
Change Order No. 1

**Scope of Work**

1.1 Final contract adjustment ( Differing site conditions)

---

City of Pahokee Inflow and Infiltration Improvements- Phase III  
Project No. WUD 12-049  
District Number 6  
Contract No. R2013-0160  
Change Order No. 1

Summary

<u>C.O. #</u>	<u>Description</u>	<u>Additions</u>	<u>(Deletions)</u>	<u>Net Change</u>
1.1	Final contract adjustment		\$36,450.70	
	Total			-\$36,450.70

---



**Final Adjustment of Quantities**

Description	Scheduled Value	Actual Value	Difference
Point Repair	14	26	\$7,200.00
6" co w/ lat	28	43	\$46,000.00
wye or tee	30	10	-\$600.00
connect sewer to main	10	7	-\$3,000.00
mh coating	160	58	-\$19,380.00
ring and cover	10	0	-\$2,000.00
inflow protector	10	11	\$60.00
asphalt removal	400	80	-\$3,200.00
sidewalk repl	200	0	-\$8,000.00
curb and gutter removal	500	0	-\$8,000.00
sod replacement	750	199.94	-\$11,001.20
demuck	500	0	-\$13,500.00
smoke test	10000	10441	\$220.50
tv insp	10000	9375	-\$1,250.00
video	10000	0	-\$10,000.00
allowance	10000	0	-\$10,000.00
			<b>-\$36,450.70</b>



Jackie Michels

Palm Beach County Water Utilities

8100 Forest Hill Blvd.

West Palm Beach, Florida 33416

Dear Ms. Michels:

Re: Time Extension Project WUD 12-049

JCC kindly requests an 82 day extension on our project. There were various delays in progress due to heavy rains which resulted in frequent surcharges in the system. The surcharges prevented us from executing any work whatsoever. The longest instance recorded was from July 9<sup>th</sup> through July 28<sup>th</sup>.

As a small business, we make every effort to complete our work effectively and in a timely matter. Unfortunately we were confronted with situations that were beyond our control.

Thank you for your time and consideration.

Regards,


  
Jenny McGregor Cudd

President


Broward  
1800 S. Ocean Drive #4304  
Hallandale Beach, FL 33009

Miami  
2441 NW 93<sup>rd</sup> Ave Suite 103  
Doral, FL 33172

Tel: (954) 732-2474 Fax: (754) 263-3595  
[www.jccent.com](http://www.jccent.com)



**Palm Beach County  
Water Utilities  
Department  
Service Area (SA) and  
Major Facilities**

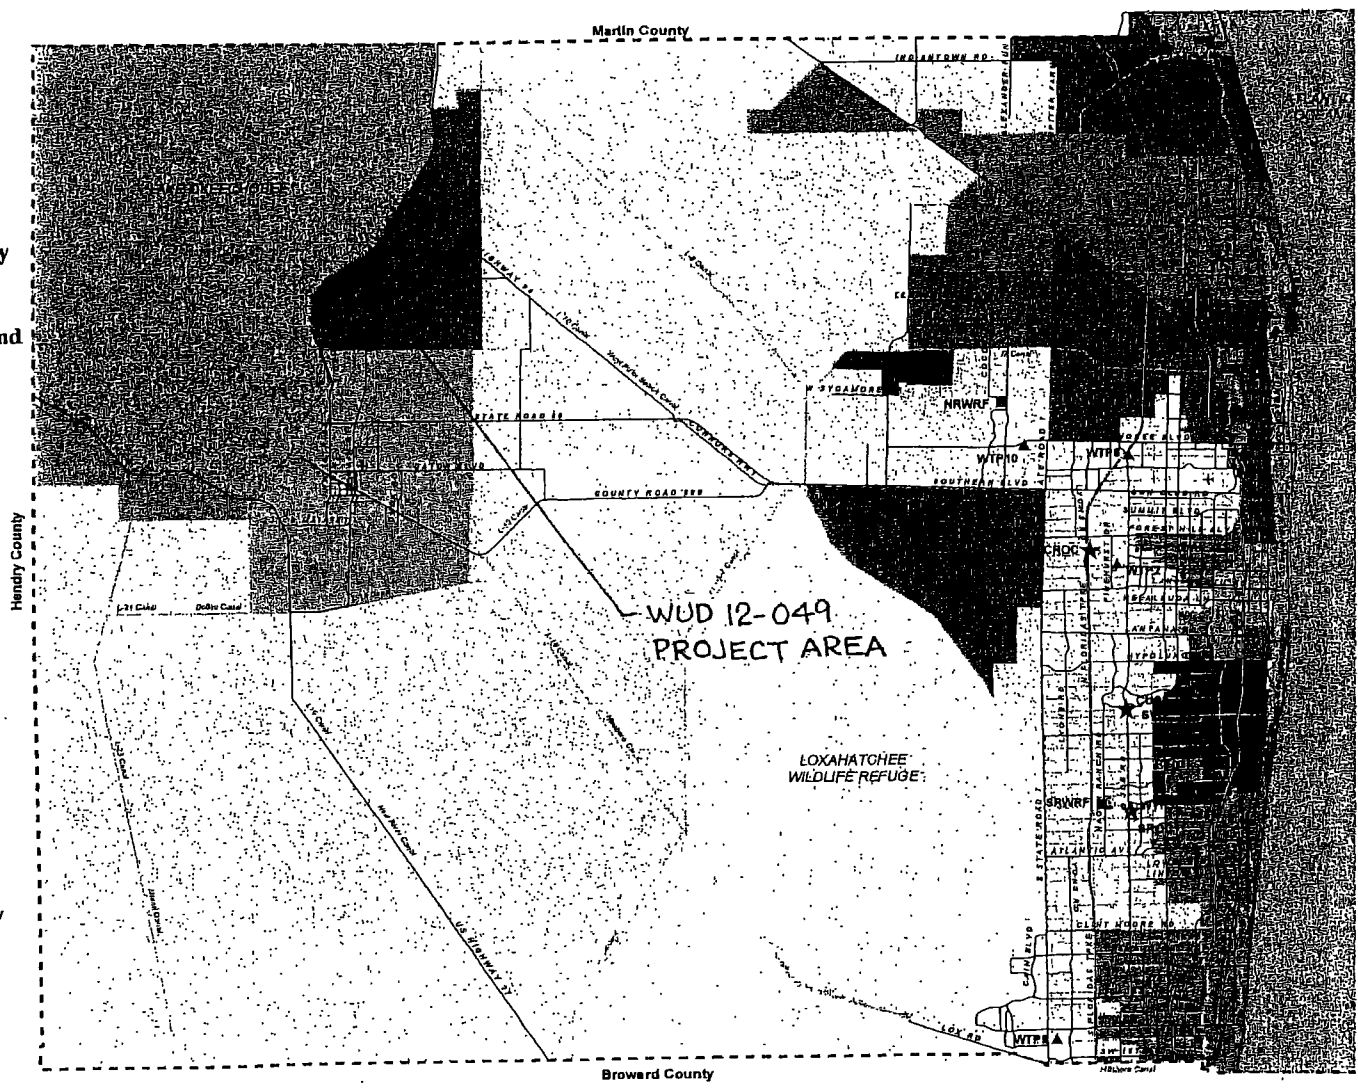

**Legend**

- P.B.C.W.U.D. SA
- Mandatory Reclaimed SA
- Palm Beach County Limits
- Administration
- Water Reclamation Facility
- Water Treatment Facility
- Wetlands



NOT TO SCALE

SCHEDULE 1

PARTICIPATION BY M/WBE SUBCONTRACTORS

PROJECT NAME: City Of Pahokee Inflow and Infiltration Improvements Phase III 12-049  
 NAME OF PRIME CONTRACTOR: JCC Enterprises Labor, Inc. Change Order NO.1 \_\_\_\_\_  
 CONTACT PERSON: Jenny McGregor PHONE NO: \_\_\_\_\_ FAX NO. \_\_\_\_\_  
 Change Order No: 1 DEPARTMENT: Water Utilities

Name, Address and Phone Number of M/WBE	Type of Work To Be Performed	Subcontract Amount			
		Black	Hispanic	Women	Other (Please Specify)
1.		---	---	---	---
2.		---	---	---	---
3.		---	---	---	---
4.		---	---	---	---
5.		---	---	---	---
6.		---	---	---	---
7.		---	---	---	---
8.		---	---	---	---
9.		---	---	---	---
10.		---	---	---	---
Totals		\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00

<b>Original Contract Amount</b>	<u>\$248,650.00</u>	<b>Original Participation</b>	_____	<b>Percent Participation</b>	<u>100%</u>
<b>Adjusted Contract Amount</b>	<u>\$212,199.30</u>	<b>Adjusted Participation</b>	_____	<b>Adjusted Percent</b>	<u>100%</u>

M/WBE

**CHANGE ORDER ADDITIONS/DELETIONS SUMMARY**

PROJECT:	City of Pahokee Inflow & Infiltration Improvements Phase III	<u>APPROVAL LIMITS:</u>							
CONTRACTOR:	JCC Enterprises Labor, Inc. 2441 NW 93 Ave Ste 103 Doral, Florida 33172	DEPARTMENT HEAD		CONTRACT REVIEW COMMITTEE		DEPARTMENT HEAD PLUS CONTRACT REVIEW COMMITTEE			
PROJECT NO.:	WUD 12-049								
RESOLUTION NO.:	R2013-0160		(Amount)	(Days)	(Amount)	(Days)	(Amount)	(Days)	
DATE APPROVED:	February 5, 2013	INDIVIDUAL C.O.	\$50,000.00	25 Days	\$50,000.00	25 Days	\$100,000.00	N/A	
CONTRACT AMOUNT:	\$248,650	CUMMULATIVE C.O.	\$100,000.00	50 Days	\$200,000.00	100 Days	\$200,000.00	N/A	

C.O. #	DATE APPROVED	NET CHANGE	DEPARTMENT HEAD		CONTRACT REVIEW COMMITTEE		TOTAL DEPT. HEAD & CONTRACT REVIEW COMM.		BOARD OF COUNTY COMMISSIONERS		TOTALS
			(ADDS PLUS DEDUCTS) AMOUNT	DAYS	(ADDS PLUS DEDUCTS) AMOUNT	DAYS	(ADDS PLUS DEDUCTS) AMOUNT	DAYS	(ADDS PLUS DEDUCTS) AMOUNT	DAYS	
1	Pending	(\$36,450.70)							(\$36,450.70)	82	(\$36,450.70)
<b>TOTAL</b>			(\$36,450.70)	0	0	0	0	0	0	87	(\$36,450.70)

**Notes:**

1. Net Change reflects the net amount of additions plus deductions.
2. Adds plus Deducts reflects the absolute value of unrelated changes for use in determining the approval authority for the Change Order.
3. Liquidated Damages = \$2,000 per day and \$1,000 per day (After Substantial Completion).

**FINAL CONTRACT SUMMARY**

**Submitted by: WATER UTILITIES DEPARTMENT (Engineering Division)**

**Final Acceptance and Final Payment** in the amount of \$56,885.85 to JCC Enterprises Labor, Inc. for construction of the Contract for City of Pahokee Inflow & Infiltration Improvements- Phase III Project No. WUD 12-049; Document R2013-0160.

Account No. 4011-721-W040-6546

**District No. 6**

**SUMMARY:** On February 5, 2013, the Palm Beach County Board of County Commissioners approved Contract R2013-0160 with JCC Enterprises Labor, Inc for construction of the City of Pahokee Inflow & Infiltration Improvements- Phase III Project. The project consisted of improvements to the City of Pahokee wastewater infrastructure. The project is subject to a 22.4% minority participation goal and a 6.9% female participation goal for trades rather than the County's SBE goals This contract with JCC Enterprises Labor, Inc. provides for 100% participation. The prime contractor is MWBE (100% minority and 0% female participation). JCC Enterprises Labor, Inc has satisfactorily completed the work required under the contract documents.

**Background and Justification:** The Water Utilities Department compiled the documentation necessary for Final Acceptance and Final Payment of the contract with to JCC Enterprises Labor, Inc

\$ 248,650 - Original Contract Amount  
\$ (36,450.70) - Change Order  
\$ 212,199.30 -Final Contract Amount  
\$ 155,313.45 -Previous Payments  
\$ 56,885.85 - Final Payment

**Attachments for Committee:**

1. Project Location Map
2. Payment Application No. 6 ( Final)
3. Final Warranty of Title
4. M/WBE Construction Activity Report, Payment Certifications and Approval
5. Contractor's Certification of Final Completion
6. Consent of Surety of Final Payment
7. Release of Liens
8. Request for Reduction of Retainage

Recommended By: *M. J. ...* 2/4/14  
Director of Engineering/WUD Date

Recommended By: *B. ...* 2/25/14  
Director of Water Utilities Department Date

Palm Beach County Board of County Commissioners

Approved By: \_\_\_\_\_  
Priscilla A. Taylor, Mayor Date

Approved as to Form and Legal Sufficiency

Attest: Sharon R. Brock, Clerk and Comptroller

By: \_\_\_\_\_  
County Attorney

By: \_\_\_\_\_  
Deputy Clerk

**PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

**FINAL CONTRACT SUMMARY**

**ATTACHMENT NO. 1**

**PROJECT LOCATION**

---





**PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

**FINAL CONTRACT SUMMARY**

**ATTACHMENT NO. 2**

**PAYMENT APPLICATION No. 6 (FINAL)**

---

**PERIODICAL ESTIMATE FOR PARTIAL PAYMENT**

Glades Utility Authority City of Pahokee Inflow and Infiltration Improvements -

PROJECT NAME: Phase III  
 PROJECT NUMBER: 12-049 CONTRACT NUMBER: \_\_\_\_\_  
 CONTRACTOR: JCC Enterprises Labor, Inc.  
 ADDRESS: 2441 NW 93rd Ave Suite 103 Doral, FL 33172  
 Application No.: 6 Period 9/28/13 to 12/5/2013  
 From: \_\_\_\_\_  
 Account Number: 4011-721-W040-6546

ANALYSIS OF ADJUSTED CONTRACT AMOUNT TO DATE:

A. Original Contract Amount (Page A-2, Col. 6)	248,650.00	✓
B. Plus: Change Order Additions (Page A-3, Col. 5)	0	
C. Less: Change Order Deletions (Page A-3, Col. 7)	0	
D. Adjusted Contract Amount as of this Estimate	248,650.00	✓

1/24/14  
 JCC

ANALYSIS OF WORK PERFORMED TO DATE:

1. Original Contract Work Performed to Date (Page A-2, Col. 8)	212,199.30
2. Extra Work Performed to Date (Page A-3, Col. 6)	0
3. Total Value of Work Performed To Date	212,199.30
4. Plus: _____ % of Stored Material and Equipment (Attach Schedule & Copies of Invoices)	0
5. Total Work Performed To Date Plus Stored Materials and Equipment	0
6. Less: 0 % Retainage	0
7. Net Amount Earned on Contract to Date	212,199.30
8. Less: Amount of Previous Payments	155,313.45
9. Plus: Reduction in Retainage from _____ % to _____ %	0
10. Balance Due This Payment	56,885.85

CERTIFICATION OF CONTRACTOR:

I hereby certify that I have checked and verified this Periodical Estimate for Payment No. 6, for the period from 9/28/2013 to 12/30/2013, inclusive, and that it is a true and correct statement of all work performed, and/or any and all material and equipment supplied by this Contractor; that all work, materials, and equipment included in Periodical Estimate No. 6 have been performed and/or supplied in full accordance with the terms and conditions of the Contract Documents and/or duly authorized deviations, substitutions, alterations and/or additions; that all terms of Periodical Estimate No. 6 have been authenticated and approved by the authorized undersigned representative of the Contractor.

JCC Enterprises Labor, Inc.  
 \_\_\_\_\_  
 (Contractor)  
 Title President

By Johnny McQueen  
 (Authorized Representative)  
 Date 1/29/2014 1/22/14

**PERIODICAL ESTIMATE FOR PARTIAL PAYMENT**

PROJECT NAME: Glades Utility Authority City of Pahokee Inflow and Infiltration Improvements - Phase III  
PROJECT NUMBER: 12-049 CONTRACT NUMBER: \_\_\_\_\_  
CONTRACTOR: JCC Enterprises Labor, Inc.  
ADDRESS: 2441 NW 93rd Ave Suite 103 Doral, FL 33172  
Application No.: 6 Period 9/28/2013 to 12/5/2013  
From: \_\_\_\_\_  
Account Number: 4011-721-W040-6546

**CERTIFICATION OF CONSTRUCTION REPRESENTATIVE:**

According to the best of my knowledge and belief, I certify that all items and amounts shown on the face of the Periodical Estimate No. 6 are correct; that the work, material and equipment shown thereon has been completed and supplied in conformance with the Contract Documents of the project between PALM BEACH COUNTY (Owner), and JCC Enterprises Labor, Inc. (Contractor), dated \_\_\_\_\_, including any authorized changes, deviations, substitutions, alterations and/or additions; that it is agreed that this Periodical Estimate for Payment No. 6 is a true and correct statement of the Contract Amount, up to and including the last day of the last day of the period covered by this Periodical Estimate No. 6 and that no part of the "balance due" this payment has been received.

\_\_\_\_\_  
PCCWED  
(Resident Project Representative) By gncld  
(Authorized Representative)  
Title PM Date 1/27/14

**CERTIFICATION OF WATER UTILITIES REPRESENTATIVE:**

To the best of my knowledge and belief, all items shown on the face of this Periodical Estimate for Partial Payment No. \_\_\_ are correct and that the work, material and equipment shown thereon has been completed and/or supplied in conformance with the Contract Documents, and is satisfactory for approval and processing for payment.

\_\_\_\_\_  
Palm Beach County Water Utilities Dept.  
(Owner) By mjt  
(Authorized Representative)  
Title Director of Engineering Date 2/9/14

# APPLICATION AND CERTIFICATE FOR PAYMENT

AIA DOCUMENT G702

RECEIVED BY: \_\_\_\_\_

JAN 23 2014

OWNER: PALM BEACH COUNTY  
8100 FOREST HILLS BLVD  
WEST PALM BEACH, FL 33416

CONTRACTOR: JCC ENTERPRISES LABOR, INC  
2441 NW 93RD SUITE 103  
DORAL, FL 33172

PROJECT: GLADES UTILITY AUTHORITY  
CITY OF PAHOKEE INFLOW AND  
INFILTRATION IMPROVEMENTS  
PHASE-III

APPLICATION NUMBER: 6  
PERIOD TO: 12/05/13  
PROJECT NOS.: 12-049

ACCT # 4011-721-W040-6546

VIA CONSTRUCTION MANAGER: JACKIE MICHELS

Distribution to:  
 OWNER  
 CONSTRUCTION  
MANAGER  
 ARCHITECT  
 CONTRACTOR

## CONTRACTOR'S APPLICATION FOR PAYMENT

Application is made for payment, as shown below, in accordance with the Contract.

Continuation Sheet, AIA Document G703, is attached.

1. ORIGINAL CONTRACT SUM	\$248,650.00
2. Net Change By Change Orders.....	\$0.00
3. CONTRACT SUM TO DATE (Line 1 +2).....	\$ 248,650.00
4. TOTAL COMPLETED & STORED TO DATE.....	\$212,199.30
5. RETAINAGE:	
a. 0% % of Completed Work	\$0.00
b. 10% % of Stored Material	\$0.00
Total Retainage (Line 5a + 5b or	\$0.00
6. TOTAL EARNED LESS RETAINAGE.....	\$212,199.30
(Line 4 less Line 5 Total)	
7. LESS PREVIOUS CERTIFICATES FOR PAYMENT	
(Line 6 from prior Certificate)	\$155,313.45
8. CURRENT PAYMENT DUE	\$56,885.85
9. BALANCE TO FINISH, INCLUDING RETAINAGE	
(Line 3 less Line 6)	\$ 36,450.70


CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous months by Owner		
Total Approved this Month		
TOTALS	\$0.00	\$0.00
NET CHANGES by Change Order		\$0.00

The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief, the Work covered by this Application for Payment has been completed in accordance with the Contract Documents, that all amounts have been paid by the Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown herein is now due.

CONTRACTOR:

BY: Johnny McGowan Add DATE 1/22/14

State of: Florida County of: Miami Dade  
Subscribed and sworn before me this 22 day of JAN 2014  
Notary Public: Marie M Charles  
My Commission Expires: 7/19/15



## CERTIFICATE FOR PAYMENT

In accordance with the Contract Documents, based on on-site observations and the data comprising the above application, the Construction Manager certifies that to the best of his knowledge, information and belief the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

AMOUNT CERTIFIED..... \$ 56,885.85

(Attach explanation if amount certified differs from the amount applied for. Initial all figures on this Application and on the Continuation Sheet that changed to conform to the amount certified.)

CONSTRUCTION MGR:

By: \_\_\_\_\_ Date: \_\_\_\_\_

ARCHITECT:

By: \_\_\_\_\_ Date: \_\_\_\_\_

This certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.

**CONTINUATION SHEET**

AIA DOCUMENT G703

AIA Document G702, APPLICATION AND CERTIFICATE FOR PAYMENT,  
 containing Contractor's signed Certification is attached.  
 In tabulations below, amounts are stated to the nearest dollar.

A ITEM NO.	B DESCRIPTION OF WORK	C UNITS	D QTY	E UNIT PRICE	F TOTAL CONTRACT PRICE	G QUANTITY COMPLETED PREVIOUS	H TOTAL COMPLETED PREVIOUS	I QUANTITY COMPLETED CURRENT	J TOTAL COMPLETED CURRENT	K TOTAL COMPLETED TO DATE	L % COMP	M BALANCE TO FINISH	N RETAINAGE
1	Point Repairs 8", 10 and 12" pipe at depths up to 4 9 ft	L.F.	5	\$600.00	\$3,000.00	18.00	\$10,800.00	8 00	\$4,800.00	\$15,600.00	520%	-21	\$1,560.00
2	Point Repairs 8", 10 and 12" pipe at depths up to 5 ft to 7.9 ft	L.F.	5	\$600.00	\$3,000.00	0.00	\$0.00	0.00	\$0.00	\$0 00	0%	5	\$0 00
3	Point Repairs 8", 10 and 12" pipe at depths up to 5 ft to 7.9 ft	L.F.	2	\$600.00	\$1,200.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	2	\$0.00
4	Point Repairs 8", 10 and 12" pipe at depths up to 10 ft to 12 ft	L.F.	2	\$27.00	\$1,200.00	0.00	\$0.00	0 00	\$0.00	\$0.00	0%	2	\$0.00
5	6" PVC SDR 26 Gravity Service Lateral with cleanout- 0'-6' deep	EA.	5	\$3,200.00	\$16,000.00	0 00	\$0 00	0 00	\$0.00	\$0 00	0%	5	\$0 00
6	6" PVC SDR 26 Gravity Service Lateral with cleanout- 6'-8' deep	EA.	5	\$3,200.00	\$16,000.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	5	\$0.00
7	6" PVC SDR 26 Gravity Service Lateral with cleanout- 8'-10' deep	EA.	2	\$3,300 00	\$6,600.00	0 00	\$0.00	0 00	\$0.00	\$0.00	0%	2	\$0.00
8	6" PVC SDR 26 Gravity Service Lateral with cleanout-10'-12' deep	EA.	2	\$3,500.00	\$7,000.00	0 00	\$0.00	0 00	\$0.00	\$0 00	0%	2	\$0.00
9	4" PVC SDR 26 Gravity Service Lateral with cleanout- 0'-6' deep	EA.	5	\$3,200.00	\$16,000.00	36.00	\$115,200.00	7.00	\$22,400.00	\$137,600.00	860%	-38	\$13,760.00
10	4" PVC SDR 26 Gravity Service Lateral with cleanout- 6'-8' deep	EA.	5	\$3,200.00	\$16,000.00	0.00	\$0.00	0.00	\$0.00	\$0 00	0%	5	\$0.00
11	4" PVC SDR 26 Gravity Service Lateral with cleanout- 8'-10' deep	EA.	2	\$3,500.00	\$7,000.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	2	\$0.00
12	4" PVC SDR 26 Gravity Service Lateral with cleanout-10'-12' deep	EA.	2	\$3,500.00	\$7,000.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	2	\$0.00
13	8"x6" PVC Tee or Wye with Coupling	EA.	15	\$30.00	\$450.00	1.00	\$30.00	9.00	\$270.00	\$300.00	67%	5	\$30.00
14	10"x6" PVC Tee or Wye with Coupling	EA.	15	\$30.00	\$450.00	0.00	\$0.00	0.00	\$0 00	\$0 00	0%	15	\$0.00
15	Connect New Gravity Sanitary Sewer Line to Existing Manhole	EA.	10	\$1,000.00	\$10,000.00	5.00	\$5,000.00	2.00	\$2,000.00	\$7,000.00	70%	3	\$700.00
16	Sewer Manhole coating (4-ft Diam. Manhole) Add.# 2	V F	160	\$190.00	\$30,400.00	58.00	\$11,020.00	0.00	\$0.00	\$11,020.00	36%	102	\$1,102.00
17	Sewer Manhole Ring & Covers	EA.	10	\$200.00	\$2,000.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	10	\$0 00
18	Sewer Manhole Inflow Protectors	EA.	10	\$60.00	\$600.00	0.00	\$0.00	11.00	\$660.00	\$660.00	110%	-1	\$66.00
19	Asphalt Pavment Removal and Restoration	Sq. Yd.	400	\$10 00	\$4,000.00	80.00	\$800.00	0.00	\$0 00	\$800.00	20%	320	\$80.00
20	Concrete Sidewalk Replacement	Sq. Yd.	200	\$40.00	\$8,000.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	200	\$0.00
21	Concrete Curb and Gutter Replacement	L.F.	500	\$16.00	\$8,000.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	500	\$0.00
22	Sod Replacement	Sq. Yd.	750	\$20.00	\$15,000.00	0.00	\$0.00	199.94	\$3,998.80	\$3,998 80	27%	550	\$399.88

A	B	C	D	E	F	G	H	I	J	K	L	M	N
ITEM NO.	DESCRIPTION OF WORK	UNITS	QUANTITY	UNIT PRICE	TOTAL CONTRACT PRICE	QUANTITY COMPLETED PREVIOUS	TOTAL COMPLETED PREVIOUS	QUANTITY COMPLETED CURRENT	TOTAL COMPLETED CURRENT	TOTAL COMPLETED TO DATE	% COMP.	BALANCE TO FINISH	RETAINAGE
23	Demucking with Imported Clean Fill	Cu.yd	500	\$27.00	\$13,500.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	500	\$0.00
24	Maintenance of Traffic (M.O.T)	L.F	2500	\$0.50	\$1,250.00	1,500.00	\$750.00	1000.00	\$500.00	\$1,250.00	100%	0	\$125.00
25	Smoke Test	L.F.	10000	\$0.50	\$5,000.00	10,441.00	\$5,220.50	0.00	\$0.00	\$5,220.50	104%	-441	\$522.05
26	Sewer Line/Lateral TV Inspection		10000	\$2.00	\$20,000.00	9,375.00	\$18,750.00	0.00	\$0.00	\$18,750.00	94%	625	\$1,875.00
27	Pre-Construction Video	L.F.	10000	\$1.00	\$10,000.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	10000	\$0.00
28	Mobilization/Demobilization	L.S.	1	\$10,000.00	\$10,000.00	0.50	\$5,000.00	0.50	\$5,000.00	\$10,000.00	100%	0	\$1,000.00
29	Contract Allowance for Miscellaneous Items	L.S.	1	\$10,000.00	\$10,000.00	0.00	\$0.00	0.00	\$0.00	\$0.00	0%	1	\$0.00
30													
31	<b>TOTALS</b>				\$248,650.00		\$172,570.50		\$39,628.80	\$212,199.30			\$21,219.93
	<b>TOTALS AFTER RETAINAGE</b>						\$155,313.45						

**PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

**FINAL CONTRACT SUMMARY**

**ATTACHMENT NO. 3**

**FINAL WARRANTY OF TITLE**

---

FINAL WARRANTY OF TITLE

STATE OF FLORIDA \_\_\_\_\_ )

COUNTY OF Palm Beach )

*Jimmy McGregor Caud*

Before me, the undersigned authority, personally appeared \_\_\_\_\_, who was duly sworn and says:

1. Affiant is the President of XCC Enterprises Labor, Inc a Florida (hereinafter called the "Contractor").

2. Contractor entered into a Contract dated the 5<sup>th</sup> day of February, 2013 (hereinafter called the "Contract") with the **PALM BEACH COUNTY**, a political subdivision of the State of Florida (hereinafter called the "County"), being Contract No. 12-049 for the construction of certain improvements and the performance of certain Work more particularly described in the Contract Documents (such construction and performance being hereinafter collectively referred to as the "Work"), on property owned and or controlled by the County, located in 12-049.

3. Contractor has fully completed the Work and all individuals, firms, and corporations furnishing materials, labor, equipment, tools, supplies, manufactured articles and services incident to the completion of the Work, and all payrolls, bills for materials, equipment, tools, supplies, manufactured articles, and all other indebtedness connected with the Work, have been paid in full, except for the following:

None, unless set forth below:

Name	Address	Amount Due or to Become Due and Unpaid
_____	_____	_____
_____	_____	_____
_____	_____	_____

(Attach additional sheets, if more space is needed)

4. Receipt by Contractor of the Final Payment from County in the amount of \$ 5,885.85 shall constitute a full release and discharge by Contractor to said County of all claims and liens of the Contractor against said County arising out of, connected with, or resulting from performance of the Contract or the Work.

5. The undersigned further certifies that all non-exempt taxes imposed by Chapter 212, Florida Statutes (Sales and Use Tax Act), as amended, have been paid and discharged.

6. Contractor agrees to forever indemnify, defend, and hold said County harmless from and against all costs and expenses, including reasonable attorney's fees, including fees on appeal, resulting from individuals, firms, or corporations who claim to have not been paid for material, labor, equipment, tools, supplies, manufactured articles or services furnished incident to the Work.

7. This Affidavit is made for the purpose of inducing Final Payment from the County to the Contractor under the Contract in compliance with the Contract Documents.





**PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

**FINAL CONTRACT SUMMARY**

**ATTACHMENT NO. 4**

**M/WBE CONSTRUCTION ACTIVITY REPORT  
PAYMENT CERTIFICATIONS AND APPROVALS**

---

**SCHEDULE 3  
SBE-M/WBE ACTIVITY FORM**

SBE-M/WBE ACTIVITY FOR MONTH ENDING \_\_\_\_\_ PROJECT # 12-049

PROJECT NAME Glades Utility Authority City of Pahokee Inflow and Infiltration Improvements - Phase III

PRIME CONTRACTOR NAME JCC ENTERPRISES LABOR, INC.

PROJECT SUPERVISOR \_\_\_\_\_

Schedule 3 is used to show the monthly payment activity for work performed by each SBE-M/WBE Subcontractor on the project and in conformity with the SBE-M/WBE's submitted on schedule 2. It also shows approved change orders as they impact the SBE-M/WBE Subcontractors. Schedule 3 is to be submitted by the Prime with each payment request to Palm Beach County. In the SBE-M/WBE Subcontracting Information section, list the name(s) of each SBE-M/WBE Subcontractor on the project and the total contracted amount for each SBE-M/WBE Subcontractor on the project. As the project proceeds, please complete each column under the SBE-M/WBE Subcontracting Information section accordingly. In the SBE-M/WBE Category, please check the appropriate category that represents each SBE-M/WBE Subcontractor.

SBE-M/WBE SUBCONTRACTING INFORMATION								SBE-M/WBE Category (check all applicable)						
Name of SBE-M/WBE Subcontractor	SBE-M/WBE Total Contract Amount	Approved Change Orders	Revised SBE-M/WBE Contract Amount	Amount drawn for SBE-M/WBE Sub This Period	Amount drawn for SBE-M/WBE Sub to Date	Amount Paid to Date for SBE-M/WBE Subcontractor	Actual Starting Date	Minority Business (✓)	Small Business (✓)	Black	Hispanic	Women	Caucasian	Other (Please Specify)
<b>JCC IS A SELF PERFORMING W/WBE</b>														

I hereby certify that the above information is true to the best of my knowledge \_\_\_\_\_  
(Signature and Title)

Return to: Palm Beach County

Additional Sheets May Be Used As Necessary

**NOTE:** Firms may be certified as an SBE and/or an M/WBE. If firms are certified as both an SBE and M/WBE, the dollar amount will not be counted twice.



**PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

**FINAL CONTRACT SUMMARY**

**ATTACHMENT NO. 5**

**CONTRACTOR'S CERTIFICATE OF FINAL COMPLETION**

---

**CONTRACTOR'S CERTIFICATION OF FINAL COMPLETION**

TO: PBCWUD Date 12/5/13

PROJECT 12-049 JOB NO. \_\_\_\_\_

CONTRACT NO. R2013-0160

ATTN: Jackie Michels

COUNTY: Palm Beach

ENGINEER \_\_\_\_\_

FROM: JCC Enterprise Labor, Inc  
(Firm or Corporation)

This is to certify that I, Jenny M Greer Cudd am an authorized official of JCC Enterprise Labor, Inc working in the capacity of President and have

been properly authorized by said firm or corporation to sign the following statements pertaining to the subject Contract:

I know of my own personal knowledge, and do hereby certify, that the work of the Contract described above has been performed, and materials used and installed in every particular, in accordance with, and in conformity to, the Contract Documents and approved changes thereto.

The contract work is now complete in all parts and requirements, and ready for your final inspection.

I understand that neither the determination by the Engineer that the work is complete, nor the acceptance thereof by the County, shall operate as a bar to claim against the Contractor under the terms of the guarantee provisions of the Contract Documents.

BY: Jenny M Greer Cudd TITLE President  
FOR JCC Enterprise Labor, Inc

Recommended by the ENGINEER:

By: J Michels Professional Engineer Jackie Michels Date: 1/27/14  
Print Name

County acknowledges receipt of this Certificate of Final Completion:

By: M L Director of Engineering Maurice Tobon Date: 2/4/14  
Print Name

**PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

**FINAL CONTRACT SUMMARY**

**ATTACHMENT NO. 6**

**CONSENT OF SURETY OF FINAL PAYMENT**

---

CONSENT OF SURETY FOR FINAL PAYMENT

PROJECT NAME: Glades Utility Authority City of Pahokee Inflow and Infiltration Improvements - Phase III

PROJECT LOCATION: City of Pahokee

PROJECT NO.: 12-049 CONTRACT NO: \_\_\_\_\_ CONTRACT DATE: \_\_\_\_\_

CONTRACT TYPE: \_\_\_\_\_

CONTRACT AMOUNT: \$212,199.30 ENGINEER'S PROJECT NO.: \_\_\_\_\_

ENGINEER: \_\_\_\_\_

In accordance with the provisions of the above named Contract between the County and the Contractor, the following named Surety


American Contractors Indemnity Company

on the PUBLIC CONSTRUCTION BOND of the following named Contractor: JCC Enterprises Labor, Inc.

hereby approves of final payment by County to the Contractor and further agrees that said final payment to the Contractor shall not relieve the Surety Company named herein of any of its obligations to the following named County as set forth in said Surety Company's bond.

Palm Beach County

IN WITNESS WHEREOF, the Surety Company has hereunto set its hand and seal this 10th day of January 2014.

  
\_\_\_\_\_  
(Attest) Jeremy Crawford, Vice President

American Contractors Indemnity Company  
(Name of Surety Company)

(Affix corporate seal)

  
\_\_\_\_\_  
(Signature of Authorized Representative)

TITLE: Andrea J. Michael Haight, Attorney-in-fact

RECEIVED BY: \_\_\_\_\_  
JAN 15 2014  
PBCWUD ENGINEERING



POWER OF ATTORNEY

AMERICAN CONTRACTORS INDEMNITY COMPANY UNITED STATES SURETY COMPANY U.S. SPECIALTY INSURANCE COMPANY

KNOW ALL MEN BY THESE PRESENTS: That American Contractors Indemnity Company, a California corporation, United States Surety Company, a Maryland corporation and U.S. Specialty Insurance Company, a Texas corporation (collectively, the "Companies"), do by these presents make, constitute and appoint:

Andrea J. Michael Haight or Bradford J. Quiri of Tampa, Florida

its true and lawful Attorney(s)-in-fact, each in their separate capacity if more than one is named above, with full power and authority hereby conferred in its name, place and stead, to execute, acknowledge and deliver any and all bonds, recognizances, undertakings or other instruments or contracts of suretyship to include riders, amendments, and consents of surety, providing the bond penalty does not exceed \*\*\*\*\*Three Million\*\*\*\*\* Dollars (\$ \*\*3,000,000.00\*\*), This Power of Attorney shall expire without further action on December 08, 2016. This Power of Attorney is granted under and by authority of the following resolutions adopted by the Boards of Directors of the Companies:

Be it Resolved, that the President, any Vice-President, any Assistant Vice-President, any Secretary or any Assistant Secretary shall be and is hereby vested with full power and authority to appoint any one or more suitable persons as Attorney(s)-in-Fact to represent and act for and on behalf of the Company subject to the following provisions:

Attorney-in-Fact may be given full power and authority for and in the name of and on behalf of the Company, to execute, acknowledge and deliver any and all bonds, recognizances, contracts, agreements or indemnity and other conditional or obligatory undertakings, including any and all consents for the release of retained percentages and/or final estimates on engineering and construction contracts, and any and all notices and documents canceling or terminating the Company's liability thereunder, and any such instruments so executed by any such Attorney-in-Fact shall be binding upon the Company as if signed by the President and sealed and effected by the Corporate Secretary.

Be it Resolved, that the signature of any authorized officer and seal of the Company heretofore or hereafter affixed to any power of attorney or any certificate relating thereto by facsimile, and any power of attorney or certificate bearing facsimile signature or facsimile seal shall be valid and binding upon the Company with respect to any bond or undertaking to which it is attached.

IN WITNESS WHEREOF, The Companies have caused this instrument to be signed and their corporate seals to be hereto affixed, this 10th day of December, 2012.

AMERICAN CONTRACTORS INDEMNITY COMPANY UNITED STATES SURETY COMPANY U.S. SPECIALTY INSURANCE COMPANY

Corporate Seals



[Signature] Daniel P. Aguilar, Vice President


State of California

County of Los Angeles SS:

On 10th day of December, 2012, before me, Vanessa Wright, a notary public, personally appeared Daniel P. Aguilar, Vice President of American Contractors Indemnity Company, United States Surety Company and U.S. Specialty Insurance Company who proved to me on the basis of satisfactory evidence to be the person whose name is subscribed to the within instrument and acknowledged to me that he executed the same in his authorized capacity, and that by his signature on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct. I witness my hand and official seal.

Signature [Signature] (Seal)



I, Jeannie Lee, Assistant Secretary of American Contractors Indemnity Company, United States Surety Company and U.S. Specialty Insurance Company, do hereby certify that the above and foregoing is a true and correct copy of a Power of Attorney, executed by said Companies, which is still in full force and effect; furthermore, the resolutions of the Boards of Directors, set out in the Power of Attorney are in full force and effect.

In Witness Whereof, I have hereunto set my hand and affixed the seals of said Companies at Los Angeles, California this 10th day of January, 2014.

Corporate Seals

Bond No. 1000883703 Agency No. 17595



[Signature] Jeannie Lee, Assistant Secretary

**PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

**FINAL CONTRACT SUMMARY**

**ATTACHMENT NO. 7**

**RELEASE OF LIENS**

---

WAIVER AND RELEASE OF LIEN  
FINAL PAYMENT



Customer No: 0588292


The undersigned lienor, in consideration of the final payment in the amount of \$6,158.40, hereby waives and releases its lien and right to claim a lien for labor, services or materials furnished to JCC ENTERPRISES LABOR INC on the job of RESIDENCE owned by PALM BEACH COUNTY WATER UTILITIES DEPARTMENT, to the following described property:

RESIDENCE 494 E JORDAN BLVD, PAHOKEE FL PUBLIC; CONTRACT # 12-049 Account No. 0588292


DATED 12/19/2013

**SUNBELT RENTALS INC**

2015 Directors Row  
Orlando, FL 32809  
407-816-1591

By:   
Danny Chipp, Regional Credit Manager

SUBSCRIBED, SWORN TO AND ACKNOWLEDGED BEFORE ME this 19 day of December 2013 by Danny Chipp, agent for Sunbelt Rentals Inc., who is personally known to me or who has produced \_\_\_\_\_ as identification, and who did/did not take an oath.

  
NOTARY PUBLIC, Orange County, FL

My Commission Expires: \_\_\_\_\_

Document prepared by Darlene Walker



**FINAL WAIVER AND RELEASE OF LIEN  
AND PAYMENT BOND CLAIM**

The undersigned lienor, in consideration of the sum of **\$8,940.00** hereby waives and releases its lien and right to claim a lien and claim against JCC Enterprises Labor, Inc. and its payment bond, and Palm Beach County, for labor, services, or materials furnished to JCC Enterprises Labor, Inc. on the job of Project No: 12-049 Project Name: Glades Utility Authority City of Pahokee Inflow and Infiltration Improvements – Phase III

DATED on December 20, 2013<sup>1300</sup>

**Company:** **Hinterland Group, Inc.**  
**5401 North Haverhill Road**  
**Suite 114**  
**West Palm Beach, Florida 33407**

By: \_\_\_\_\_  
Print name: Daniel Duke  
Title: President

**STATE OF FLORIDA**  
**COUNTY OF** Palm Beach

The foregoing instrument was acknowledged before me this 20 / December 2013 by Daniel Duke, who is personally known to me or who has produced \_\_\_\_\_ (type of identification) and who (did/did not) take an oath.

\_\_\_\_\_  
Notary Public, State of Florida  
Chase Rogers  
Type or Print Name  
My Commission expires:



Broward 1800 S. Ocean Drive #4304 Hallandale Beach, FL 33009 Tel: (954) 732-2474 Fax: (754) 263-3595 www.jccent.com  
Miami 2441 NW 93<sup>rd</sup> Ave Suite 103 Doral, FL 33172

**FINAL WAIVER AND RELEASE OF LIEN  
AND PAYMENT BOND CLAIM**

The undersigned lienor, in consideration of the sum of 1,500.00 hereby waives and releases its lien and right to claim a lien and claim against JCC Enterprises Labor, Inc. and its payment bond, and Palm Beach County, for labor, services, or materials furnished to JCC Enterprises Labor, Inc. on the job of Project No: 12-049 Project Name: Glades Utility Authority City of Pahokee Inflow and Infiltration Improvements - Phase III

DATED on 27<sup>th</sup> December, 2013

Company: **BP Concrete Inc.**  
101100 Caribbean Blvd  
Miami, FL 33139

By: [Signature]  
Print name: Benjamin Padilla 12/27/13  
Title: President


STATE OF FLORIDA

COUNTY OF Miami Dade

The foregoing instrument was acknowledged before me this 27<sup>th</sup> Dec 2013 by Benjamin Padilla, who is personally known to me or who has produced a Florida Dr Lic. (type of identification) and who (did/did not) take an oath.

[Signature]  
Notary Public, State of Florida  
Albert Garcia

Type or Print Name  
My Commission expires:



Broward  
1800 S. Ocean Drive #4304  
Hallandale Beach, FL 33009

Miami  
2441 NW 93<sup>rd</sup> Ave Suite 103  
Doral, FL 33172

Tel: (954) 732-2474 Fax: (754) 263-3595  
www.jccent.com

**PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

**FINAL CONTRACT SUMMARY**

**ATTACHMENT NO. 8**

**REQUEST FOR REDUCTION OF RETAINAGE**

---

**REQUEST FOR ADJUSTMENT OF RETAINAGE**

Bond No. 1000883763

PROJECT NAME: Glades Utility Authority City of Pahokee Inflow and Infiltration Improvements - Phase III

PROJECT NO.: 12-049

County: Palm Beach CONTRACT NO.: R2013-0160

ENGINEER: \_\_\_\_\_ PROJECT MANAGER Jackie Michels

CONTRACTOR: JCC Enterprises Labor, Inc.

The Contractor, JCC Enterprises Labor, Inc. hereby requests that the percentage of partial payment estimates retained by the County under the provisions of the Contract Documents be REDUCED from 10 % to 0 %.

By Jenny M. Gray Ludd Date 1/26/14  
Contractor Representative  
Title President

The Surety on the Public Construction Bond for said project:

American Contractors Indemnity Company  
hereby approves the foregoing request.

By Andrea J. Michael Haight Date 01/23/14  
Andrea J. Michael Haight, Attorney-in-fact

Power of Attorney must be attached to original copy

Approval IS/IS NOT recommended. The percentage of completed work as of 1/26/14,  
2014 is 100 % and the present percentage of elapsed contract time as of 1/26/14,  
2014 is 100 %

By J. Michels Date 1/27/14  
Resident Project Representative

Approval  IS/IS NOT recommended:

By J. Michels Date 1/27/14  
Project Manager

APPROVED/DISAPPROVED:

By [Signature] Date 2/4/14  
County's Representative

POWER OF ATTORNEY

AMERICAN CONTRACTORS INDEMNITY COMPANY UNITED STATES SURETY COMPANY U.S. SPECIALTY INSURANCE COMPANY

KNOW ALL MEN BY THESE PRESENTS: That American Contractors Indemnity Company, a California corporation, United States Surety Company, a Maryland corporation and U.S. Specialty Insurance Company, a Texas corporation (collectively, the "Companies"), do by these presents make, constitute and appoint:

Andrea J. Michael Haight or Bradford J. Quiri of Tampa, Florida

its true and lawful Attorney(s)-in-fact, each in their separate capacity if more than one is named above, with full power and authority hereby conferred in its name, place and stead, to execute, acknowledge and deliver any and all bonds, recognizances, undertakings or other instruments or contracts of suretyship to include riders, amendments, and consents of surety, providing the bond penalty does not exceed \*\*\*\*\* Three Million \*\*\*\*\* Dollars (\$ \*\*3,000,000.00\*\*). This Power of Attorney shall expire without further action on December 08, 2016. This Power of Attorney is granted under and by authority of the following resolutions adopted by the Boards of Directors of the Companies:

Be it Resolved, that the President, any Vice-President, any Assistant Vice-President, any Secretary or any Assistant Secretary shall be and is hereby vested with full power and authority to appoint any one or more suitable persons as Attorney(s)-in-Fact to represent and act for and on behalf of the Company subject to the following provisions:


Attorney-in-Fact may be given full power and authority for and in the name of and on behalf of the Company, to execute, acknowledge and deliver any and all bonds, recognizances, contracts, agreements or indemnity and other conditional or obligatory undertakings, including any and all consents for the release of retained percentages and/or final estimates on engineering and construction contracts, and any and all notices and documents canceling or terminating the Company's liability thereunder, and any such instruments so executed by any such Attorney-in-Fact shall be binding upon the Company as if signed by the President and sealed and effected by the Corporate Secretary.

Be it Resolved, that the signature of any authorized officer and seal of the Company heretofore or hereafter affixed to any power of attorney or any certificate relating thereto by facsimile, and any power of attorney or certificate bearing facsimile signature or facsimile seal shall be valid and binding upon the Company with respect to any bond or undertaking to which it is attached.

IN WITNESS WHEREOF, The Companies have caused this instrument to be signed and their corporate seals to be hereto affixed, this 10th day of December, 2012.

AMERICAN CONTRACTORS INDEMNITY COMPANY UNITED STATES SURETY COMPANY U.S. SPECIALTY INSURANCE COMPANY

Corporate Seals



[Signature] Daniel P. Aguilar, Vice President


State of California

County of Los Angeles SS:

On 10th day of December, 2012, before me, Vanessa Wright, a notary public, personally appeared Daniel P. Aguilar, Vice President of American Contractors Indemnity Company, United States Surety Company and U.S. Specialty Insurance Company who proved to me on the basis of satisfactory evidence to be the person whose name is subscribed to the within instrument and acknowledged to me that he executed the same in his authorized capacity, and that by his signature on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct. WITNESS my hand and official seal.

Signature [Signature] (Seal)



I, Jeannie Lee, Assistant Secretary of American Contractors Indemnity Company, United States Surety Company and U.S. Specialty Insurance Company do hereby certify that the above and foregoing is a true and correct copy of a Power of Attorney, executed by said Companies, which is still in full force and effect, furthermore, the resolutions of the Boards of Directors, set out in the Power of Attorney are in full force and effect.

In Witness Whereof, I have hereunto set my hand and affixed the seals of said Companies at Los Angeles, California this 23rd day of January, 2014.

Corporate Seals

Bond No. 1000883763 Agency No. 17595



[Signature] Jeannie Lee, Assistant Secretary




Acknowledgment of Surety

State of Florida  
County of Hillsborough

On this 23<sup>rd</sup> day of **January, 2014** before me personally appeared **Andrea J. Michael Haight** who acknowledged that she is the attorney in fact who is authorized to sign on behalf of **American Contractors Indemnity Company** (surety company), the foregoing instrument, and she thereupon duly acknowledged to me that she executed the same.



  
Notary Public
