

**PALM BEACH COUNTY
BOARD OF COUNTY COMMISSIONERS
AGENDA ITEM SUMMARY**

Meeting Date:	June 10, 2025	{X} Consent { } Workshop	{ } Regular { } Public Hearing
Department:	Engineering & Public Works		
Submitted By:	Engineering & Public Works		
Submitted For:	Construction Coordination Division		

I. EXECUTIVE BRIEF

Motion and Title: Staff recommends motion to approve: Change Order No. 6 in the amount of \$587,939.25 and a retroactive time extension of 538 days to the contract dated February 9, 2021 (R2021-0212) (Contract) with Ranger Construction Industries, Inc. (Ranger) for Palmetto Park Road, SW 7th Avenue to SW 5th Avenue (Project).

SUMMARY: In accordance with Contract General Provisions (GP) 4-3, 5-12.2.2, and 8-7.3.2, the approval of Change Order No. 6 will provide compensation to Ranger for additional time and costs resulting from multiple unforeseen circumstances as follows:

1. Work was delayed for 11 days after the notice to proceed (NTP) on August 2, 2021, due to unresolved AT&T utility relocations. Ranger could not begin work until August 13, 2021, leading to monetary compensation of \$2,182.24 for this delay.
2. Pursuant to Contract GP 8-6.1, clearing and grubbing operations were temporarily suspended due to the presence of mangroves, protected trees impacted by construction activities along the shoreline of the El Rio Canal. An additional specialized permit was required before work could continue on the north side of the proposed bridge. The necessary permit was submitted on August 30, 2021, and final approval was granted on October 15, 2021. As the suspension of operations was not due to Ranger's fault, GP 8-7.3.2 supports the 46-day time extension for the delay in obtaining the tree permit.
3. An existing 24-inch drainage pipe was found to be misaligned by 9 feet from its location outlined in the plans. This differing site condition required the procurement of additional pipe, the removal of the existing pipe, and the performance of connection work. These activities caused a 137-day delay from April 16, 2022, to August 31, 2022.
4. Compensation and a 46-calendar-day time extension are requested due to delays and additional work associated with paving operations. Specifically, asphalt overbuild was required to accommodate elevation modifications necessary to achieve Americans with Disabilities Act (ADA) compliance at the crosswalk located at the driveway entrance to St. Paul Lutheran Church. This claim amounts to \$76,008.61 and includes costs incurred by Ranger for the additional asphalt overbuild, delays related to overhead, supervision, surveying, labor, and equipment necessary for the removal and replacement of affected sidewalks, curbs, and traffic control devices.
5. During Phase 3 of the proposed bridge construction, Ranger's subcontractor, Anzac, encountered unforeseen underground obstructions that impeded the installation of concrete piles and precast sheet piles. These unexpected conditions were encountered multiple times and significantly disrupted Anzac's progress. Ranger requested additional compensation and a time extension due to the resulting schedule impacts. The total claim amount is \$470,476.74 and 142 additional days, encompassing Anzac's direct costs and Ranger's overhead, supervision, and traffic control devices expenses.
6. Concurrent utility issues with overhead electrical lines required a shift of pile locations, as well as pile cap and sheet pile wall redesign for construction, totaling \$39,271.66 for additional associated work.

Continued on Page 3

Background and Justification:

Continued on Page 3

Attachments:

1. Location Map
2. Change Order No. 6 with Exhibits A, B, C, D, and E

Recommended by: J. Carroll Kiser FOR
YBH/TEL County Engineer

05/19/2025
Date

Approved by: Pao
Deputy County Administrator

5/23/25
Date

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

Fiscal Years	2025	2026	2027	2028	2029
Capital Expenditures	\$587,940	-0-	-0-	-0-	-0-
Operating Costs	-0-	-0-	-0-	-0-	-0-
External Revenues	-0-	-0-	-0-	-0-	-0-
Program Income (County)	-0-	-0-	-0-	-0-	-0-
In-Kind Match (County)	-0-	-0-	-0-	-0-	-0-
NET FISCAL IMPACT	\$587,940	-0-	-0-	-0-	-0-
# ADDITIONAL FTE					
POSITIONS (Cumulative)	-0-	-0-	-0-	-0-	-0-

Is Item Included in Current Budget?

Yes ☒ No ☐

Is this item using Federal Funds?

Yes ☐ No ☒

Is this item using State Funds?

Yes ☐ No ☒

Budget Account No :

FUND: 3505 DEPT: 361 UNIT: 1515 OBJECT: 6551

Recommended Sources of Funds/Summary of Fiscal Impact:

Road Impact Fee Zone 5/Palmetto Park Rd. over LWDD E-4 Canal, Bridge Replacement

Fiscal Note: Change Order No. 6 in the amount of \$587,939.25 and a retroactive time extension of 538 days to the contract dated February 9, 2021 (R2021-0212) (Contract) with Ranger Construction Industries, Inc. (Ranger) for Palmetto Park Road SW 7th Avenue to SW 5th Avenue (Project).

Impact Fee Project Description:

This change order is to provide compensation for time and cost resulting from several unforeseen issues during construction. The project includes widening the existing road and bridge for additional turn lanes and through lanes which will allow for additional capacity needed to serve new development within Impact Fee Zone 5. Use of Impact Fees is in accordance with Article 13, Chapter H, Section 4 of the ULDC.

C. Departmental Fiscal Review:

Darney Runklesingh

III. REVIEW COMMENTS

A. OFMB Fiscal and/or Contract Dev. and Control Comments:

Jim Martin 5/20/2024
MD 5/20 OFMB Jim Martin 5/15/25 QA 550

Brundage Machels 5/20/25
Contract Dev. and Control 249/1/25

B. Approved as to Form and Legal Sufficiency:

[Signature] 5/22/25
Assistant County Attorney

C. Other Department Review:

Department Director

This summary is not to be used as a basis for payment.

SUMMARY (Continued from Page 1):

7. Between the NTP and substantial completion achieved on June 17, 2024, 85 days were affected by inclement weather, during which work could not proceed, and 71 holidays. Time extensions for holidays are in accordance with GP 8-6, and per GP 8-7.3.2 for weather-related delays.

Pursuant to GP 4-3.2 and 8-7.3.2, staff recommends approval for equitable adjustment of monetary compensation and Contract time for delay claims. Per PPM CW-F-050, the total amount of this Change Order exceeds the threshold of \$200,000 and allowable time extensions relating to staff approvals of change orders to contracts and requires the Board of County Commissioners (BCC) approval. The Contract was approved on February 9, 2021, in the amount of \$4,337,120.16. Previous change orders totaling \$110,266.09 plus this Change Order bring the total change order amount to \$698,205.34 for the Contract. The total Contract amount, including this Change Order and previous change orders, is \$5,035,325.50. With approval of the retroactive time extension associated with Change Order No. 6, the new revised completion date was June 23, 2024, with substantial completion on June 17, 2024.

This Contract was presented to the Goal Setting Committee on September 17, 2020, and the Committee established an Affirmative Procurement Initiative (API) of a 20% minimum mandatory Small Business Enterprise (SBE) participation. The proposed SBE participation for Change Order No. 6 is 0%. To date, the overall SBE participation achieved on this Contract is 18.51%. District 4 (YBH)


Background and Justification (Continued from Page 1):

After reviewing Change Order No. 6 and finding it to be in proper order, the Engineering and Public Works Department recommends approval by the BCC.

PROJECT LOCATION

PALMETTO PARK ROAD, SW 7TH AVENUE TO SW 5TH AVENUE

PBC PROJECT #2013531

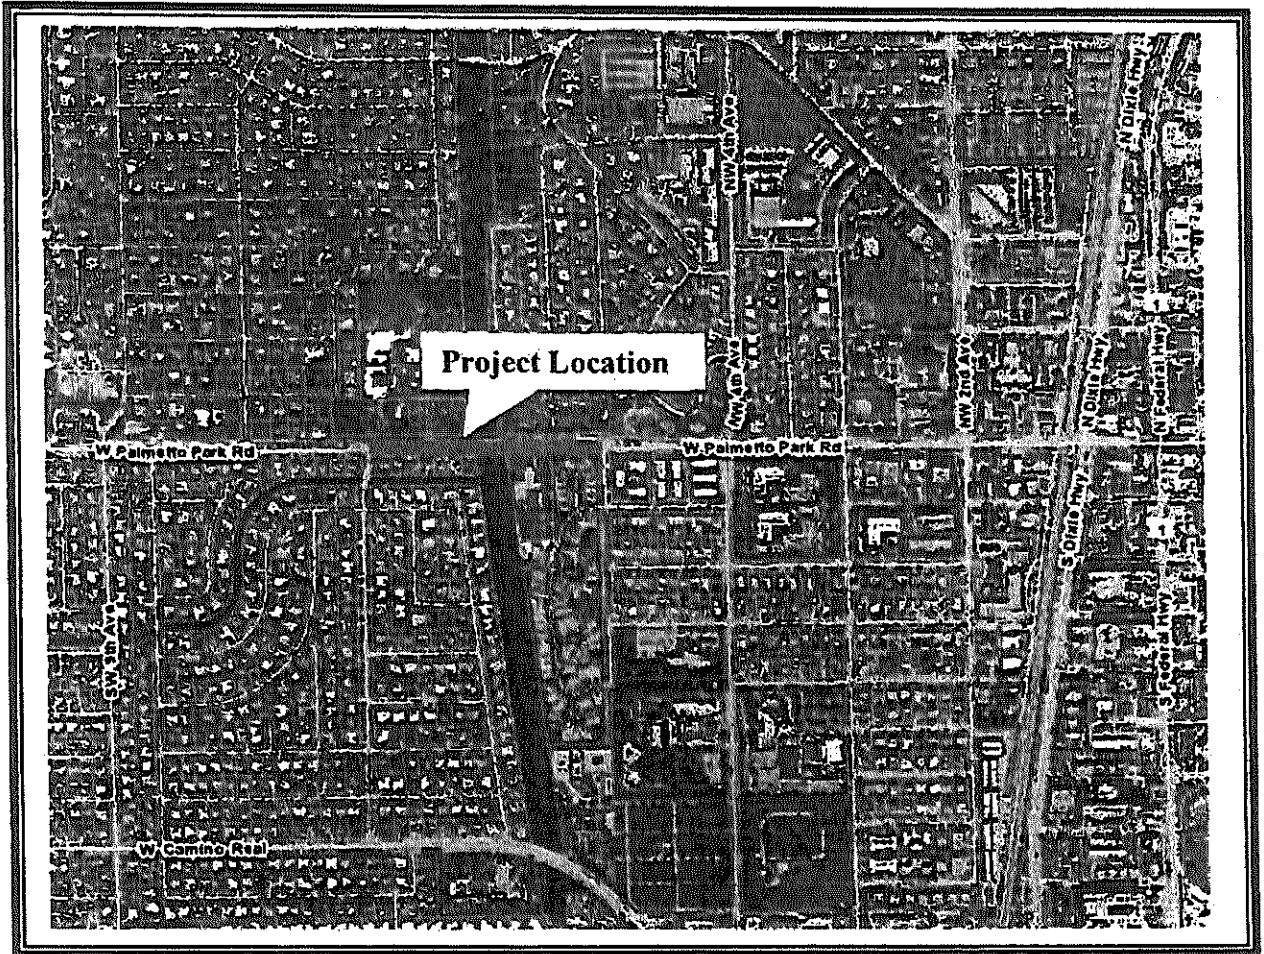



PALM BEACH COUNTY BOARD OF COUNTY COMMISSIONERS
ENGINEERING & PUBLIC WORKS DEPARTMENT
P. O. BOX 21229, WEST PALM BEACH, FL 33416-1229

REQUEST:

☐ WORK ORDER NO. _____
☐ NEW AUTHORIZATION _____
☒ CHANGE ORDER NO. 6
☐ SUPPLEMENTAL NO. _____
☐ OTHER: _____

REQUESTING DIVISION:

☐ ROAD & BRIDGE
☐ TRAFFIC
☐ ROADWAY PRODUCTION
☒ CONSTRUCTION COOR.
☐ STREETScape

INFORMATION:

DATE: 2/1/25
REQUESTOR: William Tanto
COMMISSION DISTRICT NO: 4
RESOLUTION NO: R2021-0212
PBC PO NUMBER: _____

PROJECT LOCATION/LIMITS: Palmetto Park Road SW 7th Avenue to SW 5th Avenue

PROJECT NUMBER: 2013531

CONTRACT NO: N/A

BUDGET LINE ITEM: 3505-361-1515-6551

CONTRACT DATE: February 9, 2021

CONTRACTOR/CONSULTANT/VENDOR: Ranger Construction Industries, Inc.

VENDOR:

CONTACT: Greg Reilly

CONTACT PHONE NUMBER: 561-784-3481

DETAILS. Change Order No. 6 will provide compensation to Ranger for additional time and costs resulting from multiple unforeseen circumstances. First, work was delayed 11 days after the notice to proceed on August 2, 2021, due to unresolved AT&T utility relocations. Ranger could not begin until August 13, 2021, leading to monetary compensation of \$2,182.24 for this delay. Second, pursuant to Contract Specification 8-6.1, clearing and grubbing operations were suspended due to the presence of mangroves—protected trees that would be impacted by construction activities along the shoreline of the El Rio Canal. This unforeseen condition required an additional specialized permit before work could continue on the north side of the proposed bridge. The necessary permit was submitted on August 30, 2021, and final approval was granted on October 15, 2021. This delay, which was beyond Ranger's control, resulted in a 46-day impact to the project schedule. Third, an existing 24-inch drainage pipe was found to be misaligned by 9 feet from its location outlined in the plans. This differing site condition required the procurement of additional pipe, the removal of the existing pipe, and the performance of connection work. These activities caused a 137-day delay from April 16, 2022 to August 31, 2022. Fourth, compensation is requested for the impacts to paving operations required to meet elevation adjustments at the driveway entrance to St. Paul Lutheran Church, as well as the adjacent concrete sidewalks and curbs. This claim amounts to \$76,008.61 and includes costs incurred by Ranger for delays related to overhead, supervision, surveying, labor, and equipment necessary for the removal and replacement of affected sidewalks, curbs, and traffic control devices. In addition, Ranger is requesting a 46-day time extension from December 9, 2022, to January 24, 2023. Fifth, during Phase 3 of the proposed bridge construction, Ranger's subcontractor, Anzac, encountered unforeseen underground obstructions that impeded the installation of concrete piles and precast sheet piles. These unexpected conditions were encountered multiple times and significantly disrupted Anzac's progress. As a result, Ranger is requesting additional compensation and a time extension due to the resulting schedule impacts. The total claim amounts to \$470,476.74 and 142 additional days, encompassing Anzac's direct costs and Ranger's overhead, supervision, and traffic control devices expenses. Sixth, concurrent utility issues with overhead electrical lines required a shift of pile locations as well as pile cap and sheet pile wall redesign for construction, totaling \$39,271.66 for additional associated work. Seventh, between the notice to proceed on August 2, 2021, and substantial completion achieved on June 17, 2024, there have been 85 days affected by inclement weather, during which work could not proceed, and 71 holidays. Time extensions are granted in accordance with Specification 8-6 for holidays and per Specification 8-7.3.2 for weather-related delays. Pursuant to GP 4-3.2 and 8-7.3.2, staff recommends approval for equitable adjustment of monetary compensation and Contract time for delay claims.

Provide a 538 day time extension to the contract.

Exhibit "A" - Change Order Details Exhibit "D" - Certificate of Insurance
Exhibit "B" - Bond Rider Exhibit "E" - Certificate of Resolution or Sunbiz
Exhibit "C" - EBO Schedules Exhibit "F" - Change Order History

The total amount of this request, per the attached documentation, is not to exceed \$ 587,939.25

The Contractor's proposed Small Business Enterprise (SBE) goal for this project was 20.3 %

The estimated SBE participation for this request is 0 %

The cumulative SBE participation to date for this contract including this request is: 18.51 %

The Minority/Women Owned Business Enterprise (M/WBE) for this contract is N/A %

The estimated M/WBE participation for this request is N/A %

The cumulative M/WBE participation to date for this Contract including this request is N/A %

Palm Beach County Engineering and Public Works Contact:

Albert W. Hoffman
Name

Director, Construction Coordination
Title

561-684-4180
Telephone Number

CONTRACTOR/CONSULTANT/VENDOR APPROVALS

Please indicate your receipt of this request by signing and returning this original document to our office.

ENGINEER OF RECORD (If applicable)

[Signature] 05/07/2025
Signature Date

Signature Date

Jamie Timming - Vice President
Print Name and Title

Print Name and Title

PALM BEACH COUNTY APPROVALS

[Signature] 5/15/25
Division Approval Date
[Signature] 05/19/2025
Deputy County Engineer Date

BOARD APPROVAL? YES Date: JUNE 10, 2025

[Signature] 05/09/2025
Budget Approval Date

PBC Board of Co. Commissioner Date

ATTEST: Joseph Abruzzo,
Clerk of the Circuit Court
& Comptroller

(Deputy Clerk) Date

Approved as to Form and Legal
Sufficiency:

[Signature] 5/22/25
(County Attorney) Date

CHANGE ORDER

☐ Owner Initiated

☒ Differing Site Conditions

☐ Zoning/Code/Ordinance Changes

☐ Errors/Omissions/In Design

EXHIBIT "A" (Page 1 of 3)

☐ Quantity Overruns/Underruns

☐ Request By Another Agency/Outside Party:

☐ A. Reimbursable

☐ B. Non-Reimbursable

Other:

PROJECT: Palmetto Park Road SW 7th Avenue to SW 5th Avenue

TO: Ranger Construction Industries, Inc.

CHANGE ORDER NO: 6 (Six)

COUNTY PROJECT NO: 2013531

CONTRACT DATE: 2/9/2021

RESOLUTION NO: R2021-0212

DISTRICT NO: 4

In accordance with Contract Specification Sections 4-3, 5-12.2.2, 8-6.1, and 8-7.3.2, Change Order No. 6 compensates Ranger for additional time and costs resulting from multiple unforeseen issues. Pursuant to GP 4-3.2 and 8-7.3.2, staff recommends approval for equitable adjustment of monetary compensation and Contract time for delay claims.

- 1.) An 11-day delay occurred due to AT&T utility relocations, totaling \$2,182.24.
- 2.) Clearing and grubbing operations were temporarily suspended due to the presence of mangroves. Permit approval process extended contract time by 46 days from August 30 to October 15, 2021.
- 3.) A misaligned 24" drainage pipe caused a 137-day delay and required additional material procurement, extra materials, and work
- 4.) A 46-day contract time extension and compensation of \$76,008.61 for paving adjustments at St. Paul Lutheran Church driveway and sidewalk replacements.
- 5.) A 142-day extension due to unforeseen underground obstructions affecting subcontractor Anzac's performance of work, with additional costs of \$470,476.74.
- 6.) Concurrent costs related to overhead electrical utility conflicts led to redesign of work outlined in the plans, totaling \$39,271.66.
- 7.) Between the notice to proceed on August 2, 2021, and substantial completion achieved on June 17, 2024, there have been 85 days affected by inclement weather, during which work could not proceed, and 71 holidays. Time extensions are granted in accordance with Specifications

	Total: \$587,939.25
The original Contract Sum was	\$ 4,337,120.16
Net change by previous Change Orders	\$ 110,266.09
The Contract Sum prior to this Change Order was	\$ 4,447,386.25
The Contract Sum will be <u>increased</u> by this Change Order	\$ 587,939.25
The new Contract Sum including this Change Order will be	\$ 5,035,325.50
The Contract Time will be <u>increased</u> by.	538 Days
The Date of Completion including this Change Order therefore is	June 23, 2024

EXECUTION OF THIS CHANGE ORDER ACKNOWLEDGES FINAL SETTLEMENT OF, AND RELEASES ALL CLAIMS FOR, COSTS AND TIME ASSOCIATED, DIRECTLY OR INDIRECTLY, WITH THE ABOVE-STATED MODIFICATION(S). INCLUDING ALL CLAIMS FOR CUMULATIVE DELAYS OR DISRUPTIONS RESULTING FROM, CAUSED BY, OR INCIDENT TO, SUCH MODIFICATION(S), AND INCLUDING ANY CLAIM THAT THE ABOVE-STATED MODIFICATION(S) CONSTITUTES, IN WHOLE OR PART, A CARDINAL CHANGE TO THE CONTRACT.

Ranger Construction Industries, Inc.


CONTRACTOR

1645 North Congress Ave.

Address

West Palm Beach, FL. 33409

NAME: Jamie Timmering

SIGNATURE: 

TITLE: Vice President

DATE: 05/07/2025



Certified Request for Equitable Adjustment


TO: Palm Beach County Engineering and Public Works – Construction Coordination

Name of Project: Palmetto Park Road SW 7th Avenue to SW 5th Avenue
 Project #: 2013531
 Change Order #: 06

We hereby request a Change Order for the following:

Change order 06 in the amount of \$587,939.25 will compensate Ranger Construction for time and cost resulting from several unforeseen issues associated as follows. An 11-day AT&T utility delay with a cost of \$2,182.24. Clearing and grubbing experienced a 46-day delay due to the City of Boca Raton permit approval process. A misaligned 24" drainage pipe resulting in a 137-day delay that required procurement of additional materials. Paving adjustments at the St. Paul Lutheran Church 46-day time extension and compensation of \$76,008.61. Underground obstructions 142-day delay to bridge construction and compensation of \$470,476.74. Florida Power and Light's relocation of overhead electrical lines compensation of \$39,271.66.

In accordance with the Contract, the undersigned certifies under oath and in writing, that the request is made in good faith, that any supportive data submitted is accurate and complete to Ranger Construction Industries, Inc. best knowledge and belief, and that the amount of the request accurately reflects what Ranger Construction Industries, Inc. in good faith believes to be Palm Beach County's responsibility.


 Contractor's Representative Date 3/4/25
Jamie Timming
 Printed Name


STATE OF FLORIDA
 COUNTY OF PAIM BEACH

The foregoing instrument was acknowledged before me by means of ☒ physical presence or ☐ online notarization, this 3 day of MARCH, 2025, by JAMIE TIMMING

as VICE PRESIDENT for Ranger Construction, on behalf
(title of officer/member/partner) (name of corporation/company/partnership)

of the CORPORATION, who is ☒ personally known to me or has
[choose one] corporation/company/partnership

produced _____ (type of identification) as identification.



(Print, Type, or Stamp Commissioned Name of Notary Public)


 (Signature of Notary Public - State of Florida)

Specification 8-6.4 Suspension of Contractor's Operations-Holidays: the Contractor shall not work on the following days: Martin Luther King, Jr. Day; Memorial Day; the Saturday and Sunday immediately preceding Memorial Day; Independence Day; Labor Day; the Friday, Saturday, and Sunday immediately preceding Labor Day; Veterans Day; Thanksgiving Day; the Friday, Saturday and Sunday immediately following Thanksgiving Day; and December 24 through January 2, inclusive.		
2021 Holidays	Date(s)	Time Extension
Labor Day	Friday, Sept. 3 through Monday, Sept 6, 2021	4 Days
Veterans Day	Thursday, November 11, 2021	1 Day
Thanksgiving	Thursday, Nov. 25 through Sunday, Nov. 28, 2021	4 Days
Christmas	Friday Dec. 24 through Friday, Dec. 31, 2021	8 Days
2021 TOTAL DAYS GRANTED		17 Days
2022 Holidays	Date(s)	Time Extension
New Year	Saturday, January 1 through Sunday, January 2, 2022	2 Days
Martin Luther King Jr. Day	Monday, January 17, 2022	1 Day
Memorial Day	Saturday, May 28 through Monday, May 30, 2022	3 Days
Independence Day	Monday, July 4, 2022	1 Day
Labor Day	Friday, Sept. 2 through Monday Sept. 5, 2022	4 Days
Veterans Day	Friday, November 11, 2022	1 Day
Thanksgiving	Thursday, Nov. 24 through Sunday Nov. 27, 2022	4 Days
Christmas	Saturday, Dec. 24 through Saturday, Dec. 31, 2022	8 Days
2022 TOTAL DAYS GRANTED		24 Days
2023 Holidays	Date(s)	Time Extension
New Year	Sunday, January 1 through Monday, January 2, 2023	2 Days
Martin Luther King Jr. Day	Monday, January 16, 2023	1 Day
Memorial Day	Saturday, May 27 through Monday, May 29, 2023	3 Days
Independence Day	Tuesday, July 4, 2023	1 Day
Labor Day	Friday, Sept. 1 through Monday Sept. 4, 2023	4 Days
Veterans Day	Friday, November 10, 2023	1 Day
Thanksgiving	Thursday, Nov. 23 through Sunday Nov. 26, 2023	4 Days
Christmas	Sunday, Dec. 24 through Sunday Dec. 31, 2023	8 Days
2023 TOTAL DAYS GRANTED		24 Days
2024 Holidays	Date(s)	Time Extension
New Year	Monday, January 1 through Tuesday January 2, 2024	2 Days
Martin Luther King Jr. Day	Monday, January 15, 2024	1 Day
Memorial Day	Saturday, May 25 through Monday, May 27, 2024	3 Days
2024 TOTAL DAYS GRANTED		6 Days

Total contract time extension from August 2, 2021 to June 17, 2024 for Holidays 71 Days

8-7.3.2 Contract Time Extensions: The Department will grant time extensions, on a day for day basis, for delays caused by the effects of rains or other inclement weather conditions, related adverse soil conditions or suspension of operations as defined in 8-6.4 that prevent the Contractor from productively performing controlling items of work	
2021 Weather dates granted	Time Extension
Friday, October 22, 2021	1 Day
Monday, October 25, 2021	1 Day
Friday, November 5, 2021	1 Day
Friday, November 19, 2021	1 Day
Wednesday, December 15, 2021	1 Day
2021 TOTAL DAYS GRANTED	5 Days
2022 Weather dates granted	Time Extension
Wednesday, February 9, 2022	1 Day
Thursday, March 24, 2022	1 Day
Friday, May 20, 2022	1 Day
Friday, June 3, 2022	1 Day
Friday, September 9, 2022	1 Day
Thursday, September 15, 2022	1 Days
Tuesday, Sept. 27 through Thursday Sept. 28, 2022	2 Days
Thursday, October 13, 2022	1 Days
Wednesday, October 19, 2022	1 Day
Wednesday, Nov. 9 through Friday Nov. 11, 2022	3 Days
Monday, Nov. 21 through Wednesday Nov. 23, 2022	3 Days
Wednesday, Dec. 14 through Friday Dec. 16, 2022	3 Days
2022 TOTAL DAYS GRANTED	19 Days
2023 Weather dates granted	Time Extension
Friday, April 7 through Wednesday April 12, 2023	4 Days
Wednesday, June 14, 2023	1 Day
Tuesday, June 20 through Friday June 23, 2023	4 Days
Monday, June 26 through Friday June 30, 2023	5 Day
Monday, July 3, 2023	1 Day
Monday, July 10 through Wednesday July 12, 2023	3 Days
Monday July 17 through Tuesday July 18, 2023	2 Days
Monday, July 24, 2023	1 Day
Thursday, July 27, 2023	1 Day
Friday August 4 through Monday August 7, 2023	2 Days
Wednesday, Dec. 13 through, Friday Dec. 15, 2023	3 Days
Monday, December 18, 2023	1 Day
Monday Sept.11 through Tuesday Sept. 12, 2023	2 Days
Friday, September 15, 2023	1 Day
Wednesday, September 20, 2023	1 Day
Monday Sept. 25 through Friday Sept. 29, 2023	5 Days
Monday, October 2, 2023	1 Day
Cont.	

Contract time extension for
inclement weather

Monday, October 9, 2023	1 Day
Friday, October 13, 2023	1 Day
Thursday Nov. 9, through Friday Nov. 10, 2023	2 Days
Tuesday, Nov. 14 through Wednesday Nov. 22, 2023	7 Days
Wednesday, December 13, 2023	1 Day
Monday, December 18, 2023	1 Day
Thursday, December 28, 2023	1 Day
Friday, December 29, 2023	1 Day
2023 TOTAL DAYS GRANTED	53 Days
2024 Weather dates granted	Time Extension
Monday, March 4, 2024	1 Days
Friday, March 22, 2024	1 Day
Monday, March 25 through March 26, 2024	2 Days
Monday, May 1 through Tuesday May 2, 2024	2 Days
Tuesday, June 11 through Wednesday, June 12, 2024	2 Days
2024 TOTAL DAYS GRANTED	8 Days
Total contract time extension from January 13, 2021 to June 17, 2024 due to weather	85 Days



1645 N. Congress Ave
West Palm Beach, FL 33409
Phone: (561) 793-9400

www.rangerconstruction.com

Calculation and Summary for Delay Claims 1-6

Submitted To: Albert Hoffman, P.E.	Date: 20-Feb-25
Address: Palm Beach County 2300 Jog Rd West Palm Beach, 33411	Phone:
Contact: Albert Hoffman, P.E.	Fax:
	Job Name: 2013531 - Palmetto Park Rd
	RCI No. 300-3303
	Job Location: City of Boca Raton
	Owner: Palm Beach County

Claim Cost Calculations

Claim No.	DESCRIPTION	Delay Days	QUANTITY	UM	UNIT PRICE	EXTENSION
1	AT&T Work not complete before project start	11	1.00	LS	\$ 2,182.24	\$2,182.24
2	City of Boca Tree Permit	46	1.00	LS	\$ -	\$0.00
3	24" Pipe and CO Delay	137	1.00	LS	\$ -	\$0.00
4	Overbuild Information on WB Lanes	46	1.00	LS	\$ 76,008.61	76,008.61
5	Underground Obstructions	142	1.00	LS	\$ 470,476.74	\$470,476.74
6	FPL Conflicts with Pile Installation	0	1.00	LS	\$ 39,271.66	39,271.66
				LS	\$ -	\$0.00

Total Delay Days 382

ESTIMATED TOTAL = \$587,939.25

Total Compensable Days

Average OH Cost Per Day (A*C)/B
A = Original Contract Amount \$ 4,337,120.16
B = Original Contract Time (Days) 450.00
C = 8%
Average OH Cost Per Day \$ 771.04

NOTES:
Labor Costs Include 45.98% Labor Burden, and 17.5% Markup
Equipment Costs Include 17.5% Markup
Daily OH Rate \$771.04
Includes Average Daily Cost for MOT Devices of \$119.44 + 10% Markup

ACCEPTED: The above prices, specifications and conditions are satisfactory and are hereby accepted.	CONFIRMED: Ranger Construction Industries, Inc.
Owner _____	Authorized Signature
Signature _____	Name & Title Alejandro Uribe, P.E. - Project Manager
Date of Acceptance _____	



1645 N. Congress Ave
West Palm Beach, FL 33409
Phone: (561) 793-9400

www.rangerconstruction.com

Claim No. 1 - ATT Delay

Submitted To: Albert Hoffman	Date: 5-Jun-24
Address: Palm Beach County 2300 Jog Rd West Palm Beach, 33411	Phone:
Contact: Albert Hoffman	Fax:
	Job Name: 2013531 - Palmetto Park Rd
	RCI No. 300-3303
	Job Location: City of Boca Raton
	Owner: Palm Beach County

Claim Cost Calculation

Claim No.	DESCRIPTION	Delay Days	QUANTITY	UM	UNIT PRICE	EXTENSION
1	AT&T Work not complete before project start	11	1.00	LS	\$ 2,182.24	\$2,182.24
	Total Delay Days	11			ESTIMATED TOTAL =	\$2,182.24
	Total Compensable Days	1				
					Average OH Cost Per Day	(A*C)/B
					A = Original Contract Amount	\$ 4,337,120.16
					B = Original Contract Time (Days)	450.00
					C =	8%
					Average OH Cost Per Day	\$ 771.04

NOTES:
Daily OH Rate \$771.04
Includes Average Daily Cost for MOT Devices of \$119.44

ACCEPTED: The above prices, specifications and conditions are satisfactory and are hereby accepted.	CONFIRMED: Ranger Construction Industries, Inc.
Owner _____	Authorized Signature
Signature _____	Name & Title Alejandro Uribe, P.E. - Project Manager
Date of Acceptance _____	



Ranger Construction Industries
1645 N. Congress Ave.
West Palm Beach, FL 33409
Phone: 561-793-9400

RCI PROJECT NUMBER
PROJECT NAME
Delay Cause
Total Compensable Delay Days
Delay Dates

3003303
Palmetto Park Rd
AT&T Work not complete before project start
1
8/2/2021 to 8/13/2021

Claim No. 1 - ATT Delay


ITEM	CODE	DESCRIPTION	Base Rate	QUANT	UOM	BURDEN	TOTAL	Mark Up 17.5%
		LABOR						
		Foreman	\$ 45.00	8	HR	45.98%	\$ 525.53	\$ 91.97
		Project Manager (25% of Time)	\$ 62.50	2	HR	45.98%	\$ 182.48	\$ 31.93
							\$ -	\$ -
							\$ -	\$ -
							\$ 708.00	\$ 123.90
		EQUIPMENT						
		F-150 Pickup Foreman	\$ 38.12	8	HR		\$ 304.96	\$ 53.37
		F-150 Pickup Project Manager	\$ 38.12	2	HR		\$ 76.24	\$ 13.34
							\$ 381.20	\$ 66.71
							\$ -	
		Overhead Cost	\$ 771.04	1	DAY		\$ 771.04	
							\$ -	
							\$ 771.04	\$ -
		Subcontractors						Mark Up 10%
	ACME	MOT Devices	\$ 119.44	1	DAY		\$ 119.44	\$ 11.94
							\$ -	\$ -
							\$ 119.44	\$ 11.94
SUMMARY								
LABOR							\$ 708.00	\$ 123.90
EQUIPMENT							\$ 381.20	\$ 66.71
Subcontractors							\$ 119.44	\$ 11.94
Overhead Cost							\$ 771.04	\$ -
TOTAL								\$ 2,182.24

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Adjustments for F150 XLT 4x4 in All Saved Models December 21, 2023

Ford F-150 XLT 4X4 GAS
Light Duty Trucks

Size Class:
2
Weight:
N/A



Configuration for F-150 XLT 4X4 GAS

Power Mode Gasoline Wheelbase 122.8 Inches
Model Trim XLT Gross Vehicle Weight Rating 6050 Pounds

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs Hourly	FHWA Rate** Hourly
	Monthly	Weekly	Daily	Hourly		
Published Rates	USD \$2,805.00	USD \$785.00	USD \$195.00	USD \$29.00	USD \$30.66	USD \$46.60
Adjustments						
Region (100%)	-	-	-	-		
Model Year (2022: 99.26%)	(USD \$20.68)	(USD \$5.79)	(USD \$1.44)	(USD \$0.21)		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)						
Total:	USD \$2,784.32	USD \$779.21	USD \$193.56	USD \$28.79	USD \$30.66	USD \$46.48

Non-Active Use Rates

	Hourly
Standby Rate	USD \$8.70
Idling Rate	USD \$36.54

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	23%	USD \$645.15/mo
Overhaul (ownership)	45%	USD \$1,262.25/mo
CFC (ownership)	16%	USD \$448.80/mo
Indirect (ownership)	16%	USD \$448.80/mo
Fuel (operating) @ USD 3.87	67.58%	USD \$20.72/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book® Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for CRAIG VORSTER (craig.vorster@vecelliogroup.com)



1645 N. Congress Ave
West Palm Beach, FL 33409
Phone: (561) 793-9400

www.rangerconstruction.com

Claim No. 2 - City of Boca Tree Permit

Submitted To: Albert Hoffman	Date: 5-Jun-24
Address: Palm Beach County 2300 Jog Rd West Palm Beach, 33411	Phone:
Contact: Albert Hoffman	Fax:
	Job Name: 2013531 - Palmetto Park Rd
	RCI No. 300-3303
	Job Location: City of Boca Raton
	Owner: Palm Beach County

Claim Cost Calculation

Claim No.	DESCRIPTION	Delay Days	QUANTITY	UM	UNIT PRICE	EXTENSION
2	City of Boca Tree Permit	46	1.00	LS	\$ -	\$0.00
	Bond Cost 1.5%		1.00	LS	\$0.00	\$0.00
Total Delay Days		46	ESTIMATED TOTAL =			
Total Compensable Days			\$0.00			
Average OH Cost Per Day						(A*C)/B
A = Original Contract Amount						\$ 4,337,120.16
B = Original Contract Time (Days)						450.00
C =						8%
Average OH Cost Per Day						\$ 771.04

NOTES:
Labor Costs Include 45.98% Labor Burden, and 17.5% Markup
Equipment Costs Include 17.5% Markup
Daily OH Rate \$771.04
Includes Average Daily Cost for MOT Devices of \$119.44 + 10% Markup

ACCEPTED: The above prices, specifications and conditions are satisfactory and are hereby accepted.	CONFIRMED: Ranger Construction Industries, Inc.
Owner _____	Authorized Signature
Signature _____	Name & Title Alejandro Uribe, P.E. - Project Manager
Date of Acceptance _____	



Ranger Construction Industries

1645 N. Congress Ave.
West Palm Beach, FL 33409
Phone: 561-793-8400

RCI PROJECT NUMBER

PROJECT NAME

Delay Cause

Delay Days

Delay Dates

3003303

Palmetto Park Rd

City of Boca Tree Permit

46

AGREED TIME ONLY

9/1/2021

to

10/15/2021

Claim No. 2 - City of Boca Tree Permit

ITEM	CODE	DESCRIPTION	Base Rate	QUANT	UOM	BURDEN	TOTAL
		LABOR					
		Foreman	\$ 45.00	0	HR	45.98%	\$ - \$ -
		Project Manager (25% of Time)	\$ 62.50	0	HR	45.98%	\$ - \$ -
							\$ - \$ -
							\$ - \$ -
							\$ - \$ -
							\$ - \$ -
		EQUIPMENT					\$ - \$ -
		F-150 Pickup Foreman	\$ 46.48	0	HR		\$ - \$ -
		F-150 Pickup Project Manager	\$ 46.48	0	HR		\$ - \$ -
							\$ - \$ -
		Overhead Cost Ranger	\$ 771.04	0	DAY		\$ - \$ -
							\$ - \$ -
							\$ - \$ -
							\$ - \$ -
		Subcontractors					\$ - \$ -
			\$ -	0	DAY		\$ - \$ -
			\$ -	0	LS		\$ - \$ -
							\$ - \$ -
							\$ - \$ -
							\$ - \$ -
SUMMARY							\$ - \$ -
LABOR							\$ - \$ -
EQUIPMENT							\$ - \$ -
Subcontractors							\$ - \$ -
Overhead Cost Ranger							\$ - \$ -
TOTAL							\$ - \$ -



ENGINEERING PERMIT APPLICATION

CITY OF BOCA RATON • 201 W. PALMETTO PARK ROAD • BOCA RATON, FL 33432

PERMIT #: 21 ROW 2778

Date: 10/15/2021

Is this a sub-permit application? ☐ YES ☒ NO

CONTRACT AMOUNT: \$ 4,337,120.16

Description of Work: Removal of trees and installation of riprap near the E-4 (El Rio) Canal in the right of way of the City of Boca.Job Address: Palmetto Park Rd from SW 7th Ave to SW 5th AveContractor's Name: Hardrives, Inc.Phone: 561-278-0456State Certification #: CUC 056790Certificate of Competency #: .Contractor's Address: 2101 South Congress Ave, Delray Beach, FL 33445Fax: 561-278-2147Tax Folio Number: Owner's Name: Palm Beach CountyPhone: 561-684-4180Owner's Address: 2300 N Jog Rd, West Palm Beach, FL 33411Fax: 561-684-4165Architect/Engineer's Name: Brett FullerPhone: 561-687-2220Architect/Engineer's Address: 2035 Vista Parkway, West Palm Beach, FL 33411Fax: 561-687-1110

1. Application is hereby made to obtain a permit to do the work and installations as herein indicated. I certify that no work or installation has been affected prior to the issuance of said permit and that all work will be performed to meet the standards of all laws regulating construction in this jurisdiction. I understand that separate permits must be obtained for electrical, plumbing, air conditioning, roofing, paving, signs, pools, fences, etc. It is further understood that other approvals from federal, state or county agencies, homeowner or condominium associations or similar authorities, may be required prior to commencing the work described in this permit.

2. Warning to owner: Your failure to record a notice of commencement may result in your paying twice for improvements to your property. A notice of commencement must be recorded and posted on the job site before the first inspection.

3. If you intend to obtain financing, consult with your lender or an attorney before commencing work or recording your notice of commencement.

4. Applicants/Permit Holders are advised to determine if any deed restrictions, Homeowner Association rules, or other applicable provisions or restrictions apply to any work that may be authorized by this permit. The issuance of any permit or other action by the City in relation to any permit does not relieve the Applicant/Permit Holder of the duty, if any, to comply with any other applicable rules, obligations, provisions, or restrictions relating to the work and/or the permit. The City of Boca Raton is not responsible for compliance with or the enforcement of any such obligations, restrictions, rules, or provisions. The City reserves the right, in its sole and absolute discretion, to require, as a condition of the permit, approval from any entity the City deems appropriate for work that may be authorized by a permit.

OWNER'S AFFIDAVIT: I certify that all the foregoing information is accurate and that all work will be done in compliance with all applicable laws regulating construction and zoning.

and Kathleen O. Farrell
(Signature of Owner or Agent)

STATE OF FLORIDA • COUNTY OF PALM BEACH
Sworn to (or affirmed) and subscribed before me this 23rd day of September (month), 2021 (year),

by: Kathleen O. Farrell
(Print name of Owner or Agent)

David Kuzmenko
(Signature of Notary Public)

(Print, Type or Stamp Commission # DAVID KUZMENKO Notary Public)

✓ Personally known Commission # GG 855107

Type of Identification Produced: Expire March 23, 2024

Bonded thru Troy Fahn Insurance 800-385-7019

CONTRACTOR'S AFFIDAVIT: I certify that I have the authority to make the foregoing application, that the application is true and correct and the contract amount for the work is listed above.

Craig K. Elmore
(Signature of Contractor)

STATE OF FLORIDA • COUNTY OF PALM BEACH
Sworn to (or affirmed) and subscribed before me this 23rd day of September (month), 2021 (year),

by: Craig K. Elmore
(Print name of Contractor)

DERORAH VINT
(Signature of Notary Public)

(Print, Type or Stamp Commission # DERORAH VINT Notary Public)

✓ Personally known Commission # GG 233642

Type of Identification Produced: Expire June 28, 2022

Bonded thru Troy Fahn Insurance 800-385-7019



ENGINEERING PERMIT APPLICATION

CITY OF BOCA RATON • 201 W. PALMETTO PARK ROAD • BOCA RATON, FL 33432

PERMIT #: _____ Date: 8/30/2021

Is this a sub-permit application? ☐ YES ☒ NO

CONTRACT AMOUNT: \$ 4,337,120.16

Description of Work: Reconstruction of the El Rio bridge, construction of turn lanes, milling, resurfacing, and underground work

Job Address: Palmetto Park Rd from SW 7th Ave to SW 5th Ave

Contractor's Name: Hardrives, Inc.

Phone: 561-278-0456

State Certification #: CUC 056790

Certificate of Competency #: _____

Contractor's Address: 2101 South Congress Ave, Delray Beach, FL 33445

Fax: 561-278-2147

Tax Folio Number: _____

Owner's Name: Palm Beach County

Phone: 561-684-4180

Owner's Address: 2300 N Jog Rd, West Palm Beach, FL 33411

Fax: 561-684-4165

Architect/Engineer's Name: Brett Fuller

Phone: 561-687-2220

Architect/Engineer's Address: 2035 Vista Parkway, West Palm Beach, FL 33411

Fax: 561-687-1110

1. Application is hereby made to obtain a permit to do the work and installations as herein indicated. I certify that no work or installation has been affected prior to the issuance of said permit and that all work will be performed to meet the standards of all laws regulating construction in this jurisdiction. I understand that separate permits must be obtained for electrical, plumbing, air conditioning, roofing, paving, signs, pools, fences, etc. It is further understood that other approvals from federal, state or county agencies, homeowner or condominium associations or similar authorities, may be required prior to commencing the work described in this permit.
2. Warning to owner: Your failure to record a notice of commencement may result in your paying twice for improvements to your property. A notice of commencement must be recorded and posted on the job site before the first inspection.
3. If you intend to obtain financing, consult with your lender or an attorney before commencing work or recording your notice of commencement.
4. Applicants/Permit Holders are advised to determine if any deed restrictions, Homeowner Association rules, or other applicable provisions or restrictions apply to any work that may be authorized by this permit. The issuance of any permit or other action by the City in relation to any permit does not relieve the Applicant/Permit Holder of the duty, if any, to comply with any other applicable rules, obligations, provisions, or restrictions relating to the work and/or the permit. The City of Boca Raton is not responsible for compliance with or the enforcement of any such obligations, restrictions, rules, or provisions. The City reserves the right, in its sole and absolute discretion, to require, as a condition of the permit, approval from any entity the City deems appropriate for work that may be authorized by a permit.

OWNER'S AFFIDAVIT: I certify that all the foregoing information is accurate and that all work will be done in compliance with all applicable laws regulating construction and zoning.

Morton L. Rose
(Signature of Owner or Agent)

STATE OF FLORIDA • COUNTY OF PALM BEACH
Sworn to (or affirmed) and subscribed before me this 15 day of SEPTEMBER (month), 2021 (year).

by: MORTON L. ROSE
(Print name of Owner or Agent)

(Signature of Notary Public)

Notary Public State of Florida
Brent Enck
My Commission GG 912442

(Print/Type or Stamp Commission Number of Notary Public)

Personally known _____ Produced Identification _____

Type of Identification Produced: _____

CONTRACTOR'S AFFIDAVIT: I certify that I have the authority to make the foregoing application, that the application is true and correct and the contract amount for the work is listed above.

Craig K. Elmore
(Signature of Contractor)

STATE OF FLORIDA • COUNTY OF PALM BEACH
Sworn to (or affirmed) and subscribed before me this 30th day of August (month), 2021 (year).

by: Craig K. Elmore
(Print name of Contractor)

(Signature of Notary Public)


Notary Public State of Florida
DEBORAH VINT
My Commission Expires 08/31/2022

(Print/Type or Stamp Commission Number of Notary Public)

Personally known _____ Produced Identification _____

Type of Identification Produced: _____

EXHIBIT 14 (Page 1 of 1)

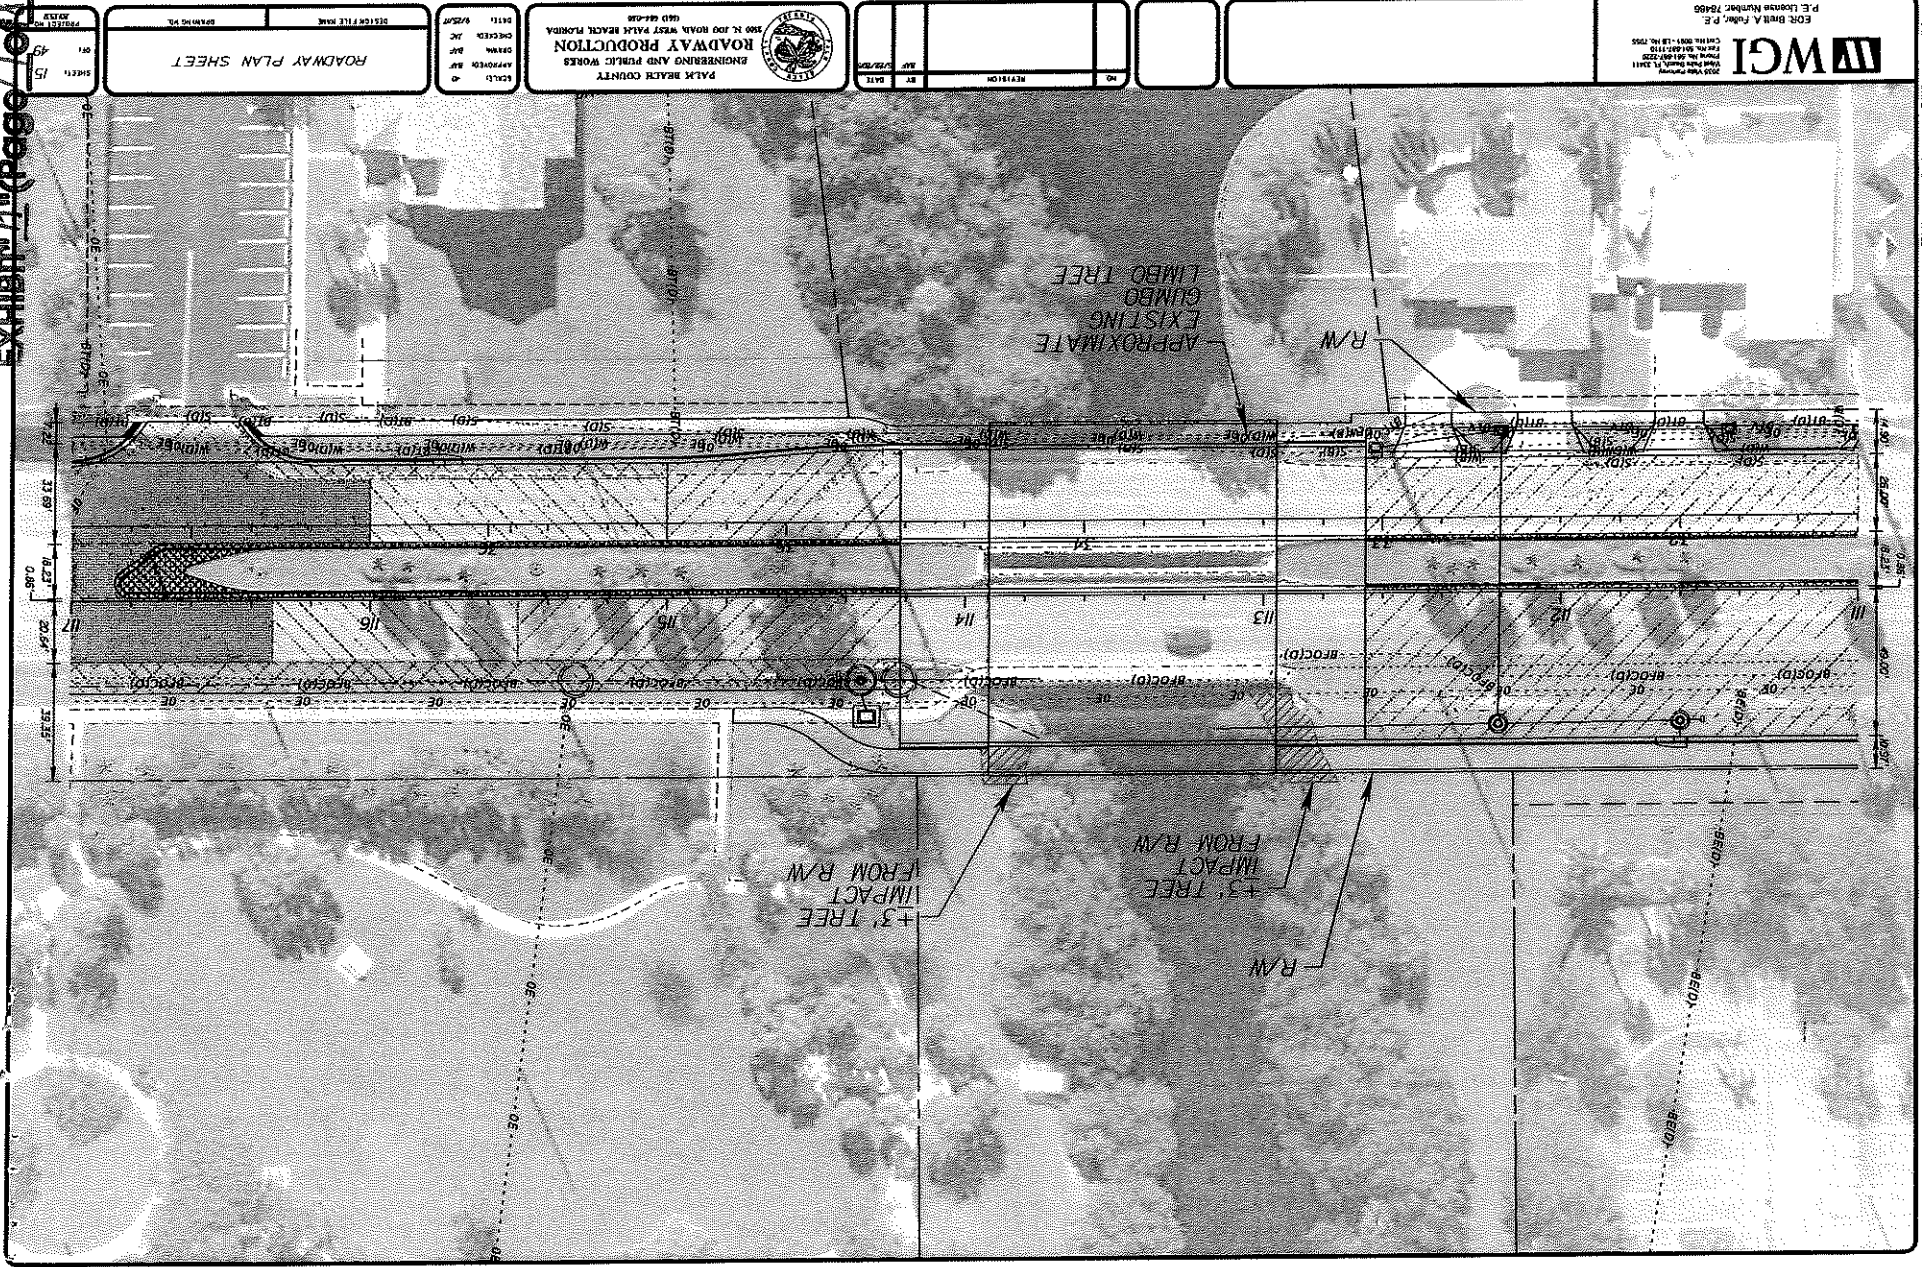

WGI
W.G. International, Inc.
2005 West Palm Beach, FL 33411
Phone: 561-837-1100
Fax: 561-837-1105
E-Mail: info@wgi.com
P.E. License Number: 78486
P.E. Brian A. Fisher, P.E.

NO.	REVISION	DATE	BY

ROADWAY PRODUCTION
ENGINEERING AND PUBLIC WORKS
P.O. BOX 1000
WEST PALM BEACH, FLORIDA 33402
P.E. License Number: 78486
P.E. Brian A. Fisher, P.E.

ROADWAY PLAN SHEET
DATE: 8/20/07
CHECKED: JAC
DRAWN: BAF
APPROVED: BAF
SCALE: AS SHOWN



1645 N. Congress Ave
West Palm Beach, FL 33409
Phone: (561) 793-9400

www.rangerconstruction.com

Delay Claim No. 3 - 24" RCP Pipe

Submitted To: Patricio Ayala	Date: 28-Mar-24
Address: Palm Beach County 2300 Jog Rd West Palm Beach, 33411	Phone:
Contact: Patricio Ayala	Fax:
	Job Name: 2013531 - Palmetto Park Rd
	RCI No. 300-3303
	Job Location: City of Boca Raton
	Owner: Palm Beach County

Claim Cost Calculation

<u>Claim No.</u>	<u>DESCRIPTION</u>	<u>Delay Days</u>	<u>QUANTITY</u>	<u>UM</u>	<u>UNIT PRICE</u>	<u>EXTENSION</u>
4	24" Pipe Delay	137	1.00	LS	\$ -	\$0.00
	Bond Cost 1.5%		1.00	LS	\$0.00	\$0.00
	Total Delay Days	137	ESTIMATED TOTAL =			\$0.00
	Total Compensable Days					
			Average OH Cost Per Day (A*C)/B			
			A = Original Contract Amount \$ 4,337,120.16			
			B = Original Contract Time (Days) 450.00			
			C = 8%			
			Average OH Cost Per Day \$ 771.04			

NOTES:
Labor Costs Include 45.98% Labor Burden
Daily OH Rate \$771.04
Includes Average Daily Cost for MOT Devices of \$119.44

ACCEPTED:
The above prices, specifications and conditions are satisfactory and are hereby accepted.

Owner _____

Signature _____

Date of Acceptance _____

CONFIRMED:
Ranger Construction Industries, Inc.

Authorized Signature

Name & Title **Alejandro Uribe, P.E. - Project Manager**



Ranger Construction Industries

1645 N. Congress Ave.
West Palm Beach, FL 33409
Phone: 561-793-8400

RCI PROJECT NUMBER

PROJECT NAME

Delay Cause

Delay Days

Delay Dates

3003303

Palmetto Park Rd

24" Pipe Delay

137.00	AGREED TIME ONLY
--------	------------------

4/16/2022

to

8/31/2022

Delay Claim No. 3 - 24" RCP Pipe

[illegible]

Patricio Ayala

From: Christian Asfour <Christian.Asfour@rangerconstruction.com>
Sent: Wednesday, July 6, 2022 4:09 PM
To: John Kopelakis
Cc: John Drevas
Subject: FW: 2013531 Palmetto Park Rd - RFI 13: Unknown Structure
Attachments: RFI 13- Unknown Structure Palmetto.pdf

***** Note: This email was sent from a source external to Palm Beach County. Links or attachments should not be accessed unless expected from a trusted source. *****

Will send photos that John Drevas sent separately, your email is rejecting it, thanks.

From: Christian Asfour
Sent: Wednesday, July 6, 2022 3:59 PM
To: John Kopelakis <jkopelak@pbcgov.org>
Cc: John Drevas <JDrevas@pbcgov.org>; Alejandro Uribe <Alejandro.Uribe@rangerconstruction.com>; Everett Ash <Everett.Ash@rangerconstruction.com>; Thomas Elmore <Thomas.Elmore@rangerconstruction.com>; Robert Ueltschi <Robert.Ueltschi@rangerconstruction.com>
Subject: 2013531 Palmetto Park Rd - RFI 13: Unknown Structure

John,

Please see attached RFI regarding an unknown structure recently found on Palmetto Park Rd along with photos. Thank you.

Best regards,
Christian Asfour
PROJECT MANAGER – SOUTH DIVISION
RANGER CONSTRUCTION INDUSTRIES, INC.
101 Sansbury's Way
West Palm Beach, FL 33411
561-793-9400 (Office)
561-351-7199 (Cell)
christian.asfour@rangerconstruction.com

LEGAL DISCLAIMER The information in this message is confidential and may be privileged. It is intended solely for the addressee. Access to this message by anyone else is unauthorized. If the reader of this is not the intended recipient, any dissemination, distribution, or copying of this communication, or any action or omission taken by the reader in reliance on it is prohibited and may be unlawful. Thank you



REQUEST FOR INFORMATION
No.: 13

Project: 2013531 Palmetto Park Rd Number: 300-3303
To: John Kopelakis / PBC From: Ranger Construction, Christian Asfour
Re: Unknown Structure Found Date: 7/6/22

Ranger would like to request the following information regarding the unknown structure that was found on Palmetto Park Rd on July 1st:

- The structure is 9.0 FT Southwest from where structure S-6 will be located to tie in to the existing 24" storm line. This structure is not shown on the plans, nor is a "mirror" drain on the opposite corner. Please have the EOR advise on this situation. Attached are photos of the structure, thank you.

Signed by: Christian Asfour, Project Manager Date: 7/6/22

Response:

☐ Attachments

Response From: _____ To: _____ Date Rec'd: _____ Date Ret'd: _____
Signed by: _____ Date: _____
Copies: ☐ Owner ☐ Consultants ☐ _____ ☐ _____ ☐ _____ ☐ _____ ☐ File

From: Antolina Michel-Diaz A. <AMichelDiaz@pbcgov.org>
Sent: Thursday, April 28, 2022 7:33 AM
To: John Kopelakis <JKopelak@pbcgov.org>
Cc: Christopher Little W. <CWLittl@pbcgov.org>; John Drevas <JDrevas@pbcgov.org>; Thomas Elmore <Thomas.Elmore@rangerconstruction.com>; Roland Hembree <Roland.Hembree@rangerconstruction.com>; Alejandro Uribe <Alejandro.Uribe@rangerconstruction.com>; Robert Ueltschi <Robert.Ueltschi@rangerconstruction.com>; Kathleen Farrell <KFarrell@pbcgov.org>
Subject: FW: [EXTERNAL] FW: 2013531 Palmetto Park Rd - RFI: 24" Pipe

Good morning John,
Please see attached and below.
Thanks,
Antolina

From: Jerome Saval <Jerome.Saval@wginc.com>
Sent: Wednesday, April 27, 2022 4:50 PM
To: Brett Fuller <Brett.Fuller@wginc.com>
Subject: RE: [EXTERNAL] FW: 2013531 Palmetto Park Rd - RFI: 24" Pipe

Attached are the plans marked-up to show the modifications to the drainage design.
S-6 will shift south over the existing 24" drainage pipe.
A new 24" pipe will be constructed between S-6 and S-10.
Structure S-6 can remain the same, (e.g., flowlines, pipe sizes, and direction) however, the top elevation will have to match the finished grade of the pavement.



Jerome Saval, PE
Chief Engineer

2035 Vista Parkway
West Palm Beach, FL 33411

561.687.2220 | 561.472.8131 (direct) | 561.239.5980 (cell)



[\[nam02.safelinks.protection.outlook.com\]](https://nam02.safelinks.protection.outlook.com)



[\[nam02.safelinks.protection.outlook.com\]](https://nam02.safelinks.protection.outlook.com)

From: Brett Fuller <Brett.Fuller@wginc.com>
Sent: Wednesday, April 27, 2022 11:48 AM
To: Jerome Saval <Jerome.Saval@wginc.com>
Subject: FW: [EXTERNAL] FW: 2013531 Palmetto Park Rd - RFI: 24" Pipe
Importance: High

EXHIBIT A (Page 2 of 2)

COMPONENTS OF CONTRACT PLANS

ROADWAY PLANS
SIGNING AND PAVEMENT MARKINGS PLANS (FOR INFORMATION ONLY)
BRIDGE PLANS
UTILITY RELOCATION PLANS

COUNTY OF PALM BEACH
STATE OF FLORIDA

BOARD OF COUNTY COMMISSIONERS

PROJECT NO. 2013531

PALMETTO PARK ROAD OVER LWDD E-4 CANAL

(EL RIO CANAL) BRIDGE REPLACEMENT

(SW 7TH AVE. TO SW 5TH AVE.)

HAL R. VALECHE
DISTRICT 1

GREGG K. WEISS
DISTRICT 2


ROBERT S. WEINROTH
DISTRICT 4

MELISSA MCKINLAY
DISTRICT 6

DAVE KERNER
DISTRICT 3

MARY LOU BERGER
DISTRICT 5

MACK BERNARD
DISTRICT 7




SHEET NO.	SHEET DESCRIPTION
1	KEY SHEET
2	DRAINAGE MAP
3	EXISTING DRAINAGE STRUCTURE DATA
4 - 10	TYPICAL SECTIONS
11	SUMMARY OF QUANTITIES
12	GENERAL NOTES
13	SUMMARY OF DRAINAGE STRUCTURES
14 - 16	ROADWAY PLAN SHEETS
17 - 18	PROFILE SHEETS
19 - 24	DRAINAGE STRUCTURES
25 - 31	CROSS SECTIONS
32 - 35	DRIVEWAY CROSS SECTIONS
36 - 37	STORM WATER POLLUTION PREVENTION PLAN
38 - 40	UTILITY SHEETS
41 - 42	SUBSURFACE PROFILES
43 - 49	SPECIFIC PURPOSE SURVEY PLANS

GOVERNING STANDARDS AND SPECIFICATIONS:

THESE PLANS HAVE BEEN PREPARED IN ACCORDANCE WITH AND GOVERNED BY THE FLORIDA DEPARTMENT OF TRANSPORTATION DESIGN STANDARDS DATED JANUARY, 2017, AND SUPPLEMENTS THERETO. THE FLORIDA DEPARTMENT OF TRANSPORTATION STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION, SUPPLEMENTS THERETO, AND SPECIAL PROVISIONS AS NOTED IN THE CONTRACT SPECIFICATIONS FOR THIS PROJECT.

REVISIONS

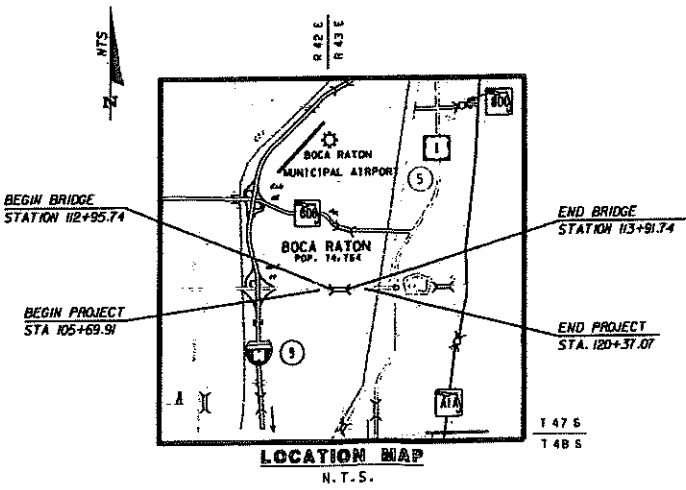

LENGTH OF PROJECT		
	LINEAR FEET	MILES
ROADWAY	1371.16	0.260
BRIDGES	96.00	0.018
NET LENGTH OF PROJ.	1467.16	0.278
EXCEPTIONS		
GROSS LENGTH OF PROJ.	1467.16	0.278

THIS PROJECT IS DESIGNED TO
NAVD, 1988 DATUM

PLANS PREPARED BY:

WGI
Wantman Group, Inc.

2015 Vista Parkway
West Palm Beach, FL 33411
Phone No. 561.687.3220
Fax No. 561.687.1110
E-Mail: WGI@wantmangroup.com
Cert No. 61091 - LB No. 7055
Vendor No. 65-0271367

ATTENTION IS DIRECTED TO THE FACT THAT THESE PLANS MAY HAVE BEEN CHANGED IN SIZE BY REPRODUCTION. THIS MUST BE CONSIDERED WHEN OBTAINING SCALED DATA.

I HEREBY CERTIFY THAT THE ABOVE PLANS AND DESIGNS ARE IN SUBSTANTIAL COMPLIANCE WITH THE DESIGN STANDARDS AND CRITERIA IN EFFECT ON THIS DATE FOR PALM BEACH COUNTY AND THE STATE OF FLORIDA DEPARTMENT OF TRANSPORTATION.

DATE 5/12/2018
BRETT J. FULLER, P.E. NO. 78486
PROFESSIONAL ENGINEER

PALM BEACH COUNTY
ENGINEERING AND PUBLIC WORKS
ROADWAY PRODUCTION
200 N. JOO ROAD, WEST PALM BEACH, FL 33411
USD 664-690

PROJECT: PALMETTO PARK ROAD
DESIGN FILE NAME: KEYSRD01.DGN
SHEET: 1
OF: 49
PROJECT NO. 2013531

LEGEND:

- DENOTES EXISTING PAVEMENT REMOVAL
- DENOTES MILLING & RESURFACING LIMITS
- DENOTES ASPHALT OVERBUILD LIMITS
- DENOTES RECONSTRUCTION LIMITS
- DENOTES WIDENING LIMITS
- LANE IDENTIFICATION

BVI
HAS NAIL & TIN TAB
STA. 105+46.15 (43.71' LT)
N: 73405.67
E: 950738.32
EL = 5.57 (MAYD 88)

EXISTING DRAINAGE STRUCTURE NOTE:




EXIST. STRUCTURES LABELED IN THE TABLE ON THE DRAINAGE MAPS WITH AN "E" PREFIX REFER TO EXIST. STRUCTURES LABELED ON THE PLAN.

EXAMPLE: EM (IN TABLE) REFERS TO (H) (ON PLAN).

BEGIN PROJECT
BEGIN MILLING & RESURFACING (RT.)

STA. 105+69.91 (Q CONST. PALMETTO PARK ROAD)
STA. 26+09.98 (14.23' (B) (R SURVEY))

* EXISTING IRRIGATION TO BE CAPPED AT CURB LINE.

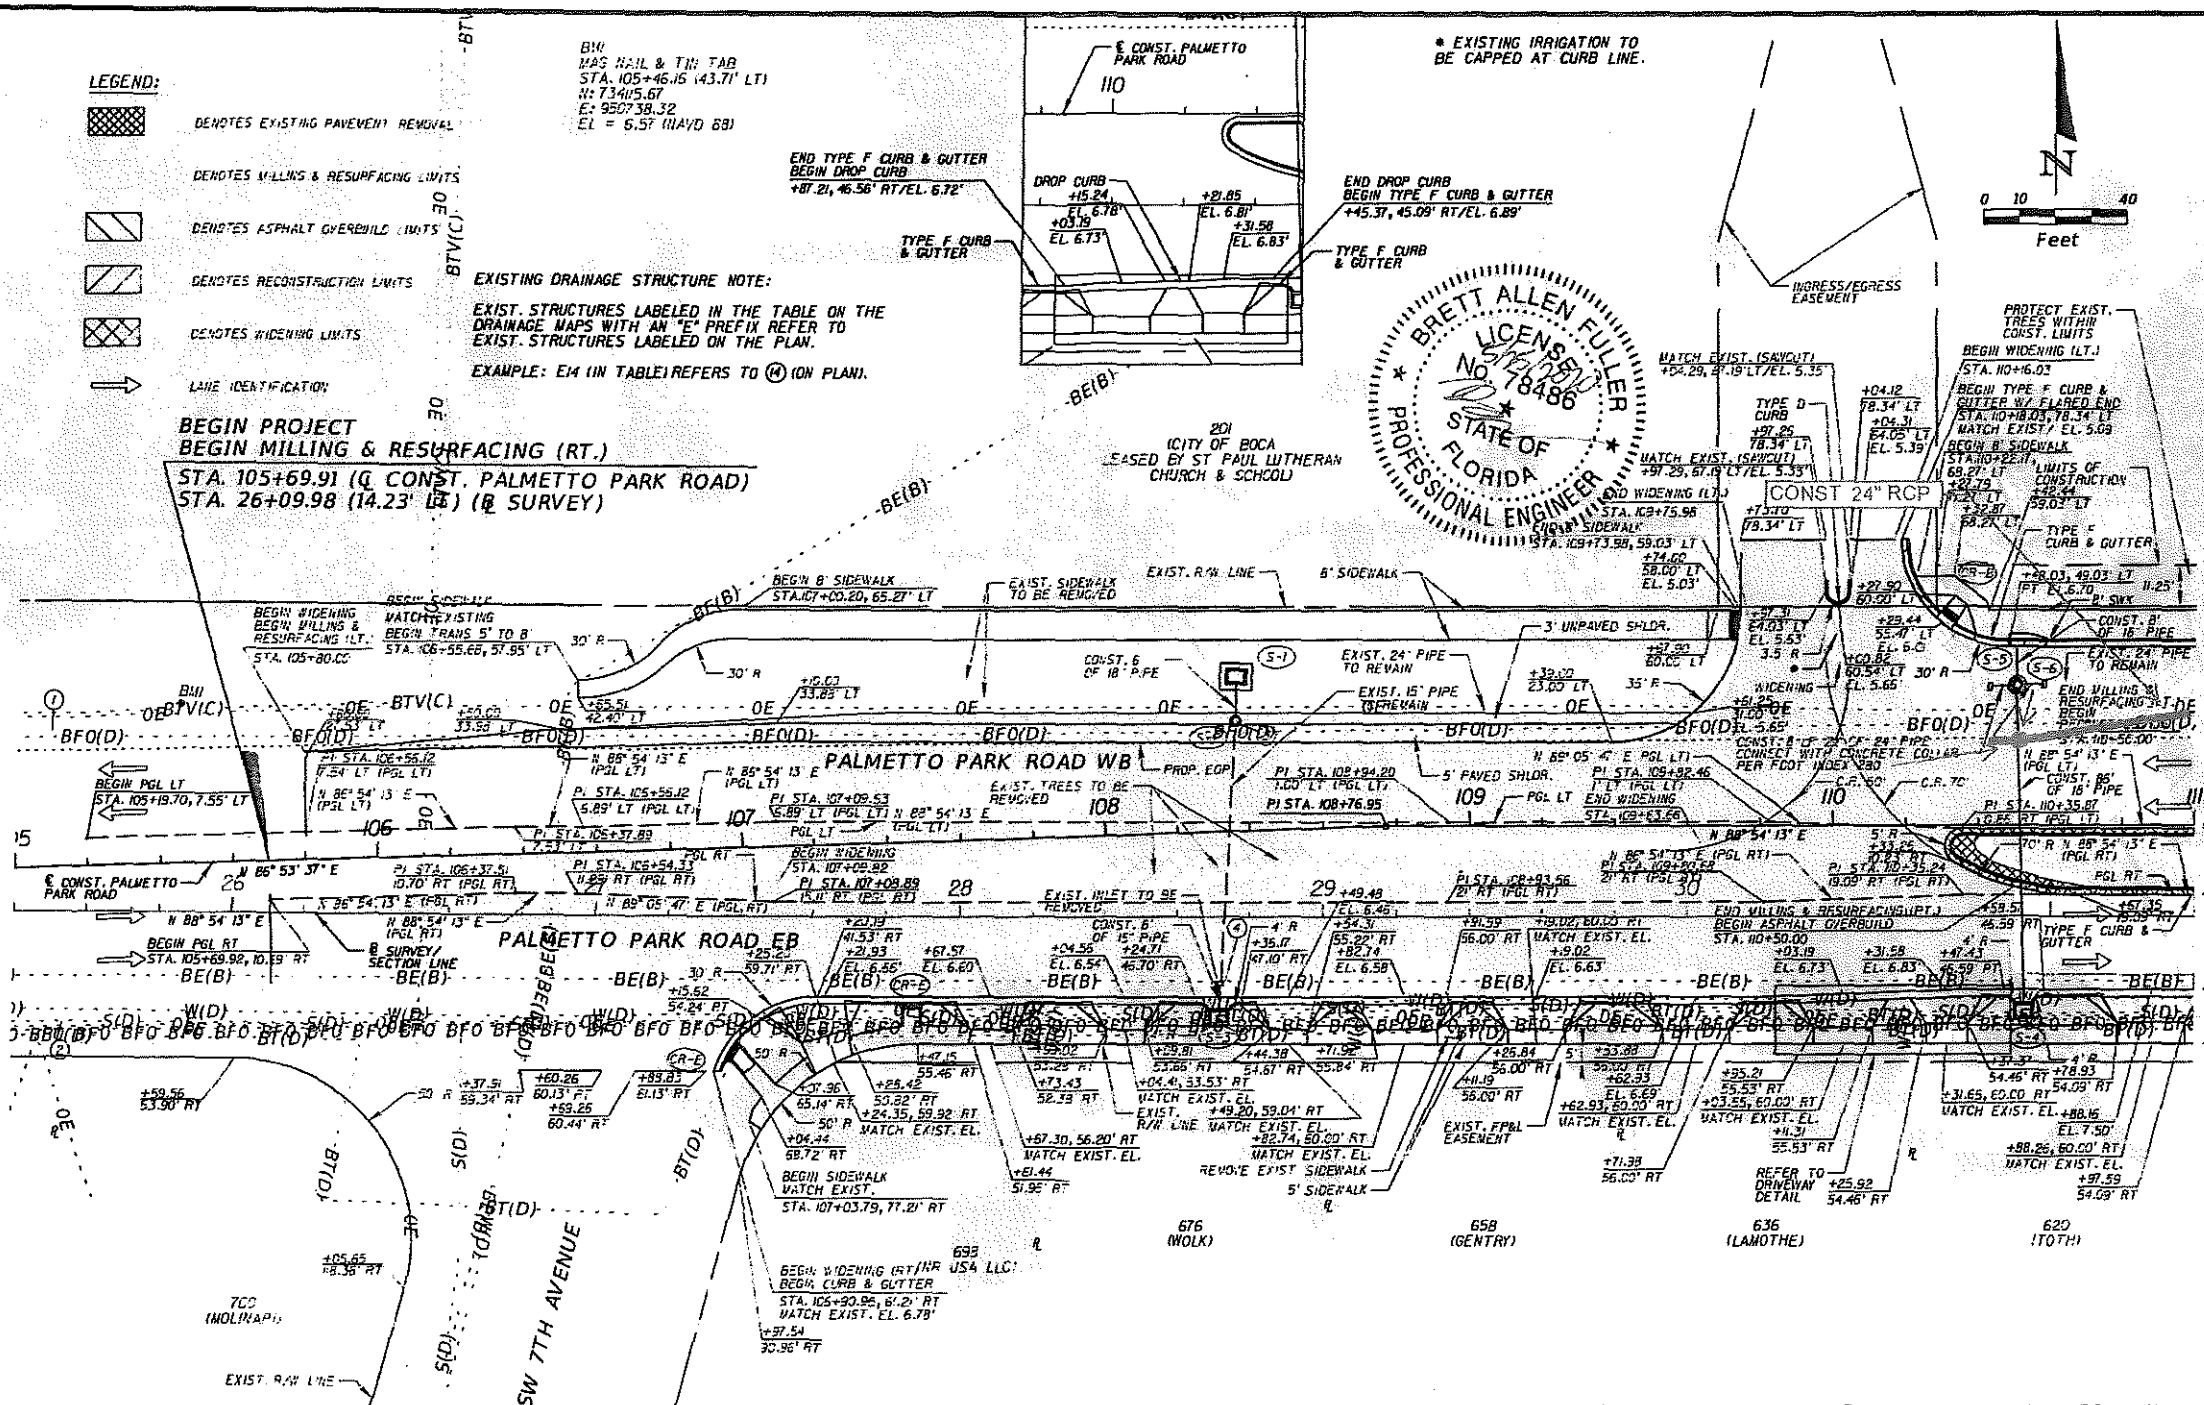

NOTE: REFER TO UTILITY SHEETS FOR UTILITY INFORMATION



2025 Vista Parkway
West Palm Beach, FL 33411
Phone No. 561-872-2220
Fax No. 561-872-1110
Cell No. 561-1616 2025

NO.	REVISION	BY	DATE



PALM BEACH COUNTY
ENGINEERING AND PUBLIC WORKS
ROADWAY PRODUCTION
200 N. 100 ROAD, WEST PALM BEACH, FLORIDA
1000 1000

SCALE: 40
APPROVED: BAF
DRAWN: BAF
CHECKER: JAC
DATE: 9/25/17

ROADWAY PLAN SHEET

SHEET: 14
OF: 49

PROJECT NO.




LEGEND:

- DENOTES EXISTING PAVEMENT REMOVAL
- DENOTES MILLING & RESURFACING LIMITS
- DENOTES ASPHALT OVERBUILD LIMITS
- DENOTES RECONSTRUCTION LIMITS
- DENOTES EASEMENT LIMITS
- LANE IDENTIFICATION

BME
NAD 84 & T&E TAB
STA. 144+8.36 133.84 LT
N: 73+43.44
E: 95+60.70
EI = 5.65 (NAD 83)

EXISTING DRAINAGE STRUCTURE NOTES:

EXIST. STRUCTURES LABELED IN THE TABLE ON THE DRAINAGE MAPS WITH AN "E" PREFIX REFER TO EXIST. STRUCTURES LABELED ON THE PLAN.
EXAMPLE: EM (IN TABLE) REFERS TO (M) (ON PLAN).

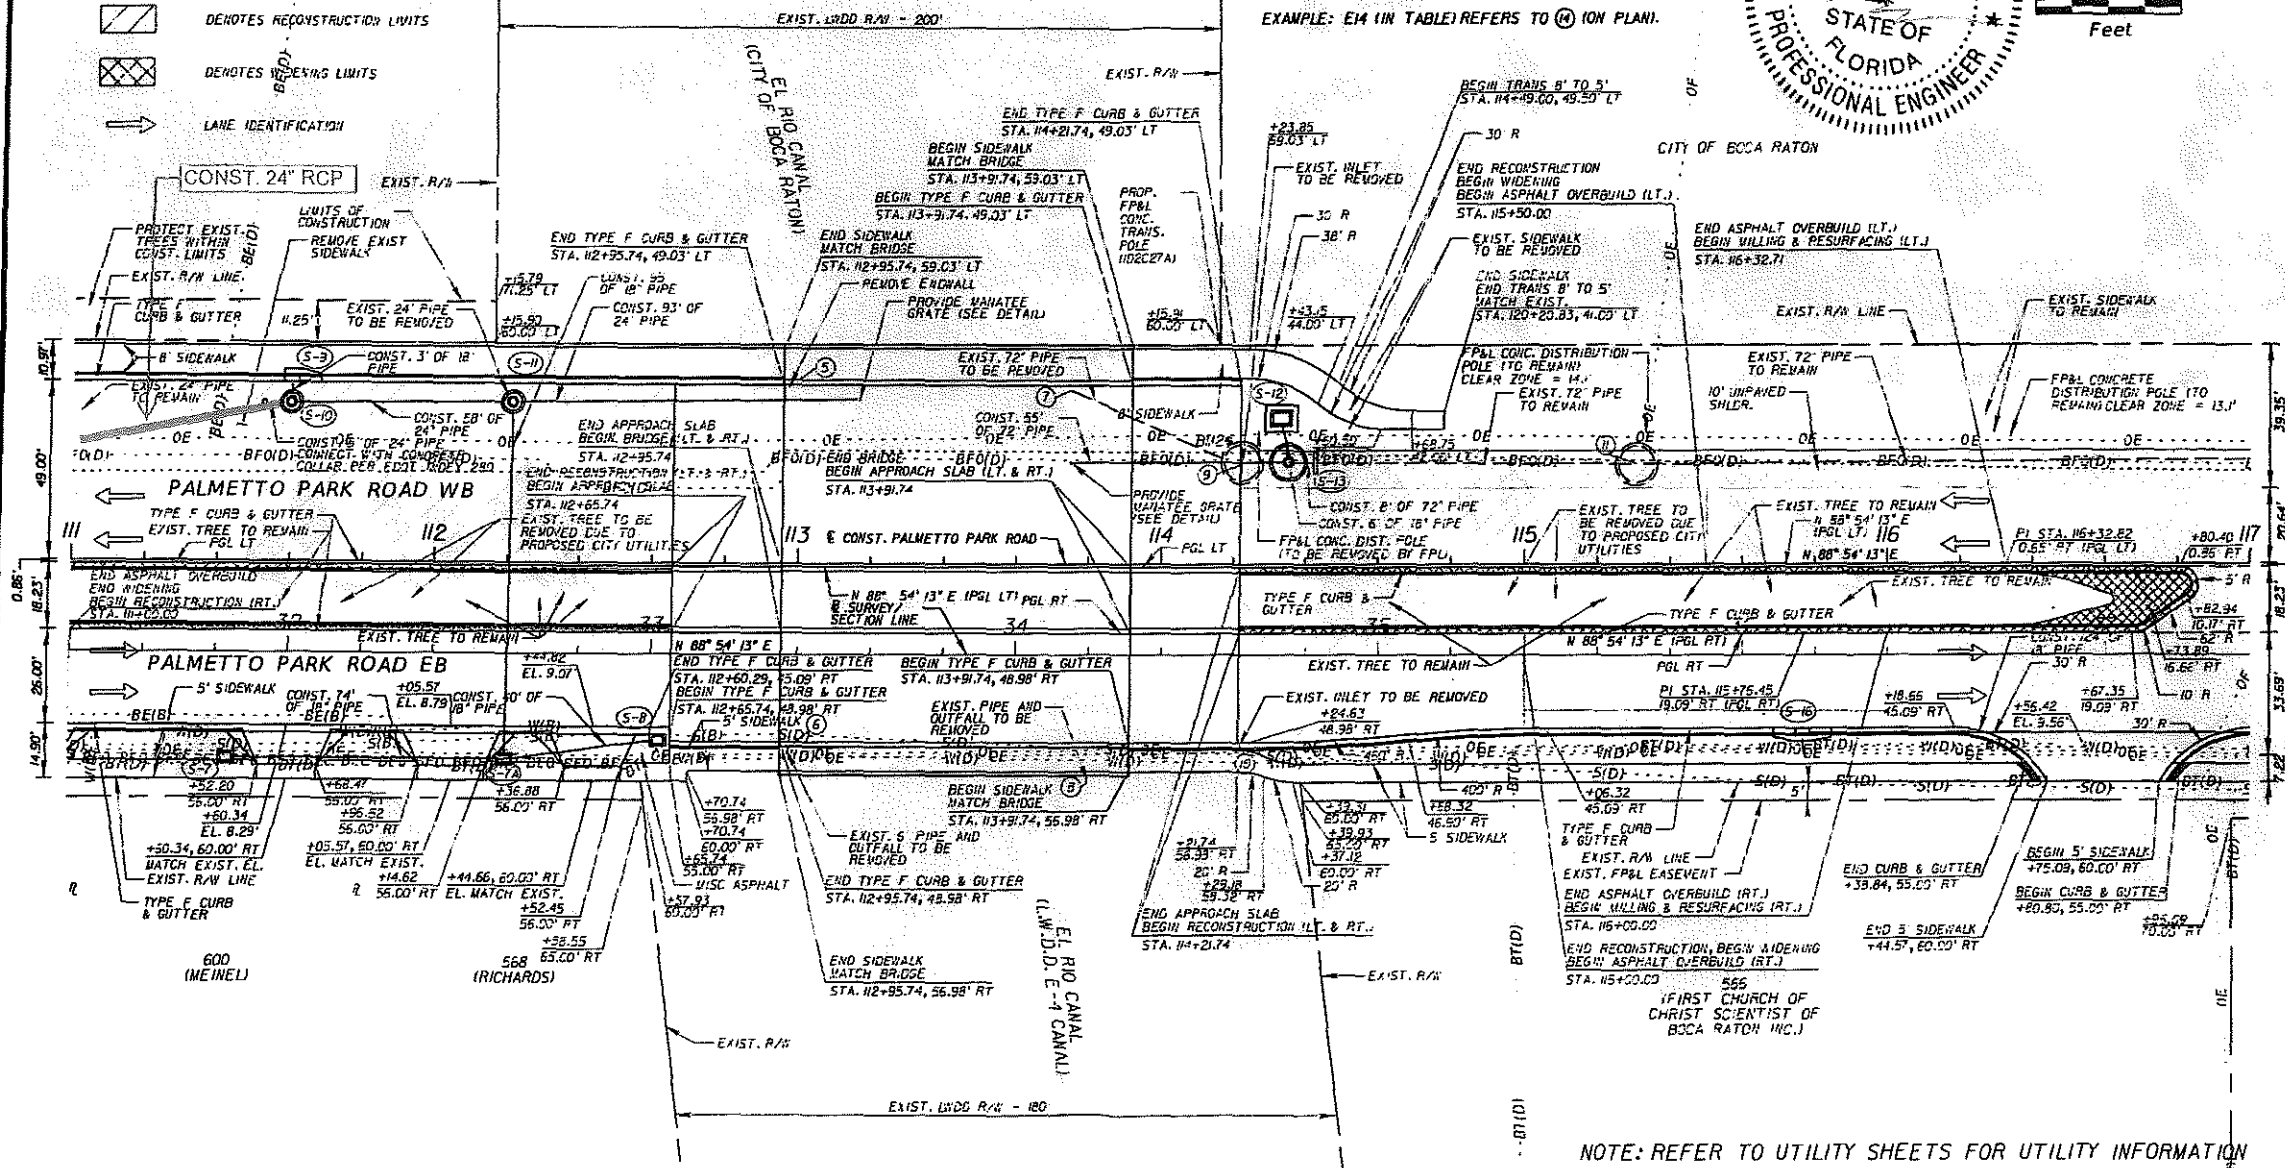

NOTE: REFER TO UTILITY SHEETS FOR UTILITY INFORMATION



2024 WGI
West Palm Beach, FL 33411
Phone No. 561-467-3320
Fax No. 561-467-1110
Email: info@wgi.com

NO.	REVISION	BY	DATE
1	REVISED	BAF	7/2/2024




PALM BEACH COUNTY
ENGINEERING AND PUBLIC WORKS
ROADWAY PRODUCTION
2800 N. JOE ROAD, WEST PALM BEACH, FLORIDA
33411

SCALE: 40
APPROVED: BAF
DRAWN: BAF
CHECKED: JAC
DATE: 9/25/24

ROADWAY PLAN SHEET


SHEET: 15
OF: 49

PROJECT NO. 2024-01

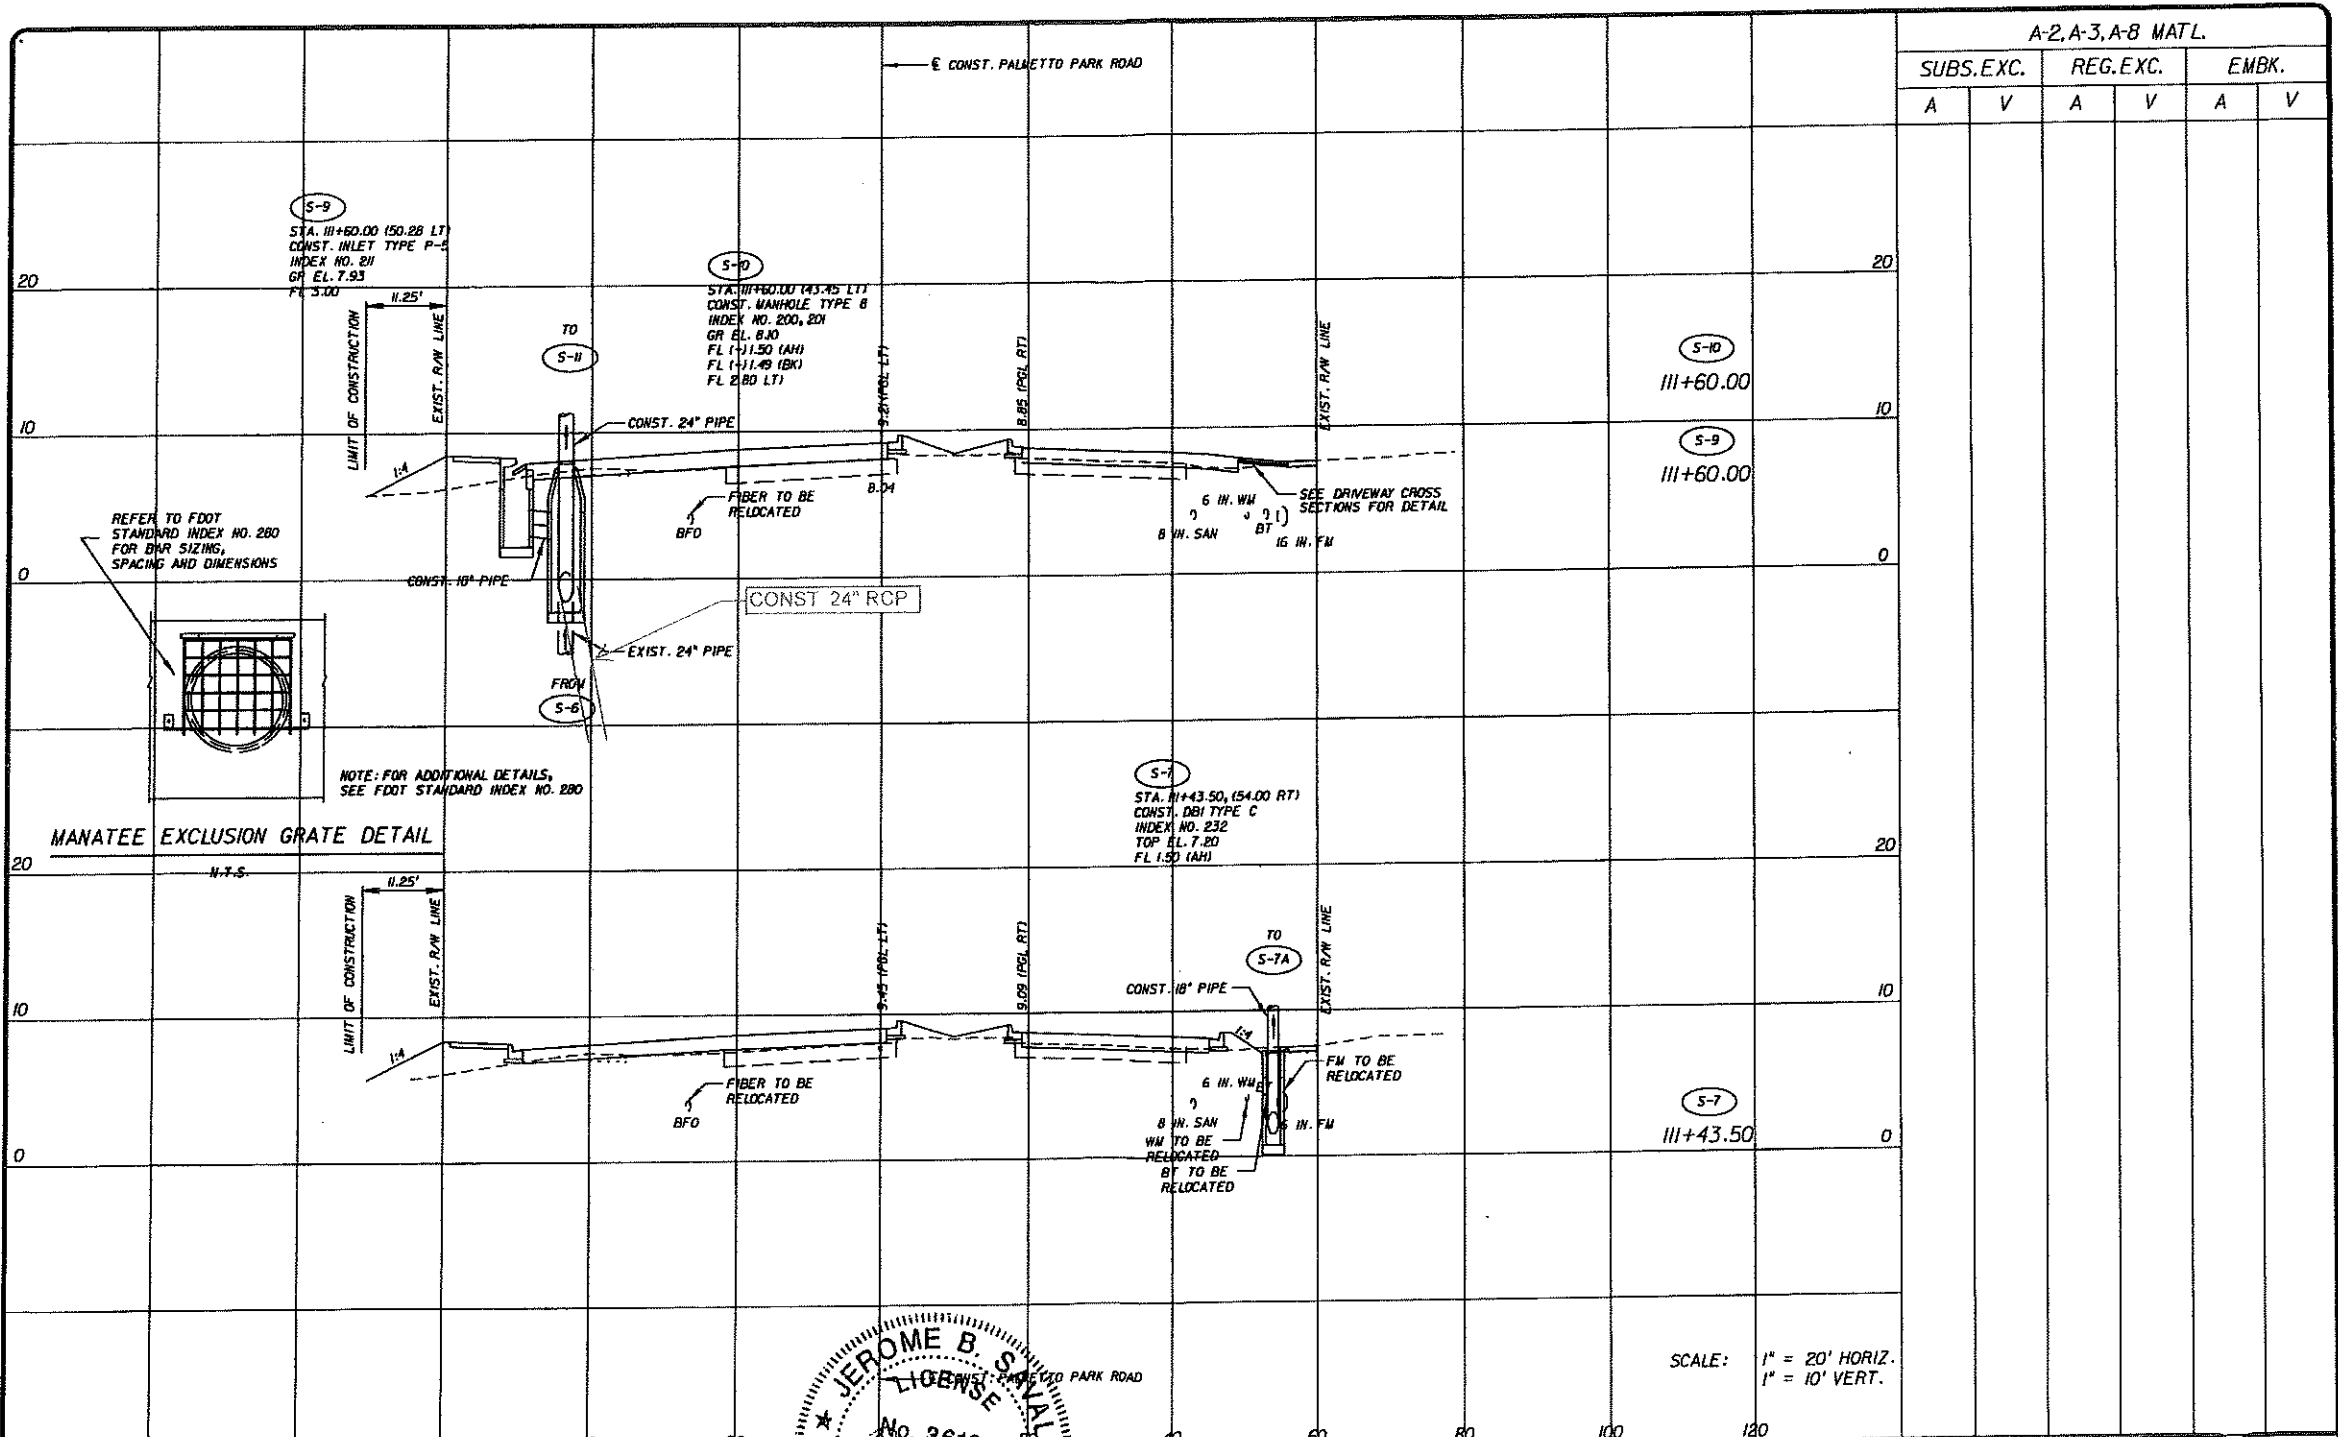

A-2, A-3, A-8 MATL.					
SUBS. EXC.		REG. EXC.		EMBK.	
A	V	A	V	A	V


SCALE: 1" = 20' HORIZ.
1" = 10' VERT.





2025 West Palm Beach, FL 33411
Phone No. 561-833-2220
Fax No. 561-833-1110
Circled 05/11/19 10:05

1000 Hammer Road, DE



PALM BEACH COUNTY
ENGINEERING AND PUBLIC WORKS
ROADWAY PRODUCTION
2200 N. JUDY ROAD, WEST PALM BEACH, FLORIDA
(407) 834-1100

SCALE:	40
APPROVED:	DAF
DRAWN:	DAF
CHECKED:	JAC
DATE:	8/25/17

DRAINAGE STRUCTURES PALMETTO PARK ROAD	
DESIGN FILE NAME	DRAWING NO.

SHEET: 21
OF: 49
PROJECT NO.
REVISED



1645 N. Congress Ave
West Palm Beach, FL 33409
Phone: (561) 793-9400

www.rangerconstruction.com

CLAIM No. 4 - Overbuild Information WB Lanes

Submitted To: Albert Hoffman	Date: 26-Jun-24
Address: Palm Beach County 2300 Jog Rd West Palm Beach, 33411	Phone:
Contact: Albert Hoffman	Fax:
	Job Name: 2013531 - Palmetto Park Rd
	RCI No. 300-3303
	Job Location: City of Boca Raton
	Owner: Palm Beach County

Claim Cost Calculation

Claim No.	DESCRIPTION	Delay Days	QUANTITY	UM	UNIT PRICE	EXTENSION
6	Overbuild Information on WB Lanes	46	1.00	LS	\$ 74,885.33	\$74,885.33
	Bond Cost 1.5%		1.00	LS	\$1,123.28	\$1,123.28
	Total Delay Days	46	ESTIMATED TOTAL =			
	Total Compensable Days	46	\$76,008.61			
		Average OH Cost Per Day		(A*C)/B		
		A = Original Contract Amount		\$ 4,337,120.16		
		B = Original Contract Time (Days)		450.00		
		C =		8%		
		Average OH Cost Per Day		\$ 771.04		

NOTES:
Daily OH Rate \$771.04

ACCEPTED: The above prices, specifications and conditions are satisfactory and are hereby accepted.	CONFIRMED: Ranger Construction Industries, Inc.
Owner _____	Authorized Signature
Signature _____	Name & Title
Date of Acceptance _____	Alejandro Uribe, P.E. - Project Manager



Ranger Construction Industries
1645 N. Congress Ave.
West Palm Beach, FL 33409
Phone: 561-793-9400

RCI PROJECT NUMBER
PROJECT NAME
Delay Cause
Total Compensable Delay Days
Delay Dates

3003303
Palmetto Park Rd
Overbuild Information on WB Lanes
46 Concurrent Delay with Bridge Inspection
12/9/2022 to 1/24/2023

CLAIM No. 4 Overbuild Information WB Lanes

ITEM	CODE	DESCRIPTION	Base Rate	QUANT	UOM	9/26/2024	TOTAL	Mark Up 17.5%
LABOR								
		Everet Ash (Superintendent)	\$ 57.00	62.00	HR	45.98%	\$ 5,158.93	\$ -
		Steve Summas (Foreman)	\$ 45.00	104.00	HR	45.98%	\$ 6,831.86	\$ -
		Pablo Monjaraz (Foreman)	\$ 44.50	3	HR	45.98%	\$ 194.88	\$ -
		Alejandro Uribe (Project Manager)	\$ 62.50	46.4	HR	45.98%	\$ 4,233.42	\$ -
		Roland Hembree (Foreman)	\$ 48.00	12.00	HR	45.98%	\$ 840.84	\$ -
		Karl Jones	\$ 25.00	12.00	HR	45.98%	\$ 437.94	\$ -
		Jean B. Bien Aime	\$ 23.00	12.00	HR	145.98%	\$ 678.90	\$ -
							\$ 18,376.79	\$ -
EQUIPMENT								
		F-150 Pickup Superintendent	\$ 46.48	62.00	HR		\$ 2,881.76	\$ -
		F-150 Pickup Foreman	\$ 46.48	119.00	HR		\$ 5,531.12	\$ -
		F-150 Pickup Project Manager	\$ 46.48	46.4	HR		\$ 2,156.67	\$ -
		Loader 256C Skid Steer 07	\$ 60.00	12	HR		\$ 720.00	\$ -
		Dump Truck	\$ 92.04	12	HR		\$ 1,104.48	\$ -
							\$ 12,394.03	\$ -
Materials								
		SP TLC Asphalt Placed WB Lanes	\$ 136.15		TN		\$ -	\$ -
							\$ -	\$ -
							\$ -	\$ -
		Overhead Cost	\$ 771.04	46	DAY		\$ 35,467.84	\$ -
							\$ -	\$ -
							\$ 35,467.84	\$ -
Subcontractors								
	ACME	MOT Devices (Actual invoice cost)	\$ 5,674.17	1	LS		\$ 5,674.17	\$ -
	C&W	Additional Survey Invoice #4444185 (2/9/23)	\$ 2,972.50	1	LS		\$ 2,972.50	\$ -
							\$ 8,646.67	\$ -
SUMMARY								
LABOR							\$ 18,376.79	\$ -
EQUIPMENT							\$ 12,394.03	\$ -
MATERIALS							\$ -	\$ -
Subcontractors							\$ 8,646.67	\$ -
Overhead Cost							\$ 35,467.84	\$ -
TOTAL								\$ 74,885.33



CAULFIELD & WHEELER INC.
Consulting Engineers, Surveyors & Mappers, Landscape Architecture

Engineering E80003581
Surveying LB0003591
Landscape Architecture LC0000318

Caulfield & Wheeler
7900 Glades Road
Suite 100
Boca Raton, FL 33434

Ranger Construction
1645 North Congress Ave
Email: Goya.Estrella@RangerConstruction.com
RangercentralAP@rangerconstruction.com
West Palm Beach, FL 33409

Invoice number 4444185
Date 02/09/2023
Project 9557 PALMETTO PARK ROAD - SW 7TH
AVE TO SW 5TH AVE

For Professional Services Through February 09, 2023

Professional Services
Hourly - Surveying Services

	Hours	Rate	Billed Amount
01/05/2023			
Field Survey Crew-GPS			
Hourly	2.00	165.00	330.00
MARK FILLS ON ASPHALT FOR OVERLAY AT SCHOOL ENTRANCE AREA PER ASH			
01/18/2023			
Field Survey Crew-GPS			
Hourly	8.00	165.00	1,320.00
SPRAY ASPHALT FOR OVERLAY FROM WEST OF BRIDGE TO WEST OF SCHOOL ENTRANCE A FEW HUNDRED FEET STAKE AND GRADE EP WEST SIDE SCHOOL ENTRANCE PER ASH & STEVEN			
01/20/2023			
Field Survey Crew-GPS			
Hourly	2.50	165.00	412.50
RESPRAY ASPHALT FOR OVERLAY AGAIN INTERSECTION AREA BY SCHOOL ENTRANCE PER REVISED DETAIL			
Professional Land Surveyor			
Hourly	3.00	140.00	420.00
BRIDGE ASBUILT FOR NORTHERN HALF PER ALEJANDRO URIBE.			
	3.50	140.00	490.00
CALCULATIONS OF SCHOOL ENTRANCE REVISIONS AND ADJUSTEMNTS PER ASH AND STEVE.			
Professional Services subtotal	19.00		2,972.50
Invoice total			2,972.50

Aging Summary

Invoice Number	Invoice Date	Outstanding	Current	Over 30	Over 60	Over 90	Over 120
4440528	10/10/2022	235.00					235.00
4442565	12/13/2022	412.50		412.50			
4443266	01/10/2023	2,082.50		2,082.50			



CAULFIELD & WHEELER INC.
Consulting Engineers, Surveyors & Mappers, Landscape Architecture

EXHIBIT "A" (Page 2 of 2) Celebrating 30 years

Engineering EB0003591
Surveying LB0003591
Landscape Architecture LC0000318

Ranger Construction
Project 9557 PALMETTO PARK ROAD - SW 7TH AVE TO SW 5TH AVE

Invoice number 4444185
Date 02/09/2023

Aging Summary

Invoice Number	Invoice Date	Outstanding	Current	Over 30	Over 60	Over 90	Over 120
4444185	02/09/2023	2,972.50	2,972.50				
	Total	5,702.50	2,972.50	2,495.00	0.00	0.00	235.00

Approved by:
Raymond D. Dowling
Project Manager

**FOR YOUR CONVENIENCE, WE NOW ACCEPT VISA, MASTERCARD, DISCOVER AND AMERICAN EXPRESS.
PLEASE USE OUR SECURE WEBSITE <https://cwi-assoc.com> TO MAKE YOUR CREDIT CARD PAYMENT.**

Office: 561-392-1991 Fax: 561-750-1452

Ranger Construction

Invoice number 4444185
Page 2 of 2

Invoice date 02/09/2023



Send Payments To:
Acme Barricades LC
Attn: Accounts Receivable
9800 Normandy Blvd., Jacksonville, FL 32221-2036
Tel: (904) 781-1950 Fax: (904) 781-1921
Federal Tax ID #59-3541899

INVOICE

Invoice No 316859
Date 12/31/22

Orlando Division 508 Clifton St Orlando, FL 32808 Tel (407) 253-4337 Fax (407) 253-1342	Panhandle Division 1675 Commerce Blvd Midway, Florida 32343 Tel (850) 765-8546 Fax (850) 765-8549	Tampa Division 2611 South 82nd Street, Tampa, FL 33619 Tel: (813) 623-ACME Fax: (813) 623-2045	Miami Division 4601 Oakes Road Davie, FL 33314 Tel: (954)-321-8205 Fax: (954)-791-0921	West Palm Beach 3705 Interstate Pkwy West Palm Beach, FL 33404 Tel: (561)-657-8222 Fax: (561)-657-8226
--	--	---	---	---

Ranger Construction, Inc.
1645 North Congress Avenue
West Palm Beach, FL 33409

Job No 3303
P.O. # **Bills w/BW**
ACME Job 27597
Email **Goya.Estrella@RangerConstructio
n.com

JAN 11 2023

Customer Phone 407-656-9255
Customer Fax 407-656-3188

REF: Palmetto Park Road, SW 7th Ave to SW
5th Ave (PBC Project #2013531)

Terms Net 30

Item	Equipment and Labor	From	To	Hrs/Days	Qty	Price	Amount
Rentals:							
102-74-6	Pedestrian LCD - ED	12/01/22	12/31/22	31	7	\$0.30	\$65.10
C	Drum w/SB	12/01/22	12/31/22	31	180	\$0.12	\$669.60
CCC	Type III w/flasher	12/01/22	12/31/22	31	9	\$0.25	\$69.75
D	B-Light 6V	12/01/22	12/31/22	31	16	\$0.10	\$49.60
DDDD	Arrowboard	12/01/22	12/31/22	31	2	\$5.00	\$310.00
E	Message Board	12/01/22	12/31/22	31	4	\$12.00	\$1,488.00
EEE	Large Sign Portable	12/01/22	12/31/22	31	34	\$0.22	\$231.88
EEEE	Post Mounted Sign	12/01/22	12/31/22	31	32	\$0.22	\$218.24
F	Flag	12/01/22	12/31/22	31	11	\$0.00	\$0.00
MMMM	Water Filled Barrier Wall	12/01/22	12/31/22	31	4	\$3.00	\$372.00
Rentals:						Subtotal	\$3,474.17
						Tax	\$0.00

Progress Bill

Total Amount	\$3,474.17
Total Taxes	\$0.00
Invoice Total	\$3,474.17 ✓



Send Payments To:
Acme Barricades LC
Attn: Accounts Receivable
9800 Normandy Blvd., Jacksonville, FL 32221-2036
Tel: (904) 781-1950 Fax: (904) 781-1921
Federal Tax ID #59-3541899

EXHIBIT A (Page 32 of 83)
INVOICE

Invoice No 317207
Date 01/31/23

Orlando Division 508 Clifton St Orlando, FL 32808 Tel: (407) 253-4337 Fax: (407) 253-1342	Panhandle Division 1675 Commerce Blvd Midway, Florida 32343 Tel:(850) 765-8546 Fax:(850) 765-8549	Tampa Division 2611 South 82nd Street, Tampa ,FL 33619 Tel: (813) 623-ACME Fax: (813) 623-2045	Miami Division 4601 Oakes Road Davie, FL 33314 Tel: (954)-321-8205 Fax: (954)-791-0921	West Palm Beach 3705 Interstate Pkwy West Palm Beach, FL 33404 Tel: (561)-657-8222 Fax: (561)-657-8226
--	--	---	---	---

Ranger Construction, Inc.
1645 North Congress Avenue
West Palm Beach, FL 33409

Job No 3303
P.O. # **Bills w/BW**
ACME Job 29244
Email **Goya.Estrella@RangerConstructio
n.com

Customer Phone 407-656-9255
Customer Fax 407-656-3188

REF: (Extras) Palmetto Park Road, SW 7th Ave
to SW 5th Ave (PBC Project #2013531)

Terms Net 30

Item	Equipment and Labor	From	To	Hrs/Days	Qty	Price	Amount
Services:							
100-100	3 Man Crew Labor	01/29/23		1	1	\$2,200.00	\$2,200.00
Services:						Subtotal	\$2,200.00
						Tax	\$0.00

Services Bill

Total Amount \$2,200.00
Total Taxes \$0.00
Invoice Total \$2,200.00

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Adjustments for F150 XLT 4x4 in All Saved Models

December 21, 2023

Ford F-150 XLT 4X4 GAS
Light Duty Trucks

Size Class:
2
Weight:
N/A



Configuration for F-150 XLT 4X4 GAS

Power Mode Model Trim	Gasoline XLT	Wheelbase Gross Vehicle Weight Rating	122.8 Inches 6050 Pounds
Blue Book Rates			
** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.			
	Ownership Costs		
	Monthly	Weekly	Daily
Published Rates	USD \$2,805.00	USD \$785.00	USD \$195.00
Adjustments			
Region (100%)	-	-	-
Model Year (2022: 99.26%)	(USD \$20.68)	(USD \$5.79)	(USD \$1.44)
Adjusted Hourly Ownership Cost (100%)	-	-	-
Hourly Operating Cost (100%)			
Total:	USD \$2,784.32	USD \$779.21	USD \$193.56
			USD \$28.79
			Estimated Operating Costs
			Hourly
			USD \$30.66
			FHWA Rate**
			Hourly
			USD \$46.60

Non-Active Use Rates		Hourly
Standby Rate		USD \$8.70
Idling Rate		USD \$36.54

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	23%	USD \$645.15/mo
Overhaul (ownership)	45%	USD \$1,262.25/mo
CFC (ownership)	18%	USD \$448.80/mo
Indirect (ownership)	16%	USD \$448.80/mo
Fuel (operating) @ USD 3.87	67.58%	USD \$20.72/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book® Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for CRAIG VORSTER (craig.vorster@veceliigroup.com)

Albert Hoffman

Subject: FW: [EXTERNAL] FW: Palmetto Park - Plans Conflicting Information

From: Brett Fuller <Brett.Fuller@wginc.com>
Sent: Friday, January 27, 2023 4:41 PM
To: John Kopelakis <JKopelak@pbcgov.org>
Cc: Antolina Michel-Diaz A. <AMichelDiaz@pbcgov.org>; John Drevas <JDrevas@pbcgov.org>
Subject: RE: [EXTERNAL] FW: Palmetto Park - Plans Conflicting Information

John,

I see no issue with what ranger is proposing.

Regards,
Brett



Brett Fuller, PE, PTOE
Project Engineer
2035 Vista Parkway
West Palm Beach, FL 33411
561.687.2220



From: John Kopelakis <JKopelak@pbcgov.org>
Sent: Tuesday, January 24, 2023 6:43 AM
To: Brett Fuller <Brett.Fuller@wginc.com>
Cc: Antolina Michel-Diaz A. <AMichelDiaz@pbcgov.org>; John Drevas <JDrevas@pbcgov.org>
Subject: [EXTERNAL] FW: Palmetto Park - Plans Conflicting Information

Brett,
For your review/comment.
Please see highlighted below.
They will be overbuilding tonight.
Thanks,

From: Alejandro Uribe <Alejandro.Uribe@rangerconstruction.com>
Sent: Friday, January 20, 2023 1:13 PM
To: John Drevas <JDrevas@pbcgov.org>; John Kopelakis <JKopelak@pbcgov.org>
Cc: Everett Ash <Everett.Ash@rangerconstruction.com>
Subject: FW: Palmetto Park - Plans Conflicting Information

This Message Is From an External Sender

This message came from outside your organization.

John,

Please forward to EOR and confirm this is acceptable.

Also, please confirm Ranger will get paid for removing and replacing the sidewalk to the west of the entrance. Do we send you a proposal or do we treat it as T&M?

Thanks

ALEJANDRO URIBE, P.E.
Project Manager



1645 N. Congress Ave.
West Palm Beach, FL 33409
OFFICE: (561) 793-9400
CELL: (561) 719-0397
auribe@rangerconstruction.com
www.rangerconstruction.com
[\[rangerconstruction.com\]](http://rangerconstruction.com)

From: Ray Dowling

Sent: Thursday, January 19, 2023 11:02 AM

To: Alejandro Uribe <Alejandro.Uribe@rangerconstruction.com>; John Drevas <JDrevas@pbcgov.org>

Cc: Everett Ash <Everett.Ash@rangerconstruction.com>; Steve Summas <Steve.Summas@rangerconstruction.com>;

Mario Mendoza <mario@cwiasoc.com>

Subject: RE: Palmetto Park - Plans Conflicting Information

We are going to set new grades and disregard the walk on the west side school entrance per Ash. That walk is coming out; Once the walk is raised a few inches it should be damn close. Just keep in mind the PGL is still raising as the road goes east so the side slope may be a bit over 3% but the cross slope will be 3 if that makes sense to you. I had a lot of people bring up if they turn their smart level 45° it's over % and that is why.

John- do you have any thoughts on this?

From: Alejandro Uribe [<mailto:Alejandro.Uribe@rangerconstruction.com>]

Sent: Thursday, January 19, 2023 8:04 AM

To: Ray Dowling <ray@cwiasoc.com>; John Kopelakis (JKopelak@pbcgov.org) <jkopelak@pbcgov.org>; John Drevas <JDrevas@pbcgov.org>

Cc: Everett Ash <Everett.Ash@rangerconstruction.com>; Steve Summas <Steve.Summas@rangerconstruction.com>;

Mario Mendoza <mario@cwiasoc.com>

Subject: RE: Palmetto Park - Plans Conflicting Information

Ray,

Are you working on calculating the new grades/slopes? If so, this needs to be approved by the EOR before we pave on Monday.

ALEJANDRO URIBE, P.E.
Project Manager



1645 N. Congress Ave.
West Palm Beach, FL 33409
OFFICE: (561) 793-9400
CELL: (561) 719-0397
auribe@rangerconstruction.com
www.rangerconstruction.com
[\[rangerconstruction.com\]](http://rangerconstruction.com)

From: Ray Dowling <ray@cwiasoc.com>

Sent: Wednesday, January 18, 2023 4:32 PM

To: Alejandro Uribe <Alejandro.Uribe@rangerconstruction.com>; John Kopelakis (JKopelak@pbcgov.org) <jkopelak@pbcgov.org>; John Drevas <JDrevas@pbcgov.org>

Cc: Everett Ash <Everett.Ash@rangerconstruction.com>; Steve Summas <Steve.Summas@rangerconstruction.com>; Mario Mendoza <mario@cwiasoc.com>


Subject: RE: Palmetto Park - Plans Conflicting Information

John,

See attached grades. We had to tweak one spot 25' east of station 109+0 to 6.78 elev. If we interpolated down to school installed ADA ramp el 5.21 58' LT we would have had to cut 6" of road out. In turn we went down 2% from new crown grade and sloped to the ADA ramp; from there and everything works. Long story short everything works in my opinion; we maintain ada standards within ada and we have a section at 4%. We held either, profile, section or spot grades to make SW school exit work but all 3 would not perfectly collate.

Thanks,

Ray

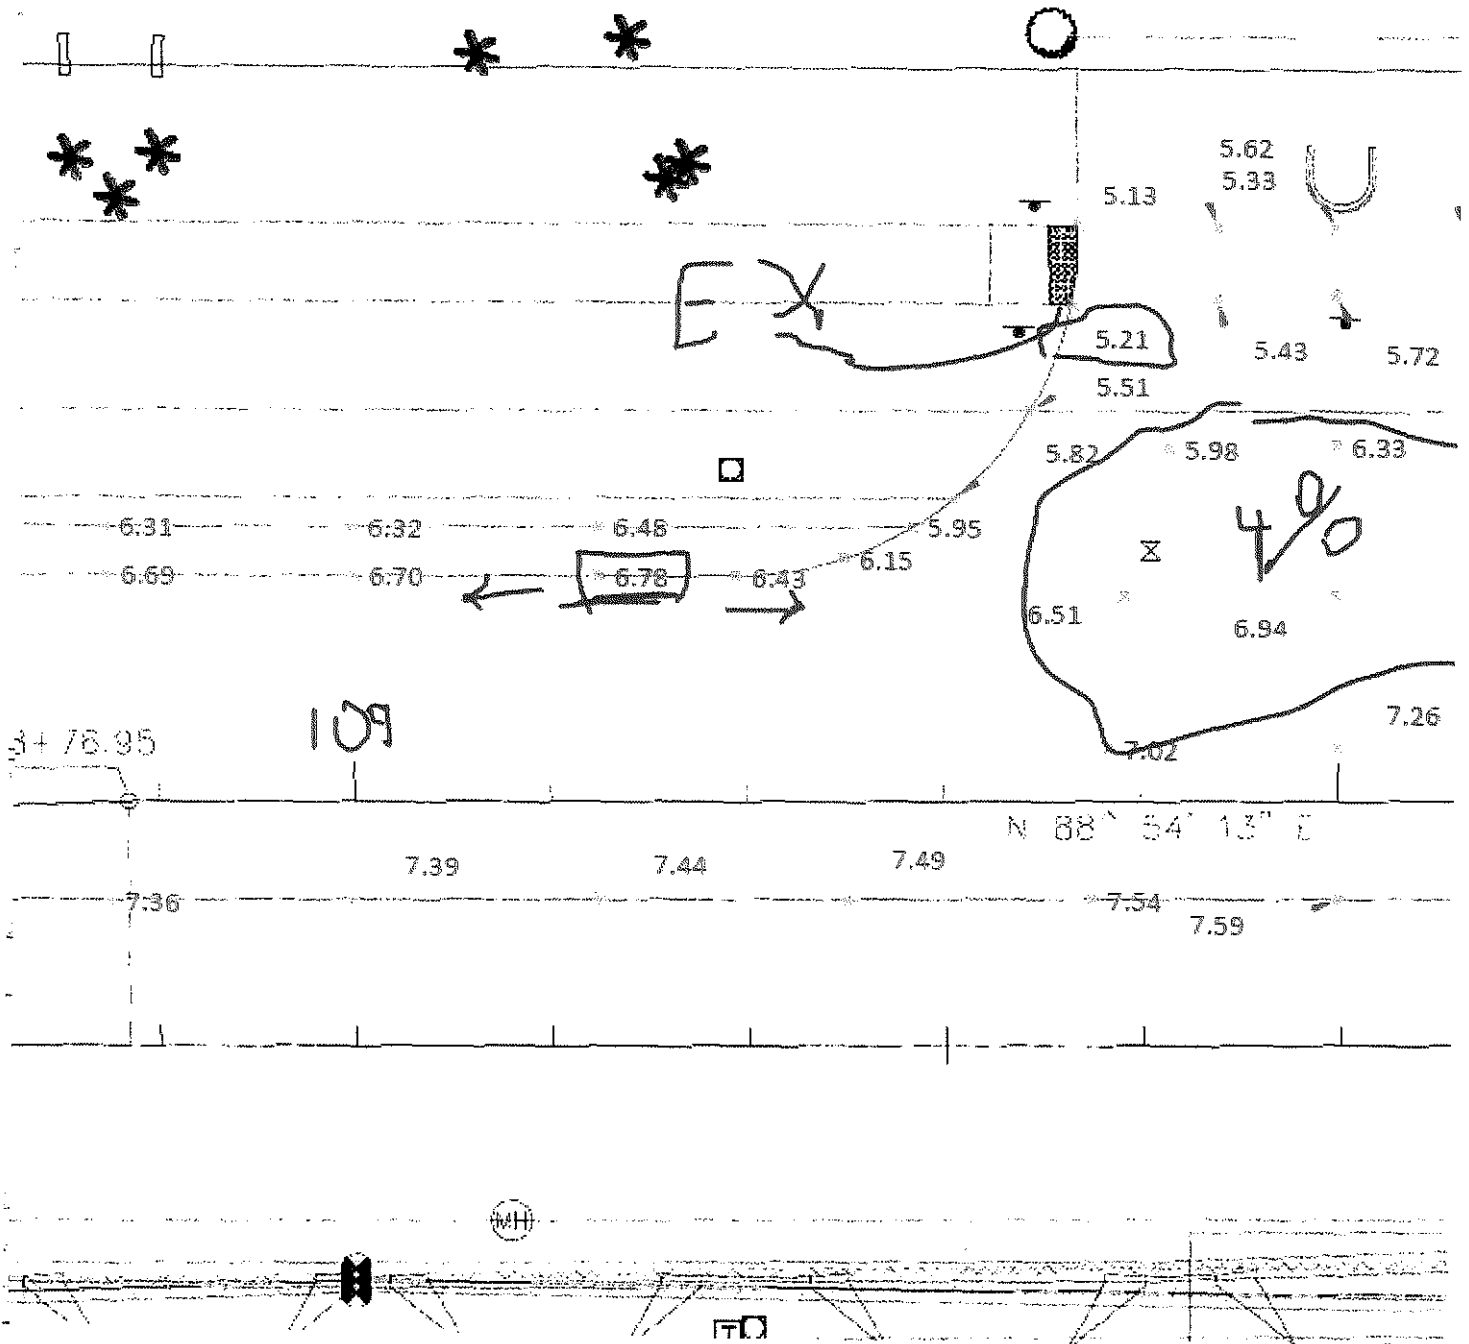



From: Alejandro Uribe [mailto:Alejandro.Uribe@rangerconstruction.com]
 Sent: Wednesday, January 18, 2023 4:09 PM
 To: John Kopelakis [mailto:JKopelak@pbcgov.org] <jkopelak@pbcgov.org>; John Drevas [mailto:JDrevas@pbcgov.org]
 Cc: Everett Ash [mailto:Everett.Ash@rangerconstruction.com]; Steve Summas [mailto:Steve.Summas@rangerconstruction.com]; Ray Dowling [mailto:ray@cwiasoc.com]; Mario Mendoza [mailto:mario@cwiasoc.com]
 Subject: Palmetto Park - Plans Conflicting Information

John,

Plans seem to have conflicting information. Roadway Plan Sheet 14 shows median starting at ~STA 110+30, but Typical Section No. 2, plan sheet 5, shows median starting at ~STA 109+64. See screen shots below.

Please request clarification from EOR.

Thanks

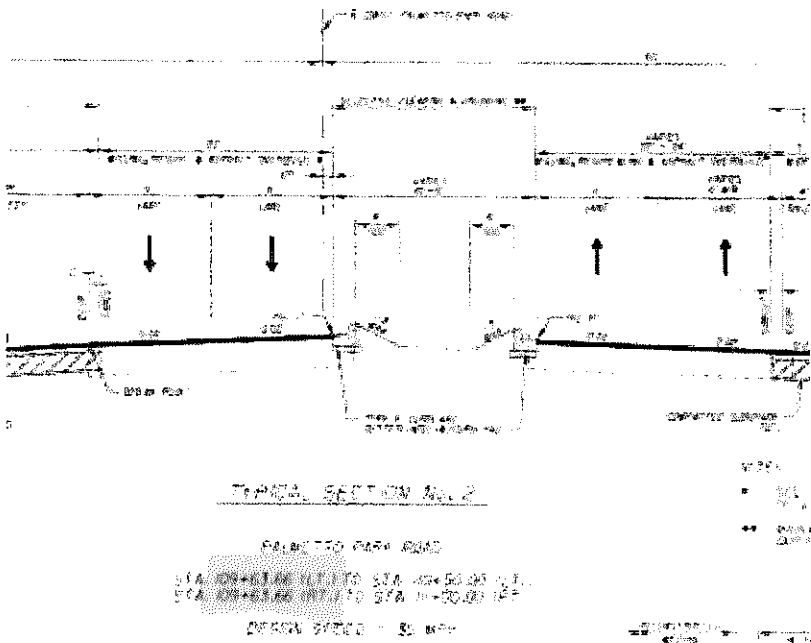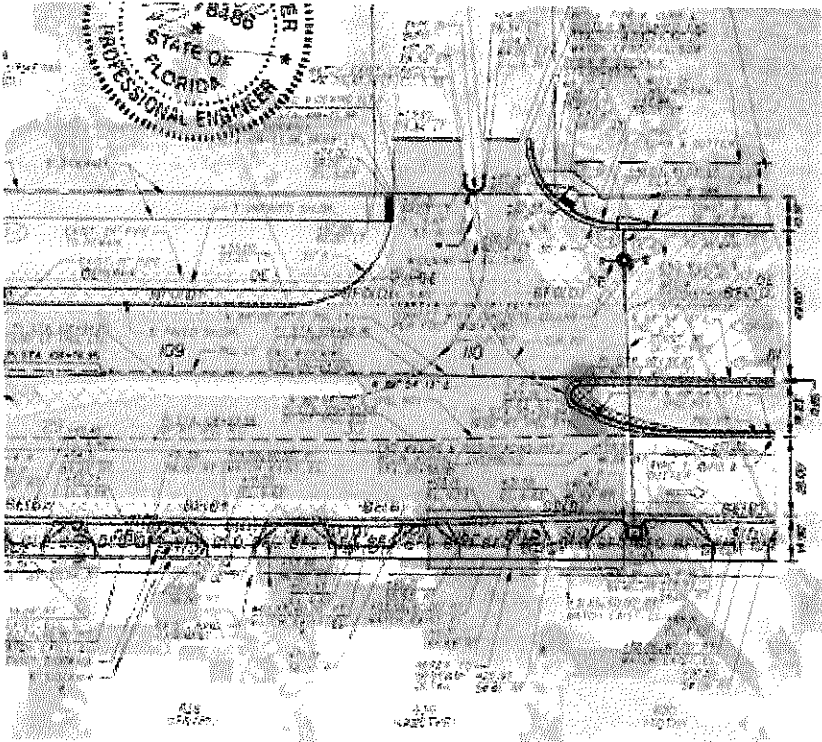

ALEJANDRO URIBE, P.E.
Project Manager



1645 N. Congress Ave.
West Palm Beach, FL 33409
OFFICE: (561) 793-9400
CELL: (561) 719-0397
auribe@rangerconstruction.com



1645 N. Congress Ave
West Palm Beach, FL 33409
Phone: (561) 793-9400

www.rangerconstruction.com

Delay Claim No. 5 - UNDERGROUND OBSTRUCTIONS

Submitted To: Patricio Ayala	Date: 19-Apr-24
Address: Palm Beach County 2300 Jog Rd West Palm Beach, 33411	Phone:
	Fax:
	Job Name: 2013531 - Palmetto Park Rd
Contact: Patricio Ayala	RCI No. 300-3303
	Job Location: City of Boca Raton
	Owner: Palm Beach County

Claim Cost Calculation

Claim No.	DESCRIPTION	Delay Days	QUANTITY	UM	UNIT PRICE	EXTENSION
9	Underground Obstructions	142	1.00	LS	\$ 463,523.88	\$463,523.88
	Bond Cost 1.5%		1.00	LS	\$6,952.86	\$6,952.86
Total Delay Days		142	ESTIMATED TOTAL =			
Total Compensable Days		128	\$470,476.74			
Average OH Cost Per Day						(A*C)/B
A = Original Contract Amount						\$ 4,337,120.16
B = Original Contract Time (Days)						450.00
C =						8%
Average OH Cost Per Day						\$ 771.04

NOTES:
Labor Costs Include 45.98% Labor Burden
Daily OH Rate \$771.04
Includes Actual Invoice cost for MOT Devices

ACCEPTED: The above prices, specifications and conditions are satisfactory and are hereby accepted.	Ranger Construction Industries, Inc.
Owner _____	Authorized Signature _____
Signature _____	Name & Title Gregory W. Reilly - Project Manager
Date of Acceptance _____	



Ranger

Construction

Ranger Construction Industries

1645 N. Congress Ave.
West Palm Beach, FL 33409
Phone: 561-793-9400

RCI PROJECT NUMBER	3003303
PROJECT NAME	Palmetto Park Rd
Delay Cause	Underground Obstructions
Total Compensable Delay Days	128.00
Delay Dates	8/1/2023 to 2/29/2024

Delay Claim No. 5 - UNDERGROUND OBSTRUCTIONS

ITEM	CODE	DESCRIPTION	Base Rate	QUANT	UOM	BURDEN	TOTAL	Mark Up 17.5%
		LABOR						
		Everet Ash (Superintendent)	\$ 57.00	472.00	HR	45.98%	\$ 39,274.46	\$ -
		Roland Hembree (Foreman)	\$ 48.00	72.00	HR	45.98%	\$ 5,045.07	\$ -
		Eyon Gordon (Foreman)	\$ 50.75	216.00	HR	45.98%	\$ 16,002.33	\$ -
		Pablo Monjaraz (Foreman)	\$ 44.50	8.00	HR	45.98%	\$ 519.69	\$ -
		Rob Sumner (Foreman)	\$ 45.00	48.00	HR	45.98%	\$ 3,153.17	\$ -
		Alejandro Uribe (Project Manager)	\$ 62.50	475.00	HR	45.98%	\$ 43,337.81	\$ -
							\$ 107,332.52	\$ -
		EQUIPMENT						
		F-150 Pickup Superintendent	\$ 46.48	472.00	HR		\$ 21,938.56	\$ -
		F-150 Pickup Foreman	\$ 46.48	344.00	HR		\$ 15,989.12	\$ -
		F-150 Pickup Project Manager	\$ 46.48	475.00	HR		\$ 22,078.00	\$ -
							\$ 60,005.68	\$ -
		Ranger Overhead Cost	\$ 771.04	128.00	DAY		\$ 98,693.12	\$ -
							\$ 98,693.12	\$ -
		Subcontractors						Mark Up 10%
	ACME	MOT Devices (Actual Invoices)	\$ 13,327.50	1	LS		\$ 13,327.50	\$ -
	ANZAC	Claim Direct Cost	\$ 184,165.06	1	LS		\$ 184,165.06	\$ -
							\$ 197,492.56	\$ -
SUMMARY								
LABOR							\$ 107,332.52	\$ -
EQUIPMENT							\$ 60,005.68	\$ -
Subcontractors							\$ 197,492.56	\$ -
Ranger Overhead Cost							\$ 98,693.12	\$ -
TOTAL								\$ 463,523.88



Send Payments To:
Acme Barricades LC
Attn: Accounts Receivable
9800 Normandy Blvd., Jacksonville, FL 32221-2036
Tel: (904) 781-1950 Fax: (904) 781-1921
Federal Tax ID #59-3541899

EXHIBIT A (Page 3 of 3)
INVOICE

Invoice No 320535
Date 10/31/23

Orlando Division 508 Clifton St Orlando, FL 32808 Tel: (407) 253-4337 Fax: (407) 253-1342	Panhandle Division 1675 Commerce Blvd Midway, Florida 32343 Tel:(850) 765-8546 Fax:(850) 765-8549	Tampa Division 2611 South 82nd Street, Tampa ,FL 33619 Tel: (813) 623-ACME Fax: (813) 623-2045	Miami Division 4601 Oakes Road Davie, FL 33314 Tel: (954)-321-8205 Fax: (954)-791-0921	West Palm Beach 3705 Interstate Pkwy West Palm Beach, FL 33404 Tel: (561)-657-8222 Fax: (561)-657-8226
--	--	---	---	---

Ranger Construction, Inc.
1645 North Congress Avenue
West Palm Beach, FL 33409

Job No 3303
P.O. # **Bills w/BW**
ACME Job 27597
Email *Goya.Estrella@RangerConstruction.com (ind pdf)

Customer Phone 407-656-9255
Customer Fax 407-656-3188

REF: Palmetto Park Road, SW 7th Ave to SW
5th Ave B. Raton (PBC Project #2013531

Terms Net 30

Item	Equipment and Labor	From	To	Hrs/Days	Qty	Price	Amount
Rentals:							
102-74-6	Pedestrian LCD - ED	10/16/23	10/31/23	16	8	\$0.30	\$38.40
102-74-6	Pedestrian LCD - ED	10/01/23	10/31/23	31	11	\$0.30	\$102.30
C	Drum w/SB	10/01/23	10/31/23	31	182	\$0.12	\$677.04
CCC	Type III w/flasher	10/01/23	10/31/23	31	14	\$0.25	\$108.50
D	B-Light 6V	10/01/23	10/31/23	31	16	\$0.10	\$49.60
DDDD	Arrowboard	10/01/23	10/31/23	31	2	\$5.00	\$310.00
E	Message Board	10/01/23	10/02/23	2	1	\$12.00	\$24.00
E	Message Board	10/03/23	10/31/23	29	1	\$12.00	\$348.00
E	Message Board	10/01/23	10/31/23	31	1	\$12.00	\$372.00
EEE	Large Sign Portable	10/01/23	10/31/23	31	36	\$0.22	\$245.52
EEE	Large Sign Portable	10/16/23	10/31/23	16	1	\$0.22	\$3.52
EEE	Large Sign Portable	10/12/23	10/31/23	20	4	\$0.22	\$17.60
EEEE	Post Mounted Sign	10/01/23	10/31/23	31	55	\$0.22	\$375.10
F	Flag	10/01/23	10/31/23	31	11	\$0.00	\$0.00
Rentals:						Subtotal	\$2,671.58
						Tax	\$0.00

Progress Bill

Total Amount \$2,671.58
Total Taxes \$0.00
Invoice Total \$2,671.58



Send Payments To:
Acme Barricades LC
Attn: Accounts Receivable
9800 Normandy Blvd., Jacksonville, FL 32221-2036
Tel: (904) 781-1950 Fax: (904) 781-1921
Federal Tax ID #59-3541899

EXHIBIT A (Page 3 of 3)
INVOICE

Invoice No 320905
Date 11/30/23

Orlando Division 508 Clifton St Orlando, FL 32808 Tel: (407) 253-4337 Fax: (407) 253-1342	Panhandle Division 1675 Commerce Blvd Midway, Florida 32343 Tel: (850) 765-8546 Fax: (850) 765-8549	Tampa Division 2611 South 82nd Street, Tampa, FL 33619 Tel: (813) 623-ACME Fax: (813) 623-2045	Miami Division 4601 Oakes Road Davie, FL 33314 Tel: (954)-321-8205 Fax: (954)-791-0921	West Palm Beach 3705 Interstate Pkwy West Palm Beach, FL 33404 Tel: (561)-657-8222 Fax: (561)-657-8226
--	--	---	---	---

Ranger Construction, Inc.
1645 North Congress Avenue
West Palm Beach, FL 33409

Job No 3303
P.O. # **Bills w/BW**
ACME Job 27597
Email *Goya.Estrella@RangerConstruction.com (ind pdf)

Customer Phone 407-656-9255
Customer Fax 407-656-3188

REF: Palmetto Park Road, SW 7th Ave to SW
5th Ave B. Raton (PBC Project #2013531)

Terms Net 30

Item	Equipment and Labor	From	To	Hrs/Days	Qty	Price	Amount
Rentals:							
102-74-6	Pedestrian LCD - ED	11/01/23	11/30/23	30	19	\$0.30	\$171.00
C	Drum w/SB	11/01/23	11/30/23	30	182	\$0.12	\$655.20
CCC	Type III w/flasher	11/01/23	11/30/23	30	14	\$0.25	\$105.00
D	B-Light 6V	11/01/23	11/30/23	30	16	\$0.10	\$48.00
DDDD	Arrowboard	11/01/23	11/01/23	1	1	\$5.00	\$5.00
DDDD	Arrowboard	11/02/23	11/30/23	29	1	\$5.00	\$145.00
DDDD	Arrowboard	11/01/23	11/30/23	30	1	\$5.00	\$150.00
E	Message Board	11/01/23	11/30/23	30	2	\$12.00	\$720.00
EEE	Large Sign Portable	11/01/23	11/30/23	30	41	\$0.22	\$270.60
EEE	Large Sign Portable	11/10/23	11/30/23	21	1	\$0.22	\$4.62
EEEE	Post Mounted Sign	11/01/23	11/30/23	30	55	\$0.22	\$363.00
F	Flag	11/01/23	11/30/23	30	11	\$0.00	\$0.00
Rentals:						Subtotal	\$2,637.42
						Tax	\$0.00

Progress Bill

Total Amount	\$2,637.42
Total Taxes	\$0.00
Invoice Total	\$2,637.42



Send Payments To:
Acme Barricades LC
Attn: Accounts Receivable
9800 Normandy Blvd., Jacksonville, FL 32221-2036
Tel: (904) 781-1950 Fax: (904) 781-1921
Federal Tax ID #59-3541899

Invoice No 321292
Date 12/31/23

Orlando Division 508 Clifton St Orlando, FL 32808 Tel: (407) 253-4337 Fax: (407) 253-1342	Panhandle Division 1675 Commerce Blvd Midway, Florida 32343 Tel:(850) 765-8546 Fax:(850) 765-8549	Tampa Division 2611 South 82nd Street, Tampa ,FL 33619 Tel: (813) 623-ACME Fax: (813) 623-2045	Miami Division 4601 Oakes Road Davie, FL 33314 Tel: (954)-321-8205 Fax: (954)-791-0921	West Palm Beach 3705 Interstate Pkwy West Palm Beach, FL 33404 Tel: (561)-657-8222 Fax: (561)-657-8226
--	--	---	---	---

Ranger Construction, Inc.
1645 North Congress Avenue
West Palm Beach, FL 33409

Job No 3303
P.O. # **Bills w/BW**
ACME Job 27597
Email *Goya.Estrella@RangerConstruction.com (ind pdf)

Customer Phone 407-656-9255
Customer Fax 407-656-3188

REF: Palmetto Park Road, SW 7th Ave to SW
5th Ave B. Raton (PBC Project #2013531)

Terms Net 30

Item	Equipment and Labor	From	To	Hrs/Days	Qty	Price	Amount
Rentals:							
102-74-6	Pedestrian LCD - ED	12/01/23	12/31/23	31	19	\$0.30	\$176.70
C	Drum w/SB	12/01/23	12/31/23	31	182	\$0.12	\$677.04
C	Drum w/SB	12/21/23	12/22/23	2	4	\$0.12	\$0.96
CCC	Type III w/flasher	12/01/23	12/31/23	31	14	\$0.25	\$108.50
D	B-Light 6V	12/01/23	12/31/23	31	16	\$0.10	\$49.60
DDDD	Arrowboard	12/01/23	12/31/23	31	2	\$5.00	\$310.00
E	Message Board	12/01/23	12/31/23	31	2	\$12.00	\$744.00
E	Message Board	12/21/23	12/22/23	2	1	\$12.00	\$24.00
EEE	Large Sign Portable	12/01/23	12/31/23	31	42	\$0.22	\$286.44
EEEE	Post Mounted Sign	12/01/23	12/31/23	31	55	\$0.22	\$375.10
F	Flag	12/01/23	12/31/23	31	11	\$0.00	\$0.00
Rentals:						Subtotal	\$2,752.34
						Tax	\$0.00

Progress Bill

Total Amount	\$2,752.34
Total Taxes	\$0.00
Invoice Total	\$2,752.34



Send Payments To:
Acme Barricades LC
Attn: Accounts Receivable
9800 Normandy Blvd., Jacksonville, FL 32221-2036
Tel: (904) 781-1950 Fax: (904) 781-1921
Federal Tax ID #59-3541899

EXHIBIT "A" (Page 37 of 83)
INVOICE

Invoice No 321649
Date 01/31/24

Orlando Division 508 Clifton St Orlando, FL 32808 Tel: (407) 253-4337 Fax: (407) 253-1342	Panhandle Division 1675 Commerce Blvd Midway, Florida 32343 Tel:(850) 765-8546 Fax:(850) 765-8549	Tampa Division 2611 South 82nd Street, Tampa, FL 33619 Tel: (813) 623-ACME Fax: (813) 623-2045	Miami Division 4601 Oakes Road Davie, FL 33314 Tel: (954)-321-8205 Fax: (954)-791-0921	West Palm Beach 3705 Interstate Pkwy West Palm Beach, FL 33404 Tel: (561)-657-8222 Fax: (561)-657-8226
--	--	---	---	---

Ranger Construction, Inc.
1645 North Congress Avenue
West Palm Beach, FL 33409

Job No 3303
P.O. # **Bills w/BW**
ACME Job 27597
Email *Goya.Estrella@RangerConstruction.com (ind pdf)

Customer Phone 407-656-9255
Customer Fax 407-656-3188

REF: Palmetto Park Road, SW 7th Ave to SW
5th Ave B. Raton (PBC Project #2013531

Terms Net 30

Item	Equipment and Labor	From	To	Hrs/Days	Qty	Price	Amount
Rentals:							
102-74-6	Pedestrian LCD - ED	01/01/24	01/31/24	31	19	\$0.30	\$176.70
C	Drum w/SB	01/01/24	01/31/24	31	182	\$0.12	\$677.04
CCC	Type III w/flasher	01/01/24	01/31/24	31	14	\$0.25	\$108.50
D	B-Light 6V	01/01/24	01/31/24	31	16	\$0.10	\$49.60
DDDD	Arrowboard	01/01/24	01/31/24	31	2	\$5.00	\$310.00
E	Message Board	01/01/24	01/31/24	31	1	\$12.00	\$372.00
E	Message Board	01/06/24	01/31/24	26	1	\$12.00	\$312.00
E	Message Board	01/01/24	01/05/24	5	1	\$12.00	\$60.00
EEE	Large Sign Portable	01/01/24	01/31/24	31	42	\$0.22	\$286.44
EEEE	Post Mounted Sign	01/01/24	01/31/24	31	55	\$0.22	\$375.10
F	Flag	01/01/24	01/31/24	31	11	\$0.00	\$0.00
Rentals:						Subtotal	\$2,727.38
						Tax	\$0.00

Progress Bill

Total Amount	\$2,727.38
Total Taxes	\$0.00
Invoice Total	\$2,727.38



Send Payments To:
Acme Barricades LC
Attn: Accounts Receivable
9800 Normandy Blvd., Jacksonville, FL 32221-2036
Tel: (904) 781-1950 Fax: (904) 781-1921
Federal Tax ID #59-3541899

EXHIBIT A (Page 2 of 2)
INVOICE

Invoice No 322034
Date 02/29/24

Orlando Division 508 Clifton St Orlando, FL 32808 Tel: (407) 253-4337 Fax: (407) 253-1342	Panhandle Division 1675 Commerce Blvd Midway, Florida 32343 Tel:(850) 765-8546 Fax:(850) 765-8549	Tampa Division 2611 South 82nd Street, Tampa ,FL 33619 Tel: (813) 623-ACME Fax: (813) 623-2045	Miami Division 4601 Oakes Road Davie, FL 33314 Tel: (954)-321-8205 Fax: (954)-791-0921	West Palm Beach 3705 Interstate Pkwy West Palm Beach, FL 33404 Tel: (561)-657-8222 Fax: (561)-657-8226
--	--	---	---	---

Ranger Construction, Inc.
1645 North Congress Avenue
West Palm Beach, FL 33409

Job No 3303
P.O. # **Bills w/BW**
ACME Job 27597
Email *Goya.Estrella@RangerConstruction.com (ind pdf)

Customer Phone 407-656-9255
Customer Fax 407-656-3188

REF: Palmetto Park Road, SW 7th Ave to SW
5th Ave B. Raton (PBC Project #2013531

Terms Net 30

Item	Equipment and Labor	From	To	Hrs/Days	Qty	Price	Amount
Rentals:							
102-74-6	Pedestrian LCD - ED	02/01/24	02/29/24	29	16	\$0.30	\$139.20
102-74-6	Pedestrian LCD - ED	02/01/24	02/26/24	26	3	\$0.30	\$23.40
C	Drum w/SB	02/01/24	02/26/24	26	3	\$0.12	\$9.36
C	Drum w/SB	02/01/24	02/29/24	29	179	\$0.12	\$622.92
CCC	Type III w/flasher	02/01/24	02/29/24	29	11	\$0.25	\$79.75
CCC	Type III w/flasher	02/01/24	02/26/24	26	3	\$0.25	\$19.50
D	B-Light 6V	02/01/24	02/29/24	29	16	\$0.10	\$46.40
DDDD	Arrowboard	02/01/24	02/29/24	29	2	\$5.00	\$290.00
E	Message Board	02/01/24	02/15/24	15	1	\$12.00	\$180.00
E	Message Board	02/22/24	02/29/24	8	1	\$12.00	\$96.00
E	Message Board	02/01/24	02/29/24	29	1	\$12.00	\$348.00
E	Message Board	02/16/24	02/21/24	6	1	\$12.00	\$72.00
EEE	Large Sign Portable	02/01/24	02/26/24	26	10	\$0.22	\$57.20
EEE	Large Sign Portable	02/01/24	02/29/24	29	32	\$0.22	\$204.16
EEEE	Post Mounted Sign	02/01/24	02/29/24	29	55	\$0.22	\$350.90
F	Flag	02/01/24	02/29/24	29	11	\$0.00	\$0.00
Rentals:						Subtotal	\$2,538.79
						Tax	\$0.00

Progress Bill

Total Amount \$2,538.79
Total Taxes \$0.00
Invoice Total \$2,538.79

PALMETTO PARK RD BRIDGE - COSTS INCURRED DUE TO UNFORESEEN UNDERGROUND OBSTRUCTIONS									
DATES	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	TOTAL	ANZAC PROFIT	MARK UP PERCENTAGE	TOTAL	COMMENTS
THURSDAY, 8/17/23	DISCOVERED UNDERGROUND OBSTRUCTION WHILE ATTEMPTING TO JET PILE #40, IB #2.								
	GEORGE VALDES	1.00	HR	\$77.36	\$77.36	\$13.54	17.50%	\$90.90	
	SUPERVISOR'S TRUCK	1.00	HR	\$39.27	\$39.27	\$6.87	17.50%	\$46.14	
	HECTOR BENEGAS	2.00	HR	\$47.89	\$95.78	\$16.76	17.50%	\$112.54	
	FORMAN'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	REGINALD WATSON	2.00	HR	\$73.68	\$147.36	\$25.79	17.50%	\$173.15	
	CRANE OPERATOR'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	LUIS CAPADEVILA	2.00	HR	\$35.36	\$70.72	\$12.38	17.50%	\$83.10	
	FELIX VAZQUEZ	2.00	HR	\$28.00	\$56.00	\$9.80	17.50%	\$65.80	
	YEISON MONZON	2.00	HR	\$36.84	\$73.68	\$12.89	17.50%	\$86.57	
	JUAN MEDRANO	2.00	HR	\$36.84	\$73.68	\$12.89	17.50%	\$86.57	
	ISUZU CREW CAB FLAT BED TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	2.00	HR	\$454.27	\$908.54	\$158.99	17.50%	\$1,067.53	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	2.00	HR	\$21.12	\$42.24	\$7.39	17.50%	\$49.63	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	2.00	HR	\$18.31	\$36.62	\$6.41	17.50%	\$43.03	
	GENERATOR AND TORCH SET	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	2.00	HR	\$21.39	\$42.78	\$7.49	17.50%	\$50.27	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	2.00	HR	\$5.00	\$10.00	\$1.75	17.50%	\$11.75	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
FRIDAY, 8/18/23	ATTEMPTED JETTING PILE #40, IB #2 AGAIN TO SEE IF WE MIGHT BE ABLE TO JET THROUGH AND CLEAR THE UNDERGROUND OBSTRUCTION. IT SEEMS TO ACT LIKE A PIPE, THEREFORE IT WAS ASSUMED TO BE THE EXISTING ABANDONED FORCE MAIN								
	GEORGE VALDES	1.00	HR	\$77.36	\$77.36	\$13.54	17.50%	\$90.90	
	SUPERVISOR'S TRUCK	1.00	HR	\$39.27	\$39.27	\$6.87	17.50%	\$46.14	
	HECTOR BENEGAS	2.00	HR	\$47.89	\$95.78	\$16.76	17.50%	\$112.54	
	FORMAN'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	REGINALD WATSON	2.00	HR	\$73.68	\$147.36	\$25.79	17.50%	\$173.15	
	CRANE OPERATOR'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	LUIS CAPADEVILA	2.00	HR	\$35.36	\$70.72	\$12.38	17.50%	\$83.10	
	FELIX VAZQUEZ	2.00	HR	\$28.00	\$56.00	\$9.80	17.50%	\$65.80	
	YEISON MONZON	2.00	HR	\$36.84	\$73.68	\$12.89	17.50%	\$86.57	
	ISUZU CREW CAB FLAT BED TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	2.00	HR	\$454.27	\$908.54	\$158.99	17.50%	\$1,067.53	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	2.00	HR	\$21.12	\$42.24	\$7.39	17.50%	\$49.63	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	2.00	HR	\$18.31	\$36.62	\$6.41	17.50%	\$43.03	
	GENERATOR AND TORCH SET	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	2.00	HR	\$21.39	\$42.78	\$7.49	17.50%	\$50.27	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	2.00	HR	\$5.00	\$10.00	\$1.75	17.50%	\$11.75	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
WEDNESDAY, 8/23/23	ATTEMPTED JETTING PILE #40, IB #2 TO SEE WHERE WE MIGHT MOVE IT TO CLEAR THE UNDERGROUND OBSTRUCTION. IT APPEARS THAT MOVING THE PILE LOCATION 13' TO THE SOUTH WILL CLEAR THE OBSTRUCTION. REPORTED THIS INFORMATION TO RANGER AND PBC FOR THEIR CONSIDERATION								
	GEORGE VALDES	4.50	HR	\$77.36	\$348.12	\$60.92	17.50%	\$409.04	
	SUPERVISOR'S TRUCK	4.50	HR	\$39.27	\$176.72	\$30.93	17.50%	\$207.64	
	HECTOR BENEGAS	4.50	HR	\$47.89	\$215.51	\$37.71	17.50%	\$253.22	
	FORMAN'S TRUCK	4.50	HR	\$32.93	\$148.19	\$25.93	17.50%	\$174.12	
	REGINALD WATSON	4.50	HR	\$73.68	\$331.56	\$58.02	17.50%	\$389.58	
	CRANE OPERATOR'S TRUCK	4.50	HR	\$32.93	\$148.19	\$25.93	17.50%	\$174.12	
	LUIS CAPADEVILA	4.50	HR	\$35.36	\$159.12	\$27.85	17.50%	\$186.97	
	YEISON MONZON	4.50	HR	\$36.84	\$165.78	\$29.01	17.50%	\$194.79	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.50	HR	\$454.27	\$2,044.22	\$357.74	17.50%	\$2,401.95	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	4.50	HR	\$21.12	\$95.04	\$16.63	17.50%	\$111.67	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	4.50	HR	\$18.31	\$82.40	\$14.42	17.50%	\$96.81	
	GENERATOR AND TORCH SET	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	4.50	HR	\$21.39	\$96.26	\$16.84	17.50%	\$113.10	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	4.50	HR	\$5.00	\$22.50	\$3.94	17.50%	\$26.44	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE

MONDAY, 8/28/23	JET PILES AT IB #3, DISCOVERED SAME SUBAQUEOUS OBSTRUCTION AT PILE #58. ADVISED RANGER AND PBC.								
	GEORGE VALDES	2.00	HR	\$77.36	\$154.72	\$27.08	17.50%	\$181.80	
	SUPERVISOR'S TRUCK	2.00	HR	\$39.27	\$78.54	\$13.74	17.50%	\$92.28	
	HECTOR BANEGAS	2.00	HR	\$47.89	\$95.78	\$16.78	17.50%	\$112.54	
	FORMAN'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	REGINALD WATSON	2.00	HR	\$73.68	\$147.36	\$25.79	17.50%	\$173.15	
	CRANE OPERATOR'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	LUIS CAPADEVILA	2.00	HR	\$35.36	\$70.72	\$12.38	17.50%	\$83.10	
	FELIX VAZQUEZ	2.00	HR	\$28.00	\$56.00	\$9.80	17.50%	\$65.80	
	JUAN MEDRANO	2.00	HR	\$36.84	\$73.68	\$12.89	17.50%	\$86.57	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	2.00	HR	\$454.27	\$908.54	\$158.99	17.50%	\$1,067.53	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	2.00	HR	\$21.12	\$42.24	\$7.39	17.50%	\$49.63	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	2.00	HR	\$18.31	\$36.62	\$6.41	17.50%	\$43.03	
	GENERATOR AND TORCH SET	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	2.00	HR	\$21.39	\$42.78	\$7.49	17.50%	\$50.27	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	2.00	HR	\$5.00	\$10.00	\$1.75	17.50%	\$11.75	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
TUESDAY, 8/29/23	ADJUST PILE TEMPLATE TO MOVE PILE LOCATIONS TO CLEAR UNDERGROUND OBSTRUCTION. ANZAC, RANGER, WGI AND PBC MET TO DISCUSS FPL OVERHEAD POWERLINE CONFLICT AND UNDERGROUND CONFLICT. IT WAS AGREED TO MOVE PILE TO THE NORTH OF THE UNDERGROUND OBSTRUCTION								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BANEGAS	4.00	HR	\$47.89	\$191.56	\$33.52	17.50%	\$225.08	
	FORMAN'S TRUCK	4.00	HR	\$32.93	\$131.72	\$23.05	17.50%	\$154.77	
	REGINALD WATSON	4.00	HR	\$73.68	\$294.72	\$51.58	17.50%	\$346.30	
	CRANE OPERATOR'S TRUCK	4.00	HR	\$32.93	\$131.72	\$23.05	17.50%	\$154.77	
	LUIS CAPADEVILA	4.00	HR	\$35.36	\$141.44	\$24.75	17.50%	\$168.19	
	FELIX VAZQUEZ	4.00	HR	\$28.00	\$112.00	\$19.60	17.50%	\$131.60	
	JUAN MEDRANO	4.00	HR	\$36.84	\$147.36	\$25.79	17.50%	\$173.15	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.00	HR	\$454.27	\$1,817.08	\$317.99	17.50%	\$2,135.07	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.00	HR	\$136.80	\$547.20	\$95.76	17.50%	\$642.96	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	4.00	HR	\$21.12	\$84.48	\$14.78	17.50%	\$99.26	
	2010 MILLER 400 AMP WELDER	4.00	HR	\$7.25	\$29.00	\$5.06	17.50%	\$34.06	IDLE RATE
	GENERATOR AND TORCH SET	4.00	HR	\$18.31	\$73.24	\$12.82	17.50%	\$86.06	
	GENERATOR AND TORCH SET	4.00	HR	\$7.32	\$29.28	\$5.12	17.50%	\$34.40	IDLE RATE
	MWI JET PUMP & HOSES	4.00	HR	\$21.39	\$85.56	\$14.97	17.50%	\$100.53	
	MWI JET PUMP & HOSES	4.00	HR	\$10.14	\$40.56	\$7.10	17.50%	\$47.66	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	4.00	HR	\$5.00	\$20.00	\$3.50	17.50%	\$23.50	
	STEEL WORK BARGE, 20' X 12'	4.00	HR	\$5.00	\$20.00	\$3.50	17.50%	\$23.50	IDLE RATE
THURSDAY, 8/31/23	REMOVED PILES #40 AND #58 FROM THE TEMPLATE. REWELD THE PILE POCKETS TO THE NORTH OF THE UNDERGROUND OBSTRUCTION TO CLEAR IT.								
	GEORGE VALDES	3.00	HR	\$77.36	\$232.08	\$40.61	17.50%	\$272.69	
	SUPERVISOR'S TRUCK	3.00	HR	\$39.27	\$117.81	\$20.62	17.50%	\$138.43	
	HECTOR BANEGAS	8.00	HR	\$47.89	\$383.12	\$67.05	17.50%	\$450.17	
	FORMAN'S TRUCK	8.00	HR	\$32.93	\$263.44	\$46.10	17.50%	\$309.54	
	REGINALD WATSON	8.00	HR	\$73.68	\$589.44	\$103.15	17.50%	\$692.59	
	CRANE OPERATOR'S TRUCK	8.00	HR	\$32.93	\$263.44	\$46.10	17.50%	\$309.54	
	LUIS CAPADEVILA	8.00	HR	\$35.36	\$282.88	\$49.50	17.50%	\$332.38	
	FELIX VAZQUEZ	8.00	HR	\$28.00	\$224.00	\$39.20	17.50%	\$263.20	
	JUAN MEDRANO	8.00	HR	\$36.84	\$294.72	\$51.58	17.50%	\$346.30	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$454.27	\$3,634.16	\$635.98	17.50%	\$4,270.14	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	8.00	HR	\$21.12	\$168.96	\$29.57	17.50%	\$198.53	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	8.00	HR	\$18.31	\$146.48	\$25.63	17.50%	\$172.11	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	8.00	HR	\$21.39	\$171.12	\$28.95	17.50%	\$201.07	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	8.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
FRIDAY, 9/1/23	RELOCATE PILES TO AVOID UNDERGROUND OBSTRUCTION								
	GEORGE VALDES	4.00	HR	\$77.36	\$309.44	\$54.15	17.50%	\$363.59	
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57	
	HECTOR BANEGAS	8.00	HR	\$47.89	\$383.12	\$67.05	17.50%	\$450.17	
	FORMAN'S TRUCK	8.00	HR	\$32.93	\$263.44	\$46.10	17.50%	\$309.54	

WEDNESDAY, 8/6/23	REGINALD WATSON	8.00	HR	\$73.68	\$589.44	\$103.15	17.50%	\$692.58
	CRANE OPERATOR'S TRUCK	8.00	HR	\$29.93	\$283.44	\$46.10	17.50%	\$309.54
	LUIS CAPADEVILA	8.00	HR	\$35.36	\$282.88	\$46.50	17.50%	\$332.38
	FELIX VAZQUEZ	8.00	HR	\$28.00	\$224.00	\$39.20	17.50%	\$263.20
	JUAN MEDRANO	8.00	HR	\$51.84	\$294.72	\$51.58	17.50%	\$346.30
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$484.27	\$3,634.16	\$635.98	17.50%	\$4,270.14
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.60	\$0.00	\$0.00	17.50%	\$0.00
	DELTA MAG D30-02	8.00	HR	\$25.08	\$200.48	\$35.08	17.50%	\$235.56
	2010 MILLER 400 AMP WELDER	8.00	HR	\$21.32	\$168.96	\$29.57	17.50%	\$188.53
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00
	GENERATOR AND TORCH SET	8.00	HR	\$18.31	\$146.48	\$23.63	17.50%	\$172.11
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00
	MW/JET PUMP & HOSES	8.00	HR	\$21.39	\$171.12	\$28.85	17.50%	\$201.07
	MW/JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00
	STEEL WORK BARGE, 20' X 12'	8.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00
	WAITING ON PLAN REVISIONS FOR B #2 AND B #3							
	WEDNESDAY, 8/6/23							
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00
THURSDAY, 8/7/23 - WED, 8/13/23	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00
	REGINALD WATSON	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00
	CRANE OPERATOR'S TRUCK	0.00	HR	\$22.93	\$0.00	\$0.00	17.50%	\$0.00
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00
	JUAN MEDRANO	0.00	HR	\$51.84	\$0.00	\$0.00	17.50%	\$0.00
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$484.27	\$0.00	\$0.00	17.50%	\$0.00
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	5.00	HR	\$136.60	\$684.00	\$118.70	17.50%	\$803.70
	DELTA MAG D30-02	0.00	HR	\$25.08	\$0.00	\$0.00	17.50%	\$0.00
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.32	\$0.00	\$0.00	17.50%	\$0.00
	2010 MILLER 400 AMP WELDER	5.00	HR	\$7.25	\$36.25	\$6.34	17.50%	\$42.59
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00
	GENERATOR AND TORCH SET	5.00	HR	\$7.32	\$36.60	\$6.41	17.50%	\$43.01
	MW/JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00
	MW/JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00
	STEEL WORK BARGE, 20' X 12'	5.00	HR	\$5.00	\$25.00	\$4.38	17.50%	\$29.38
	WAITING ON PLAN REVISIONS FOR B #2 AND B #3							
THURSDAY, 8/16/23	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00
	REGINALD WATSON	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00
	CRANE OPERATOR'S TRUCK	0.00	HR	\$22.93	\$0.00	\$0.00	17.50%	\$0.00
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00
	JUAN MEDRANO	0.00	HR	\$51.84	\$0.00	\$0.00	17.50%	\$0.00
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$484.27	\$0.00	\$0.00	17.50%	\$0.00
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	40.00	HR	\$136.60	\$5,472.00	\$957.60	17.50%	\$6,429.60
	DELTA MAG D30-02	0.00	HR	\$25.08	\$0.00	\$0.00	17.50%	\$0.00
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.32	\$0.00	\$0.00	17.50%	\$0.00
	2010 MILLER 400 AMP WELDER	40.00	HR	\$7.25	\$290.00	\$60.75	17.50%	\$350.75
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00
	GENERATOR AND TORCH SET	40.00	HR	\$7.32	\$292.80	\$51.24	17.50%	\$344.04
	MW/JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00
	MW/JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00
	STEEL WORK BARGE, 20' X 12'	40.00	HR	\$5.00	\$200.00	\$36.00	17.50%	\$236.00
	EXTRA WORK TO BUILD 1 DROP AT SOUTH END OF B #3 PER O.P. REQUIRED DUE TO MODIFIED PILE SPACING TO AVOID UNDERGROUND OBSTRUCTION.							
THURSDAY, 8/16/23	WEDNESDAY, 8/16/23							
	GEORGE VALDES	4.00	HR	\$77.36	\$309.44	\$54.15	17.50%	\$363.59
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57
	HECTOR BENEGAS	6.00	HR	\$47.89	\$287.34	\$50.28	17.50%	\$337.62
	FORMAN'S TRUCK	6.00	HR	\$32.93	\$197.58	\$34.58	17.50%	\$232.16
	LUIS CAPADEVILA	8.00	HR	\$51.84	\$252.88	\$49.50	17.50%	\$302.38
	FELIX VAZQUEZ	8.00	HR	\$28.00	\$224.00	\$39.20	17.50%	\$263.20
	JUAN MEDRANO	0.00	HR	\$51.84	\$0.00	\$0.00	17.50%	\$0.00
THURSDAY, 8/16/23	VINCENT BROWN	8.00	HR	\$29.47	\$235.76	\$41.26	17.50%	\$277.02
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.00	HR	\$484.27	\$1,937.08	\$317.99	17.50%	\$2,255.07

	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	4.00	HR	\$21.12	\$84.48	\$14.78	17.50%	\$99.26	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	4.00	HR	\$18.31	\$73.24	\$12.62	17.50%	\$86.06	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	4.00	HR	\$5.00	\$20.00	\$3.50	17.50%	\$23.50	IDLE RATE
MONDAY, 10/30/23	ENCOUNTERED UNFORESEEN UNDERGROUND OBSTRUCTION WHILE ATTEMPTING TO JET AN 18" PILE INTO THE TEMPLATE AT EB #1. REMOVED THE 18" PILE AND USE A STEEL BEAM AND VIBRO HAMMER ATTEMPTING TO CLEAR THE OBSTRUCTION. THIS METHOD WAS UNSUCCESSFUL.								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BENEGAS	2.00	HR	\$47.89	\$95.78	\$16.76	17.50%	\$112.54	
	FORMAN'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	JOSE LOPEZ, CRANE OPERATOR	2.00	HR	\$35.36	\$70.72	\$12.38	17.50%	\$83.10	
	LUIS CAPADEVILA	2.00	HR	\$35.36	\$70.72	\$12.38	17.50%	\$83.10	
	FELIX VAZQUEZ	2.00	HR	\$28.00	\$56.00	\$9.80	17.50%	\$65.80	
	JUAN MEDRANO	2.00	HR	\$36.84	\$73.68	\$12.89	17.50%	\$86.57	
	VINCENT BROWN	2.00	HR	\$29.47	\$58.94	\$10.31	17.50%	\$69.25	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	2.00	HR	\$454.27	\$908.54	\$158.99	17.50%	\$1,067.53	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	3.00	HR	\$97.15	\$291.45	\$51.00	17.50%	\$342.45	
	ICE MODEL 416L VIBRATORY PILE HAMMER	5.00	HR	\$29.84	\$149.20	\$26.11	17.50%	\$175.31	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	2.00	HR	\$21.12	\$42.24	\$7.39	17.50%	\$49.53	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	2.00	HR	\$18.31	\$36.62	\$6.41	17.50%	\$43.03	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	2.00	HR	\$21.39	\$42.78	\$7.49	17.50%	\$50.27	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	2.00	HR	\$5.00	\$10.00	\$1.75	17.50%	\$11.75	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
WEDNESDAY, 11/1/23	REMOVE PART OF PILE TEMPLATE TO ALLOW FOR EXCAVATING IN THE AREA OF THE UNDERGROUND OBSTRUCTION. ATTEMPT TO EXCAVATE AND REMOVE WHAT SEEMS TO BE THE EXISTING FORCE MAIN								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BENEGAS	8.00	HR	\$47.89	\$383.12	\$67.05	17.50%	\$450.17	
	FORMAN'S TRUCK	8.00	HR	\$32.93	\$263.44	\$46.10	17.50%	\$309.54	
	JOSE LOPEZ, CRANE OPERATOR	8.00	HR	\$53.05	\$424.40	\$74.27	17.50%	\$496.67	
	LUIS CAPADEVILA	8.00	HR	\$35.36	\$282.88	\$49.50	17.50%	\$332.38	
	FELIX VAZQUEZ	8.00	HR	\$28.00	\$224.00	\$39.20	17.50%	\$263.20	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	8.00	HR	\$29.47	\$235.76	\$41.26	17.50%	\$277.02	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$454.27	\$3,634.16	\$635.98	17.50%	\$4,270.14	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$29.84	\$238.72	\$41.78	17.50%	\$280.50	IDLE RATE
	2018 CAT 315 F EXCAVATOR	8.00	HR	\$105.55	\$852.40	\$149.17	17.50%	\$1,001.57	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	8.00	HR	\$21.12	\$168.96	\$29.57	17.50%	\$198.53	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	8.00	HR	\$18.31	\$146.48	\$25.63	17.50%	\$172.11	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	8.00	HR	\$10.14	\$81.12	\$14.20	17.50%	\$95.32	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	8.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
THURSDAY, 11/2/23	EXCAVATED AND EXPOSED PART OF EXISTING FORCE MAIN PIPE OBSTRUCTION. BROKE SOME OF THE PIPE & REMOVED A PORTION. USED STEEL PLATES TO RETAIN THE EXCAVATION BUT HIGH TIDE EVENTUALLY OVERWELMED TO AREA. WILL HAVE TO WAIT FOR LOW TIDE AND ATTEMPT REMOVAL AGAIN TOMORROW								
	GEORGE VALDES	4.00	HR	\$77.36	\$309.44	\$54.15	17.50%	\$363.59	
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57	
	HECTOR BENEGAS	4.00	HR	\$47.89	\$191.56	\$33.52	17.50%	\$225.08	
	FORMAN'S TRUCK	4.00	HR	\$32.93	\$131.72	\$23.05	17.50%	\$154.77	
	JOSE LOPEZ, CRANE OPERATOR	8.00	HR	\$53.05	\$424.40	\$74.27	17.50%	\$498.67	
	LUIS CAPADEVILA	4.00	HR	\$35.36	\$141.44	\$24.75	17.50%	\$166.19	
	FELIX VAZQUEZ	4.00	HR	\$28.00	\$112.00	\$18.60	17.50%	\$131.60	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	8.00	HR	\$29.47	\$235.76	\$41.26	17.50%	\$277.02	

	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.00	HR	\$454.27	\$1,817.08	\$317.99	17.50%	\$2,135.07	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.00	HR	\$136.80	\$547.20	\$95.76	17.50%	\$542.86	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$29.84	\$238.72	\$41.78	17.50%	\$280.50	IDLE RATE
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$106.55	\$426.20	\$74.58	17.50%	\$500.78	
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$34.97	\$139.88	\$24.46	17.50%	\$164.36	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	4.00	HR	\$21.12	\$84.48	\$14.78	17.50%	\$99.26	
	2010 MILLER 400 AMP WELDER	4.00	HR	\$7.25	\$29.00	\$5.08	17.50%	\$34.08	IDLE RATE
	GENERATOR AND TORCH SET	4.00	HR	\$18.31	\$73.24	\$12.82	17.50%	\$86.06	
	GENERATOR AND TORCH SET	4.00	HR	\$7.32	\$29.28	\$5.12	17.50%	\$34.40	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	8.00	HR	\$10.14	\$81.12	\$14.20	17.50%	\$95.32	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	4.00	HR	\$5.00	\$20.00	\$3.50	17.50%	\$23.50	
	STEEL WORK BARGE, 20' X 12'	4.00	HR	\$5.00	\$20.00	\$3.50	17.50%	\$23.50	IDLE RATE
FRIDAY, 11/3/23	EXCAVATED AND BROKE EXISTING (HEAVY WALL) FORCE MAIN. REMOVED PORTION TO CLEAR THE 18" PILE AT EB #1								
	GEORGE VALDES	8.50	HR	\$77.36	\$667.56	\$115.07	17.50%	\$772.63	
	SUPERVISOR'S TRUCK	8.50	HR	\$39.27	\$333.80	\$58.41	17.50%	\$392.21	
	HECTOR BENEGAS	8.50	HR	\$47.89	\$407.07	\$71.24	17.50%	\$478.30	
	FORMAN'S TRUCK	8.50	HR	\$32.93	\$279.91	\$48.98	17.50%	\$328.89	
	JOSE LOPEZ, CRANE OPERATOR	8.50	HR	\$53.05	\$450.93	\$78.91	17.50%	\$529.84	
	LUIS CAPADEVILA	8.50	HR	\$35.35	\$300.56	\$52.60	17.50%	\$353.16	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	8.50	HR	\$36.84	\$313.14	\$54.80	17.50%	\$367.94	
	VINCENT BROWN	8.50	HR	\$28.47	\$250.50	\$43.84	17.50%	\$294.33	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.50	HR	\$454.27	\$3,861.30	\$675.73	17.50%	\$4,537.02	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$29.84	\$238.72	\$41.78	17.50%	\$280.50	IDLE RATE
	2018 CAT 315 F EXCAVATOR	8.50	HR	\$106.55	\$905.68	\$158.49	17.50%	\$1,064.17	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	8.50	HR	\$21.12	\$179.52	\$31.42	17.50%	\$210.94	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	8.50	HR	\$18.31	\$155.64	\$27.24	17.50%	\$182.87	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	8.00	HR	\$10.14	\$81.12	\$14.20	17.50%	\$95.32	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	8.50	HR	\$5.00	\$42.50	\$7.44	17.50%	\$49.94	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
MONDAY, 11/6/23	REBUILT PILE TEMPLATE. STAND AND JET PILE #19. HIT AN UNFORSEEN OBSTRUCTION AT ~15' BELOW THE TEMPLATE WITH A 14" STEEL BEAM. ATTEMPTED TO CLEAR THE OBSTRUCTION.								
	GEORGE VALDES	8.50	HR	\$77.36	\$667.56	\$115.07	17.50%	\$772.63	
	SUPERVISOR'S TRUCK	8.50	HR	\$39.27	\$333.80	\$58.41	17.50%	\$392.21	
	HECTOR BENEGAS	8.50	HR	\$47.89	\$407.07	\$71.24	17.50%	\$478.30	
	FORMAN'S TRUCK	8.50	HR	\$32.93	\$279.91	\$48.98	17.50%	\$328.89	
	JOSE LOPEZ, CRANE OPERATOR	8.50	HR	\$53.05	\$450.93	\$78.91	17.50%	\$529.84	
	LUIS CAPADEVILA	8.50	HR	\$35.35	\$300.56	\$52.60	17.50%	\$353.16	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	8.50	HR	\$36.84	\$313.14	\$54.80	17.50%	\$367.94	
	VINCENT BROWN	8.50	HR	\$28.47	\$250.50	\$43.84	17.50%	\$294.33	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.50	HR	\$454.27	\$3,861.30	\$675.73	17.50%	\$4,537.02	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$29.84	\$238.72	\$41.78	17.50%	\$280.50	IDLE RATE
	2018 CAT 315 F EXCAVATOR	8.50	HR	\$106.55	\$905.68	\$158.49	17.50%	\$1,064.17	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	8.50	HR	\$21.12	\$179.52	\$31.42	17.50%	\$210.94	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	8.50	HR	\$18.31	\$155.64	\$27.24	17.50%	\$182.87	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	8.00	HR	\$10.14	\$81.12	\$14.20	17.50%	\$95.32	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	8.50	HR	\$5.00	\$42.50	\$7.44	17.50%	\$49.94	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
TUESDAY, 11/7/23	ATTEMPTED TO STAND AND JET PILE #20 BUT HITTING AN UNKNOWN UNDERGROUND OBSTRUCTION ~18' BELOW THE TEMPLATE. REMOVED THE 18" PILE AND USED A STEEL BEAM AND VIBRO HAMMER ATTEMPTING TO CLEAR THE OBSTRUCTION. NO SUCCESS.								
	GEORGE VALDES	8.00	HR	\$77.36	\$618.88	\$108.30	17.50%	\$727.16	
	SUPERVISOR'S TRUCK	8.00	HR	\$39.27	\$314.16	\$54.96	17.50%	\$369.14	

	HECTOR BENEGAS	8.00	HR	\$47.89	\$389.12	\$67.05	17.50%	\$450.17	
	FORMAN'S TRUCK	8.00	HR	\$32.93	\$263.44	\$46.10	17.50%	\$309.54	
	JOSE LOPEZ, CRANE OPERATOR	8.00	HR	\$53.05	\$424.40	\$74.27	17.50%	\$498.67	
	LUIS CAPADEVILA	8.00	HR	\$35.36	\$282.88	\$49.50	17.50%	\$332.38	
	FELIX VAZQUEZ	8.00	HR	\$28.00	\$224.00	\$39.20	17.50%	\$263.20	
	JUAN MEDRANO	8.00	HR	\$36.84	\$294.72	\$51.58	17.50%	\$346.30	
	VINCENT BROWN	8.00	HR	\$29.47	\$235.76	\$41.26	17.50%	\$277.02	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$454.27	\$3,634.16	\$635.98	17.50%	\$4,270.14	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.60	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$97.15	\$777.20	\$136.01	17.50%	\$913.21	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$28.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	8.00	HR	\$106.55	\$852.40	\$149.17	17.50%	\$1,001.57	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	8.00	HR	\$21.12	\$168.96	\$29.57	17.50%	\$198.53	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	8.00	HR	\$18.31	\$146.48	\$25.63	17.50%	\$172.11	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	4.00	HR	\$21.39	\$85.56	\$14.97	17.50%	\$100.53	
	MWI JET PUMP & HOSES	4.00	HR	\$10.14	\$40.56	\$7.10	17.50%	\$47.66	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	6.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
WEDNESDAY, 11/8/23	STAND AND VIBRATE 14" STEEL BEAM AT PILE #20 ATTEMPTING TO BREAK AND CLEAR OBSTRUCTION. STAND AND JET PILE #20 AGAIN BUT IT WILL NOT GO DOWN, STILL HITTING OBSTRUCTION. RECONFIGURE TEMPLATE TO RECEIVE AN AUGER. LOAD AUGER AT ANOTHER PROJECT SITE IN SOUTH BAY, FL AND DELIVER TO THIS SITE. WILL ATTEMPT TO DRILL THRU THE OBSTRUCTION TOMORROW.								
	GEORGE VALDES	8.00	HR	\$77.36	\$618.88	\$108.30	17.50%	\$727.16	
	SUPERVISOR'S TRUCK	8.00	HR	\$39.27	\$314.16	\$54.98	17.50%	\$369.14	
	HECTOR BENEGAS	8.00	HR	\$47.89	\$389.12	\$67.05	17.50%	\$450.17	
	FORMAN'S TRUCK	8.00	HR	\$32.93	\$263.44	\$46.10	17.50%	\$309.54	
	JOSE LOPEZ, CRANE OPERATOR	8.00	HR	\$53.05	\$424.40	\$74.27	17.50%	\$498.67	
	LUIS CAPADEVILA	8.00	HR	\$35.36	\$282.88	\$49.50	17.50%	\$332.38	
	FELIX VAZQUEZ	8.00	HR	\$28.00	\$224.00	\$39.20	17.50%	\$263.20	
	JUAN MEDRANO	8.00	HR	\$36.84	\$294.72	\$51.58	17.50%	\$346.30	
	VINCENT BROWN	8.00	HR	\$29.47	\$235.76	\$41.26	17.50%	\$277.02	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$454.27	\$3,634.16	\$635.98	17.50%	\$4,270.14	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.60	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$97.15	\$777.20	\$136.01	17.50%	\$913.21	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$28.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 3060 TOP DRIVE AUGER	0.00	HR	\$113.82	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 3060 TOP DRIVE AUGER	8.00	HR	\$36.27	\$306.16	\$53.58	17.50%	\$359.74	IDLE RATE
	2018 CAT 315 F EXCAVATOR	8.00	HR	\$106.55	\$852.40	\$149.17	17.50%	\$1,001.57	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	8.00	HR	\$21.12	\$168.96	\$29.57	17.50%	\$198.53	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	8.00	HR	\$18.31	\$146.48	\$25.63	17.50%	\$172.11	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	4.00	HR	\$21.39	\$85.56	\$14.97	17.50%	\$100.53	
	MWI JET PUMP & HOSES	4.00	HR	\$10.14	\$40.56	\$7.10	17.50%	\$47.66	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	6.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	11.00	HR	\$125.00	\$1,375.00	\$240.63	17.50%	\$1,615.63	
THURSDAY, 11/9/23	ATTEMPTED TO DRILL AND CLEAR OBSTRUCTION. WORKED IN THE RAIN. NO SUCCESS.								
	GEORGE VALDES	4.00	HR	\$77.36	\$309.44	\$54.15	17.50%	\$363.59	
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57	
	HECTOR BENEGAS	4.00	HR	\$47.89	\$191.56	\$33.52	17.50%	\$225.08	
	FORMAN'S TRUCK	4.00	HR	\$32.93	\$131.72	\$23.05	17.50%	\$154.77	
	JOSE LOPEZ, CRANE OPERATOR	4.00	HR	\$53.05	\$212.20	\$37.14	17.50%	\$249.34	
	LUIS CAPADEVILA	4.00	HR	\$35.36	\$141.44	\$24.75	17.50%	\$166.19	
	FELIX VAZQUEZ	4.00	HR	\$28.00	\$112.00	\$19.60	17.50%	\$131.60	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	4.00	HR	\$29.47	\$117.88	\$20.63	17.50%	\$138.51	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.00	HR	\$454.27	\$1,617.08	\$317.99	17.50%	\$2,135.07	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.00	HR	\$136.60	\$547.20	\$95.76	17.50%	\$642.96	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$28.84	\$238.72	\$41.78	17.50%	\$280.50	IDLE RATE
	ICE MODEL 3060 TOP DRIVE AUGER	4.00	HR	\$113.82	\$455.28	\$79.67	17.50%	\$534.95	
	ICE MODEL 3060 TOP DRIVE AUGER	4.00	HR	\$36.27	\$153.08	\$26.79	17.50%	\$179.87	IDLE RATE
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$106.55	\$426.20	\$74.59	17.50%	\$500.79	
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$34.97	\$139.88	\$24.48	17.50%	\$164.36	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	4.00	HR	\$21.12	\$84.48	\$14.78	17.50%	\$99.26	

	2010 MILLER 400 AMP WELDER	4.00	HR	\$7.25	\$28.00	\$5.08	17.50%	\$34.08	IDLE RATE
	GENERATOR AND TORCH SET	4.00	HR	\$18.31	\$73.24	\$12.82	17.50%	\$86.06	
	GENERATOR AND TORCH SET	4.00	HR	\$7.32	\$28.28	\$5.12	17.50%	\$34.40	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	8.00	HR	\$10.14	\$81.12	\$14.20	17.50%	\$95.32	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	4.00	HR	\$5.00	\$20.00	\$3.50	17.50%	\$23.50	
	STEEL WORK BARGE, 20' X 12'	4.00	HR	\$5.00	\$20.00	\$3.50	17.50%	\$23.50	IDLE RATE
FRIDAY, 11/10/23	ATTEMPTED TO DRILL AND CLEAR OBSTRUCTION AT PILE #20. EVENTUALLY DRILLED TO ~30 FEET DOWN FROM TEMPLATE. STOOD PILE #20 AND JETTED IT DOWN TO ~30' BELOW TEMPLATE. SCHEDULED TO DRIVE IT WITH PILE HAMMER ON MONDAY.								
	GEORGE VALDES	4.00	HR	\$77.36	\$309.44	\$54.15	17.50%	\$363.59	
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57	
	HECTOR BENEGAS	8.50	HR	\$47.89	\$407.07	\$71.24	17.50%	\$478.30	
	FORMAN'S TRUCK	8.50	HR	\$32.93	\$279.91	\$48.98	17.50%	\$328.89	
	JOSE LOPEZ, CRANE OPERATOR	8.50	HR	\$53.05	\$450.93	\$78.91	17.50%	\$529.84	
	LUIS CAPEDEVILA	8.50	HR	\$35.36	\$300.56	\$52.60	17.50%	\$353.16	
	FELIX VAZQUEZ	8.50	HR	\$28.00	\$238.00	\$41.65	17.50%	\$279.65	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	8.50	HR	\$28.47	\$250.50	\$43.84	17.50%	\$294.33	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.50	HR	\$454.27	\$3,861.30	\$675.73	17.50%	\$4,537.02	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$29.84	\$238.72	\$41.78	17.50%	\$280.50	IDLE RATE
	ICE MODEL 3060 TOP DRIVE AUGER	4.00	HR	\$113.82	\$455.28	\$79.67	17.50%	\$534.95	
	ICE MODEL 3060 TOP DRIVE AUGER	4.00	HR	\$38.27	\$153.08	\$26.79	17.50%	\$179.87	IDLE RATE
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$106.55	\$426.20	\$74.59	17.50%	\$500.79	
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$34.97	\$139.88	\$24.48	17.50%	\$164.36	IDLE RATE
	DELMAG D30-02	8.00	HR	\$25.06	\$200.48	\$35.08	17.50%	\$235.56	IDLE RATE
	2010 MILLER 400 AMP WELDER	8.50	HR	\$21.12	\$179.52	\$31.42	17.50%	\$210.94	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	8.50	HR	\$18.31	\$155.64	\$27.24	17.50%	\$182.87	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	4.00	HR	\$21.39	\$85.56	\$14.97	17.50%	\$100.53	
	MWI JET PUMP & HOSES	4.00	HR	\$10.14	\$40.56	\$7.10	17.50%	\$47.66	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	8.50	HR	\$5.00	\$42.50	\$7.44	17.50%	\$49.94	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
MONDAY, 11/13/23	BRING TRACTOR AND EMPTY TRAILER FROM ANZAC'S HOMESTEAD YARD. LOAD AUGER AND MOVE IT OUT OF THE WAY. THEN BRIDGE TRAILER LOADED WITH DELMAG PILE HAMMER FROM EAST SIDE TO WEST SIDE. UNLOAD AND RIG HAMMER. DRIVE PILE #20								
	GEORGE VALDES	4.00	HR	\$77.36	\$309.44	\$54.15	17.50%	\$363.59	
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57	
	HECTOR BENEGAS	7.00	HR	\$47.89	\$335.23	\$58.67	17.50%	\$393.90	
	FORMAN'S TRUCK	7.00	HR	\$32.93	\$230.51	\$40.34	17.50%	\$270.85	
	JOSE LOPEZ, CRANE OPERATOR	7.00	HR	\$53.05	\$371.35	\$64.99	17.50%	\$436.34	
	LUIS CAPEDEVILA	7.00	HR	\$35.36	\$247.52	\$43.32	17.50%	\$290.84	
	FELIX VAZQUEZ	7.00	HR	\$28.00	\$196.00	\$34.30	17.50%	\$230.30	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	7.00	HR	\$29.47	\$206.29	\$36.10	17.50%	\$242.39	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	7.00	HR	\$454.27	\$3,179.89	\$556.48	17.50%	\$3,736.37	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	8.00	HR	\$29.84	\$238.72	\$41.78	17.50%	\$280.50	IDLE RATE
	ICE MODEL 3060 TOP DRIVE AUGER	0.00	HR	\$113.82	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 3060 TOP DRIVE AUGER	8.00	HR	\$38.27	\$306.16	\$53.58	17.50%	\$359.74	IDLE RATE
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$106.55	\$426.20	\$74.59	17.50%	\$500.79	
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$34.97	\$139.88	\$24.48	17.50%	\$164.36	IDLE RATE
	DELMAG D30-02	7.00	HR	\$25.06	\$175.42	\$30.70	17.50%	\$206.12	IDLE RATE
	2010 MILLER 400 AMP WELDER	7.00	HR	\$21.12	\$147.84	\$25.87	17.50%	\$173.71	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	7.00	HR	\$18.31	\$128.17	\$22.43	17.50%	\$150.60	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	8.00	HR	\$10.14	\$81.12	\$14.20	17.50%	\$95.32	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	7.00	HR	\$5.00	\$35.00	\$6.13	17.50%	\$41.13	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	11.00	HR	\$125.00	\$1,375.00	\$240.63	17.50%	\$1,615.63	
FRIDAY, 12/15/23	LAYOUT, CUT, CREATE KEYWAYS AND EPOXY PERCAST WALL PANEL TO ALLOW FOR REVISED PILE SPACINGS								
	GEORGE VALDES	1.00	HR	\$77.36	\$77.36	\$13.54	17.50%	\$90.90	
	SUPERVISOR'S TRUCK	1.00	HR	\$39.27	\$39.27	\$6.87	17.50%	\$46.14	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	4.00	HR	\$47.89	\$191.56	\$33.52	17.50%	\$225.08	
	FORMAN'S TRUCK	4.00	HR	\$32.93	\$131.72	\$23.05	17.50%	\$154.77	

	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	4.00	HR	\$28.00	\$112.00	\$19.60	17.50%	\$131.60	
	JUAN MEDRANO	4.00	HR	\$36.84	\$147.36	\$25.79	17.50%	\$173.15	
	JEAN DUVAL	4.00	HR	\$39.78	\$159.12	\$27.85	17.50%	\$168.97	
	FORMAN'S TRUCK	4.00	HR	\$32.93	\$131.72	\$23.05	17.50%	\$154.77	
	VINCENT BROWN	4.00	HR	\$29.47	\$117.88	\$20.63	17.50%	\$138.51	
	LEONARDO NUNEZ	4.00	HR	\$30.94	\$123.76	\$21.66	17.50%	\$145.42	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.13	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$106.55	\$426.20	\$74.59	17.50%	\$500.79	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	
MONDAY, 1/29/23	HIT AN UNFORSEEN UNDERGROUND OBSTRUCTION AT EB #4 WHILE ATTEMPTING TO JET 18" PILE IN PLACE								
	GEORGE VALDES	2.00	HR	\$77.36	\$154.72	\$27.08	17.50%	\$181.80	
	SUPERVISOR'S TRUCK	2.00	HR	\$39.27	\$78.54	\$13.74	17.50%	\$92.28	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	2.00	HR	\$28.00	\$56.00	\$9.80	17.50%	\$65.80	
	JUAN MEDRANO	2.00	HR	\$36.84	\$73.68	\$12.69	17.50%	\$86.57	
	JEAN DUVAL	2.00	HR	\$39.78	\$79.56	\$13.92	17.50%	\$93.48	
	FORMAN'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	2.00	HR	\$30.94	\$61.88	\$10.83	17.50%	\$72.71	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	2.00	HR	\$454.27	\$908.54	\$158.99	17.50%	\$1,067.53	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.13	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	2.00	HR	\$21.39	\$42.78	\$7.49	17.50%	\$50.27	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	2.00	HR	\$5.00	\$10.00	\$1.75	17.50%	\$11.75	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	
WEDNESDAY, 1/31/23	CUT 14" PILE TO 22.5' TO USE AT EB #4 SE WING WALL UNDER FPL OVERHEAD LINES. ADJUSTED PILE TEMPLATE TO THE NORTH ATTEMPTING TO CLEAR OBSTRUCTION. MOBILIZED VIBRO HAMMER TO SITE. USE VIBRO HAMMER AND STEEL BEAM TO CLEAR UNDERGROUND OBSTRUCTION. USED JET AFTER STEEL BEAM TO SEE IF ARE WAS CLEAR FOR PLACING THE 18" PILE. SEEMS TO BE CLEAR. WILL STAND AND JET THE 18" PILE TOMORROW MORNING								
	GEORGE VALDES	8.00	HR	\$77.36	\$618.88	\$108.30	17.50%	\$727.18	
	SUPERVISOR'S TRUCK	8.00	HR	\$39.27	\$314.16	\$54.98	17.50%	\$369.14	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	8.00	HR	\$47.89	\$383.12	\$67.05	17.50%	\$450.17	
	FORMAN'S TRUCK	8.00	HR	\$32.93	\$263.44	\$46.10	17.50%	\$309.54	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	

	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	8.00	HR	\$28.00	\$224.00	\$39.20	17.50%	\$263.20	
	JUAN MEDRANO	8.00	HR	\$36.84	\$294.72	\$51.58	17.50%	\$346.30	
	JEAN DUVAL	8.00	HR	\$39.78	\$318.24	\$55.69	17.50%	\$373.93	
	FORMAN'S TRUCK	8.00	HR	\$32.93	\$263.44	\$45.10	17.50%	\$309.54	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	8.00	HR	\$30.94	\$247.52	\$43.32	17.50%	\$290.84	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$454.27	\$3,634.16	\$835.98	17.50%	\$4,270.14	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.13	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	4.00	HR	\$97.15	\$388.60	\$68.01	17.50%	\$456.61	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	8.00	HR	\$34.97	\$279.76	\$48.96	17.50%	\$328.72	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	8.00	HR	\$21.12	\$168.96	\$29.57	17.50%	\$198.53	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	8.00	HR	\$18.31	\$146.48	\$25.63	17.50%	\$172.11	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	8.00	HR	\$21.39	\$171.12	\$29.95	17.50%	\$201.07	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	8.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	
	FERGUSON - CONCRETE SAW BLADE & ITEMS TO CUT 14" PILES	1.00	LS	\$314.97	\$314.97	\$55.12	17.50%	\$370.09	
WEDNESDAY, 2/14/23	CUT PRECAST WALL PANELS, MAKE NEW KEYWAYS TO FIT REVISED PILE SPACINGS AT EB #4								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	8.00	HR	\$73.68	\$589.44	\$103.15	17.50%	\$692.59	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	8.00	HR	\$36.84	\$294.72	\$51.58	17.50%	\$346.30	
	JEAN DUVAL	8.00	HR	\$39.78	\$318.24	\$55.69	17.50%	\$373.93	
	FORMAN'S TRUCK	8.00	HR	\$32.93	\$263.44	\$45.10	17.50%	\$309.54	
	VINCENT BROWN	8.00	HR	\$29.47	\$235.76	\$41.26	17.50%	\$277.02	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	DARWIN BLACKETT	8.00	HR	\$30.94	\$247.52	\$43.32	17.50%	\$290.84	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	8.00	HR	\$477.13	\$3,817.04	\$667.98	17.50%	\$4,485.02	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	8.00	HR	\$106.55	\$852.40	\$149.17	17.50%	\$1,001.57	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	8.00	HR	\$7.25	\$58.00	\$10.15	17.50%	\$68.15	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	8.00	HR	\$7.32	\$58.56	\$10.25	17.50%	\$68.81	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	8.00	HR	\$10.14	\$81.12	\$14.20	17.50%	\$95.32	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	8.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	
	WHITE CAP - CONCRETE SAW BLADE TO CUT PRECAST PANELS	1.00	LS	\$160.50	\$160.50	\$28.09	17.50%	\$188.59	
	WHITE CAP - EPOXY TO SEAL CUTS IN PRECAST PANELS	1.00	LS	\$170.30	\$170.30	\$29.80	17.50%	\$200.10	
MONDAY, 2/19/23	HIT AN UNFORSEEN UNDERGROUND OBSTRUCTION AT EB #4 WHILE ATTEMPTING TO JET PRECAST WALL PANEL IN PLACE AT ~11' BELOW GRADE. REMOVED WALL PANEL AND ATTEMPTED TO EXCAVATE TO REMOVE OBSTRUCTION. NO SUCCESS.								
	GEORGE VALDES	6.00	HR	\$77.36	\$464.16	\$81.23	17.50%	\$545.39	
	SUPERVISOR'S TRUCK	6.00	HR	\$39.27	\$235.62	\$41.23	17.50%	\$276.85	
	HECTOR BENEGAS	6.00	HR	\$47.89	\$287.34	\$50.28	17.50%	\$337.62	
	FORMAN'S TRUCK	6.00	HR	\$32.93	\$197.58	\$34.58	17.50%	\$232.16	
	CARLOS MACHIAVELLO	6.00	HR	\$47.89	\$287.34	\$50.28	17.50%	\$337.62	

	FORMAN'S TRUCK	6.00	HR	\$32.93	\$197.58	\$34.58	17.50%	\$232.16	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	8.00	HR	\$35.36	\$212.16	\$37.13	17.50%	\$249.29	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	6.00	HR	\$36.84	\$221.04	\$38.68	17.50%	\$259.72	
	JEAN DUVAL	0.00	HR	\$39.78	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	DARWIN BLACKETT	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	6.00	HR	\$454.27	\$2,725.62	\$476.98	17.50%	\$3,202.60	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.13	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	6.00	HR	\$106.55	\$639.30	\$111.88	17.50%	\$751.18	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	6.00	HR	\$7.25	\$43.50	\$7.61	17.50%	\$51.11	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	6.00	HR	\$7.32	\$43.92	\$7.69	17.50%	\$51.61	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	6.00	HR	\$10.14	\$60.84	\$10.65	17.50%	\$71.49	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	6.00	HR	\$5.00	\$30.00	\$5.25	17.50%	\$35.25	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	
TUESDAY, 2/20/23 - THURSDAY, 2/22/24	WAITING FOR DIRECTION ON HOW TO PROCEED, CUT PANEL, ETC?								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	JEAN DUVAL	0.00	HR	\$39.78	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	DARWIN BLACKETT	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	24.00	HR	\$136.80	\$3,283.20	\$974.56	17.50%	\$3,857.76	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.13	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	24.00	HR	\$34.97	\$839.28	\$146.67	17.50%	\$996.15	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	24.00	HR	\$7.25	\$174.00	\$30.45	17.50%	\$204.45	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	24.00	HR	\$7.32	\$175.68	\$30.74	17.50%	\$206.42	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	24.00	HR	\$10.14	\$243.36	\$42.59	17.50%	\$285.95	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	24.00	HR	\$5.00	\$120.00	\$21.00	17.50%	\$141.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	
FRIDAY, 2/23/24	MADE ANOTHER ATTEMPT TO EXCAVATE AND REMOVE UNKNOWN OBSTRUCTION. NO SUCCESS.								
	GEORGE VALDES	4.00	HR	\$77.36	\$309.44	\$54.15	17.50%	\$363.59	
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	

	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	JEAN DUVAL	0.00	HR	\$36.78	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	4.00	HR	\$29.47	\$117.88	\$20.63	17.50%	\$138.51	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	DARWIN BLACKETT	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.13	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$106.55	\$426.20	\$74.59	17.50%	\$500.79	
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$34.97	\$139.88	\$24.48	17.50%	\$164.36	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	8.00	HR	\$7.25	\$58.00	\$10.15	17.50%	\$68.15	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	8.00	HR	\$7.32	\$58.56	\$10.25	17.50%	\$68.81	IDLE RATE
	MWJ JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWJ JET PUMP & HOSES	8.00	HR	\$10.14	\$81.12	\$14.20	17.50%	\$95.32	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	8.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
MONDAY, 2/27/24	ATTEMPT TO EXCAVATE AND REMOVE UNKNOWN OBSTRUCTION WITH STEEL PLATES AND PUMP. NO SUCCESS. RECEIVED VERBAL APPROVAL FROM WGI - 3PM THAT WE CAN CUT THE PANEL TO ALLOW INSTALLATION								
	GEORGE VALDES	4.00	HR	\$77.36	\$309.44	\$54.15	17.50%	\$383.59	
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	8.00	HR	\$36.84	\$294.72	\$51.58	17.50%	\$346.30	
	JEAN DUVAL	0.00	HR	\$36.78	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	8.00	HR	\$29.47	\$235.76	\$41.26	17.50%	\$277.02	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	DARWIN BLACKETT	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.13	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$106.55	\$426.20	\$74.59	17.50%	\$500.79	
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$34.97	\$139.88	\$24.48	17.50%	\$164.36	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	8.00	HR	\$7.25	\$58.00	\$10.15	17.50%	\$68.15	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	8.00	HR	\$7.32	\$58.56	\$10.25	17.50%	\$68.81	IDLE RATE
	MWJ JET PUMP & HOSES	4.00	HR	\$21.39	\$85.56	\$14.97	17.50%	\$100.53	
	MWJ JET PUMP & HOSES	4.00	HR	\$10.14	\$40.56	\$7.10	17.50%	\$47.66	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	8.00	HR	\$5.00	\$40.00	\$7.00	17.50%	\$47.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	
WEDNESDAY, 2/28/24	CUT PANEL TO ALLOW INSTALLATION AT OBSTRUCTION AND INSTALL IT								
	GEORGE VALDES	8.50	HR	\$77.36	\$657.56	\$115.07	17.50%	\$772.63	

	SUPERVISOR'S TRUCK	8.50	HR	\$39.27	\$333.80	\$58.41	17.50%	\$392.21	
	HECTOR BENEGAS	6.50	HR	\$47.89	\$311.29	\$54.47	17.50%	\$355.78	
	FORMAN'S TRUCK	6.50	HR	\$32.93	\$214.05	\$37.46	17.50%	\$251.60	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	8.50	HR	\$36.84	\$313.14	\$54.80	17.50%	\$367.94	
	JEAN DUVAL	0.00	HR	\$39.78	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	8.50	HR	\$30.94	\$262.99	\$46.02	17.50%	\$309.01	
	DARWIN BLACKETT	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.19	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	8.50	HR	\$115.63	\$982.66	\$172.00	17.50%	\$1,154.65	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	8.50	HR	\$106.55	\$905.68	\$158.49	17.50%	\$1,064.17	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	8.00	HR	\$7.25	\$58.00	\$10.15	17.50%	\$68.15	IDLE RATE
	GENERATOR AND TORCH SET	8.50	HR	\$18.31	\$155.64	\$27.24	17.50%	\$182.87	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	8.50	HR	\$21.39	\$181.82	\$31.82	17.50%	\$213.63	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	8.50	HR	\$5.00	\$42.50	\$7.44	17.50%	\$49.94	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	
MONDAY, 4/1/24	EXCAVATE ALONG LANDSIDE OF PRECAST WALL PANEL THAT WAS CUT TO CLEAR THE UNFORESSEEN UNDERGROUND OBSTRUCTION AT EB #4. RECEIVE AND PLACE EXCAVATABLE FLOWABLE FILL AS DIRECTED BY P&C								
	GEORGE VALDES	4.00	HR	\$77.35	\$309.44	\$54.15	17.50%	\$363.59	
	SUPERVISOR'S TRUCK	4.00	HR	\$39.27	\$157.08	\$27.49	17.50%	\$184.57	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	JEAN DUVAL	4.00	HR	\$39.78	\$159.12	\$27.85	17.50%	\$186.97	
	FORMAN'S TRUCK	4.00	HR	\$32.93	\$131.72	\$23.05	17.50%	\$154.77	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	DARWIN BLACKETT	4.00	HR	\$30.94	\$123.75	\$21.68	17.50%	\$145.42	
	ALFORD MCKENZIE	4.00	HR	\$38.31	\$153.24	\$26.82	17.50%	\$180.08	
	MONTRELL LEATHERWOOD	4.00	HR	\$26.62	\$106.08	\$18.56	17.50%	\$124.64	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$136.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.19	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	4.00	HR	\$106.55	\$426.20	\$74.59	17.50%	\$500.79	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE

	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	\$0.00	17.50%	\$0.00	
	STERLING TRACTOR AND DUMP TRAILER (2 LOADS)	8.00	HR	\$125.00	\$1,000.00	\$175.00	\$1,175.00	17.50%	\$1,175.00	DISPOSE OF CONC CUT OFFS & PILES
	TITAN CONCRETE - FLOWABLE FILL	1.00	LS	\$816.34	\$816.34	\$142.69	\$658.02	17.50%	\$658.02	
TOTAL	*WAGE RATES INCLUDE 47.35% BURDEN*				\$156,736.22	\$27,428.84			\$184,165.06	

INVOICE

WHITE CAP®

White Cap, L.P.
PO Box 4944
Orlando, FL 32802-4944

BRANCH ADDRESS
236 - POMPANO BEACH (002C)
(954) 979-3030
2007 N.W. 15TH AVENUE
POMPANO BEACH FL 33069
BROWARD

INVOICE NUMBER
10019371595
INVOICE DATE
01/22/2024
CUSTOMER PO NUMBER
157CM2201

TO VIEW AND PAY ONLINE GO TO:
<http://whitecap.billtrust.com>
ENROLLMENT TOKEN:
DSP ZDX VQQ

TERRITORY:
SHIP TO: 10003231275

MAKE CHECKS PAYABLE TO:

White Cap, L.P.
P.O. Box 4852
ORLANDO, FL 32802-4852

SOLD TO: 148363000

ANZAC CONTRACTORS INC
7475 SW 50TH TERRACE
MIAMI FL 33155

PALMETTO PARK ROAD EL RIO CANAL #157
PALMETTO PARK ROAD& EL RIO CANAL
BOCA RATON FL 33432

ORDER DATE		ORDER NO.		ACCOUNT MANAGER		TAKEN BY													
01/22/2024		57259642		BURTON, DAVID R		DEPAUL, PEYTON													
BRANCH		ACCT JOB NO.		TERMS		SHIP VIA / ROUTING													
236		10003231275		NET 30 DAYS		5. WALK IN													
LINE		PART NUMBER		DESCRIPTION		QTY ORD		UNIT PRICE		QTY BKO		QTY SHP		EXTENDED PRICE		TAX AMT			
1		15141650		50LB 16D BRIGHT COMMON NAIL		1		86.09 BOX		0		1		86.09		6.03			
2		15151650		50LB 16D DUPLEX NAIL SOLD/BOX		2		72.79 BOX		0		2		145.58		10.19			
3		579A221N		22OZ ULTRABOND 1 SBS CARTRIDGE EPOXY		4 12 X		39.79 EA		0		12		477.48		33.42			
				GEL ADHESIVE FOR ANCHORING AND DOWELING W/NOZZLE VDOT LIST 29 ATC															
4		11334BNK		3/4" BANAK WOOD CHAMFER		2000		0.1791 FT		0		2000		358.20		25.07			
5		1514DBF05		5LB 4D BRIGHT FINISH NAIL		1		33.29 BOX		0		1		33.29		2.33			
6		444BR12610		55GAL TRASH BAG 20/BOX		1		38.49 EA		0		1		38.49		2.69			
<div>USED 4 UNITS OF EPOXY TO SEAL CUTS IN PRECAST WALL PIERCES. (EXTRA)</div>																<div>TAX \$159.16 11.14 \$170.30</div>			
<div>The White Cap Family of Brands includes All-Tex Waterproofing Solutions, Hammac, Kenseal, Marvel Building & Masonry Supply, MASONPRO, Williams Equipment & Supply, Valley Supply Co, and Diamond Tool. Learn more at About.WhiteCap.com</div> <div>Pay your invoices online by visiting: https://whitecap.billtrust.com</div> <div>Sales Tax Exemption Questions or Certificates: TaxExemptCredit@whitecap.com</div> <div>THESE ITEMS ARE CONTROLLED BY THE U.S. GOVERNMENT AND AUTHORIZED FOR EXPORT ONLY TO THE COUNTRY OF ULTIMATE DESTINATION FOR USE BY THE ULTIMATE CONSIGNEE OR END-USER(S) HEREIN IDENTIFIED. THEY MAY NOT BE RESOLD, TRANSFERRED OR OTHERWISE DISPOSED OF TO ANY OTHER COUNTRY OR ANY PERSON OTHER THAN THE AUTHORIZED ULTIMATE CONSIGNEE OR END-USER(S), EITHER IN THEIR ORIGINAL FORM OR AFTER BEING INCORPORATED INTO OTHER ITEMS, WITHOUT FIRST OBTAINING APPROVAL FROM THE U.S. GOVERNMENT OR AS OTHERWISE AUTHORIZED BY U.S. LAW AND REGULATIONS.</div>																			
For questions regarding this invoice please call 1-866-857-0295.												TOTAL GROSS		1,139.13					
NO REFUNDS OR EXCHANGES ON NON STOCK MERCHANDISE Visit https://www.whitecap.com/terms/terms-conditions-of-sale-terms to view complete terms and conditions.												TOTAL TAX		79.73					
												TOTAL SHIPPING AND HANDLING		0.00					
RECEIVED BY:												SIGNATURE COPY ON FILE		TOTAL INVOICE		1,218.86			

FERGUSON
WATERWORKS
1950 NW 18TH STREET
POMPANO BEACH, FL 33069-1394

Please contact with Questions: 954-973-8100

ANZAC CONTRACTORS INC
7475 SW 50TH TERRACE
MIAMI, FL 33155

EXHIBIT "A" (Page 2 of 2)

INVOICE NUMBER	TOTAL DUE	CUSTOMER	PAGE
1261037	\$314.97	64801	1 of 1


PLEASE REFER TO INVOICE NUMBER WHEN
MAKING PAYMENT AND REMIT TO:

FEL-POMPANO BEACH, FL WW #125
PO BOX 100286
ATLANTA, GA 30384-0286

MASTER ACCOUNT NUMBER: 971888

SHIP TO:

COUNTER PICK UP
1950 NW 18TH STREET
POMPANO BEACH, FL 33069-1394

SHIP WHSE.	SELL WHSE.	TAX CODE	CUSTOMER ORDER NUMBER	SALESMAN	JOB NAME	INVOICE DATE	BATCH
125	125	FL2BRO	JEAN	ACF	SHOP	01/26/24	IO 126561
ORDERED	SHIPPED	ITEM NUMBER	DESCRIPTION	UNIT PRICE	UM	AMOUNT	
2	2	S42381404404	FILTER KIT (TS 410/420)	23.260	EA	46.52	
1	1	CHSM14125	14X.125X1 20MM CNCRT SAW BLD	239.990	EA	239.99	
1	1	J22609	NEMESIS S/GLS CAMO / SMOK	7.850	EA	7.85	
			INVOICE SUB-TOTAL			294.36	
			TAX	Broward		20.61	
LEAD LAW WARNING: IT IS ILLEGAL TO INSTALL PRODUCTS THAT ARE NOT "LEAD FREE" IN ACCORDANCE WITH US FEDERAL OR OTHER APPLICABLE LAW IN POTABLE WATER SYSTEMS ANTICIPATED FOR HUMAN CONSUMPTION PRODUCTS WITH *NP IN THE DESCRIPTION ARE NOT LEAD FREE AND CAN ONLY BE INSTALLED IN NON-POTABLE APPLICATIONS. BUYER IS SOLELY RESPONSIBLE FOR PRODUCT SELECTION							
TO CUT 14" PIPES (EXTRA)							
Looking for a more convenient way to pay your bill?							
Log in to Ferguson.com and request access to Online Bill Pay.							
							

TERMS:	NET 10TH PROX	ORIGINAL INVOICE	TOTAL DUE	\$314.97
--------	---------------	------------------	-----------	----------

All past due amounts are subject to a service charge of 1.5% per month, or the maximum allowed by law, if lower. If Buyer fails to pay within terms, then in addition to other remedies, Buyer agrees to pay Seller all costs of collection, including reasonable attorney fees. Complete terms and conditions are available upon request or at <https://www.ferguson.com/content/website-info/terms-of-sale>, incorporated by reference. Seller may convert checks to ACH.

WHITE CAP®

White Cap, L.P.
PO Box 4944
Orlando, FL 32802-4944

BRANCH ADDRESS
236 - POMPANO BEACH (002C)
(954) 979-3030
2007 N.W. 15TH AVENUE
POMPANO BEACH FL 33069
BROWARD

INVOICE NUMBER
10019484845
INVOICE DATE
02/14/2024
CUSTOMER PO NUMBER
GEORGE

TO VIEW AND PAY ONLINE GO TO:
http://whitecap.billtrust.com
ENROLLMENT TOKEN:
DSP ZDX VQQ

TERRITORY:
SHIP TO: 10003231275

MAKE CHECKS PAYABLE TO:
White Cap, L.P. P.O. Box 4852 ORLANDO, FL 32802-4852

SOLD TO: 148363000

ANZAC CONTRACTORS INC
7475 SW 50TH TERRACE
MIAMI FL 33155

PALMETTO PARK ROAD EL RIO CANAL #157
PALMETTO PARK ROAD& EL RIO CANAL
BOCA RATON FL 33432


ORDER DATE	ORDER NO.	ORDERED BY	ACCOUNT MANAGER	TAKEN BY				
02/14/2024	57657881	GEORGE VALDES	BURTON, DAVID R	DEPAUL, PEYTON				
BRANCH	ACCT JOB NO.	TERMS	SHIP VIA / ROUTING	CUSTOMER JOB NO.				
236	10003231275	NET 30 DAYS	5. WALK IN	PALMETTO PARK				
LINE	PART NUMBER	DESCRIPTION	QTY ORD	UNIT PRICE	QTY BKO	QTY SHP	EXTENDED PRICE	TAX AMT
1	617534973220	14" HUSQVARNA VARI-CUT BLADE HUSQVARNA CONSTRUCTION PRODUCTS (UOM IS EA) <div>EXTRA CUT PRECAST WALL PANELS</div>	1	150.000 CS	0	1	150.00	10.50
<div>The White Cap Family of Brands includes All-Tex Waterproofing Solutions, Harmac, Kenseal, Marvel Building & Masonry Supply, MASONPRO, Williams Equipment & Supply, Valley Supply Co, and Diamond Tool. Learn more at About.WhiteCap.com</div> <div>Pay your invoices online by visiting: https://whitecap.billtrust.com</div> <div>Sales Tax Exemption Questions or Certificates: TaxExemptCredit@whitecap.com</div> <div>THESE ITEMS ARE CONTROLLED BY THE U.S. GOVERNMENT AND AUTHORIZED FOR EXPORT ONLY TO THE COUNTRY OF ULTIMATE DESTINATION FOR USE BY THE ULTIMATE CONSIGNEE OR END-USER(S) HEREIN IDENTIFIED. THEY MAY NOT BE RESOLD, TRANSFERRED OR OTHERWISE DISPOSED OF TO ANY OTHER COUNTRY OR ANY PERSON OTHER THAN THE AUTHORIZED ULTIMATE CONSIGNEE OR END-USER(S), EITHER IN THEIR ORIGINAL FORM OR AFTER BEING INCORPORATED INTO OTHER ITEMS, WITHOUT FIRST OBTAINING APPROVAL FROM THE U.S. GOVERNMENT OR AS OTHERWISE AUTHORIZED BY U.S. LAW AND REGULATIONS.</div>								
For questions regarding this invoice please call 1-866-857-0295.						TOTAL GROSS		150.00
NO REFUNDS OR EXCHANGES ON NON STOCK MERCHANDISE Visit https://www.whitecap.com/terms/terms-conditions-of-sale-terms to view complete terms and conditions.						TOTAL TAX		10.50
						TOTAL SHIPPING AND HANDLING		0.00
						TOTAL INVOICE		160.50
RECEIVED BY:			SIGNATURE COPY ON FILE					



"Thank you - We appreciate your business"

Pompano Beach RM
1385 Hammonville Rd
Pompano Beach, FL. 33060

Ticket No.
181707

Delivery Date	Plant	Truck	Driver	Truck Size	Job Type
04/01/2024	138	15037	JACKSON, ROGERS	4.00	FLOWABLE FILL
Customer No.	Customer Name			Slump	Time Due
1000034097	ANZAC CONTRACTORS INC			9.50	10:09 AM
Project No	Order No	Customer PO No		Do not write in this section	
40050608	30699				
Delivery Name and Address					
PALMETTO PARK RD BRIDGE NON-DOT PALMETTO PARK RD AT EL RIO CANAL BOCA RATON					
Instructions					
95 SB TO PALMETTO PARK BLVD EAST.....DRIVER MUST BE HEADING EAST GPS = 566 W PALMETTO ROAD					

Quantity			Product	UM	Unit Price	Amount
Load	Cumulative	Ordered	Code	Description		
4.00	4.00	4.00	DF017000	FLOW FILL EXC 04-FF-1	CY	
1.00	1.00	1.00	98000446	DOUBLE CALL BACK CHAF	LD	
1.00	1.00	1.00	98000303	VARIABLE FUEL SURCHAF	LD	
1.00	1.00	1.00	98000442	ENVIRON SURCHG/LD	LD	
1.00	1.00	1.00	98000448	SHORT LOAD	LD	

Load	Arrive Job Site	Start Discharge	Finish Discharge	Leave Job Site	Arrive Plant	Subtotal	
						Sales Tax	
						Total	
Additional water added to this concrete will reduce its strength. Any water added is at customer's risk.							
Gallons of Water Added: _____ Gallons of Water Added: _____ Gallons of Water Added: _____ Amt of CY Retained: _____							
Customer Approval: _____ Customer Approval: _____ Customer Approval: _____ Customer Approval: _____							
Tested		Tested Properly		Authorized and Received By			
<input type="checkbox"/> Yes <input type="checkbox"/> No		<input type="checkbox"/> Yes <input type="checkbox"/> No		X			
Safety is a constant state of mind, with every employee feeling responsible and empowered to act to cause him and others to work safely, on the belief that all accidents are preventable and that zero incidents is the only goal.				Lot: _____			
				Block: _____			
				Address: _____ Correct _____ Not Correct			



Titan Florida LLC
Attn: Accounts Receivable Dept
455 FAIRWAY DRIVE SUITE 200
DEERFIELD BEACH FL 33441-1805

CUSTOMER ID	INVOICE DATE	INVOICE NUMBER
US51-1000034097	04/01/2024	3001766067

Payment Inquiries: 800-330-3380
Billing Inquiries: 800-204-0632

We appreciate your business

BILL TO

ANZAC CONTRACTORS INC
7475 SW 50TH TERR
MIAMI, FL 33155-4463

SHIP TO:

PO#
PALMETTO PARK RD BRIDGE NON-DOT
PALMETTO PARK RD AT EL RIO CANAL
BOCA RATON
Lot: 1

DATE		TICKET	MATERIAL	DESCRIPTION	BILLING			GROSS
MO	DAY	NUMBER	NUMBER		QUANTITY	U/M	UNIT PRICE	AMOUNT
04	01	181707	1006225	R138-Pompano RMC Plant DF017000 FLOW FILL EXC 04-FF-170	4.00	YD3	136.00	544.00
04	01	181707	98000442	ENVIRON SURCHG	1.00	LD	15.00	15.00
04	01	181707	98000448	SHORT LOAD	1.00	LD	175.00	175.00
04	01	181707	98000303	VARIABLE FUEL SURCHARGE	1.00	LD	28.00	28.00
				PRODUCT RECAP				
				1006225 DF017000 FLOW FILL EXC 04-FF-170	4.00			
				98000303 VARIABLE FUEL SURCHARGE	1.00			
				98000442 ENVIRON SURCHG	1.00			
				98000448 SHORT LOAD	1.00			
Net Total:								762.00
Sales Tax:								53.34

ORDER # 0040050608-5000054569
SALES REP JORGE CHARBONIER
ORDER INFO Delivered
SHIP VIA SiloTruck-Commercial
SHIPPED FROM Pompano RMC Plant

Titan America Corporate
Values:
Safety
Integrity
Know-how
Value to the Customer
Commit to and Deliver Results
Continuous Improvement
Corporate Social Responsibility

Total Quantity	DISCOUNT	INVOICE TOTAL
4.00	5.87	815.34

DISC.DUE	NET DUE DATE
05/10/2024	05/31/2024

Remit To
TITAN FLORIDA LLC
P.O. BOX 932622
ATLANTA, GA 31193-2622

CUSTOMER ID	INVOICE DATE	INVOICE NUMBER
US51-1000034097	04/01/2024	3001766067

To ensure proper credit to your account, please designate invoices being paid.
Visit our website at: <http://www.titanamerica.com/salesterms> for terms and conditions.
A service charge shall be imposed on invoices not paid in accordance with the standard terms, at the rate of 1.5% per month.

www.equipmentwatch.com

All prices shown in US Dollars (\$)

Rental Rate Blue Book®

December 8, 2023

Manitowoc 777 SERIES 1 (disc. 2002)
Crawler Mounted Lattice Boom Cranes



Size Class
349.5 - 200.4 mt
Weight:
273520 lbs

Configuration for 777 SERIES 1 (disc. 2002)

Boom Base Length	60.0 ft	Maximum Lift Capacity	154.2 mt
Power Mode	Diesel		

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$42,460.00	USD \$11,890.00	USD \$2,975.00	USD \$445.00	USD \$222.41	USD \$463.66
Adjustments						
Region (Florida: 97.1%)	(USD \$1,231.34)	(USD \$344.61)	(USD \$86.28)	(USD \$12.90)		
Model Year (1999: 98.98%)	(USD \$421.99)	(USD \$118.17)	(USD \$29.57)	(USD \$4.42)		
Adjusted Hourly Ownership Cost (100%)						
Hourly Operating Cost (100%)						
Total:	USD \$40,806.66	USD \$11,427.02	USD \$2,859.16	USD \$427.67	USD \$222.41	USD \$454.27

Non-Active Use Rates

Hourly

Standby Rate	USD \$136.80
Idling Rate	USD \$281.10

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	26%	USD \$11,039.60/mo
Overhaul (ownership)	41%	USD \$17,408.60/mo
CFC (ownership)	17%	USD \$7,218.20/mo
Indirect (ownership)	16%	USD \$6,793.60/mo
Fuel (operating) @ USD 4.39	22.14%	USD \$49.24/hr

Revised Date: 4th quarter 2023


These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for Pedro Anguita (pedro.anguita@ohla-usa.com)

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book® December 8, 2023

P & H CN150 (disc. 1996)
Rough Terrain Hydraulic Cranes



Size Class
39.5 - 49.4 mt
Weight
78357 lbs

Configuration for CN150 (disc. 1996)

Axle Configuration	4 X 4	Maximum Boom Length	110.0 ft
Maximum Lift Capacity	45.4 mt	Power Mode	Diesel

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$42,295.00	USD \$11,845.00	USD \$2,950.00	USD \$445.00	USD \$241.14	USD \$481.45
Adjustments						
Region (Florida: 98.2%)	(USD \$761.31)	(USD \$213.21)	(USD \$53.28)	(USD \$8.01)		
Model Year (1996: 100%)	-	-	-	-		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)						
Total:	USD \$41,533.69	USD \$11,631.79	USD \$2,906.72	USD \$436.99	USD \$241.14	USD \$477.13

Non-Active Use Rates

	Hourly
Standby Rate	USD \$115.63
Idling Rate	USD \$268.47

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	23%	USD \$9,727.85/mo
Overhaul (ownership)	51%	USD \$21,570.45/mo
CFC (ownership)	16%	USD \$6,767.20/mo
Indirect (ownership)	10%	USD \$4,229.50/mo
Fuel (operating) @ USD 4.39	13.47%	USD \$32.48/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.


The equipment represented in this report has been exclusively prepared for Pedro Anguita (pedro.anguita@ohla-usa.com)

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book® October 4, 2023

Watson 5000
Vertical Earth Drills For Crane Mounting

Size Class:
All
Weight:
N/A



Configuration for 5000

Average Drill Depth: 1200.0 in Triple
Kelly Bar Design
Horsepower: 190.0
Power Mode: Diesel

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$9,905.00	USD \$2,775.00	USD \$695.00	USD \$105.00	USD \$57.54	USD \$113.82
Adjustments						
Region (100%)	-	-	-	-		
Model Year (2023 100%)	-	-	-	-		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)					-	
Total:	USD \$9,905.00	USD \$2,775.00	USD \$695.00	USD \$105.00	USD \$57.54	USD \$113.82

Non-Active Use Rates

Standby Rate	Hourly
Idling Rate	USD \$38.27
	USD \$81.30

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	26%	USD \$2,575.30/mo
Overhaul (ownership)	32%	USD \$3,169.60/mo
CFC (ownership)	20%	USD \$1,981.00/mo
Indirect (ownership)	22%	USD \$2,179.10/mo
Fuel (operating) @ USD 4.39	43.48%	USD \$25.02/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.


The equipment represented in this report has been exclusively prepared for Yelitza Carreno (yelitza.carreno@exp.com)

www.equipmentwatch.com
All prices shown in US dollars (\$)

Rental Rate Blue Book® May 12, 2021

ICE 416L (disc. 2018)
Vibratory Hammers/Extractors

Size Class:
30.0 - 44.9 Tons
Weight:
20706 lbs



Configuration for 416L (disc. 2018)

Horsepower	335.0		Power Mode		Diesel	
Blue Book Rates						
** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.						
Ownership Costs					Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$8,555.00	USD \$2,395.00	USD \$600.00	USD \$90.00	USD \$51.94	USD \$100.55
Adjustments						
Region (Florida: 93%)	(USD \$598.85)	(USD \$167.65)	(USD \$42.00)	(USD \$6.30)		
Model Year (2018: 100%)	-	-	-	-		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)						
Total:	USD \$7,956.15	USD \$2,227.35	USD \$558.00	USD \$83.70	USD \$51.94	USD \$97.15

Non-Active Use Rates		Hourly
Standby Rate		USD \$29.84
Idling Rate		USD \$74.91

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	51%	USD \$4,363.05/mo
Overhaul (ownership)	34%	USD \$2,908.70/mo
CFC (ownership)	4%	USD \$342.20/mo
Indirect (ownership)	11%	USD \$941.05/mo
Fuel (operating) @ USD 2.53	57%	USD \$29.70/hr

Revised Date: 1st half 2021

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for MARIO CUELLO (mcuello@mcm-us.com)




www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book®

October 2, 2023

Miller BIG BLUE 500D CC/CV
Portable Welders

Size Class:
401 - 500 A
Weight
N/A



Configuration for BIG BLUE 500D CC/CV

Current Power Mode	DC-CC/CV Diesel	Horsepower	48.9 hp
--------------------	-----------------	------------	---------

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$1,595.00	USD \$445.00	USD \$110.00	USD \$17.00	USD \$12.06	USD \$21.12
Adjustments						
Region (100%)	-	-	-	-		
Model Year (2023 100%)	-	-	-	-		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)						
Total:	USD \$1,595.00	USD \$445.00	USD \$110.00	USD \$17.00	USD \$12.06	USD \$21.12

Non-Active Use Rates

	Hourly
Standby Rate	USD \$7.25
Idling Rate	USD \$17.92

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	39%	USD \$622.05/mo
Overhaul (ownership)	20%	USD \$319.00/mo
CFC (ownership)	20%	USD \$319.00/mo
Indirect (ownership)	21%	USD \$334.95/mo
Fuel (operating) @ USD 4.39	73.47%	USD \$8.86/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for Yelitza Carreno (yelitza.carreno@exp.com)

www.equipmentwatch.com

All prices shown in US Dollars (\$)

Rental Rate Blue Book®

December 8, 2023

Caterpillar M315F (disc. 2019)
Wheel Mounted Hydraulic Excavators

Size Class:
15.5 - 17.4 mt
Weight:
N/A



Configuration for M315F (disc. 2019)

Horsepower	150.0 hp	Operating Weight	36972.0 lbs
Power Mode	Diesel		

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost

	Ownership Costs				Estimated Operating Costs Hourly	FHWA Rate** Hourly
	Monthly	Weekly	Daily	Hourly		
Published Rates	USD \$11,005.00	USD \$3,080.00	USD \$770.00	USD \$115.00	USD \$45.21	USD \$107.74
Adjustments						
Region (Florida: 98.1%)	(USD \$209.10)	(USD \$58.52)	(USD \$14.63)	(USD \$2.18)		
Model Year (2018: 100%)	USD \$0.39	USD \$0.11	USD \$0.03	USD \$0.00		
Adjusted Hourly Ownership Cost (100%)						
Hourly Operating Cost (100%)						
Total:	USD \$10,796.30	USD \$3,021.59	USD \$755.40	USD \$112.82	USD \$45.21	USD \$106.55

Non-Active Use Rates

	Hourly
Standby Rate	USD \$34.97
Idling Rate	USD \$75.37

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	31%	USD \$3,411.55/mo
Overhaul (ownership)	43%	USD \$4,732.15/mo
CFC (ownership)	16%	USD \$1,760.80/mo
Indirect (ownership)	10%	USD \$1,100.50/mo
Fuel (operating) @ USD 4.39	31.03%	USD \$14.63/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.


The equipment represented in this report has been exclusively prepared for Pedro Anguita (pedro.anguita@ohla-usa.com)

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book® December 8, 2023

Deilmag D30-32
Diesel Hammers

Size Class:
50,000 - 74,999 ft-lb
Weight:
13472 lbs



Configuration for D30-32

Hammer Type	Single Acting	Horsepower	44.0
Maximum Rated Energy	75452.0 ft-lb	Power Mode	Diesel

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost

Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly
Published Rates	USD \$10,185.00	USD \$2,850.00	USD \$715.00	USD \$110.00	USD \$33.63
Adjustments					USD \$91.50
Region (Florida: 97.6%)	(USD \$244.44)	(USD \$68.40)	(USD \$17.16)	(USD \$2.64)	
Model Year (2000: 88.72%)	(USD \$1,120.91)	(USD \$313.66)	(USD \$78.69)	(USD \$12.11)	
Adjusted Hourly Ownership Cost (100%)					
Hourly Operating Cost (100%)					
Total:	USD \$8,819.65	USD \$2,467.94	USD \$619.15	USD \$95.25	USD \$33.63
					USD \$83.74

Non-Active Use Rates		Hourly
Standby Rate		USD \$25.06
Idling Rate		USD \$57.56

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	32%	USD \$3,259.20/mo
Overhaul (ownership)	44%	USD \$4,481.40/mo
CFC (ownership)	13%	USD \$1,324.05/mo
Indirect (ownership)	11%	USD \$1,120.35/mo
Fuel (operating) @ USD 4.39	22.15%	USD \$7.45/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for Pedro Anguita (pedro.anguita@ohla-usa.com)

www.equipmentwatch.com

All prices shown in US Dollars (\$)

Adjustments for F150 XLT 4x4 in All Saved Models

December 21, 2023

Ford F-150 XLT 4X4 GAS


Light Duty Trucks

Size Class:

2

Weight:

N/A



Configuration for F-150 XLT 4X4 GAS

Power Mode

Gasoline

Wheelbase

122.8 Inches

Model Trim

XLT

Gross Vehicle Weight Rating

6050 Pounds

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$2,805.00	USD \$785.00	USD \$195.00	USD \$29.00	USD \$30.66	USD \$46.60
Adjustments						
Region (100%)	-	-	-	-		
Model Year (2022: 99.25%)	(USD \$20.68)	(USD \$5.79)	(USD \$1.44)	(USD \$0.21)		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)					-	
Total:	USD \$2,784.32	USD \$779.21	USD \$193.56	USD \$28.79	USD \$30.66	USD \$46.48

Non-Active Use Rates

Hourly

Standby Rate

USD \$8.70

Idling Rate

USD \$36.54

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	23%	USD \$645.15/mo
Overhaul (ownership)	45%	USD \$1,262.25/mo
CFC (ownership)	16%	USD \$448.80/mo
Indirect (ownership)	16%	USD \$448.80/mo
Fuel (operating) @ USD 3.87	67.58%	USD \$20.72/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book® Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for CRAIG VORSTER (craig.vorster@veceliigroup.com)



July 24, 2023

Via Email

Patrick Ayala

Palm Beach County

2300 N Jog Rd.

West Palm Beach, FL 33411

Re: RCI Project: 300-3303

PBC: 2013531 - Palmetto Park Rd from SW 7th Ave to SW 5th Ave

Sub: NOI #10 – 16" FM Location Under Canal El Rio

Mr. Ayala,

Ranger Construction Industries, Inc. (RCI) is presenting this Notice of Intent to pursue claim(s) for Unforeseeable Work, Extra Work, Claims for Delay and Contract Time Extension.

On RFI #25 submitted on June 7, 2023, Ranger made Palm Beach County aware that the existing 16" FM was not embedded on the bridge as originally thought, but it actually goes subaqueous, under Canal El Rio. This line has been grouted for abandonment.

The RFI was answered on July 19, 2023, directing Ranger to follow up with City of Boca and request them to locate the line. Ranger requested City of Boca to locate the line that same day.

Pile driving is part of our schedule's Critical Path. Our Bridge contractor (Anzac) should begin pile installation by July 28th, 2023. Should City of Boca be able to locate the line before then, and the line be in conflict with the pile driving operation, Anzac will be forced to cease activities until PBC provides a solution. If the line is not located before July 28th, Anzac will not be able to continue either in fears of damage to the concrete piles or to the 16" FM to be abandoned.

This possible conflict should have been addressed at design stage of the project.

RCI reserves all rights under the Contract, including seeking an equitable adjustment to the Contract for all time and costs both realized and unrealized as it pertains to this issue.

A handwritten signature in black ink, appearing to read 'Alejandro Uribe', is written over a horizontal line.

Respectfully,

Alejandro Uribe, PE

Project Manager

Ranger Construction Industries, Inc.

From: Steve McNamara
To: Alejandro Uribe
Cc: Everett Ash; Robert Ueltschi; George Valdes
Subject: Re: [EXTERNAL] RE: 230724 NOI#10 - 16" FM Location under Canal El Rio - Palmetto Park Rd
Date: Friday, August 18, 2023 12:55:25 PM
Attachments: [image001.png](#)
[image002.png](#)
[image003.jpg](#)
[image004.png](#)
[image005.png](#)
[image006.png](#)
[image007.png](#)
[image008.png](#)
[image009.jpg](#)

Alejandro,

While attempting to jet down Pile #40 (IB 2) there was an obstruction encountered at approximately 8-9' below the canal bottom. According to the crew, it seems like it might be the existing subaqueous pipe.

We will proceed with driving the other 5 piles on Monday. We have held on to the rental jet pump and can let the County witness the issue by attempting to jet it again once we have finished the pile driving on Monday. At that time, we brainstorm a solution.

Thanks,
Steve
Sent from my iPhone

On Jul 31, 2023, at 7:37 AM, Alejandro Uribe
<Alejandro.Uribe@rangerconstruction.com> wrote:

Steve,

Thanks for your response. We have made PBC aware of it.

Ranger is yet to receive a response to the attached letter. We are on week 7 of bridge removal, which is 2 weeks longer than the approved CPM. Please provide a recovery schedule to bring the bridge activities back on schedule. This project cannot take any more delays.

Thanks.

Alejandro Uribe, P.E.
Project Manager

1645 N. Congress Ave.
West Palm Beach, FL 33409
OFFICE: (561) 793-9400
CELL: (561) 719-0397
auribe@rangerconstruction.com
www.rangerconstruction.com

<image001.png>

From: Steve McNamara <Steve@anzaccontractors.com>
Sent: Saturday, July 29, 2023 3:54 PM
To: Alejandro Uribe <Alejandro.Uribe@rangerconstruction.com>
Cc: Everett Ash <Everett.Ash@rangerconstruction.com>; Robert Ueltschi <Robert.Ueltschi@rangerconstruction.com>; George Valdes <george@anzaccontractors.com>
Subject: RE: [EXTERNAL] RE: 230724 NOI#10 - 16" FM Location under Canal El Rio - Palmetto Park Rd

Hi Alejandro,

Still catching up. Yes, we are ok with proceeding with the pile installation as per the comments below. if we encounter any issues or obstructions while installing the piles, we will notify Ranger and PBC immediately and work with the team on a resolution.

All the piles were removed in the canal as of the end of the day yesterday. Today we had the crew working on cutting the piles so we can load and dispose of them this coming week. We will be using the same crew to load the vibratory hammer and steel beams in our Homestead Yard early this coming week and then deliver these items to the job to begin building templates. This will be followed by prestressed concrete pile deliveries to the site and standing piles in the templates.

Thanks,

Steven R. McNamara
President

ANZAC CONTRACTORS, INC.

7475 SW 50th Terrace
Miami, FL 33155

305.669.1986 Office
305.986.0480 Cell
305.669.1180 Fax

Steve@AnzacContractors.com
www.AnzacContractors.com
<image002.png>

From: Alejandro Uribe <Alejandro.Uribe@rangerconstruction.com>
Sent: Friday, July 28, 2023 11:00 AM
To: Steve McNamara <Steve@anzaccontractors.com>; George Valdes <george@anzaccontractors.com>
Cc: Everett Ash <Everett.Ash@rangerconstruction.com>; Robert Ueltschi <Robert.Ueltschi@rangerconstruction.com>
Subject: FW: [EXTERNAL] RE: 230724 NOI#10 - 16" FM Location under Canal El Rio - Palmetto Park Rd

Steve,

Please see below and confirm Anzac is comfortable driving piles following EOR's recommendation. Also, please provide a 2-week look ahead so we can all plan accordingly.

Alejandro Uribe, P.E.
Project Manager

1645 N. Congress Ave.
West Palm Beach, FL 33409
OFFICE: (561) 793-9400
CELL: (561) 719-0397
auribe@rangerconstruction.com
www.rangerconstruction.com

<image001.png>

From: Albert Hoffman <AWHoffman@pbcgov.org>
Sent: Friday, July 28, 2023 10:47 AM
To: Alejandro Uribe <Alejandro.Uribe@rangerconstruction.com>
Cc: Patricio Ayala <PAyala@pbcgov.org>; Chris LaForte <chris.laforte@wginc.com>
Subject: FW: [EXTERNAL] RE: 230724 NOI#10 - 16" FM Location under Canal El Rio - Palmetto Park Rd

Alejandro,
Please see the response below from Chris LaForte of WGI regarding the abandoned subaqueous 16-inch force main and the proposed piles for the bridge.
In the letter regarding NOI 10, it was mentioned that Anzac was supposed to start driving piles on July 28. However, they are still busy removing the existing piles and haven't begun building the pile template yet. Can you provide a 2-week look ahead?

Thank you,

Albert Hoffman
Director, Construction Coordination Division

Palm Beach County
Engineering & Public Works
2300 N. Jog Rd. • West Palm Beach • Florida 33411
O: 561-684-4180 | F: 561-684-4165
<image003.jpg>

From: Chris LaForte <chris.laforte@wginc.com>
Sent: Thursday, July 27, 2023 5:20 PM


To: Albert Hoffman <AWHoffman@pbcgov.org>
Cc: Patricio Ayala <PAyala@pbcgov.org>; Kathleen Farrell <KFarrell@pbcgov.org>; Chris Holmes <Chris.Holmes@wginc.com>; Brett Fuller <Brett.Fuller@wginc.com>
Subject: RE: [EXTERNAL] RE: 230724 NOI#10 - 16" FM Location under Canal El Rio - Palmetto Park Rd

This Message Is From an External Sender
This message came from outside your organization.

Albert,

As we discussed yesterday, the presence of the existing 16 inch force main along the south side of the bridge was discussed during the utility coordination meetings throughout the design process. The plans call out for this force main to be grouted and placed out of service. WGI does not believe that damage to the prestressed piling is likely to occur due to a potential impact with this abandoned pipe. Contractor is to take normal care during pile driving and if an obstruction occurs during driving that results in a pile shifting out of location or needing to have an alternate pile depth or location that can be reviewed at that time. If there are any additional questions or anything else that we can help with, please let us know. Thank you.

Chris LaForte



Chris LaForte, PE
Senior Project Manager
2035 Vista Parkway
West Palm Beach, FL 33411
561.687.2220 (office)

[<image005.png>](#) [<image006.png>](#) [<image007.png>](#) [<image008.png>](#)
[\[linkedin.com\]](#) [\[facebook.com\]](#) [\[instagram.com\]](#) [\[youtube.com\]](#)

[<image009.jpg>](#)
[\[survey.hsforms.com\]](#)

Under Florida law, e-mail addresses are public records. If you do not want your e-mail address released in response to a public records request, do not send electronic mail to this entity. Instead, contact this office by phone or in writing.
LEGAL DISCLAIMER The information in this message is confidential and may be privileged. It is intended solely for the addressee. Access to this message by anyone else is

unauthorized. If the reader of this is not the intended recipient, any dissemination, distribution, or copying of this communication, or any action or omission taken by the reader in reliance on it is prohibited and may be unlawful. Thank you

*****LEGAL DISCLAIMER***** The information in this message is confidential and may be privileged. It is intended solely for the addressee. Access to this message by anyone else is unauthorized. If the reader of this is not the intended recipient, any dissemination, distribution, or copying of this communication, or any action or omission taken by the reader in reliance on it is prohibited and may be unlawful. Thank you

<230721 3rd Letter of Concern Anzac.pdf>



1645 N. Congress Ave
West Palm Beach, FL 33409
Phone: (561) 793-9400

www.rangerconstruction.com

Delay Claim No. 6 - FPL Conflict with Pile Installation

Submitted To: Albert Hoffman	Date: 14-Oct-24
Address: Palm Beach County 2300 Jog Rd West Palm Beach, 33411	Phone:
Contact: Albert Hoffman	Fax:
	Job Name: 2013531 - Palmetto Park Rd
	RCI No. 300-3303
	Job Location: City of Boca Raton
	Owner: Palm Beach County

Claim Cost Calculation

<u>Claim No.</u>	<u>DESCRIPTION</u>	<u>Delay Days</u>	<u>QUANTITY</u>	<u>UM</u>	<u>UNIT PRICE</u>	<u>EXTENSION</u>
10	FPL Conflict with Pile Installation	0	1.00	LS	\$ 38,691.29	\$38,691.29
	Bond Cost 1.5%		1.00	LS	\$580.37	\$580.37
	Total Delay Days	0	ESTIMATED TOTAL =			\$39,271.66
	Total Compensable Days	0				
Average OH Cost Per Day (A*C)/B						
A = Original Contract Amount \$ 4,337,120.16						
B = Original Contract Time (Days) 450.00						
C = 8%						
Average OH Cost Per Day \$ 771.04						

NOTES:
Labor Costs Include 45.98% Labor Burden
Daily OH Rate \$771.04
This calculation for compensable days applies only if Claim #9 is accepted on its entirety by PBC.

ACCEPTED: The above prices, specifications and conditions are satisfactory and are hereby accepted.	Ranger Construction Industries, Inc.
Owner _____	Authorized Signature _____
Signature _____	Name & Title Gregory W. Reilly - Project Manager
Date of Acceptance _____	



Ranger Construction Industries

1645 N. Congress Ave.
West Palm Beach, FL 33409
Phone: 561-793-9400

	RCI PROJECT NUMBER
	PROJECT NAME
	Delay Cause
Total Compensable Delay Days	
	Delay Dates

3003303
Palmetto Park Rd
FPL Conflict with Pile Installation
0 Concurrent Delay
8/16/2023 to 2/6/2024

Delay Claim No. 6 - FPL Conflict with Pile Installation

[illegible]

PALMETTO PARK RD BRIDGE - COSTS INCURRED DUE TO UNFORESEEN CONFLICT WITH FPL OVERHEAD LINES									
DATES	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	TOTAL	ANZAC PROFIT	MARK UP PERCENTAGE	TOTAL	COMMENTS
THURSDAY, 8/24/23	STEVE MCNAMARA, GEORGE VALDES, HECTOR BANEGAS AND LUIS CAPDEVILA MET ONSITE TO COMPARE THE "AS-BUILT" SURVEY OF THE FPL OH LINES FROM PBC TO THE LOCATIONS THAT ANZAC LAID ON THE TEMPLATES FOR REVISED PILE LOCATIONS TO AVOID THE FPL OH LINES. THE SURVEY DONE BY PBC INDICATES THAT THE PILE LOCATIONS LAID OUT BY ANZAC ARE EVEN CLOSER TO THE OH LINES THEN WE ESTIMATED.								
	GEORGE VALDES	2.00	HR	\$77.36	\$154.72	\$27.08	17.50%	\$181.80	
	SUPERVISOR'S TRUCK	2.00	HR	\$39.27	\$78.54	\$13.74	17.50%	\$92.28	
	HECTOR BANEGAS	2.00	HR	\$47.89	\$95.78	\$16.76	17.50%	\$112.54	
	FORMAN'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	REGINALD WATSON	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	CRANE OPERATOR'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	2.00	HR	\$35.36	\$70.72	\$12.36	17.50%	\$83.10	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	4.50	HR	\$136.80	\$615.60	\$107.73	17.50%	\$723.33	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	4.50	HR	\$7.25	\$32.63	\$5.71	17.50%	\$38.33	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	4.50	HR	\$7.25	\$32.63	\$5.71	17.50%	\$38.33	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	4.50	HR	\$10.14	\$45.63	\$7.99	17.50%	\$53.62	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	4.50	HR	\$5.00	\$22.50	\$3.94	17.50%	\$26.44	IDLE RATE
TUESDAY, 11/14/23	MOBILIZE 50 TON P&H ROUGH TERRAIN CRANE TO BE ABLE TO WORK UNDER THE EXISTING FPL OVERHEAD LINES TO BUILD TEMPLATE AND INSTALL 14" PILES, SW WING END BENT #1								
	GEORGE VALDES	2.00	HR	\$77.36	\$154.72	\$27.08	17.50%	\$181.80	
	SUPERVISOR'S TRUCK	2.00	HR	\$39.27	\$78.54	\$13.74	17.50%	\$92.28	
	HECTOR BANEGAS	2.00	HR	\$47.89	\$95.78	\$16.76	17.50%	\$112.54	
	FORMAN'S TRUCK	2.00	HR	\$32.93	\$65.86	\$11.53	17.50%	\$77.39	
	JOSE LOPEZ, CRANE OPERATOR	2.00	HR	\$53.05	\$106.10	\$18.57	17.50%	\$124.67	
	LUIS CAPADEVILA	2.00	HR	\$35.36	\$70.72	\$12.36	17.50%	\$83.10	
	FELIX VAZQUEZ	2.00	HR	\$28.00	\$56.00	\$9.80	17.50%	\$65.80	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	2.00	HR	\$29.47	\$58.94	\$10.31	17.50%	\$69.25	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	8.00	HR	\$477.13	\$3,817.04	\$687.98	17.50%	\$4,485.02	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	8.00	HR	\$125.00	\$1,000.00	\$175.00	17.50%	\$1,175.00	IDLE RATE
TUESDAY, 11/15/23	USE 50 TON P&H ROUGH TERRAIN CRANE TO BE ABLE TO WORK UNDER THE EXISTING FPL OVERHEAD LINES TO BUILD TEMPLATE AND INSTALL 14" PILES, SW WING END BENT #1 - RAINED OUT AFTER 3.5 HRS OF WORK								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BANEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	3.50	HR	\$477.13	\$1,669.96	\$292.24	17.50%	\$1,962.20	
	P&H CN150 50 TON RT CRANE	4.50	HR	\$115.63	\$520.34	\$91.06	17.50%	\$611.39	IDLE RATE

	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
WEDNESDAY, 11/16/23	MOVE 777 MANITOWOC CRAWLER CRANE TOP THE WEST TO PROVIDE ROOM TO USE 50 TON P&H ROUGH TERRAIN CRANE TO BE ABLE TO WORK UNDER THE EXISTING FPL OVERHEAD LINES TO BUILD TEMPLATE AND INSTALL 14" PILES, SW WING END BENT #1								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPEDEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	8.00	HR	\$477.13	\$3,817.04	\$667.98	17.50%	\$4,485.02	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
THURSDAY, 12/14/23	USE 50 TON P&H ROUGH TERRAIN CRANE TO BE ABLE TO WORK UNDER THE EXISTING FPL OVERHEAD LINES TO INSTALL PRECAST WALL PANELS AT SW WING, EB #1								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPEDEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	8.00	HR	\$477.13	\$3,817.04	\$667.98	17.50%	\$4,485.02	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE

TUESDAY, 2/6/23	WORK WITH P&H RT CRANE UNDER FPL WIRES TO BUILD TEMPLATE FOR EB #4 WING WALL. STAND AND JET 14" PILES X 22.5' LONG.								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	JEAN DUVAL	0.00	HR	\$39.78	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	8.00	HR	\$136.80	\$1,094.40	\$191.52	17.50%	\$1,285.92	IDLE RATE
	P&H CN150 50 TON RT CRANE	8.00	HR	\$477.13	\$3,617.04	\$667.98	17.50%	\$4,485.02	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
WEDNESDAY, 2/7/23	WORK WITH P&H RT CRANE UNDER FPL WIRES TO REMOVE TEMPLATE FOR EB #4 WING WALL								
	GEORGE VALDES	0.00	HR	\$77.36	\$0.00	\$0.00	17.50%	\$0.00	
	SUPERVISOR'S TRUCK	0.00	HR	\$39.27	\$0.00	\$0.00	17.50%	\$0.00	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$53.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	JEAN DUVAL	0.00	HR	\$39.78	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	5.50	HR	\$136.80	\$752.40	\$131.67	17.50%	\$884.07	IDLE RATE
	P&H CN150 50 TON RT CRANE	2.50	HR	\$477.13	\$1,192.83	\$208.74	17.50%	\$1,401.57	
	P&H CN150 50 TON RT CRANE	0.00	HR	\$115.63	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$25.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MWI JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MWI JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	0.00	HR	\$125.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE

WEDNESDAY, 2/28/24	REMOBILIZE P&H RT CRANE TO WORK UNDER FPL WIRES AT EB #4 SE WING TO INSTALL PRECAST WALL PANELS.								
	GEORGE VALDES	2.00	HR	\$77.36	\$164.72	\$27.08	17.50%	\$181.80	
	SUPERVISOR'S TRUCK	2.00	HR	\$39.27	\$78.54	\$13.74	17.50%	\$92.28	
	HECTOR BENEGAS	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	CARLOS MACHIAVELLO	0.00	HR	\$47.89	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	JOSE LOPEZ, CRANE OPERATOR	0.00	HR	\$63.05	\$0.00	\$0.00	17.50%	\$0.00	
	WAYNE TURNER, CRANE OPERATOR	0.00	HR	\$73.68	\$0.00	\$0.00	17.50%	\$0.00	
	LUIS CAPADEVILA	0.00	HR	\$35.36	\$0.00	\$0.00	17.50%	\$0.00	
	FELIX VAZQUEZ	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	YEISON MONZON	0.00	HR	\$28.00	\$0.00	\$0.00	17.50%	\$0.00	
	JUAN MEDRANO	0.00	HR	\$36.84	\$0.00	\$0.00	17.50%	\$0.00	
	JEAN DUVAL	0.00	HR	\$38.78	\$0.00	\$0.00	17.50%	\$0.00	
	FORMAN'S TRUCK	0.00	HR	\$32.93	\$0.00	\$0.00	17.50%	\$0.00	
	VINCENT BROWN	0.00	HR	\$29.47	\$0.00	\$0.00	17.50%	\$0.00	
	LEONARDO NUNEZ	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	DARWIN BLACKETT	0.00	HR	\$30.94	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$454.27	\$0.00	\$0.00	17.50%	\$0.00	
	MANITOWOC MODEL 777, 200 TON CRAWLER CRANE	0.00	HR	\$138.80	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	P&H CN150 50 TON RT CRANE	0.00	HR	\$477.13	\$0.00	\$0.00	17.50%	\$0.00	
	P&H CN150 50 TON RT CRANE	5.00	HR	\$115.63	\$925.04	\$161.88	17.50%	\$1,086.92	IDLE RATE
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$97.15	\$0.00	\$0.00	17.50%	\$0.00	
	ICE MODEL 416L VIBRATORY PILE HAMMER	0.00	HR	\$29.84	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$106.55	\$0.00	\$0.00	17.50%	\$0.00	
	2018 CAT 315 F EXCAVATOR	0.00	HR	\$34.97	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	DELMAG D30-02	0.00	HR	\$26.06	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	2010 MILLER 400 AMP WELDER	0.00	HR	\$21.12	\$0.00	\$0.00	17.50%	\$0.00	
	2010 MILLER 400 AMP WELDER	0.00	HR	\$7.25	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	GENERATOR AND TORCH SET	0.00	HR	\$18.31	\$0.00	\$0.00	17.50%	\$0.00	
	GENERATOR AND TORCH SET	0.00	HR	\$7.32	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	MW1 JET PUMP & HOSES	0.00	HR	\$21.39	\$0.00	\$0.00	17.50%	\$0.00	
	MW1 JET PUMP & HOSES	0.00	HR	\$10.14	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	
	STEEL WORK BARGE, 20' X 12'	0.00	HR	\$5.00	\$0.00	\$0.00	17.50%	\$0.00	IDLE RATE
	STERLING TRACTOR AND FLAT TRAILER	8.00	HR	\$125.00	\$1,000.00	\$175.00	17.50%	\$1,175.00	
TOTAL	*WAGE RATES INCLUDE 47.35% BURDEN*				\$29,935.24	\$5,238.67		\$35,173.90	

www.equipmentwatch.com

All prices shown in US Dollars (\$)

Rental Rate Blue Book®

December 8, 2023

Manitowoc 777 SERIES 1 (disc. 2002)
Crawler Mounted Lattice Boom Cranes



Size Class:
149.5 - 200.4 mt
Weight:
273820 lbs

Configuration for 777 SERIES 1 (disc. 2002)

Boom Base Length	60.0 ft	Maximum Lift Capacity	154.2 mt
Power Mode	Diesel		

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$42,460.00	USD \$11,890.00	USD \$2,975.00	USD \$445.00	USD \$222.41	USD \$463.66
Adjustments						
Region (Florida: 97.1%)	(USD \$1,231.34)	(USD \$344.81)	(USD \$86.28)	(USD \$12.90)		
Model Year (1999: 98.98%)	(USD \$421.99)	(USD \$118.17)	(USD \$29.57)	(USD \$4.42)		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)	-	-	-	-		
Total:	USD \$40,806.66	USD \$11,427.02	USD \$2,859.16	USD \$427.67	USD \$222.41	USD \$454.27

Non-Active Use Rates

Hourly

Standby Rate	USD \$135.80
Idling Rate	USD \$281.10

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	28%	USD \$11,039.60/mo
Overhaul (ownership)	41%	USD \$17,408.60/mo
CFC (ownership)	17%	USD \$7,218.20/mo
Indirect (ownership)	16%	USD \$6,793.60/mo
Fuel (operating) @ USD 4.39	22.14%	USD \$49.24/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for Pedro Anguita (pedro.anguita@ohla-usa.com)

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book®

December 8, 2023

P & H CN150 (disc. 1996)
Rough Terrain Hydraulic Cranes

Size Class:
39.5 - 49.4 m
Weight:
78357 lbs



Configuration for CN150 (disc. 1996)

Axle Configuration	4 X 4	Maximum Boom Length	116.0 ft
Maximum Lift Capacity	45.4 mt	Power Mode	Diesel

Blue Book Rates

*1 FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$42,295.00	USD \$11,845.00	USD \$2,960.00	USD \$445.00	USD \$241.14	USD \$481.45
Adjustments						
Region (Florida: 98.2%)	(USD \$761.31)	(USD \$213.21)	(USD \$53.28)	(USD \$8.01)		
Model Year (1996: 100%)	-	-	-	-		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)						
Total:	USD \$41,533.69	USD \$11,631.79	USD \$2,906.72	USD \$436.99	USD \$241.14	USD \$477.13

Non-Active Use Rates

Standby Rate	Hourly
Idling Rate	USD \$115.63
	USD \$268.47

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	23%	USD \$2,727.85/mo
Overhaul (ownership)	51%	USD \$21,570.45/mo
CFC (ownership)	16%	USD \$6,767.20/mo
Indirect (ownership)	10%	USD \$4,229.50/mo
Fuel (operating) @ USD 4.39	13.47%	USD \$32.48/yr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.


The equipment represented in this report has been exclusively prepared for Pedro Anguita (pedro.anguita@ohla-usa.com)

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book® October 4, 2023

Watson 5000
Vertical Earth Drills For Crane Mounting

Size Class:
All
Weight:
N/A



Configuration for 5000

Average Drill Depth **1200.0 in** Horsepower **190.0**
Kelly Bar Design **Triple** Power Mode **Diesel**

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$9,905.00	USD \$2,775.00	USD \$695.00	USD \$105.00	USD \$57.54	USD \$113.82
Adjustments						
Region (100%)	-	-	-	-		
Model Year (2023 100%)	-	-	-	-		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)					-	
Total:	USD \$9,905.00	USD \$2,775.00	USD \$695.00	USD \$105.00	USD \$57.54	USD \$113.82

Non-Active Use Rates

Standby Rate Hourly USD \$38.27
Idling Rate Hourly USD \$81.30

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	26%	USD \$2,575.30/mo
Overhaul (ownership)	32%	USD \$3,169.60/mo
CFC (ownership)	20%	USD \$1,981.00/mo
Indirect (ownership)	22%	USD \$2,179.10/mo
Fuel (operating) @ USD 4.39	43.48%	USD \$25.02/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for Yelitza Carreno (yelitza.carreno@exp.com)

www.equipmentwatch.com


All prices shown in US dollars (\$)

Rental Rate Blue Book®

May 12, 2021

ICE 416L (disc. 2018)
Vibratory Hammers/Extractors

Size Class:
30.0 - 44.9 Tons
Weight:
20706 lbs



Configuration for 416L (disc. 2018)

Horsepower 335.0 Power Mode Diesel

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$8,555.00	USD \$2,395.00	USD \$600.00	USD \$90.00	USD \$51.94	USD \$100.55
Adjustments						
Region (Florida: 93%)	(USD \$598.85)	(USD \$167.65)	(USD \$42.00)	(USD \$6.30)		
Model Year (2018: 100%)	-	-	-	-		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)					-	
Total:	USD \$7,956.15	USD \$2,227.35	USD \$558.00	USD \$83.70	USD \$51.94	USD \$97.15

Non-Active Use Rates

	Hourly
Standby Rate	USD \$29.84
Idling Rate	USD \$74.91

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	51%	USD \$4,363.05/mo
Overhaul (ownership)	34%	USD \$2,908.70/mo
CFC (ownership)	4%	USD \$342.20/mo
Indirect (ownership)	11%	USD \$941.05/mo
Fuel (operating) @ USD 2.53	57%	USD \$29.70/hr

Revised Date: 1st half 2021

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.


The equipment represented in this report has been exclusively prepared for MARIO CUELLO (mcuello@mcm-us.com)

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book® October 2, 2023

Miller BIG BLUE 500D CC/CV
Portable Welders

Size Class:
401 - 500 A
Weight:
N/A



Configuration for BIG BLUE 500D CC/CV

Current Power Mode	DC-CC/CV Diesel	Horsepower	48.9 hp
--------------------	-----------------	------------	---------

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs	FHWA Rate**
	Monthly	Weekly	Daily	Hourly	Hourly	Hourly
Published Rates	USD \$1,595.00	USD \$445.00	USD \$110.00	USD \$17.00	USD \$12.06	USD \$21.12
Adjustments						
Region (100%)	-	-	-	-		
Model Year (2023 100%)	-	-	-	-		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)						
Total:	USD \$1,595.00	USD \$445.00	USD \$110.00	USD \$17.00	USD \$12.06	USD \$21.12

Non-Active Use Rates	Hourly
Standby Rate	USD \$7.25
Idling Rate	USD \$17.92

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	39%	USD \$622.05/mo
Overhaul (ownership)	20%	USD \$319.00/mo
CFC (ownership)	20%	USD \$319.00/mo
Indirect (ownership)	21%	USD \$334.95/mo
Fuel (operating) @ USD 4.39	73.47%	USD \$8.86/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for Yelitza Carreno (yelitza.carreno@exp.com)

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book®

December 8, 2023

Caterpillar M315F (disc. 2019)
Wheel Mounted Hydraulic Excavators



Size Class:
15.5 - 17.4 mt
Weight:
N/A

Configuration for M315F (disc. 2019)

Horsepower	150.0 hp	Operating Weight	36972.0 lbs
Power Mode	Diesel		

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost

	Ownership Costs				Estimated Operating Costs Hourly	FHWA Rate** Hourly
	Monthly	Weekly	Daily	Hourly		
Published Rates	USD \$11,005.00	USD \$3,060.00	USD \$770.00	USD \$115.00	USD \$45.21	USD \$107.74
Adjustments						
Region (Florida: 98.1%)	(USD \$209.10)	(USD \$58.52)	(USD \$14.63)	(USD \$2.18)		
Model Year (2018: 100%)	USD \$0.39	USD \$0.11	USD \$0.03	USD \$0.00		
Adjusted Hourly Ownership Cost (100%)						
Hourly Operating Cost (100%)						
Total:	USD \$10,796.30	USD \$3,021.59	USD \$755.40	USD \$112.82	USD \$45.21	USD \$106.55

Non-Active Use Rates

	Hourly
Standby Rate	USD \$34.97
Idling Rate	USD \$75.37

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	31%	USD \$3,411.55/mo
Overhaul (ownership)	43%	USD \$4,732.15/mo
CFC (ownership)	16%	USD \$1,760.80/mo
Indirect (ownership)	10%	USD \$1,100.50/mo
Fuel (operating) @ USD 4.39	31.03%	USD \$14.03/hr

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.


The equipment represented in this report has been exclusively prepared for Pedro Anguita (pedro.anguita@ohla-usa.com)

www.equipmentwatch.com
All prices shown in US Dollars (\$)

Rental Rate Blue Book® December 8, 2023

Deilmag D30-32
Diesel Hammers

Size Class:
50,000 - 74,999 ft-lb
Weight:
13472 lbs



Configuration for D30-32

Hammer Type: Single Acting
Maximum Rated Energy: 75452.0 ft-lb
Horsepower: 44.0
Power Mode: Diesel

Blue Book Rates

** FHWA Rate is equal to the monthly ownership cost divided by 176 plus the hourly estimated operating cost.

	Ownership Costs				Estimated Operating Costs Hourly	FHWA Rate** Hourly
	Monthly	Weekly	Daily	Hourly		
Published Rates	USD \$10,185.00	USD \$2,850.00	USD \$715.00	USD \$110.00	USD \$33.63	USD \$91.50
Adjustments						
Region (Florida: 97.6%)	(USD \$244.44)	(USD \$68.40)	(USD \$17.16)	(USD \$2.64)		
Model Year (2000: 68.72%)	(USD \$1,120.91)	(USD \$313.66)	(USD \$78.69)	(USD \$12.11)		
Adjusted Hourly Ownership Cost (100%)	-	-	-	-		
Hourly Operating Cost (100%)						
Total:	USD \$6,819.65	USD \$2,467.94	USD \$619.15	USD \$95.25	USD \$33.63	USD \$83.74

Non-Active Use Rates

Standby Rate: Hourly USD \$25.06
Idling Rate: Hourly USD \$57.56

Rate Element Allocation

Element	Percentage	Value
Depreciation (ownership)	32%	USD \$3,259.20/mo
Overhaul (ownership)	44%	USD \$4,481.40/mo
CFC (ownership)	13%	USD \$1,324.05/mo
Indirect (ownership)	11%	USD \$1,120.35/mo
Fuel (operating) @ USD 4.39	22.15%	USD \$7,454.41

Revised Date: 4th quarter 2023

These are the most accurate rates for the selected Revision Date(s). However, due to more frequent online updates, these rates may not match Rental Rate Blue Book Print. Visit the Cost Recovery Product Guide on our Help page for more information.

The equipment represented in this report has been exclusively prepared for Pedro Anguita (pedro.anguita@ohla-usa.com)



Travelers Casualty and Surety Company of
America
Hartford, Connecticut 06183

To be attached to and form part of Bond # 107544884

Issued on behalf of Ranger Construction Industries, Inc. as Principal, and in favor of
Palm Beach County, Board of County Commissioners as Obligee.

It is agreed that:

1. The Surety hereby gives its consent to change the Bond Amount

from: \$4,447,386.25
to: \$5,035,325.50


2. This rider shall become effective as of: February 28, 2025


PROVIDED, however, that the liability of the Surety under the attached bond as changed by this
Rider shall not be cumulative.

Signed, sealed and dated the 4th day of March, 2025

Ranger Construction Industries, Inc.

By: _____



Bob Schafer




Travelers Casualty and Surety Company of America

By: _____

William D. Phelps, Attorney-In-Fact and FL Resident Agent







Travelers Casualty and Surety Company of America
Travelers Casualty and Surety Company
St. Paul Fire and Marine Insurance Company

POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS: That Travelers Casualty and Surety Company of America, Travelers Casualty and Surety Company, and St. Paul Fire and Marine Insurance Company are corporations duly organized under the laws of the State of Connecticut (herein collectively called the "Companies"), and that the Companies do hereby make, constitute and appoint **WILLIAM D PHELPS** of **MELBOURNE**, **Florida**, their true and lawful Attorney(s)-in-Fact to sign, execute, seal and acknowledge any and all bonds, recognizances, conditional undertakings and other writings obligatory in the nature thereof on behalf of the Companies in their business of guaranteeing the fidelity of persons, guaranteeing the performance of contracts and executing or guaranteeing bonds and undertakings required or permitted in any actions or proceedings allowed by law.

IN WITNESS WHEREOF, the Companies have caused this instrument to be signed, and their corporate seals to be hereto affixed, this 21st day of April, 2021.



State of Connecticut

City of Hartford ss.


By: _____

Robert L. Raney
 Robert L. Raney, Senior Vice President

On this the 21st day of April, 2021, before me personally appeared **Robert L. Raney**, who acknowledged himself to be the Senior Vice President of each of the Companies, and that he, as such, being authorized so to do, executed the foregoing instrument for the purposes therein contained by signing on behalf of said Companies by himself as a duly authorized officer.

IN WITNESS WHEREOF, I hereunto set my hand and official seal.

My Commission expires the 30th day of June, 2026



Anna P. Nowik
 Anna P. Nowik, Notary Public

This Power of Attorney is granted under and by the authority of the following resolutions adopted by the Boards of Directors of each of the Companies, which resolutions are now in full force and effect, reading as follows:

RESOLVED, that the Chairman, the President, any Vice Chairman, any Executive Vice President, any Senior Vice President, any Vice President, any Second Vice President, the Treasurer, any Assistant Treasurer, the Corporate Secretary or any Assistant Secretary may appoint Attorneys-in-Fact and Agents to act for and on behalf of the Company and may give such appointee such authority as his or her certificate of authority may prescribe to sign with the Company's name and seal with the Company's seal bonds, recognizances, contracts of indemnity, and other writings obligatory in the nature of a bond, recognizance, or conditional undertaking, and any of said officers or the Board of Directors at any time may remove any such appointee and revoke the power given him or her; and it is

FURTHER RESOLVED, that the Chairman, the President, any Vice Chairman, any Executive Vice President, any Senior Vice President or any Vice President may delegate all or any part of the foregoing authority to one or more officers or employees of this Company, provided that each such delegation is in writing and a copy thereof is filed in the office of the Secretary; and it is

FURTHER RESOLVED, that any bond, recognizance, contract of indemnity, or writing obligatory in the nature of a bond, recognizance, or conditional undertaking shall be valid and binding upon the Company when (a) signed by the President, any Vice Chairman, any Executive Vice President, any Senior Vice President or any Vice President, any Second Vice President, the Treasurer, any Assistant Treasurer, the Corporate Secretary or any Assistant Secretary and duly attested and sealed with the Company's seal by a Secretary or Assistant Secretary; or (b) duly executed (under seal, if required) by one or more Attorneys-in-Fact and Agents pursuant to the power prescribed in his or her certificate or their certificates of authority or by one or more Company officers pursuant to a written delegation of authority; and it is

FURTHER RESOLVED, that the signature of each of the following officers: President, any Executive Vice President, any Senior Vice President, any Vice President, any Assistant Vice President, any Secretary, any Assistant Secretary, and the seal of the Company may be affixed by facsimile to any Power of Attorney or to any certificate relating thereto appointing Resident Vice Presidents, Resident Assistant Secretaries or Attorneys-in-Fact for purposes only of executing and attesting bonds and undertakings and other writings obligatory in the nature thereof, and any such Power of Attorney or certificate bearing such facsimile signature or facsimile seal shall be valid and binding upon the Company and any such power so executed and certified by such facsimile signature and facsimile seal shall be valid and binding on the Company in the future with respect to any bond or understanding to which it is attached.

I, **Kevin E. Hughes**, the undersigned, Assistant Secretary of each of the Companies, do hereby certify that the above and foregoing is a true and correct copy of the Power of Attorney executed by said Companies, which remains in full force and effect.

Dated this 4th day of March, 2025.



Kevin E. Hughes
 Kevin E. Hughes, Assistant Secretary

To verify the authenticity of this Power of Attorney, please call us at 1-800-421-3880.

Please refer to the above-named Attorney(s)-in-Fact and the details of the bond to which this Power of Attorney is attached.

OEBO SCHEDULE 1

SOLICITATION/PROJECT/BID NAME: Palmetto Park Road SW 7th Avenue to SW 5th Avenue
SOLICITATION OPENING/SUBMITTAL DATE: 02/09/2021

SOLICITATION/PROJECT/BID NO.: 2013531
COUNTY DEPARTMENT: Engineering and Public Works

Section A PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME CONTRACTOR/CONSULTANT* ON THE PROJECT:
NAME OF PRIME RESPONDENT/BIDDER: Ranger Construction Industries, Inc. ADDRESS: 1645 North Congress Avenue, West Palm Beach, FL 33409
CONTACT PERSON: Greg Reilly PHONE NO.: (561) 793-9400 E-MAIL: greg.reilly@rangerconstruction.com
PRIME'S DOLLAR AMOUNT OR PERCENTAGE OF WORK: \$ 365,627.79
Non-SBE MBE WBE SBE
*SMWBE Prime's must include their percentage or dollar amount in the Total Participation line under section B.

Section B PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SUBCONTRACTORS/SUBCONSULTANTS ON THE PROJECT BELOW:

Subcontractor/Sub consultant Name	(Check all Applicable Categories)				DOLLAR AMOUNT OR PERCENTAGE OF WORK					
	Non-SBE	MBE Minority Business	WBE Women Business	SBE Small Business	Black	Hispanic	Women	Caucasian	Asian	Other
1. Caulfield & Wheeler, Inc.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>				\$ 2,972.50		
2. Anzac Contractors Inc	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>				\$ 219,338.96		
3.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>						
4.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>						
5.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>						

(Please use additional sheets if necessary)

Total \$ 222,311.46

Total Bid/Offer Price \$ 587,939.25

Total Certified S/M/WBE Participation \$ 0.00

I hereby certify that the above information is accurate to the best of my knowledge: Jamie R Timming Vice President
Name & Authorized Signature Title

- Note:
- The amount listed on this form for a Subcontractor/sub consultant must be supported by price or percentage listed on the properly executed Schedule 2 or attached signed proposal.
 - Only those firms certified by Palm Beach County at the time of solicitation due date are eligible to meet the established OEBO Affirmative Procurement Initiative (API). Please check the applicable box and list the dollar amount or percentage under the appropriate demographic category.
 - Modification of this form is not permitted and will be rejected upon submittal.

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All Subcontractors/subconsultants, including any tiered Subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: 2013531
 SOLICITATION/PROJECT NAME: Palmetto Park Road SW 7th Avenue to SW 5th Avenue

Prime Contractor: Ranger Construction Industries, Inc. Subcontractor: Caulfield & Wheeler, Inc.

(Check box(s) that apply)

☐ SBE ☐ WBE ☐ MBE ☐ M/WBE ☒ Non-S/M/WBE Date of Palm Beach County Certification (if applicable): _____

The undersigned affirms they are the following (select one from each column if applicable):

Column 1	Column 2	Column 3
<input checked="" type="checkbox"/> Male <input type="checkbox"/> Female	<input type="checkbox"/> African-American/Black <input type="checkbox"/> Asian American <input checked="" type="checkbox"/> Caucasian American	<input type="checkbox"/> Supplier
	<input type="checkbox"/> Hispanic American <input type="checkbox"/> Native American	

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any **S/M/WBE** participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Quantity/ Units	Contingencies/ Allowances	Total Price/Percentage
	Additional Survey Invoice #4444185 (2/9/23)	\$ 2 ,972.50	1 LS		\$ 2 ,972.50

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$ 2,972.50

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant

Price or Percentage:

Ranger Construction Industries, Inc.

Print Name of Prime

By: Jamie R Timming
Digitally signed by Jamie R Timming
 DN: cn=Jamie R Timming,
 o=Caulfield & Wheeler, ou=18783564F0000020DE6,
 ou=RANGER CONSTRUCTION INDUSTRIES, C=US
 Date: 2025.03.05 14:44:08-05'00'
 Authorized Signature

Jamie Timming

Print Name

Vice President

Title

Date: 03/05/2025

Caulfield & Wheeler, Inc.

Print Name of Subcontractor/subconsultant

By: [Signature]
 Authorized Signature

David Lindley

Print Name

Senior Vice President

Title

Date: 03/05/2025

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All Subcontractors/subconsultants, including any tiered Subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: **2013531**SOLICITATION/PROJECT NAME: **Palmetto Park Road SW 7th Avenue to SW 5th Avenue**Prime Contractor: **Ranger Construction Industries, Inc.** Subcontractor: **Anzac Contractors Inc**

(Check box(s) that apply)

☐ SBE ☐ WBE ☐ MBE ☐ M/WBE ☒ Non-S/M/WBE

Date of Palm Beach County Certification (if applicable): _____

The undersigned affirms they are the following (select one from each column if applicable):

Column 1**Column 2****Column 3**☒ Male ☐ Female☐ African-American/Black ☐ Asian American ☒ Caucasian American☐ Supplier☐ Hispanic American ☐ Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Quantity/ Units	Contingencies/ Allowances	Total Price/Percentage
	Claim Cost No. 5 - Underground Obstructions	\$ 184,165.06	1 LS		\$ 184,165.06
	Claim Cost No. 6 - FPL Conflict with Pile Installation	\$ 35,173.90	1 LS		\$ 35,173.90

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: **\$ 219,338.96**

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant

Price or Percentage: _____

Ranger Construction Industries, Inc.

Print Name of Prime

By: **Jamie R Timming**

Authorized Signature

Jamie Timming

Print Name

Vice President

Title

Date: **3/05/2025****Anzac Contractors Inc**

Print Name of Subcontractor/subconsultant

By: 

Authorized Signature

STEVEN R. MCNAMARA, PRES.


Print Name

Title

Date: **3/5/25**

Revised 09/17/2019

OEBO Agenda Review and Briefing – SBE Participation

COMMISSION MEETING DATE:	TBD
DEPARTMENT:	Engineering and Public Works
AGENDA ITEM: 3C	2013531-Palmetto Park Road SW 7 th Ave. to SW 5 th Ave
WAIVER REQUEST APPROVAL/DENIAL:	N/A
GOAL SETTING API	20% SBE min mandatory
PROPOSED SBE PARTICIPATION: - Work/Task/Change Order? _____	20.3% SBE (commitment) Proposed amount for C.O.#6 is 0%
CUMULATIVE CONTRACT SBE PARTICIPATION:	18.51%
CONTRACTOR:	Ranger Construction Industries, Inc.
SBE SUBCONTRACTOR(S):	Pathway and TCLM
CONCERN:	Initial Contractor was Hardrives of Delray, Inc. who has since sold their business and no longer exists, committed to 20% SBE participation. Ranger inherited this participation commitment and their team. According to the department, this was an unforeseen change order, which significantly depleted their prior on track SBE participation.
Reviewed by and date: 	Angela Smith (March 13, 2025)



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
3/23/2025

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER George H. Friedlander Company 1566 Kanawha Blvd. E. Charleston WV 25311		CONTACT NAME: William Phelps PHONE (A/C, No. Ext): 321-254-8477 FAX (A/C, No): 321-988-0209 E-MAIL ADDRESS: billphelps@friedlandercompany.com		
INSURED Ranger Construction Industries, Inc. 1645 N Congress Avenue West Palm Beach FL 33409		INSURER(S) AFFORDING COVERAGE		NAIC #
		INSURER A : Charter Oak Fire Insurance		25615
		INSURER B : Travelers Indemnity Company		25658
		INSURER C : Travelers Property & Casualty		25674
		INSURER D :		
		INSURER E :		
		INSURER F :		

COVERAGES **CERTIFICATE NUMBER:** 2061915885 **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSD	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR <input checked="" type="checkbox"/> Contractual Liab GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC OTHER:	Y	Y	CO-5807B217-25	4/1/2025	4/1/2026	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 500,000 MED EXP (Any one person) \$ 10,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COMP/OP AGG \$ 2,000,000 \$
B	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input type="checkbox"/> OWNED AUTOS ONLY <input checked="" type="checkbox"/> HIRED AUTOS ONLY <input type="checkbox"/> SCHEDULED AUTOS <input checked="" type="checkbox"/> NON-OWNED AUTOS ONLY	Y	Y	CAP-5807B186-25	4/1/2025	4/1/2026	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ \$
C	<input checked="" type="checkbox"/> UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR <input type="checkbox"/> EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED RETENTION \$	Y	Y	CUP-5809B407-25	4/1/2025	4/1/2026	EACH OCCURRENCE \$ 5,000,000 AGGREGATE \$ 5,000,000 \$
A	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below	Y/N N	N/A	UB-8L888782-25	4/1/2025	4/1/2026	<input checked="" type="checkbox"/> PER STATUTE <input type="checkbox"/> OTH-ER E.L. EACH ACCIDENT \$ 1,000,000 E.L. DISEASE - EA EMPLOYEE \$ 1,000,000 E.L. DISEASE - POLICY LIMIT \$ 1,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)
Project: Palmetto Park Road from SW 7th Ave to SW 5th Ave - PBC Proj. #2013531
Palm Beach County Board Of County Commissioners, a Political Subdivision of the State of Florida, its officers, employees and agents are Additional Insured when required by written contract with respect to work performed for them by the Named Insured and at the specified project. Underground explosion/collapse (XCU) coverage and amended Watercraft liability exclusion is included. A Waiver of Subrogation for Workers Compensation coverage is included. Excess policies shown in certificate are follow form over the General Liability, Automobile Liability and Employers Liability. Should any of the above described policies be cancelled before the expiration date thereof, the issuing insurer will mail 30 days written notice to the certificate holder, but failure to do so shall impose no obligation or liability of any kind upon the insurer, its agents or representatives.

CERTIFICATE HOLDER Palm Beach County 2300 N. Jog Road, Suite 3W-33 West Palm Beach FL 33411	CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE
---	--

CERTIFICATE OF RESOLUTION

The undersigned hereby certifies that the following are true and correct statements:

1. That the undersigned is the Secretary/Treasurer (insert title) of Ranger Construction Industries, Inc. (insert business name) a Corporation (insert business organization, i.e. corporation, LLC, LLP), organized and existing in good standing under the laws of the State of Florida (Firm), and that the following Resolutions are true and correct Resolutions adopted by the Board of Directors (insert form of management) of the Firm on the 13 day of July, 2021, in accordance with the laws of the State of Florida (where Firm is organized) of the Firm, and the articles of incorporation (governing documents) of the Firm.

RESOLVED, that the Firm shall enter into that certain Contract between Palm Beach County, a political subdivision of the State of Florida, and the Firm, a copy of which is attached hereto, and be it

FURTHER RESOLVED, that Jamie Timming, the Vice President of the Firm, is hereby authorized and instructed to execute such Contract and such other instruments as may be necessary and appropriate for the Firm to fulfill its obligations under the Contract.

2. That the foregoing Resolutions have not been modified, amended, rescinded, revoked or otherwise changed and remain in full force and effect as of the date hereof.

3. That the Firm is in good standing under the laws of the State of Florida or its state of formation, as provided above, and has qualified, if legally required, to do business in the State of Florida and has the full power and authority to enter into such Contract.

IN WITNESS WHEREOF, the undersigned has set his/her hand and affixed the Seal of the Firm the 31st day of Aug, 2021.

(SEAL)


Douglas Browning
(Signature)
Douglas Browning, Secretary/Treasurer
(Print Name and Title)

STATE OF Florida
COUNTY OF Palm Beach

The foregoing instrument was acknowledged before me by means of ☒ physical presence or ☐ online notarization, this 31st day of August, 2021, by Douglas Browning (name) as Secretary/Treasurer (title) for Ranger Construction Industries, Inc. (firm), on behalf of the (choose one) corporation / company / partnership, who is ☒ personally known to me or ☐ has produced _____ (type of identification) as identification.

(Stamp/Seal)

Michelle Dryden
(Notary Signature)
Notary Public, State of _____
(Print Notary Name)



Commission Number _____
My Commission Expires _____

CC-1

Exhibit E (page 1 of 1)

PALM BEACH COUNTY PROJECT: Palmetto Park Road, SW 7th Avenue to SW 5th Avenue, 2013531									
		COUNTY ENGINEER		C.R. COMMITTEE		TOTAL DEPT. & C.R.C. APPROVALS		BOARD OF CO. COMM.	
C.O. #	DATE APPROVED	AMOUNT	TIME	AMOUNT	TIME	AMOUNT	TIME	AMOUNT	TIME
1	1/25/2023			21,008.79	10				
2	4/11/2023	35,980.54	3						
3	7/19/2023	15,249.84	1						
4	4/10/2024			0.00	34				
5	6/5/2024			38,026.92	21				
6	Pending							587,939.25	540
	TOTAL	51,230.38	4	59,035.71	65	110,266.09	69	587,939.25	540
	CUMULATIVE TOTAL	51,230.38	4	59,035.71	65	110,266.09	69		
	As of PPM CW-F-050 Dated November 16, 2024	SINGLE AMT. \$100,000.00 MAX. TIME \$375,000.00 or 10% of contract When Change Orders exceed \$375,000.00 or 10% of contract, must submit a "Receive and File" to the BCC. 10% of this Contract is _____	MAX. TIME 180 DAYS When Change Orders exceed 180 days, must submit a "Receive and File" to the BCC.	SINGLE AMT. \$200,000.00 MAX. AMT. \$375,000.00 or 10% of contract When Change Orders exceed \$375,000.00 or 10% of contract, must submit a "Receive and File" to the BCC. 10% of this Contract is _____	MAX. TIME 180 DAYS When Change Orders exceed 180 days, must submit a "Receive and File" to the BCC.	MAXIMUM CUMULATIVE CO ENG. & C.R.C. \$375,000.00 or 10% of contract When Change Orders exceed \$375,000.00 or 10% of contract, must submit a "Receive and File" to the BCC. 10% of this Contract is _____	MAX. CUM. CO ENG. & C.R.C. 180 DAYS When Change Order exceeds 180 days, must submit a "Receive and File" to the BCC	OVER \$200,000.00	OVER 180 DAYS
