

34-3

Agenda Item #:

**PALM BEACH COUNTY
BOARD OF COUNTY COMMISSIONERS
AGENDA ITEM SUMMARY**

Meeting Date: August 19, 2008

Consent

Regular

Workshop

Public Hearing

Department: Facilities Development and Operations

I. EXECUTIVE BRIEF

Motion and Title: Staff recommends motion to approve: Change Order No. 26 to the Contract with The Weitz Company, Inc., (R2003-1542) in the amount of \$77,349 for South County Regional Park Phase III.


Summary: Change Order No. 26 is for the cost of amphitheater grass seating area enhancements. The enhancements include upper seating area aeration, top dressing and rye seeding and lower seating under drain system, top soil and Bermuda sodding. These enhancements are needed to improve drainage of the flat grass areas adjacent to the stage and seating area. Although the engineer designed the area to comply with normal drainage criteria, a quick-dry and more efficient drainage system was requested to allow the seating area to be functional within hours rather than days so as not to delay or cancel scheduled activities at the amphitheater. The inadequate drainage was only discovered post-construction. These services have been completed prior to Board consideration. Change Order No. 26 must be approved by the Board of County Commissioners because this change order, when combined with previous approval would exceed the combined authority of the Contract Review Committee and Department Director for cost. There is no SBE participation for this Change Order. The SBE goal for this project is 15%. When combined with previous Change Orders, the participation to date is 19.6%. (Capital Improvements Division) District 5 (JM)

Background and Justification: On September 23, 2003, the Board entered into an annual contract with The Weitz Company, Inc., for construction management services. Amendment No. 7 (R2006-1181) authorized Weitz to provide for construction of an amphitheater, golf course support buildings, picnic pavilions, comfort station, entrance road and infrastructure improvements to Parcel A of the South County Regional Park. The seating area enhancements are needed to improve drainage of the flat grass areas adjacent to the stage.

Attachment:

1. Location Map
2. Budget Availability Statement
3. Change Order No. 26

Recommended by:

 Amy Wolf
Department Director

7/26/08
Date

Approved by:


County Administrator

8/8/08
Date

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

Fiscal Years	2008	2009	2010	2011	2012
Capital Expenditures	<u>\$77,349</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
Operating Costs	<u> </u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
External Revenues	<u> </u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
Program Income (County)	<u> </u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
In-Kind Match (County)	<u> </u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
NET FISCAL IMPACT	<u>\$77,349</u>	<u> </u>	<u> </u>	<u> </u>	<u> </u>
# ADDITIONAL FTE	<u> </u>	<u> </u>	<u> </u>	<u> </u>	<u> </u>
POSITIONS (Cumulative)	<u>0</u>	<u> </u>	<u> </u>	<u> </u>	<u> </u>

Is Item Included in Current Budget? Yes No

Budget Account No: Fund 3603 Dept 581 Unit P462 Object 6520
Reporting Category

B. Recommended Sources of Funds/Summary of Fiscal Impact:


III. REVIEW COMMENTS:

A. OFMB Fiscal and/or Contract Development and Control Comments:


Atirelhit 8.1.08
88 OFMB
8/1/08  CW
7/31/08

Don J. Jacob 8/4/08
Contract Administrator
E. Jans 8/4/08

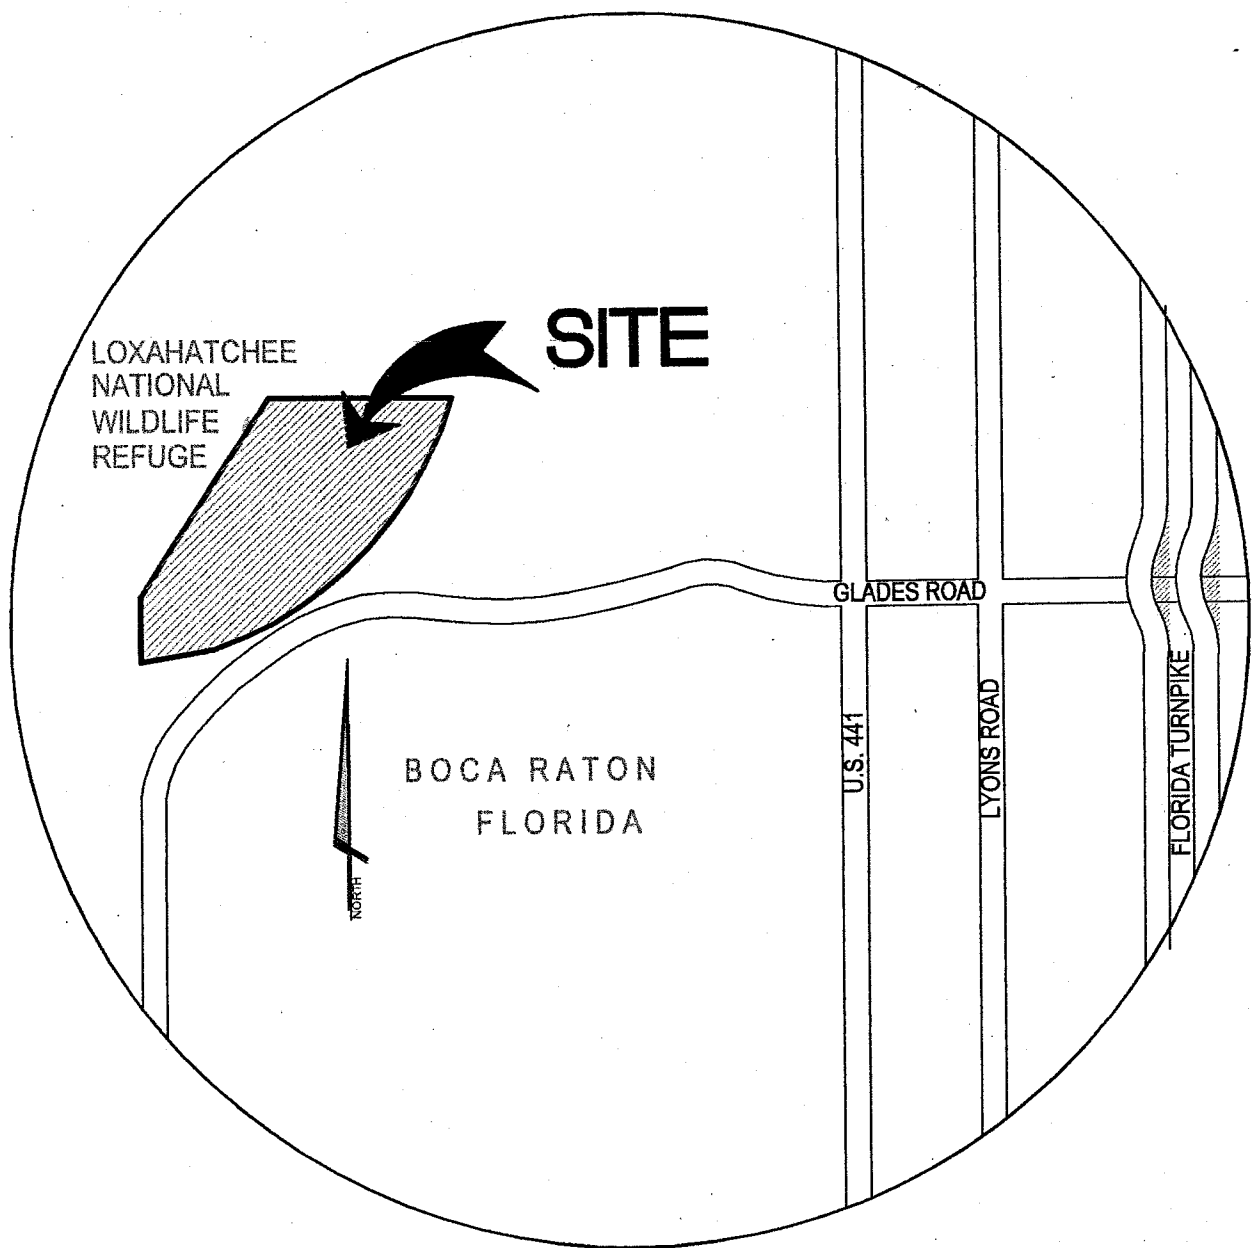
B. Legal Sufficiency:


Assistant County Attorney

C. Other Department Review:


Department Director

This summary is not to be used as a basis for payment.



LOCATION MAP

S14,15+22 T47S R41E N.T.S.

ATTACHMENT # 1

FACILITIES DEVELOPMENT & OPERATIONS BUDGET AVAILABILITY STATEMENT

REQUEST DATE: 06/24/08

REQUESTED BY: Dave Dolan

PHONE: 233-0280

FAX: 233-0270

PROJECT TITLE: South County Regional Park Parcel III

PROJECT NO.: 05215

ORIGINAL CONTRACT AMOUNT: \$17,996,464.00

BCC RESOLUTION#: _____
DATE: _____

REQUESTED AMOUNT: \$77,349.00

CSA or CHANGE ORDER NUMBER: CO #26

CONSULTANT/CONTRACTOR: The Weitz Company

PROVIDE A BRIEF STATEMENT OF THE SCOPE OF SERVICES TO BE PROVIDED BY THE CONSULTANT/CONTRACTOR:

CCP #142R3: Amphitheater grass seating area enhancements including; aeration, top dress and rye grass seeding of upper seating area and under drain system, top soil and Bermuda grass of lower seating area. These two areas will also be maintained by mowing and fertilization for 60 days.....\$77,349.00

CONSTRUCTION	\$77,349.00
PROFESSIONAL SERVICES	_____
STAFF COSTS** (DESIGN / CONST. PHASE)	_____
MISC. (permits, prints, advertising, etc)	_____
TOTAL	\$77,349.00

** By signing this BAS your department agrees to these staff costs and your account will be charged upon receipt of this BAS by FD&O. Unless there is a change in the scope of work, no additional staff charges will be billed.

BUDGET ACCOUNT NUMBER (IF KNOWN)

FUND: 3603

DEPT: 581

UNIT: P462

OBJ: 6504

FUNDING SOURCE (CHECK ALL THAT APPLY):

AD VALOREM OTHER

FEDERAL/DAVIS BACON

CSW

BAS APPROVED BY: _____



DATE: _____

ENCUMBRANCE NUMBER: _____

FUNDING SOURCE(S)	
<input type="checkbox"/>	Bond
<input checked="" type="checkbox"/>	Impact Fees
<input type="checkbox"/>	Park Improvement Fund
<input type="checkbox"/>	Ad Valorem
<input type="checkbox"/>	Other

BAS APPROVAL	
<input checked="" type="checkbox"/>	FULLY FUNDED WITHIN CURRENT BUDGET <i>CSW</i>
<input type="checkbox"/>	FULLY FUNDED PENDING BUDGET TRANSFER _____

ATTACHMENT # 2

CHANGE ORDER BRIEF
SOUTH COUNTY REGIONAL PARK PHASE III
PROJECT NO. 05215
JUNE 10, 2008

Prime Contractor..... The Weitz Company, Inc.
Change Order No.....26
Change Order Amount.....\$77,349.00
Changed Contract Time.....0 calendar days

Description of CCP's:

CCP #142R3: Amphitheater grass seating area enhancements including; aeration, top dress and rye grass seeding of upper seating area and under drain system, top soil and Bermuda grass of lower seating area. These two areas will also be maintained by mowing and fertilization for 60 days.....\$77,349.00

Explanation and Reason-for-Change Code:

1. CCP #142R3: O Parks Department staff requested these post-construction modifications.

Reason-for-change codes

D = Differing Site Conditions

E = Errors/Omissions in Design

O = Owner-Initiated

Q = Quantity Adjustments


R = Request by another Agency/Outside Party

X = Other (Specify:)

Z = Zoning/Code/Ordinance Change

Estimated premium value of errors/omissions for this change order: \$0.00

SUBMITTED:

David G. Dolan/cra 7/24/08
David G. Dolan, Project Manager  Date
Capital Improvements Division

ATTACHMENT # 3

CHANGE ORDER HISTORY
SOUTH COUNTY REGIONAL PARK PHASE III
PROJECT #05215

CO #	Description	Date Approved	Sales Tax Recovery Approved to Date	Amount Approved by Director	Amount Approved by CRC	Amount Approved by BCC	Days Approved by Director	Days Approved by CRC	Days Approved by BCC	Code
1	CCP #1 - Haul and stockpile top soil	10/3/2006		33,189.00			0			Owner Initiated
2	Sales Tax Recovery for CCP #3,7,8,9	10/29/2006	-246,425.32							Sales Tax Savings Program
3	Sales Tax Recovery for CCP #4,5, & 13	11/14/2006	-266,785.91							Sales Tax Savings Program
4	Sales Tax Recovery for CCP #6,12,15,18	12/11/2006	-219,210.60							Sales Tax Savings Program
5	Sales Tax Recovery for CCP #10	12/22/2006	-35,940.87							Sales Tax Savings Program
6	Sales Tax Recovery for CCP #43, 47 & 52	3/12/2007	-615,240.00							Sales Tax Savings Program
7	Sales Tax Recovery for CCP #49, 53 & 56	3/21/2007	-109,465.75							Sales Tax Savings Program
8	Sales Tax Recovery for CCP #67	4/9/2007	-116,702.05							Sales Tax Savings Program
9	Sales Tax Recovery for CCP #72 & 73	5/4/2007	-128,056.80							Sales Tax Savings Program
10	CCP #21, 22R,23,25,26,27,28,29,30R,31,32,33,34,35, 36,37,38,39,41,44,46,47,50R,51R,59 for a total of \$1,158,501.87	6/19/2007		0.00						
11	Sales Tax Recovery for CCP #83 & 85	7/2/2007	-90,487.50							Sales Tax Savings Program
12	Sales Tax Recovery for CCP #45R,54R,58,60,61,63R, 64R, 65,66,69,70,71,74,76,78,79,81,82 and 84	8/22/2007		0.00						
13	CCP #116	8/29/2007	-6,675.70							Sales Tax Savings Program
14	CCP #080R (reduce construction contingency by \$52,500)	9/26/2007		0.00			21			Differing Site Conditions/Request by Another Agency
15	CCP #106	10/3/2007			0.00			22		Errors/Omission in Design
16	CCP #024,077,087,088,089R, 092,093,094R,095,096,098,100,101R,103R, 105,110,111R,113,114 and 118	10/5/2007		0.00						Owner Initiated, Errors/Omission in Design
17	CCP #109 - Add additional light fixtures around dressing room mirrors	10/24/2007		19,353.54						Owner Initiated

CHANGE ORDER HISTORY
 SOUTH COUNTY REGIONAL PARK PHASE III
 PROJECT #05215

18	CCP #108R3	11/28/2007		0.00			9		Errors/Omission in Design	
19	CCP #107R3	11/27/2007			0.00			68	Owner Initiated	
20	CCP #18, 62, 68, 86R3, 115, 116, 119, 121, 122, 123R, 124, 126, 131, 132, 135, 136	11/28/2007		0.00			0		Owner Initiated, Errors/Omission in Design	
21	CCP #99R	12/3/2007		45,144.13					Owner Initiated	
22	CCP #128	12/18/2007				597.20			Differing Site Conditions	
23	CCP #138	12/29/2007	-23,037.26						Sales Tax Savings Program	
24	Reconciliation of DPO's	3/31/2008	28,247.36						Sales Tax Savings Program	
25	CCP #143R & 144	5/21/2008			52,797.10				Owner Initiated	
26	CCP #142R3	Pending				77,349.00				
				TOTAL #APPROVED TO DATE FOR SALES TAX RECOVERY	TOTAL \$ BY DIR	TOTAL \$ BY CRC	TOTAL \$ BY BCC	TOTAL DAYS BY DIR	TOTAL DAYS BY CRC	TOTAL DAYS BY BCC
			Totals	-1,829,780.40	\$97,686.67	\$52,797.10	\$77,946.20	30	90	25
					DIR + CRC DOLLARS TO DATE			DIR + CRC TOTAL DAYS TO DATE		
						\$150,483.77			120	
	ORIGINAL CONTRACT PRICE		17,996,464.00							
	PREVIOUS CHANGE ORDERS (THRU 25)		151,080.97							
	PREVIOUS SALES TAX C.O.'S		-1,829,780.40							
	THIS CHANGE ORDER (26)		77,349.00							
	ADJUSTED CONTRACT PRICE		16,395,113.57							

PALM BEACH COUNTY

CHANGE ORDER

ISSUED TO: The Weitz Company 1720 Centrepark Drive East West Palm Beach, FL 33401	CHANGE ORDER NO.: 26
PROJECT: South County Regional Park Phase III	REFERENCE CCP NO.: 142R3
PROJECT NO. 05215	RESOLUTION NO.: R2003-1542 (R2006-1181)
	DISTRICT NO.: 5

The completion date, contract price, and all terms, covenants, and conditions of the above referenced contract, except as duly modified by this and previous Change Orders, if any, shall remain in full force and effect.

DESCRIPTION OF CHANGE:

1. CCP #142R3: Amphitheater grass seating area enhancements including; aeration, top dress and rye grass seeding of upper seating area and under drain system, top soil and Bermuda grass of lower seating area. These two areas will also be maintained by mowing and fertilization for 60 days. \$77,349.00

CONTRACT PRICE

Original Contract Price:	\$17,996,464.00
Previous Change Orders:	\$151,080.97
Previous Sales Tax C.O.'s	(\$1,829,780.40)
This Change Order No. <u>26</u> :	\$77,349.00
ADJUSTED Contract Price:	\$16,395,113.57

COMPLETION DATE

Contract Completion Date will be increased by 0 calendar days

Contract Notice to Proceed Date: 07/07/06

Contract Substantial Completion Date: 12/07/07

ADJUSTED Substantial Completion Date: N/A

CONTRACTOR
Execution of this change order acknowledges final settlement of, and releases, all claims for costs and time associated, directly or indirectly, with the above stated modification(s), including all claims for cumulative delays or disruptions resulting from, caused by, or incident to such modifications(s), and including any claim that the above stated modification(s) constitutes, in whole or part, a cardinal change to the contract. The above changes are accepted:

The Weitz Company
Contractor

By: [Signature]
Title: Sr. P.M. Date: 7/1/08

DESIGN PROFESSIONAL
The above changes are recommended for approval by the Owner:

Heller Weaver & Sheremeta, Inc.
Design Professional

By: [Signature]
Title: PRVS mbr Date: 6/25/08

PALM BEACH COUNTY
Recommended By:

By: [Signature]
Title: Project Manager Date: 7/24/08

By: [Signature]
Title: Director - CID Date: 7/24/08

By: [Signature]
Title: Director, FD&O Date: 7/23/08

By: _____
Legal Sufficiency - CAO Date: _____

Approved By:
By: _____
Addie L. Greene
Title: Chairperson, BCC Date: _____

PALM BEACH COUNTY

CONSTRUCTION CHANGE PROPOSAL (CCP)

TO: Palm Beach County
Capital Improvements Division

ATTENTION: David Dolan

REFERENCE: Owner Change Order

CCP NUMBER: 142 R 3
DATE: 6/4/2008
PROJECT NAME: South County Regional Park III
PROJECT NUMBER: 05215
CONTRACT NUMBER: R2003-1542 (R2006-1181)

We propose to accomplish the MODIFICATIONS identified in FIELD BULLETIN FB # N/A and as described herein. Except as modified below, the original contract and all prior amendments shall remain in full force and effect.

DESCRIPTION: Sports Turf One – Amphitheater Seating Area Re-work:

- 1) Remove & Replace Sod and Topsoil.
- 2) Install Advantage Edge Drainage System
- 3) 60 days of Maintenance

PROPOSED CONTRACT PRICE CHANGE (increase) \$77,349

PROPOSED CONTRACT TIME CHANGE (unchanged) 0 days

PROPOSED NEW SUBSTANTIAL COMPLETION NA date

DISTRIBUTION:

FROM: The Weitz Company
CONTRACTOR

SIGNED: _____

DATE: _____



**BUILD IN
GOOD COMPANY.**

Construction Change Proposal

TWC, Detailed, Grouped by Number

Page 1 of 1

SOUTH CTY REG. PARK PHASE III

Project # F106000

12551 Glades Road
Boca Raton, FL 33428

Tel: Fax:

Directive Number: 124

Date Created: 2/10/2008

THE WEITZ COMPANY-FLORIDA is hereby directed to make the following change(s) in this contract:

Sports Turf - Sports Turf and Added Drainage @ Amp Seating Area

Description:

Itemized Details:					
Budget Code	Description	QTY	UOM	Unit Price	Est Amt
0.321200__2500	Asphalt Paving - H & J/Centerline - Add drainage @ amphitheater seating area. VOID - Work performed by Sports Turf.	1.00		\$0	\$ 0
0.328000__2500	Rework Amphitheater Seat - Sports Turf - Furnish & install additional horizontal drainline near sidewalk @ amphitheater.	1.00		\$3,323	\$ 3,323
0.328000__2500	Sports Turf re-work @ amphitheater	1.00		\$67,773	\$ 67,773
00.011505__2450	General Liability 0.98%	1.00		\$708	\$ 708
00.011570__2450	Subguard 1.5%	1.00		\$1,094	\$ 1,094
00.011560__2450	Performance Bond 0.65%	1.00		\$462	\$ 462
00.011510__2450	Builders Risk 0.92%	1.00		\$658	\$ 658
00.011501__2450	Construction Fee 4.5%	1.00		\$3,331	\$ 3,331
				Total: \$	77,349

Proposed Adjustments

1. The proposed basis of adjustment to the Contract Sum or Guaranteed Maximum Price is:

- Lump Sum increase of \$77,349
- Unit Price of _____ per _____
- As provided in Subparagraph 7.3.6 of AIA Document A201, 1997 Edition.
- Time and Material not to exceed _____
- as follows:

2. The Contract Time as a result of this work will be unchanged.
 3. Approval Required by _____ in order to not delay the project.

Upon execution by the Architect and Owner, this directive shall be effective immediately.

 ARCHITECT
 Address: _____
 By: _____
 Date: _____

 OWNER
 Address: _____
 By: _____
 Date: _____



SPORTS TURF ONE INC.
 9819 STATE ROAD 7
 BOYNTON BEACH, FL 33472
 561-369-7994 OFFICE
 561-364-1118 FAX

Estimate

Date	Estimate #
2/28/2008	2008-360

Name / Address
The Weitz Company LLC 4000 Hollywood Blvd Suite 120N Hollywood, FL 33021

Terms	Rep	Contact	Phone	Fax
Net 30	DH	Joe Whalen.	687-4830	681-3348

Description	Qty	Cost	Total
SOUTH COUNTY REGIONAL PARK IN BOCA RATON, FLORIDA REFERENCE ESTIMATE #2008-356 DATED 2/19/2008 DRAINLINES: ADD HORIZONTAL DRAINLINES NEAR SIDEWALKS LABOR, MATERIAL AND EQUIPMENT LUMP SUM:		3,323.00	3,323.00
Thank you for your business.		Total	\$3,323.00

SIGNING THIS PROPOSAL ACKNOWLEDGES ACCEPTANCE OF PRICE,
 TERMS & CONDITIONS.
 DATE _____

Signature _____



SPORTS TURF ONE INC.
 9819 STATE ROAD 7
 BOYNTON BEACH, FL 33472
 561-369-7994 OFFICE
 561-364-1118 FAX

Estimate

Date	Estimate #
2/19/2008	2008-356

Name / Address
The Weitz Company LLC 4000 Hollywood Blvd Suite 120N Hollywood, Fl. 33021

Terms	Rep	Contact	Phone	Fax
Net 30	DH	Joe Whalen.	687-4830	681-3348

Description	Qty	Cost	Total
JOB NAME:SOUTH COUNTY REGIONAL PARK IN BOCA RATON			
TURFGRASS RENOVATION SERVICES- OPTION			
A			
COMPLETE REMOVAL & REPLACEMENT OF THE LOWER BERMUDA TURF AREA AS FOLLOWS:			
REMOVE SOD & EXISTING HEAVY TOP SOIL & STOCKPILE IN PARKING LOT FOR DISPOSAL. PREPARE A 6" SUBGRADE. PRICE PER SQ FOOT.	25,500	0.28	7,140.00
LOWER LAWN AREA- DRAINAGE... LAYOUT & INSTALL A COMPLETE ADS ADVANTAGE EDGE DRAINAGE SYSTEM. INCLUDES A MAIN TRUNK LINE & LATERALS ON 20' CENTERS. PRICE PER LUMP SUM.	1	14,400.00	14,400.00
INLET WORK: CORE HOLES IN EXISTING CONCRETE INLETS- INSTALL PVC PIPE SLEEVE & MUD UP CONNECTIONS. EXCAVATE AROUND BASINS & ADD PEAROCK TO A DEPTH OF 3'. PRICE PER EACH.	2	973.35	1,946.70
IMPORT & PLACE A 6" OF 80/20 CUSTOM BLENDED USGA TOPSOIL MIX. PRICE PER SQ FOOT.	25,100	1.0384	26,063.84
PRICING VALID FOR 10 DAYS. PLEASE SIGN, DATE AND RETURN PROPOSAL FOR SCHEDULING. THANK YOU.		Total	

SIGNING THIS PROPOSAL ACKNOWLEDGES ACCEPTANCE OF PRICE, TERMS & CONDITIONS.
 DATE _____

Signature _____



SPORTS TURF ONE INC.
 9819 STATE ROAD 7
 BOYNTON BEACH, FL 33472
 561-369-7994 OFFICE
 561-364-1118 FAX

Estimate

Date	Estimate #
2/19/2008	2008-356

Name / Address
The Weitz Company LLC 4000 Hollywood Blvd Suite 120N Hollywood, Fl. 33021

Terms	Rep	Contact	Phone	Fax
Net 30	DH	Joe Whalen.	687-4830	681-3348

Description	Qty	Cost	Total
SOD REPLACEMENT- DELIVER & INSTALL NEW BERMUDA GRASS SOD. ROLL WITH A SOD ROLLER PRICE PER LUMP SUM.	25,100	0.4185	10,504.35
UPPER TURF AREA: AERIFY & ROLL UPPER AREA WITH A 5 TON SOD ROLLER . PER TRIP .	1	405.00	405.00
MAINTENANCE SERVICES: OVERSEEDING ALL THE BERMUDA WITH RYEGRASS SEED FOR DEEP GREEN COLOR. SEED AT THE RATE OF 10 LBS. PER 1000 SQ. FEET. PRICE PER LUMP SUM.	1	2,372.50	2,372.50
FERTILIZER APPLY 3-7-7- ORGANIC FERTILIZER PER MANUFACTURERS RECOMMENDATIONS. PRICE PER LUMP SUM.	1	315.00	315.00
FERTILIZER.....15-5-15 BROADCAST PER MANUFACTURERS RECOMMENDATIONS. PRICE PER LUMP SUM.	1	270.00	270.00
MAINTENANCE INCLUDING MOWING- TRIMMING WITH REEL MOWERS. PROGRAM IRRIGATION. PRICE PER MONTH.	2	1,380.00	2,760.00
PRICING VALID FOR 10 DAYS. PLEASE SIGN, DATE AND RETURN PROPOSAL FOR SCHEDULING. THANK YOU.		Total	

SIGNING THIS PROPOSAL ACKNOWLEDGES ACCEPTANCE OF PRICE, TERMS & CONDITIONS.
 DATE _____

Signature _____



SPORTS TURF ONE INC.
 9819 STATE ROAD 7
 BOYNTON BEACH, FL 33472
 561-369-7994 OFFICE
 561-364-1118 FAX

Estimate

Date	Estimate #
2/19/2008	2008-356

Name / Address
The Weitz Company LLC 4000 Hollywood Blvd Suite 120N Hollywood, FL 33021

Terms	Rep	Contact	Phone	Fax
Net 30	DH	Joe Whalen.	687-4830	681-3348

Description	Qty	Cost	Total
SAND TOPDRESSING-OF LOWER TURF AREA WITH MANUFACTURED SAND SPREAD AT THE RATE OF 23 TONS PER ACRE. DRAG OR BROOM SAND INTO TURF AS APPROPRIATE. PRICE PER ACRE. PLEASE NOTE THAT DESPITE OUR BEST EFFORT TO THE CONTRARY, SOME DAMAGE TO THE IRRIGATION SYSTEM IS UNAVOIDABLE. THE RESPONSIBILITY FOR THESE REPAIRS IS THAT OF OTHERS AND THEREFORE NOT INCLUDED ION THIS PROPOSAL. EXCLUSIONS: NO PLANS, PERMITS, TESTING, SURVEY, IRRIGATION, FUMIGATION, CONDITIONERS, SOIL AMMENDMENTS, FILL DIRT, TOP DRESSING, OR OFF SITE HAULING. NOT RESPONSIBLE FOR UNMARKED UTILITIES. ALTERNATES, NOT INCLUDED IN BID PROPOSAL PRICING: HAUL AWAY SOD & SOIL SURPLUS- \$12,700.00 ADDITIONAL.	1	1,596.00	1,596.00
			0.00
			0.00
PRICING VALID FOR 10 DAYS. PLEASE SIGN, DATE AND RETURN PROPOSAL FOR SCHEDULING. THANK YOU.			Total \$67,773.39

SIGNING THIS PROPOSAL ACKNOWLEDGES ACCEPTANCE OF PRICE, TERMS & CONDITIONS.
 DATE _____

Signature _____

SCHEDULE 1

LIST OF PROPOSED SBE-MWBE SUBCONTRACTORS
CHANGE ORDER WORK

PROJECT NAME: South County Regional Park III PROJECT NO. 05215

NAME OF GENERAL CONTRACTOR: The Weitz Company CONTACT PERSON: Bernie Potere PHONE NO: (561) 242-3575

CCP #: 142R3 (Change Order No. 26)

PLEASE IDENTIFY ALL APPLICABLE CATEGORIES OF SUBCONTRACTORS

Name, Address and Phone Number	(Check one or both Categories)		Subcontract Amount				
	Minority Business	Small Business	Black	Hispanic	Women	Caucasian	Other (Please Specify)
1.	<input type="checkbox"/>	<input type="checkbox"/>	\$	\$	\$	\$	\$
2.	<input type="checkbox"/>	<input type="checkbox"/>	\$	\$	\$	\$	\$
3.	<input type="checkbox"/>	<input type="checkbox"/>	\$	\$	\$	\$	\$
4.	<input type="checkbox"/>	<input type="checkbox"/>	\$	\$	\$	\$	\$
5.	<input type="checkbox"/>	<input type="checkbox"/>	\$	\$	\$	\$	\$
(Please use additional sheets if necessary)			Total \$	\$	\$	\$	\$

Change Order Price \$ 77,349.00

Total Value of SBE Participation \$ 0

MWBE Participation \$ 0
