

**PALM BEACH COUNTY
BOARD OF COUNTY COMMISSIONERS**

AGENDA ITEM SUMMARY

Meeting Date:	January 24, 2011	(X) Consent	() Regular
		() Workshop	() Public Hearing
Department			
Submitted By:	<u>Environmental Resources Management</u>		
Submitted For:	<u>Environmental Resources Management</u>		

I. EXECUTIVE BRIEF

Motion and Title: Staff recommends motion to:

A) approve Change Order No. 5 with The Murphy Construction Co. in the amount of \$78,076.90 and a time extension of forty-eight (48) days for additional work on the Dubois Park Redevelopment, Project No. 2009ERM10; and

B) adopt Resolution for the Clerk of the Board to disburse \$125,000 from the Vessel Registration Fee Trust Fund for the Dubois Reef Restoration Project; and

C) approve Budget Transfer of \$125,000 from reserves in the Environmental Enhancement Saltwater Fund (1224) to fund the Dubois Reef Restoration Project.

Summary: The BCC approved the Dubois Park Redevelopment Project No, 2009ERM10 on July 20, 2010. Change Order No. 5 will bring the cumulative contract amount to \$2,566,548.73 and will increase the contract time to 512 days. This Change Order will authorize required electrical work at the Dubois Pioneer Home Museum and the installation of additional rock along the Park's artificial reef in order to increase the structure's elevation. Change Order No. 5 reduces the total amount of Task 3.01 (Demolition & Miscellaneous Earthwork) for site restoration work not completed by the contractor. The Small Business Enterprise (SBE) participation of 17.34% as set forth in the Contract will be reduced to 16.48%. This change order requires BCC approval due to the fact that the net monetary increase, when combined with the value of the time extension in liquidated damages, exceeds the threshold established in PPM CW-O-050. The contract is funded from a combination of local, State and Federal grants, boater access bond funds and vessel registration fees, all non-ad valorem sources. The approval of the Budget Transfer will provide \$125,000 to cover the cost of the reef construction work order and other ancillary costs. District 1 (JM)

Background and Justification: The original Project included demolition of existing structures, installation of two bulkheads, dredging, and nine (9) fixed piers. Change Order No. 1 included replacement of a bulkhead, dredging, and construction of two fixed piers and a water taxi dock. Change Orders No. 2 & 3 approved the replacement of a failing wing wall within the project area and authorized the construction of a water taxi shelter, installation of boat lifts and the associated electrical work. Change Order No. 4 removed two tasks from the original contract that were not completed and added the relocation of a lifeguard tower and placement of additional rock and sand along the newly restored beach. Construction is expected to be completed on all portions of the project by February 2012.

Attachments:


1. Location Map
2. Change Order No. 5
3. Contract History
4. Budget Availability Statement
5. Resolution
6. Budget Transfer (1224)

Recommended by:


Department Director

1/5/12
Date

Approved by:


County Administrator

1/18/12
Date

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

Fiscal Years	2012	2013	2014	2015	2016
Capital Expenditures	\$125,000	_____	_____	_____	_____
Operating Costs	_____	_____	_____	_____	_____
External Revenues	_____	_____	_____	_____	_____
Program Income (County)	_____	_____	_____	_____	_____
In-Kind Match (County)	_____	_____	_____	_____	_____
NET FISCAL IMPACT	\$125,000	_____	_____	_____	_____
# ADDITIONAL FTE POSITIONS (Cumulative)	_____	_____	_____	_____	_____

Is Item Included in Current Budget? Yes _____ No X

Budget Account No.: Fund 1224 Department 380 Unit 3086 Object 3401

B. Recommended Sources of Funds/Summary of Fiscal Impact:

Environmental Enhancement Saltwater Fund (1224) reserves.

C. Department Fiscal Review:

JP

III. REVIEW COMMENTS

A. OFMB Fiscal and /or Contract Dev. and Control Comments:

OFMB

SB
1/11/2012

Contract Development and Control
1-17-12 B. Wheeler

Dr. J. Jacobson
1/17/12

B. Legal Sufficiency:

James C. Hays
1/19/12
Assistant County Attorney

This item complies with current
County policies.

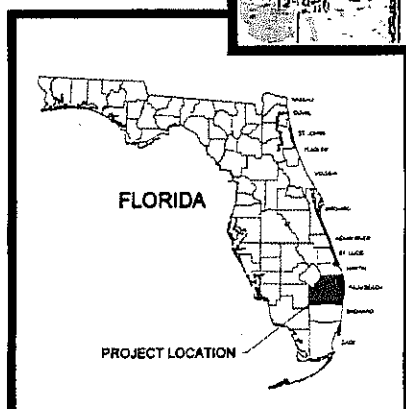
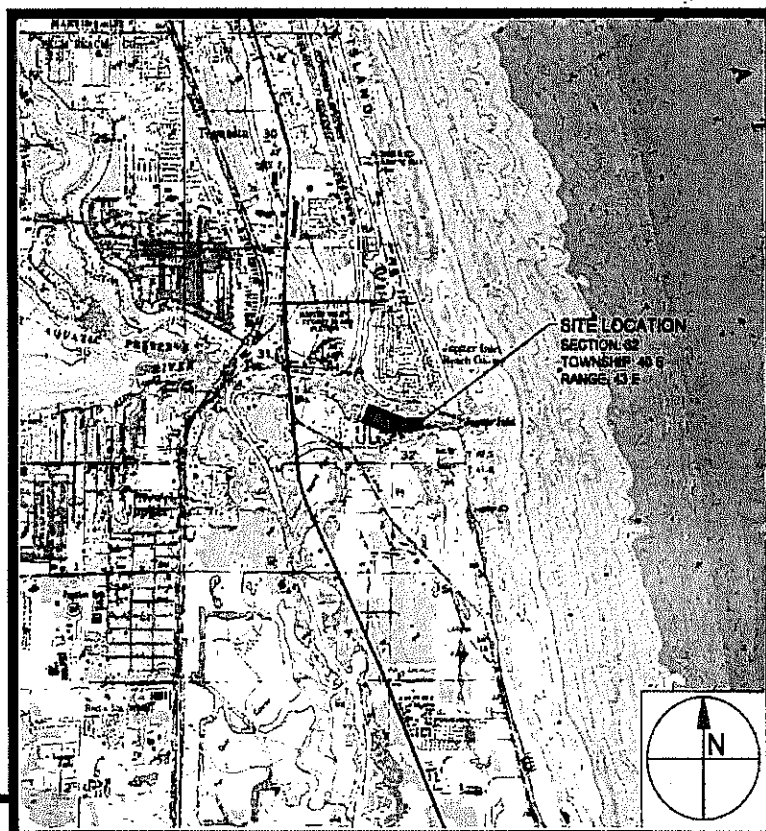
C. Other Department Review:

Department Director

DUBOIS PARK REDEVELOPMENT PROJECT

JUPITER INLET

PALM BEACH COUNTY, FL



Location Map

PALM BEACH COUNTY
DEPARTMENT OF ENVIRONMENTAL RESOURCES MANAGEMENT
2300 NORTH JOG ROAD, 4TH FLOOR
WEST PALM BEACH, FL 33411



CHANGE ORDER NO.: 5

(Mark applicable category:)

<input checked="" type="checkbox"/> Owner Initiated	<input type="checkbox"/> Quantity Overruns/Underruns
<input type="checkbox"/> Differing Site Conditions	<input type="checkbox"/> Request By Another Agency/Outside Party
<input type="checkbox"/> Zoning/Code/Ordinance Changes	<input type="checkbox"/> A. Reimbursable
<input type="checkbox"/> Errors/Omissions/In Design	<input type="checkbox"/> B. Non-Reimbursable
	<input type="checkbox"/> Other

PROJECT: 2009ERM10
Dubois Park Redevelopment
PALM BEACH COUNTY, FLORIDA

CONTRACT RESOL. NO.	<u>R2010-1129</u>
COMM. DISTRICT NO.:	<u>1</u>
CONTRACT DATE:	<u>07/20/2010</u>
NOTICE TO PROCEED DATE:	<u>08/26/2010</u>
COMMENCEMENT DATE:	<u>09/09/2010</u>
BUDGET LINE ITEM:	<u>1224-380-3086</u>

TO: The Murphy Construction Co.

You are directed to include the following change(s) in this Contract: Change Order No. 5 includes installation of an additional 1,217 tons of limestone rock along the Park's artificial reef for \$79,105.00. Placement of rock must be in accordance with the new artificial reef template (updated drawing included) and the original technical specifications and signed & sealed drawings. In addition, construction methods must comply with the Army Corps of Engineers (ACOE) Permit # SAJ-2004-02138 (IP-EGR) Modification—#1 and South Florida Water Management District Permit # 50-09160-P (previously provided). During construction, placement of turbidity curtains and daily turbidity monitoring are required as well as the completion of daily construction reports. Tonnage of rock will be confirmed by barge displacement measurements at the FIND staging site and verified by ERM staff. Items will be billed in accordance with the attached proposal.

Complete the removal and replacement of an existing exterior circuit breaker panel at the Dubois Pioneer Home Museum in accordance with the attached proposal for \$3,439.46.

In addition, the following changes have been made to the contract.

- Price reduction of \$4,467.56 for Dubois Task 3.01 (Demolition & Miscellaneous Earthwork). Restoration of the Dubois Park's parking lot was not completed. New total cost for this task is \$84,883.46.

Change Order No. 5 extends Contract Time to five hundred and twelve (512) successive calendar days after commencement date (September 9, 2010). Substantial completion is now February 3, 2012.

NOT VALID UNTIL SIGNED BY COUNTY. SIGNATURE OF THE CONTRACTOR INDICATES HIS AGREEMENT HERewith INCLUDING ANY ADJUSTMENT IN THE CONTRACT SUM OR CONTRACT TIME, AND NO ADDITIONAL COST OR TIME INDICATED HEREIN WILL BE RELATED TO THIS CHANGE.


The original Contract sum was	\$ 1,757,848.54
Net change by previous Change Orders	\$ 730,623.29
The Contract Sum prior to this Change Order was	\$ 2,488,471.83
The Contract Sum will be Increased by this Change Order	\$ 78,076.90
The new Contract Sum including this Change Order will be	\$ 2,566,548.73
The Contract Time will be INCREASED by	48 Days
Contracted Date of Substantial Completion including this Change Order	2/03/2012
Contracted Date of Final Completion including this Change Order.	To be specified in Punch List

EXECUTION OF THIS CHANGE ORDER ACKNOWLEDGES FINAL SETTLEMENT OF, AND RELEASES ALL CLAIMS FOR COSTS AND TIME ASSOCIATED, DIRECTLY OR INDIRECTLY, WITH THE ABOVE-STATED MODIFICATION(S), INCLUDING ALL CLAIMS FOR CUMULATIVE DELAYS OR

DISRUPTIONS RESULTING FROM, CAUSED BY, OR INCIDENT TO, SUCH MODIFICATION(S), AND INCLUDING ANY CLAIM THAT THE ABOVE-STATED MODIFICATION(S) CONSTITUTES, IN WHOLE OR PART, A CARDINAL CHANGE TO THE CONTRACT.

CONTRACTOR

The Murphy Construction Co.
1615 Clare Avenue
West Palm Beach, FL 33401

BY  DATE 12-29-11
John E. Murphy
President & CEO

OWNER

Palm Beach County
Board of County Commissioners


BY _____ DATE _____
Shelley Vana, Chair

ATTEST:


Sharon R. Bock, Clerk & Comptroller

BY _____ DATE _____
Deputy Clerk

Approved as to Form and Legal Sufficiency:

BY  DATE 1/19/12
Chief Assistant County Attorney

Approved as to Terms and Conditions:

BY  DATE 12-30-11
Daniel Bates, Deputy Director ERM

DUBOIS PARK PROJECT
CHANGE ORDER NO. 5
CONTRACT R#: 2010-1129

ITEM #	DESCRIPTION OF WORK	QTY	UNIT	UNIT COST	TOTAL COST
1.01	Supply, Transport, Load, Install Armor Stone/Complete Turbidity Measures per Specs/Surveying	1,217	TON	\$65.00	\$79,105.00
TOTAL COST:					\$79,105.00

PROPOSED CHANGE ORDER

Current Connections, Inc.
1620 Hill Avenue
Mangonia Park, Florida 33407

CCN # 1
Date: 11/18/2011
Project Name: Dubois Park Upland Re
Project Number: 1107
Page Number: 1

Client Address:

The Murphy Construction Co.
1615 Clare Avenue
West Palm Beach, Florida 33401

Work Description

Below is a labor and material breakdown for the work necessary to remove and replace the existing Museum exterior circuit breaker panel with a new one.

This is required by Palm Beach County Electrical Inspector Ed Wieth because the existing panel has several existing conduit entries that were not made properly and they allowed excessive moisture into the panel which caused some corrosion.

We will install a new panel of the same size and type as is existing and terminate the existing conduits in a proper fashion using sealing locknuts and weathertight conduit entry methods.

The addition of this work will require the power to the Museum be off for 24 hours when the service change is completed. We do not include the supply of temporary power for any purpose other than the operation of our own hand tools. If it is necessary for the Museum to have power overnight, these provisions must be made by the County's own forces.

Please call me if you have any questions or would like additional information.

We reserve the right to correct this quote for errors and omissions.

Itemized Breakdown

Description	Qty	Net Price U	Total Mat.	Labor U	Total Hrs.
23 #14 - #6 TERM GRNDG BAR KIT w/ 4/0 LUG	1	40.70 E	40.70	0.30 E	0.30
1 1/2" 12GA STAINLESS UNISTRUT - 304 GRADE	10	763.14 C	76.31	30.00 C	3.00
3/4" 12GA STAINLESS UNISTRUT - 304 GRADE	10	646.80 C	64.68	22.00 C	2.20
1/4" STAINLESS SPRING NUT	8	214.12 C	17.13	7.50 C	0.60
1/4" x 1" S.S. Bolts	8	24.56 C	1.96	1.20 C	0.10
1/4" S.S. Lock Washers	8	8.80 C	0.70	0.60 C	0.05
1/4" x 1 1/4" SS Fender Washers	8	48.00 C	3.84	0.72 C	0.06
15A 120/240V SP PLUG-IN CB	3	8.35 E	25.05	0.25 E	0.75
20A 120/240V SP PLUG-IN CB	6	8.35 E	50.10	0.30 E	1.80
20A 120/240V 2P PLUG-IN CB	5	19.31 E	96.55	0.45 E	2.25
40A 120/240V 2P PLUG-IN CB	1	19.31 E	19.31	0.60 E	0.60
50A 120/240V 2P PLUG-IN CB	1	19.31 E	19.31	0.60 E	0.60
70A 120/240V 2P PLUG-IN CB	1	46.79 E	46.79	0.70 E	0.70
100A 120/240V 2P PLUG-IN CB	1	66.02 E	66.02	0.90 E	0.90
SQUARE D #QO40M200RM - NEMA 3R LOADCENTE	1	484.93 E	484.93	8.00 E	8.00
MODIFY EXISTING CONDUITS AS NECESSARY	1	75.00 E	75.00	8.00 E	8.00
Totals			1,088.39		29.90

ORIGINAL

PROPOSED CHANGE ORDER

Current Connections, Inc.
1620 Hill Avenue
Mangonia Park, Florida 33407

Client Address:

The Murphy Construction Co.
1615 Clare Avenue
West Palm Beach, Florida 33401

CCN # 1
Date: 11/18/2011
Project Name: Dubois Park Upland Re
Project Number: 1107
Page Number: 2

Summary		
General Materials		1,088.39
Material Tax	(@ 6.000 %)	65.30
Material Total		1,153.69
JOURNEYMAN	(29.90 Hrs @ \$52.00)	1,554.80
FOREMAN @ 15%	(4.49 Hrs @ \$60.00)	269.40
Subtotal		2,977.89
Overhead	(@ 10.000 %)	297.79
Markup	(@ 5.000 %)	163.78
Subtotal		3,439.46
Final Amount		\$3,439.46

SCHEDULE 1
FOR CHANGE ORDER NO. 5

LIST OF PROPOSED SBE-M/WBE PRIME AND/OR SUBCONTRACTOR PARTICIPATION

PROJECT NUMBER: 2009ERM10

PROJECT NAME: Dubois Park Redevelopment

NAME OF PRIME BIDDER: The Murphy Construction Company

ADDRESS: 1615 Clare Avenue, West Palm Beach, FL 33401

CONTACT PERSON: John E. Murphy, President PHONE NO: (561) 655-3634

FAX NO: (561) 655-3674

BID OPENING DATE: 01/26/2010

DEPARTMENT: Environmental Resources Management

PLEASE IDENTIFY ALL APPLICABLE CATEGORIES OF PRIME AND/OR SUBCONTRACTORS

Name, Address and Phone Number	(Check one or both Categories)		Dollar Amount or Percentage of Work				
	M/WBE Minority Business	SBE Small Business	Black	Hispanic	Women	Caucasian	Other(Please Specify)
1. None	<input type="checkbox"/>	<input type="checkbox"/>	\$ _____	\$ _____	\$ _____	\$ _____	\$ _____
2.	<input type="checkbox"/>	<input type="checkbox"/>	\$ _____	\$ _____	\$ _____	\$ _____	\$ _____
3.	<input type="checkbox"/>	<input type="checkbox"/>	\$ _____	\$ _____	\$ _____	\$ _____	\$ _____
4.	<input type="checkbox"/>	<input type="checkbox"/>	\$ _____	\$ _____	\$ _____	\$ _____	\$ _____
5.	<input type="checkbox"/>	<input type="checkbox"/>	\$ _____	\$ _____	\$ _____	\$ _____	\$ _____
(Please use additional sheets if necessary)		Total	\$ _____	\$ _____	\$ _____	\$ _____	\$ _____

Total Bid Price \$ 78,076.90

Total SBE-M/WBE Participation \$0.00

- NOTE: 1. The amount listed on this form for a subcontractor must be supported by price or percentage listed on the signed Schedule 2 or signed proposal in order to be counted toward goal attainment.
2. Firms may be certified by Palm Beach County as an SBE and/or an M/WBE. If firms are certified as both an SBE and M/WBE, please indicate the dollar amount under the appropriate category.
3. M/WBE information is being collected for tracking purposes only.

**CONTRACT HISTORY FOR
The Murphy Construction Co.
Dubois Park Redevelopment
Project # 2009ERM10**

Contract Resol. No. R2010-1129

Contract Date: July 20, 2010

Original Contract SBE

Participation: 17.34%

\$364,718.49

Original Contract:

\$1,757,848.54

AMENDMENT/ CHANGE ORDER NUMBER	TOTAL/ SBE AMOUNT	AMENDMENT & CHANGE ORDER DESCRIPTION	APPROVED BY/DATE
Change Order 1	\$343,330.25 \$0.00	Zeke's Restoration (2 fixed docks, 1 floating dock, remove/replace bulkhead, dredging)	BCC* 12/21/2010
Change Order 2	\$40,915.63 \$0.00	Remove/replace failing wing wall at Dubois Park (just north of the pedestrian bridge)	ERM 6/16/2011
Change Order 3	\$351,056.72 \$58,459.00	Construct a water taxi shelter, install 3 boat lifts, complete electrical work, install small return wall & fabrication of additional hand	BCC 07/019/2011
Change Order 4	(\$4,679.31) \$0.00	Move lifeguard tower from Jupiter Beach Park to Dubois Park, install stainless steel eyebolts along artificial reef & install additional rock and sand along the restored shoreline	CRC 10/26/2011
Change Order 5	\$78,076.90 0.00	Remove & replace an exterior circuit breaker panel at the Dubois Pioneer Home Museum and install an additional 1,217 tons of limestone rock along the Park's artificial reef.	BCC CRC 12/28/2011

Total \$ Changes: \$808,700.19

Revised K \$: \$2,566,548.73

SBE \$ Changes: \$58,459.00

Revised SBE K \$: \$423,177.49

Revised SBE K %: 16.48%

Report File Date: December 19, 2011

Commencement Date

Original Contract Time

Additional Calendar Days Authorized by Change Order(s)

Revised Contract Time

Revised Date of Substantial Completion

Pending
9/9/2010

270 Days

242

512 Days

2/3/2012

*On 7/20/10, BCC authorized Chair to sign CO1. Chair signed on 12/21/10.

**PALM BEACH COUNTY
PARKS & RECREATION DEPARTMENT
BUDGET AVAILABILITY STATEMENT**

REQUEST DATE: 12/14/11

REQUESTED BY: Kimberly Miranda

PHONE#: 233-2465

FAX #: 233-2414

PROJECT TITLE: Dubois Park

WORK ORDER #:

SUPPLEMENT #:

CONTRACT AMOUNT: \$78,076.90 (CO #5)

BCC RESOLUTION#:

BCC RESOLUTION DATE:

CONTRACTOR/CONSULTANT: Murphy Construction

PROVIDE A BRIEF STATEMENT OF THE SCOPE OF SERVICES TO BE PROVIDED
BY THE CONSULTANT/CONTRACTOR:

Change order #5 for Parks and Recreation Department funded items:

- Credit of \$4,467.56 for parking lot restoration
- Charge of \$3,439.46 for circuit breaker panel associated with underground utilities

AMOUNT REQUESTED ON THIS BAS:

CONSTRUCTION	(\$1,028.10)
ARCHITECTURE/ENGINEER	
*STAFF COSTS	
OTHER	
TOTAL	(\$1,028.10)

BUDGET ACCOUNT NUMBER (IF KNOWN)

FUND: 3038

DEPT: 581

UNIT: P605

OBJECT: 6520

BAS APPROVED BY:

[Signature]

DATE:

ENCUMBRANCE :

FUNDING SOURCE(S)	
<input checked="" type="checkbox"/>	Grant
<input type="checkbox"/>	Interest Fee
<input type="checkbox"/>	Park Improvement Fund
<input type="checkbox"/>	Ad Valorem
<input type="checkbox"/>	Other

BAS APPROVAL

☒ FULLY FUNDED WITHIN CURRENT BUDGET *[Signature]*

☐ FULLY FUNDED PENDING BUDGET TRANSFER



BUDGET AVAILABILITY STATEMENT
Palm Beach County
Environmental Resources Management

REQUEST DATE: 12/30/2011

REQUESTED BY: Kim Miranda

PHONE: 233-2465

PROJECT TITLE: Dubois Reef Restoration

PROJECT NO: ERM-2010-030

SITE: offshore Dubois Park

ACTIVITY: Material Placement

CONTRACTOR/CONSULTANT NAME: Murphy Construction Co.

SCOPE OF SERVICES: Rock placement to increase elevation.

BCC RESOLUTION #: R2010-1129 ORIGINAL CONTRACT AMOUNT: \$2,488,471.83

CHANGE ORDER #: No.5 REQUESTED AMOUNT: \$79,105.00

BUDGET ACCOUNT NUMBER(S):

<u>Fund</u>	<u>Dept</u>	<u>Unit</u>	<u>Obj</u>	<u>SObj</u>	<u>Program</u>	<u>PPC</u>	<u>(Proj)</u> <u>Task</u>	<u>(Site)</u> <u>Sub Task</u>	<u>(Activity)</u> <u>Task Ord</u>	<u>Amount</u>
1224	380	3086	3401		3086EX		S024	PDUB	011	\$78,076.90
1224	380	3086	3401	Conting	3086EX		S024	PDUB	011	1,028.10

BAS APPROVED BY: Liz Purnin DATE: 12/30/11

ENCUMBRANCE NUMBER: Budget provided in Agenda of 1/24/2012

RESOLUTION NO. -----

**RESOLUTION OF THE BOARD OF COUNTY
COMMISSIONERS OF PALM BEACH COUNTY, FLORIDA TO
UTILIZE A PORTION OF THE COUNTY VESSEL
REGISTRATION FEES FOR CONSTRUCTING AN
ARTIFICIAL REEF AT DUBOIS PARK SITUATED SOUTH OF
THE JUPITER INLET.**

WHEREAS, Palm Beach County enacted the Vessel Registration Fee Ordinance, No. 88-40 which began collecting fees June 1, 1989; and

WHEREAS, the Vessel Registration Fee Ordinance provides that monies collected from vessel registration fees be utilized to protect coastal marine and estuarine habitats, maintain and enhance fisheries and other salt and freshwater habitats, and construct artificial reefs; and

WHEREAS, the Dubois Park Redevelopment Project No. 2009ERM10 was awarded to the Murphy Construction Company on July 20, 2010 to remove and restore existing derelict structures in the park and to construct park improvements including bulkheads, an artificial reef, fixed and floating docks, installation of boat lifts for law enforcement vessels, and a water taxi shelter; and

WHEREAS, the creation of the planned artificial reef will require additional reef materials to provide adequate wave protection for the snorkelers and additional habitat;

WHEREAS, this work currently estimated not to exceed \$125,000 will come from the County's Vessel Registration Fee Trust Fund with a completion in February, 2012; and

WHEREAS, the Board of County Commissioners and the Artificial Reef and Estuarine Enhancement Committee support the artificial reef creation and enhancement of the Dubois Reef Restoration Project; and

WHEREAS, the Director of Environmental Resources Management recommends that the Board of County Commissioners authorize the Clerk of the Court to disburse Vessel Registration Fee monies in the amount of \$125,000 to cover the additional costs for the enhancement of Dubois Reef Restoration Project.

NOW, THEREFORE, BE IT RESOLVED BY THE BOARD OF COUNTY COMMISSIONERS OF
PALM BEACH COUNTY FLORIDA, THAT:

- Section 1: The foregoing recitals are hereby adopted and ratified.
- Section 2: The Board hereby authorizes the Clerk to disburse funds of \$125,000 for the
 additional costs for the enhancement of Dubois Reef Restoration Project.

The foregoing Resolution was offered by Commissioner _____, who
moved its adoption. The motion was seconded by Commissioner _____, and upon
being put to a vote, the vote was as follows:

- | | | |
|------------|--|-------|
| District 3 | COMMISSIONER Shelley Vana, Chair | _____ |
| District 4 | COMMISSIONER Steven L. Abrams, Vice Chairman | _____ |
| District 1 | COMMISSIONER Karen T. Marcus | _____ |
| District 2 | COMMISSIONER Paulette Burdick | _____ |
| District 5 | COMMISSIONER Burt Aaronson | _____ |
| District 6 | COMMISSIONER Jess R. Santamaria | _____ |
| District 7 | COMMISSIONER Priscilla A. Taylor | _____ |

The Chair thereupon declared the Resolution duly passed and adopted this _____ day of
_____, 2012.

APPROVED AS TO FORM AND LEGAL SUFFICIENCY	PALM BEACH COUNTY, FLORIDA BY ITS BOARD OF COUNTY COMMISSIONERS
	_____, Clerk
By _____ Assistant County Attorney	By _____ Deputy Clerk



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

1/6/2012

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER Greene-Hazel and Associates, Inc. 10739 Deerwood Park Blvd S 200 Jacksonville FL 32256		CONTACT NAME: Kellie Brandes PHONE (A/C, No., Ext): 904-398-1234 FAX (A/C, No.): 904-396-7432 E-MAIL: certificates@greenehazel.com	
		INSURER(S) AFFORDING COVERAGE	
		INSURER A: Alterra America Ins Co	
		INSURER B: Travelers Insurance Company 36137	
		INSURER C: Liberty Mutual Ins Co 23043	
		INSURER D:	
		INSURER E:	
		INSURER F:	

COVERAGES

CERTIFICATE NUMBER: 813710592

REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR VWD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	GENERAL LIABILITY <input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PROJECT <input type="checkbox"/> LOC	Y	Y	MAXA30M0046737	1/1/2012	1/1/2013	EACH OCCURRENCE \$1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$300,000 MED EXP (Any one person) \$10,000 PERSONAL & ADV INJURY \$1,000,000 GENERAL AGGREGATE \$2,000,000 PRODUCTS - COM/OP AGG \$2,000,000 \$
B	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input checked="" type="checkbox"/> HIRED AUTOS <input checked="" type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> NON-OWNED AUTOS			810345K9432	1/1/2012	1/1/2013	COMBINED SINGLE LIMIT (Ea accident) \$1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ Comp/Coll Ded \$1,000
	UMBRELLA LIAB EXCESS LIAB DED RETENTION \$						EACH OCCURRENCE \$ AGGREGATE \$ \$
C	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below	Y/N N	Y	WA765D052693481	1/1/2012	1/1/2013	<input checked="" type="checkbox"/> WC STATUTORY LIMITS <input type="checkbox"/> OTHER E.L. EACH ACCIDENT \$1,000,000 E.L. DISEASE - EA EMPLOYEE \$1,000,000 E.L. DISEASE - POLICY LIMIT \$1,000,000
A	Inland Marine Installation Floater			MAXA3IM0046732	1/1/2012	1/1/2013	Leased/Rented Installation Floater \$1,500,000 \$100,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)

RE: Dubois Park Redevelopment Project#2009ERM10. The Board of County Commissioners, Palm Beach County Florida (a political subdivision of the State of Florida), its Officers, directors, agents, and employees are named as additional insured under the terms of this policy. GL Coverage is primary & non-contributory. All policies include a waiver of subrogation in favor of additional insureds

CERTIFICATE HOLDER**CANCELLATION**

Palm Beach County Dept of Environmental Resources
Managment The Board of County Commissioners
2300 N Jog Road
4th Floor
West Palm Beach FL 33411

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

© 1988-2010 ACORD CORPORATION.



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
10/13/2011

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER
Wells Fargo Insurance Services USA, Inc.
2054 Vista Parkway, Suite 400
West Palm Beach FL 33411-2718

CONTACT
NAME:
PHONE
(A/C No. Ext): (561) 655-5500 FAX (A/C No.): (561) 655-5509
E-MAIL
ADDRESS:

INSURED
Murphy Construction Company &
Terminal Equipment & Construction Company
1615 Clare Avenue
West Palm Beach FL 33401

INSURER(S) AFFORDING COVERAGE
INSURER A: AGCS Marine Insurance Company
INSURER B:
INSURER C:
INSURER D:
INSURER E:
INSURER F:

COVERAGES

CERTIFICATE NUMBER: Cert ID 233407

REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADD'L SUBR INSR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
	GENERAL LIABILITY					EACH OCCURRENCE \$
	COMMERCIAL GENERAL LIABILITY					DAMAGE TO RENTED PREMISES (Ea occurrence) \$
	CLAIMS-MADE <input type="checkbox"/> OCCUR <input type="checkbox"/>					MED EXP (Any one person) \$
						PERSONAL & ADV INJURY \$
						GENERAL AGGREGATE \$
	GEN'L AGGREGATE LIMIT APPLIES PER:					PRODUCTS - COMP/OP AGG \$
	POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC <input type="checkbox"/>					\$
	AUTOMOBILE LIABILITY					COMBINED SINGLE LIMIT (Ea accident) \$
	ANY AUTO					BODILY INJURY (Per person) \$
	ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/>					BODILY INJURY (Per accident) \$
	HIRED AUTOS <input type="checkbox"/> NON-OWNED AUTOS <input type="checkbox"/>					PROPERTY DAMAGE (Per accident) \$
						\$
	UMBRELLA LIAB <input type="checkbox"/> OCCUR <input type="checkbox"/>					EACH OCCURRENCE \$
	EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/>					AGGREGATE \$
	DED <input type="checkbox"/> RETENTION \$					\$
	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY					WC STATUTORY LIMITS <input type="checkbox"/> OTH-ER <input type="checkbox"/>
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) <input type="checkbox"/> Y/N <input type="checkbox"/>	N/A				E.L. EACH ACCIDENT \$
	If yes, describe under DESCRIPTION OF OPERATIONS below					E.L. DISEASE - EA EMPLOYEE \$
						E.L. DISEASE - POLICY LIMIT \$
A	Ocean Marine		OHL92005243	10/12/2011	10/12/2012	Hull \$404,100. \$ P&I \$1,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)
10 days notice of cancellation for nonpayment of premium. American Institute Hull Clauses and P&I Form SP-38. RE: Palm Beach County, Dubois Park Redevelopment, Project No.: 2009ERM10. The Board of County Commissioners, Palm Beach County, FL (a political subdivision of the State of Florida), its officers, directors, agents, and employees are named as additional insured under the terms of this policy.

CERTIFICATE HOLDER

Palm Beach County Board of County Commissioners
Palm Bch Cnty Dept of Environmental Resources Mgt
2300 North Jog Road, 4th FL
West Palm Beach FL 33411-2743

CANCELLATION

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

© 1988-2010 ACORD CORPORATION. All rights reserved.

BOARD OF COUNTY COMMISSIONERS
PALM BEACH COUNTY, FLORIDA


BUDGET TRANSFER
Fund 1224 Environmental Enhancement-Saltwtr

ACCOUNT NAME AND NUMBER		ORIGINAL BUDGET	CURRENT BUDGET	INCREASE	DECREASE	ADJUSTED BUDGET	ENCUMBERED / Expended 12/13/2011	REMAINING BALANCE
<u>Appropriations</u>								
<u>Reserve-Salt Water Projects</u>								
380-3891	9902-Operating Reserves	368,703	368,703	0	125,000	243,703	0	243,703
<u>Dubois Reef Restoration</u>								
380-3086	3401 - Other Contractual Services	0	0	125,000	0	125,000	0	125,000
				125,000	125,000			

Environmental Resources
Management

INITIATING DEPARTMENT/DIVISION
Administration/Budget Department Approval
OFMB Department - Posted

Signatures & Dates



12/28/11

SN
12/28/11

BY BOARD OF COUNTY COMMISSIONERS

AT MEETING OF

January 24, 2012

Deputy Clerk to the
Board of County Commissioners
