

PALM BEACH COUNTY
BOARD OF COUNTY COMMISSIONERS
AGENDA ITEM SUMMARY

Meeting Date: February 5, 2013 Consent Regular
Public Hearing

Submitted By: Water Utilities Department
Submitted For: Westgate/Belvedere Homes CRA

I. EXECUTIVE BRIEF


Motion and Title: Staff recommends motion to approve: Change Order No. 2 to the Contract with Giannetti Contracting Corporation (R2012-0339) for the Westgate/Belvedere Homes Infrastructure Improvement Project Phase I, increasing the contract price by \$194,361.50 and 90 day time extension.


Summary: On March 6, 2012, the Palm Beach County Board of County Commissioners approved a Contract with Giannetti Contracting Corporation (R2012-0339) for the Westgate/Belvedere Homes Infrastructure Improvements Phase I. These contract adjustments are necessary to reflect changed conditions encountered in the field. Funding for this Change Order is by Palm Beach County Water Utilities Department. The Small Business Enterprise (SBE) participation goal established by the SBE Ordinance is 15% overall. This Change Order includes zero overall SBE participation. This project has Federally participation goals of 22.4% MBE and 6.9% WBE. This Contract with Giannetti Contracting Corporation includes 13.27% MBE, 13.27% WBE participation. Giannetti Contracting Corporation has provided for SBE participation of 14.58% overall. (WUD Project No. 10-502 (11-022) District 7 (JM))

Background and Justification: This change order will authorize the Contractor to perform additional work due to actual field conditions with an additional 90 days added to the contract.

Attachments:

1. Location Map
2. Two (2) Original Change Order No. 2

Recommended By:  1/14/13
Department Director Date

Approved By:  1/23/13
Assistant County Administrator Date



**Palm Beach County
Water Utilities
Department
Service Area (SA) and
Major Facilities**


Attachment 1

Legend

- MANDATORY RECLAIMED SA
- 💧 Water Treatment Facility
- ★ Administration
- Water Reclamation Facility
- COUNTY LIMITS
- P.B.C.W.U.D. SA



NOT TO SCALE

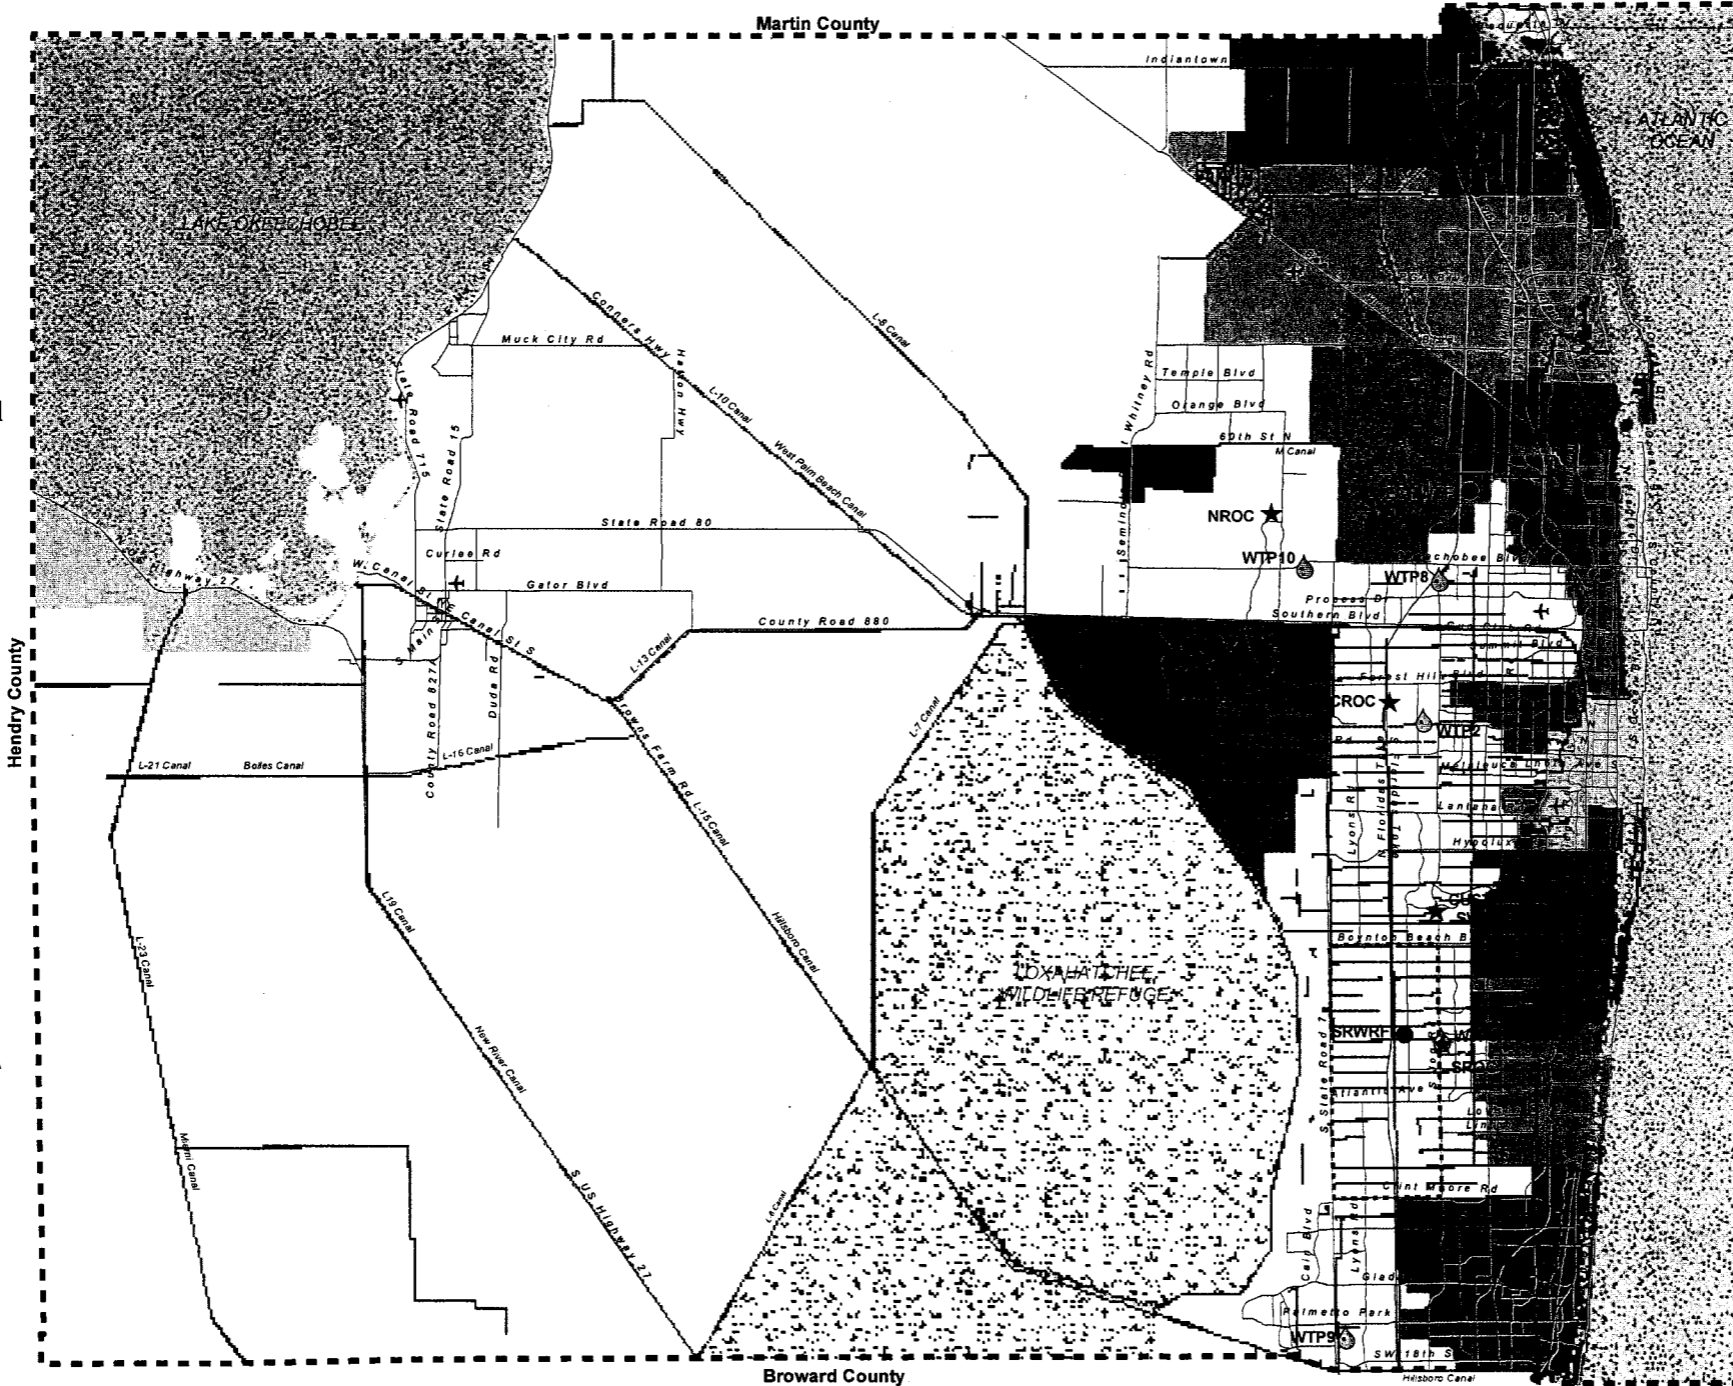

CHANGE ORDER

PROJECT: Westgate/Belvedere Homes Infrastructure Improvements
WATER UTIL. DEPT. PROJECT NO. WUD 10-502(11-022)
DISTRICT NUMBER: 2
CHANGE ORDER NO.: two (2)

TO:	DOCUMENT NO.	R2012-0339
Giannetti Contracting Corp	CONTRACT DATE:	March 6, 2012
6340 Sims Dr.	NOTICE TO PROCEED:	March 15, 2012
Sterling Heights, MI. 48313	BUDGET LINE ITEM:	4011-721-W006-6543

You are directed to make the following changes in this contract:

2.1	Roadway replacement (CO#7)	\$160,145.50
2.2	Contract overrun/underrun adjustment	\$20,525.25
2.3	Electrical Lamp Post Replacement (CO#6)	\$13,690.75
2.4	Additional time (CO#4)	0.00
		TOTAL \$194,361.50

NOT VALID UNTIL SIGNED BY BOTH OWNER AND ENGINEER. SIGNATURE OF THE CONTRACTOR INDICATES HIS AGREEMENT HEREWITH INCLUDING ANY ADJUSTMENT IN THE CONTRACT SUM OR CONTRACT TIME, AND NO ADDITIONAL COST OR TIME INDICATED HEREIN WILL BE RELATED TO THIS CHANGE

The Original Contract Sum was	<u>\$3,894,228.70</u>
Net Change by previous Change Orders	<u>98,261.67</u>
The Contract Sum prior to this Change Order was	<u>\$3,992,490.37</u>
The Contract Sum will be increased by this Change Order	<u>\$194,361.50</u>
The New Contract Sum indicating this Change Order will be ...	<u>\$4,186,851.87</u>
The Contract Time for will be increased by 90 days	<u>90 Days</u>
The Date of Substantial Compl. Including this Change Order:	<u>Feb 07, 2013</u>
The date of Final Compl. Including this Change Order:	<u>Mar 07, 2013</u>

EXECUTION OF THIS CHANGE ORDER ACKNOWLEDGES FINAL SETTLEMENT OF, AND RELEASES, ALL CLAIMS FOR COSTS AND TIME ASSOCIATED, DIRECTLY OR INDIRECTLY, WITH THE ABOVE STATED MODIFICATION (S), INCLUDING ALL CLAIMS FOR CUMULATIVE DELAYS OR DISRUPTIONS RESULTING FROM, CAUSED BY, OR INCIDENT TO SUCH MODIFICATION (S) CONSTITUTES IN WHOLE OR PART, A CARDINAL CHANGE TO THE CONTRACT.

Belvedere Homes Infrastructure
Improvements
Project No. WUD 10-502
District Number: 2
Contract No. R2012-0339
Change Order No. two(2)

Palm Beach County

Giannetti Contracting

Palm Beach County

Joseph Tanacredi, P.E.

ENGINEER

P.O. Box 16097

Address

WPB, Fl 33416

CONTRACTOR

6340 Sims Dr

Address

Sterling Hts MI, 48313

Steven L. Abrams, Chairman

OWNER:

Address


BY



DATE

11-28-12

BY



DATE

12-7-12

BY

DATE

Approved as to Form and Legal Sufficiency

By:

County Attorney

Attest: Sharon R. Bock, Clerk and Comptroller

By:

Deputy Clerk

Belvedere Homes Infrastructure
Improvements
Project No. WUD 10-502
District Number: 2
Contract No. R2012-0339
Change Order No. two(2)

CHANGE ORDER CATEGORIZATION

<input checked="" type="checkbox"/> OWNER INITIATED	<input checked="" type="checkbox"/> QUANTITY OVERRUNS/UNDER-RUNS
<input checked="" type="checkbox"/> DIFFERING SITE CONDITIONS	<input type="checkbox"/> REQUEST BY ANOTHER AGENCY/OUTSIDE
<input type="checkbox"/> ZONING/CODE/ORDINANCE CHANGES	<input type="checkbox"/> A. REIMBURSABLE
<input type="checkbox"/> ERRORS/OMISSIONS/IN DESIGN	<input type="checkbox"/> B. NON-REIMBURSABLE

Belvedere Homes Infrastructure
Improvements
Project No. WUD 10-502
District Number: 2
Contract No. R2012-0339
Change Order No. two(2)

SCOPE OF WORK

- 2.1 Road replacement and restoration(Differing site condition).
- 2.2 Contract overrun and underrun adjustment(Overrun/underrun).
- 2.3 Replace two broken electrical lamp posts along cherry road
(Owner Initiated).
- 2.4 Additional time do to excess water condtions as outline in Giannetti
letter C.O. # 4(Differing site condition).

Belvedere Homes Infrastructure
Improvements
Project No. WUD 10-502
District Number: 2
Contract No. R2012-0339
Change Order No. two(2)

SUMMARY

<u>C.O. #</u>	<u>DESCRIPTION</u>	<u>ADDITIONS</u>	<u>(DELETIONS)</u>	<u>NET CHANGE</u>
2.1	Roadway Replacement	160,145.50		160,145.50
2.2	Contract adjustment	20,525.25		20,525.25
2.3	Electrical Lamp posts	13,690.75		13,690.75
2.4	Time extension	0.00		0.00
		Total		194,361.50

Item No.	Item	Base Bid Phase I Quantity	Units	Unit Price (Ph I Only)	Total Price (Ph I Only)	Contract Under/Over Run Quantity	Under/Over Run \$\$
244	8')	1	EA	\$ 2,422.00	\$ 2,422.00	0	\$ -
245	(10'-12')	1	EA	\$ 4,141.00	\$ 4,141.00	0	\$ -
246	10')	6	EA	\$ 2,533.00	\$ 15,198.00	0	\$ -
247	10')	2	EA	\$ 2,910.00	\$ 5,820.00	0	\$ -
248	(10'-12')	1	EA	\$ 3,535.00	\$ 3,535.00	0	\$ -
249	(6'-8')	0	EA	\$ 2,010.00	\$ -	0	\$ -
250	(6'-8')	2	EA	\$ 2,367.00	\$ 4,734.00	0	\$ -
251	(8'-10')	1	EA	\$ 3,060.00	\$ 3,060.00	0	\$ -
252	(10'-12')	0	EA	\$ 3,712.00	\$ -	0	\$ -
253	(8'-10')	1	EA	\$ 3,307.00	\$ 3,307.00	0	\$ -
254	Conflict MH PB Bot. w/ MH Top 4'	2	EA	\$ 7,353.00	\$ 14,706.00	-0.25	\$ (1,838.25)
255	Conflict MH JB Bot. w/ MH Top 4'	1	EA	\$ 7,353.00	\$ 7,353.00	0	\$ -
256	Conflict MH JB Bot. w/ MH Top 5'	1	EA	\$ 7,710.00	\$ 7,710.00	0	\$ -
257	Conflict MH JB Bot. w/ MH Top 4'X6'	0	EA	\$ 7,718.00	\$ -	0	\$ -
258	Conflict MH JB Bot. w/ MH Top 5'X6'	1	EA	\$ 7,718.00	\$ 7,718.00	0	\$ -
259	Conflict MH JB Bot. w/ MH Top 4'X7'	1	EA	\$ 8,407.00	\$ 8,407.00	0	\$ -
260	Conflict MH JB Bot. w/ MH Top	1	EA	\$ 8,205.00	\$ 8,205.00	0	\$ -
261	6'x12' (1')	1	EA	\$ 10,423.00	\$ 10,423.00	0	\$ -
262	FDOT Endwall for 15" pipe	1	EA	\$ 3,327.00	\$ 3,327.00	0	\$ -
263	FDOT Endwall for 18" pipe	1	EA	\$ 3,372.00	\$ 3,372.00	0	\$ -
264	FDOT Endwall for 42" pipe	1	EA	\$ 7,549.00	\$ 7,549.00	0	\$ -
265	FDOT Endwall for 48" pipe	1	EA	\$ 8,000.00	\$ 8,000.00	0	\$ -
266	Mitered End Section for 18" pipe	1	EA	\$ 465.00	\$ 465.00	0	\$ -
267	Pole	9	EA	\$ 500.00	\$ 4,500.00	1	\$ 500.00
268	Relocated Existing Utility Pole	2	EA	\$ 2,500.00	\$ 5,000.00	-1	\$ (2,500.00)
SUBTOTAL=					\$ 1,767,610.00		
Potable Water							
301	Grout Abandoned CA WM	13,600	LF	\$ 3.65	\$ 49,640.00	1000	\$ 3,650.00
302	Removal & Disposal of CA WM	1,500	LF	\$ 18.50	\$ 27,750.00	-1000	\$ (18,500.00)
303	4" DIP Water Main	0	LF	\$ 19.00	\$ -	0	\$ -
304	6" DIP Water Main	60	LF	\$ 17.00	\$ 1,020.00	-44	\$ (748.00)
305	8" DIP Water Main	1,058	LF	\$ 16.00	\$ 16,928.00	15	\$ 240.00
306	8" C-900 PVC Water Main	13,986	LF	\$ 14.00	\$ 195,804.00	0	\$ -
307	4" Gate Valve	2	EA	\$ 654.00	\$ 1,308.00	-2	\$ (1,308.00)
308	6" Gate Valve	1	EA	\$ 756.00	\$ 756.00	-1	\$ (756.00)
309	8" Gate Valve	65	EA	\$ 1,015.00	\$ 65,975.00	-5	\$ (5,075.00)
310	Connect to Existing CA Water Main	9	EA	\$ 5,482.00	\$ 49,338.00	1	\$ 5,482.00
311	Sample Point	16	EA	\$ 263.00	\$ 4,208.00	-3	\$ (789.00)
312	Fire Hydrant Assembly, Inc. Valves &	10	EA	\$ 6,251.00	\$ 62,510.00	18	\$ 112,518.00
313	Fire Hydrant	1	EA	\$ 2,604.00	\$ 2,604.00	0	\$ -
314	Single Water Service (short, with meter	16	EA	\$ 890.00	\$ 14,240.00	-3	\$ (2,670.00)
315	Single Water Service (long, with meter	17	EA	\$ 1,000.00	\$ 17,000.00	-11	\$ (11,000.00)
316	Double Water Service (short, with	72	EA	\$ 1,100.00	\$ 79,200.00	11	\$ 12,100.00
317	Double Water Service (long, with meter	72	EA	\$ 1,300.00	\$ 93,600.00	-4	\$ (5,200.00)
318	DIP Class 153 Fittings	9.1	TN	\$ 7,279.00	\$ 66,238.90	0	\$ -
SUBTOTAL=					\$ 748,119.90		
Wastewater Collection							
401	4" PVC Vacuum Sewer with Fittings	5,109	L.F.	\$ 13.00	\$ 66,417.00	-70	\$ (910.00)
402	6" PVC Vacuum Sewer with Fittings	3,414	L.F.	\$ 15.00	\$ 51,210.00	0	\$ -
403	8" PVC Vacuum Sewer with Fittings	5,469	L.F.	\$ 18.00	\$ 98,442.00	-36	\$ (648.00)
404	4" Isolation Valve Assembly	6	EA.	\$ 680.00	\$ 4,080.00	-3	\$ (1,700.00)
405	6" Isolation Valve Assembly	7	EA.	\$ 795.00	\$ 5,565.00	-3	\$ (1,987.50)
406	8" Isolation Valve Assembly	6	EA.	\$ 1,021.00	\$ 6,126.00	-2	\$ (1,531.50)
407	Valve Pits	176	EA.	\$ 3,420.00	\$ 601,920.00	1	\$ 3,420.00
408	Service Laterals (short)	73	EA.	\$ 800.00	\$ 58,400.00	10	\$ 8,000.00
409	Service Laterals (long)	104	EA.	\$ 1,000.00	\$ 104,000.00	-10	\$ (10,000.00)
410	6" C-900 PVC Force Main	80	L.F.	\$ 18.25	\$ 1,460.00	0	\$ -
411	8" C-900 PVC Force Main	1,460	L.F.	\$ 19.50	\$ 28,470.00	7	\$ 136.50

11-1-12

C.O.#7

Belvedere Homes Roads Per Contract

1 Pavement Removal	6,307 SY	\$ 1.30	\$ 8,199.10
2 Road Restoration	6,516 SY	\$ 27.00	\$ 175,932.00
3 Milling	17,023 SY	\$ 2.00	\$ 34,046.00
4 Overlay	23,539 SY	\$ 5.80	\$ 136,526.20
			\$ 354,703.30
5 Pavement Replacement	13,361 SY	\$ 25.00	\$ 334,025.00
6 Mill Credit	1,942 SY	\$ 2.00	\$ 3,884.00
7 Overlay Credit	1,942 SY	\$ 5.80	\$ 11,263.60
			\$ 349,172.60

Road Restoration/Overlay Tot: \$ 703,875.90
Less Original Contract Amount \$ 584,030.00

Additional Amount (Per Keshavarz) \$ 119,845.90

Added Giannetti Items to Restoration

Shoulder Difference Added back to Change			
1 Order	1942 SY	\$ 17.20	\$ 33,402.40
Complete Restoration - Pine just North of			
2 Beech -	190 SY	\$ 25.00	\$ 4,750.00
Pine just North of Beech Debit (Mill & Overlay			
3 Amount)	190 SY	\$ (7.80)	\$ (1,482.00)
Complete Restoration - Osceola between			
4 Cherry & Beech	211 SY	\$ 25.00	\$ 5,275.00
Osceola just North of Cherry Debit (Mill &			
5 Overlay Amount)	211 SY	\$ (7.80)	\$ (1,645.80)
	Giannetti Subtotal		\$ 40,299.60
	Road Restoration/Overlay Tot:		\$ 703,875.90
	Total Amount of Road Work		\$ 744,175.50
	Less Original Contract Amount		\$ 584,030.00

Additional Amount Requested Per
Giannetti \$ 160,145.50 ✓

Additional Time Requested for Road Work -
Giannetti

60 Calendar Days ✓

Additional Time Requested for Water Table -
Giannetti

30 ~~60~~ Calendar Days ✓ (C.O.#4)

Total Additional Time Requested by
Giannetti

90 ~~120~~ Calendar Days

GIANNETTI CONTRACTING
CORPORATION

Main Office
6340 Sims Dr.
Sterling Heights, MI 48313
Phone: (586) 268-2090
Fax: (586) 268-7099

Florida Office
2301 W. Sample Rd. Bld. 3, Ste. 6A
Pompano Beach, FL 33073
Phone: (954) 972-8104
Fax: (954) 972-8108

BUILDING • DEVELOPMENT • INFRASTRUCTURE

CHANGE ORDER #4

Project: Belvedere Homes Infrastructure

Project #: WUD 10-502

RE: Time Extension: Unforeseen Water Conditions

Since this project started, the water conditions have been extreme and have delayed our project significantly. In the bid documents, the only reference to dewatering was made on the dewatering exhibit included with the South Florida Water Management District Dewatering Permit. There weren't any soil reports or existing water tables provided.

The only reasonable indication of the possible water table when bidding this project, could be given by the elevation of the L-2 Canal, which is close to ten feet below the top of bank. We bid this project figuring the water was at an 8.00 NGVD, which is approximately seven feet below the existing surface.

Since this project started, there have been times where the water is above a 11.00 NGVD. Our water main with 36" of cover had areas where we had to pump water, while installing.

Adding to this high water table, we've had extreme rain events since this project started. There have been many days where there was over an inch of rain, and five days where we had two inches or more of rain. August 2012 set a record for rainfall at the Palm Beach County Airport with 21.43" of rainfall. The old record was 20.12" set in August 1995.

We recently had Tropical Storm Isaac. This area was under a state of emergency. We approached the 100 year flood plain in our area. People's homes in our neighborhood were flooded.

The lack of existing drainage compounded the project ability to drain causing wetter conditions. Also, the project sequencing required us to install the water main first.

As a result of this water table and rain events, we've lost a great deal of time. Large portions of this project have been wellpointed including some areas not shown on the dewatering exhibit.

Our schedule has been significantly delayed, and we respectfully request a Time Extension of ~~90~~ Work Days.

TIME EXTENSION REQUESTED: ~~90~~ ^{CALENDAR} WORK DAYS

30

Item No.	Item	Base Bid Phase I Quantity	Units	Unit Price (Ph I Only)	Total Price (Ph I Only)
412	6" Gate Valve	2	EA.	\$ 720.00	\$ 1,440.00
413	8" Gate Valve	1	EA.	\$ 965.00	\$ 965.00
414	Connect to Ex. 6" CIP FM	1	EA.	\$ 2,986.00	\$ 2,986.00
415	8"x10" Tapping Valve & Sleeve	1	EA.	\$ 5,488.00	\$ 5,488.00
416	DIP Class 153 Fittings	0.4	TN	\$ 11,387.00	\$ 4,554.80
417	Vacuum System Manufacturer Services	1.0	L.S.	\$ 184,400.00	\$ 184,400.00
SUBTOTAL=					\$ 1,225,923.80
Contingency Items					
501	4" Line Stop Valve	1	EA.	\$ 8,500.00	\$ 8,500.00
502	6" Line Stop Valve	1	EA.	\$ 9,000.00	\$ 9,000.00
503	8" Line Stop Valve	1	EA.	\$ 9,500.00	\$ 9,500.00

Contract Under/Over Run Quantity	Under/Over Run \$\$
0	\$ -
0	\$ -
0	\$ -
0	\$ -
0	\$ -
0	\$ -
0	\$ -
-1	\$ (8,500.00)
-1	\$ (9,000.00)
-1	\$ (9,500.00)

\$ 20,525.25

BELVEDERE HOMES INFRASTRUCTURE IMPROVEMENTS
ADDITIONAL CONSTRUCTION COSTS SUMMARY

CONTRACT OVERRUN	\$ 20,525.25
CONTRACT EXTENSION	\$
	\$
	\$
	\$
ADDITIONAL PAYMENT (L.S.T.)	\$ 160,145.50
ADDITIONAL CONTRACT COST	\$

GIANNETTI CONTRACTING
CORPORATION

Main Office
6340 Sims Dr.
Sterling Heights, MI 48313
Phone: (586) 268-2090
Fax: (586) 268-7099

Florida Office
2301 W. Sample Rd. Bld. 3, Ste. 6A
Pompano Beach, FL 33073
Phone: (954) 972-8104
Fax: (954) 972-8108

BUILDING • DEVELOPMENT • INFRASTRUCTURE

CHANGE ORDER #6

Project: Belvedere Homes Infrastructure

Project #: WUD 10-502

RE: Replacement of Two Post Lights on Cherry Road

1. Two Post Lights Replacement (Sub)	1	LS	\$11,905.00	\$11,905.00
--------------------------------------	---	----	-------------	-------------

CHANGE ORDER SUBTOTAL: \$11,905.00

CONTRACTOR MARK UP 15%: \$1,785.75

TOTAL CHANGE ORDER COST: \$13,690.75 ✓

TIME EXTENSION REQUESTED: 0 WORK DAYS



43 S. Pompano Parkway Suite 513 Pompano Beach FL, 33069
 OFFICE(954)935-0900 FAX(954)935-0901
 EC-0002901

PROPOSAL

DATE: 9/3/2012
 CUSTOMER: Giannetti Contracting Corp. PROJECT NAME: Post Lights
 ADDRESS: 6430 Sims Dr. ADDRESS: Cherry Rd
 CITY: Sterling Heights. MI CITY: West Palm Beach
 ZIP: 48313 ZIP:

QUANTITY	DESCRIPTIONS AND LOCATION	UNIT PRICE	AMOUNT
1	2 Post lights replacement with lamps		
1	Installation charge		
1	Freight charge (lead time 8-10 weeks)		
SUBTOTAL:			\$ 11,905.00

DRAW SCHEDULE:
 50% UPON ACCEPTANCE \$ 5,952.50
 50% UPON FINAL \$ 5,952.50
 Total Payments \$ 11,905.00

PROPOSAL APPROVED BY: _____
SIGNATURE

PRINT NAME: _____
No work will begin without a signed proposal and deposit

Payments can be made by cash, check or credit card.
 Permit fees are not included.

CHANGE ORDER ADDITIONS/DELETIONS SUMMARY

PROJECT:	Belvedere Homes Infrastructure Improvements	<u>APPROVAL LIMITS:</u>						
CONTRACTOR:	Giannetti Contracting Corp	DEPARTMENT HEAD	CONTRACT REVIEW COMMITTEE	DEPARTMENT HEAD PLUS CONTRACT REVIEW COMMITTEE				
PROJECT NO.:	10-502							
RESOLUTION:	R2012-0339	(Amount)	(Days)	(Amount)	(Days)	(Amount)	(Days)	
DATE APPROVED:	03/06/12	INDIVIDUAL C.O.	\$50,000.00	16 Days	\$100,000.00	33 Days	\$0	0 Days
CONTRACT AMOUNT:	\$3,894,228.70	CUMMULATIVE C.O.	\$25,000.00	33 Days	\$100,000.00	33 Days	\$200,000.00	63 Days

CO	DATE APPROVED	NET CHANGE	DEPARTMENT HEAD		CONTRACT REVIEW COMMITTEE		TOTAL DEPT. HEAD & CONTRACT REVIEW COMM.		BOARD OF COUNTY COMMISSIONERS		TOTALS
			(ADDS PLUS DEDUCTS) AMOUNT	DAYS	(ADDS PLUS DEDUCTS) AMOUNT	DAYS	(ADDS PLUS DEDUCTS) AMOUNT	DAYS	(ADDS PLUS DEDUCTS) AMOUNT	DAYS	
001	pending	98,261.67	0	0	0	0	0	0	98,261.67	22	98,261.67
002	pending	194,361.50	0	0	0	0	0	0	201,361.50	90	201,361.50
TOTAL		292,623.17	0	0	0	0	0	0	292,623.17	112	292,623.17

Notes:

1. Net Change reflects the net amount of additions plus deductions.
2. Adds plus Deducts reflects the net value of unrelated changes for use in determining the approval authority for the Change Order.
3. Liquidated Damages = \$1000 (Prior to Substantial Completion) and = \$ 500 (After Substantial Completion).

SCHEDULE 1

PARTICIPATION BY SBE/WBE SUBCONTRACTORS

PROJECT NAME: Westgate/Belvedere Homes Infrastructure Improvement 10-502
 NAME OF PRIME CONTRACTOR: Giannetti Contracting Corp Change Order NO.2
 CONTACT PERSON: Bob Henning PHONE NO: FAX NO.
 Change Order No: 2 DEPARTMENT: Water Utilities

Name, Address and Phone Number of M/WBE	Type of Work To Be Performed	Subcontract Amount			
		Black	Hispanic	Women	Other (Please Specify)
1.		---	---	---	---
2.		---	---	---	---
3.		---	---	---	---
4.		---	---	---	---
5.		---	---	---	---
6.		---	---	---	---
7.		---	---	---	---
8.		---	---	---	---
9.		---	---	---	---
10.		---	---	---	---
Totals		\$ 0.00	\$ 0.00	\$ 0.00	\$ 0.00

Original Contract Amount	<u>\$3,894,228.70</u>	Original Participation	<u> </u>	Percent Participation	<u>15.00</u>
Adjusted Contract Amount	<u>\$4,186,851.87</u>	Adjusted Participation	<u> </u>	Adjusted Percent	<u>15.00</u>

M/WBE
