

PALM BEACH COUNTY
BOARD OF COUNTY COMMISSIONERS
AGENDA ITEM SUMMARY

| | | |
|-------------------------------|---|---|
| Meeting Date: August 14, 2018 | <input checked="" type="checkbox"/> Consent | <input type="checkbox"/> Regular |
| | <input type="checkbox"/> Workshop | <input type="checkbox"/> Public Hearing |

| | |
|----------------|------------------------------------|
| Department: | Engineering and Public Works |
| Submitted By: | Engineering and Public Works |
| Submitted For: | Construction Coordination Division |

I. EXECUTIVE BRIEF


Motion and Title: Staff recommends motion to approve: Change Order No. 3 with Community Asphalt Corp. (CAC) in the amount of \$16,721.74, including a time extension of 153 days, for the construction of the drainage system on Old Dixie Highway from Park Avenue to Northlake Boulevard, R2016-1316 (project).

SUMMARY: Approval of Change Order No. 3 will allow CAC to construct the drainage system required for the project, and will include a time extension of 153 days due to unforeseen field conditions. Per PPM CW-F-050, this change order exceeds the 90-day threshold relating to staff approvals of change orders to contracts, and requires the Board of County Commissioners' approval. The Small Business Enterprise (SBE) goal for all contracts is 15%. CAC proposed 15.6% SBE participation. Their SBE participation for this change order is 0.0% and their cumulative SBE participation to date is 4.4%, however, CAC should be able to meet their SBE goal by the end of the contract. District 1 & 7 (LBH)

Background and Justification: During construction of the project, it was discovered that there was a conflict between the existing Seacoast Utility Authority's force main and the proposed new drainage system. It was also determined that the bid documents did not include a bid item for adjustment of the existing force main, resulting in the need for additional work, as well as time to accomplish this additional work.

- Attachments:**
1. Location Map
 2. Change Order No. 3 with Attachments A, B – F and Schedule 1

| | |
|---|--------------|
| Recommended by:  | 18 JULY 2018 |
| Department Director | Date |

| | |
|--|---------|
| Approved by:  | 7/18/18 |
| Assistant County Administrator | Date |

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

| Fiscal Years | 2018 | 2019 | 2020 | 2021 | 2022 |
|-------------------------|-----------------|------------|------------|------------|------------|
| Capital Expenditures | <u>\$16,722</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> |
| Operating Costs | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> |
| External Revenues | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> |
| Program Income (County) | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> |
| In-Kind Match (County) | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> |
| NET FISCAL IMPACT | <u>\$16,722</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> | <u>-0-</u> |
| # ADDITIONAL FTE | | | | | |
| POSITIONS (Cumulative) | | | | | |

Is Item Included in Current Budget?

Yes X

No

Does this item include the use of federal funds?

Yes

No X

Budget Account No:

Fund 3501 Dept 361 Unit 1064 Object 6551

Recommended Sources of Funds/Summary of Fiscal Impact:

Road Impact Fee Zone 1 Fund

Old Dixie Hwy/Park Ave - Northlake

Change Order #3

\$16,721.74

C. Departmental Fiscal Review:

Aluikovalainen

III. REVIEW COMMENTS

A. OFMB Fiscal and/or Contract Dev. and Control Comments:

Jim Pore 7/10/18
OFMB
7/10/18
7/16
7/10
7/10

Dr. J. Jansburg 7/12/18
Contract Dev. and Control
7/12/18

B. Approved as to Form and Legal Sufficiency:


MB Herman 7/16/2018
Assistant County Attorney

C. Other Department Review:

Department Director

This summary is not to be used as a basis for payment.

PROJECT LOCATION
OLD DIXIE HIGHWAY FROM
PARK AVENUE TO NORTHLAKE BOULEVARD
PALM BEACH COUNTY PROJECT NO. 2004506

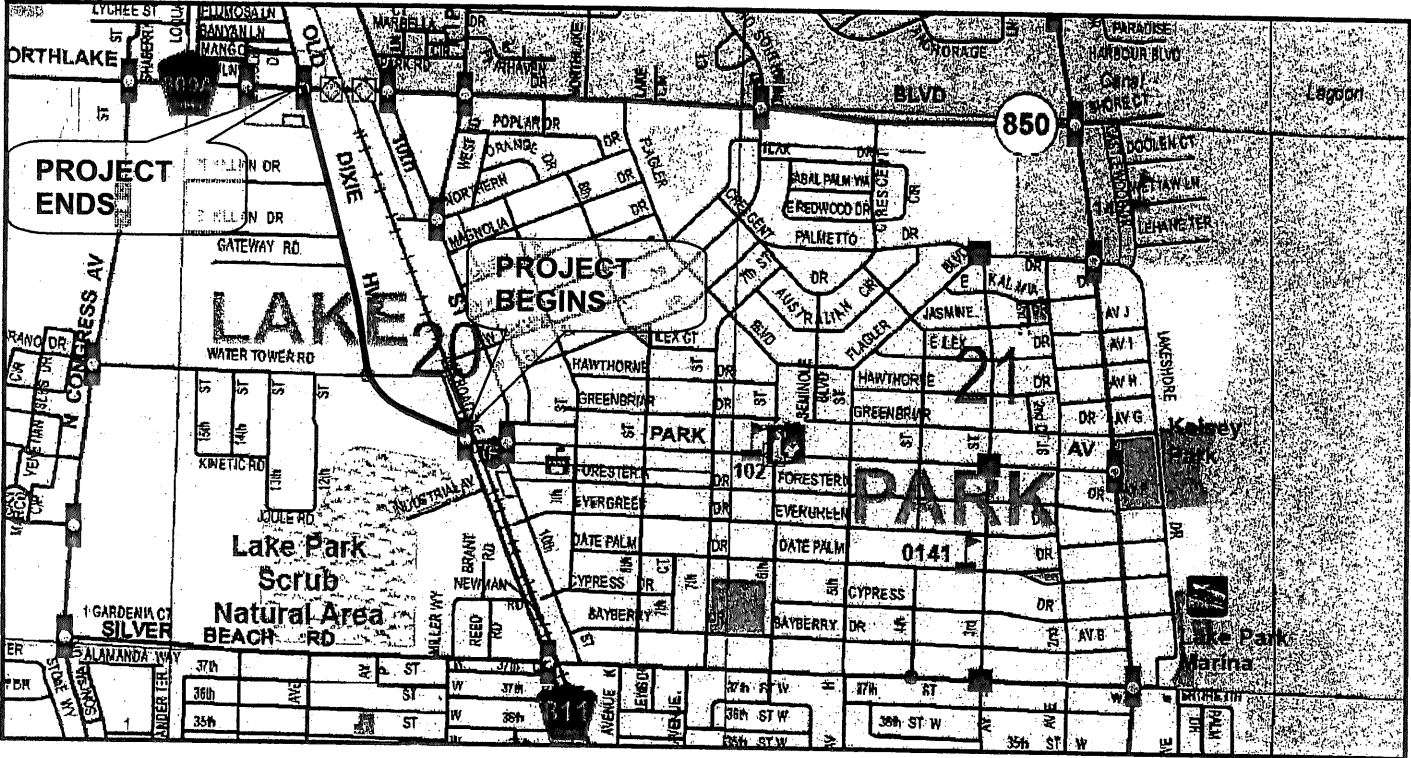

LOCATION MAP



PALM BEACH COUNTY BOARD OF COUNTY COMMISSIONERS
ENGINEERING & PUBLIC WORKS DEPARTMENT
P. O. BOX 21229, WEST PALM BEACH, FL 33416-1229



REQUEST: WORK ORDER NO. _____
NEW AUTHORIZATION _____
☒ CHANGE ORDER NO. 3 _____
SUPPLEMENTAL NO. _____
OTHER: _____

REQUESTING DIVISION: ROAD & BRIDGE _____
TRAFFIC _____
ROADWAY PRODUCTION _____
☒ CONSTRUCTION COOR. _____
STREETSCAPE _____

INFORMATION: DATE June 5, 2018
REQUESTOR Stephen O'Neil
COMMISSION DISTRICT NO: 1 and 7
RESOLUTION NO: R2016-1316
PBC PO NUMBER: KPD CSEP 100316-1

PROJECT LOCATION/LIMITS: Old Dixie Highway/Park Avenue to Northlake Boulevard
PROJECT NUMBER: 2004506 BUDGET LINE ITEM: 3501-361-1064-6551
CONTRACT NO: _____ CONTRACT DATE: September 27, 2016

CONTRACTOR/CONSULTANT/VENDOR: Community Asphalt Corp. VENDOR # COMM 0031
CONTACT: Brian Coblenz CONTACT PHONE NUMBER: 561-227-5323

Details: Change Order No. 3 for installation of conflict structure at STA. 225+00. Extend contract time 153 days.

Attachment "A" - Change Order Details
Attachment "B" - R.F.I. #1 from Contractor
Attachment "C" - P.B.C. Response to R.F.I. #1
Attachment "D" - Contractor's Submittal of Options
Attachment "E" - Seacoast Utilities Selection of Option 3
Attachment "F" - Contractor's Cost Proposal

The total amount of this request, per the attached documentation, is not to exceed \$16,721.74

The Small Business Enterprise (SBE) goal for this contract is 15.6%. The estimated SBE participation for this request is 0.0%.
The cumulative SBE participation to date for this Contract including this request is 0.9%.

Palm Beach County Engineering and Public Works Contact:

Mark A. Tomlinson Director, Construction Coordination 561-684-4180
Name Title Telephone Number

CONTRACTOR/CONSULTANT/VENDOR APPROVALS
Please indicate your receipt of this request by signing and returning this original document to our office.

Please sign below and submit with invoice at the completion of the project. Project completed in compliance with Contract and Project Specifications.

Signature Date 06/21/08

Signature Date

Paul Subellentrop, Executive Vice President
Print Name and Title

Print Name and Title

PALM BEACH COUNTY APPROVALS

BOARD APPROVAL? YES Date: 8/14/18

Signature Date 6/27/18

Signature Date 6/24/18

Deputy County Engineer Date 6/29/18

PBC Board of Co. Commissioner Date

ATTEST: Sharon R. Bock,
Clerk & Comptroller

Approved as to Form and Legal
Sufficiency:

(Deputy Clerk) Date

(County Attorney)

CHANGE ORDER

ATTACHMENT "A"

☐ Owner Initiated

☒ Differing Site Conditions

☐ Zoning/Code/Ordinance Changes

☐ Errors/Omissions/In Design

☐ Quantity Overruns/Underruns

☐ Request By Another Agency/Outside Party:

☐ A. Reimbursable

☐ B. Non-Reimbursable

☐ Other:

PROJECT: Old Dixie Highway/Park Avenue to Northlake Boulevard
(Name)
TO: Community Asphalt Corp.
(Contractor)

CHANGE ORDER NO: Three (3)
COUNTY PROJECT NO: 2004506
CONTRACT DATE: 9/27/16
RESOLUTION NO: R2016-1316
DISTRICT NO: 1 and 7

You are directed to make the following changes in this Contract:

In order to resolve an unforeseen conflict between the proposed new drainage and an existing 6" force main, install a conflict structure at STA. 225+00, including joint restraints, casing and spacers.

Extend contract time 153 days.

TOTAL

\$16,721.24

| | |
|---|--------------------|
| The original Contract Sum was | \$ 3,084,001.95 |
| Net change by previous Change Orders | \$ 30,122.07 |
| The Contract Sum prior to this Change Order was | \$3,114,124.02 |
| The Contract Sum will be increased by this Change Order | \$ 16,721.74 |
| The new Contract Sum including this Change Order will be | \$ 3,130,845.76 |
| The Contract Time will be increased by. | (153) Days |
| The Date of Completion including this Change Order therefore is | September 18, 2018 |

EXECUTION OF THIS CHANGE ORDER ACKNOWLEDGES FINAL SETTLEMENT OF, AND RELEASES ALL CLAIMS FOR COSTS AND TIME ASSOCIATED, DIRECTLY OR INDIRECTLY, WITH THE ABOVE-STATED MODIFICATION(S), INCLUDING ALL CLAIMS FOR CUMULATIVE DELAYS OR DISRUPTIONS RESULTING FROM, CAUSED BY, OR INCIDENT TO, SUCH MODIFICATION(S), AND INCLUDING ANY CLAIM THAT THE ABOVE-STATED MODIFICATION(S) CONSTITUTES, IN WHOLE OR PART, A CARDINAL CHANGE TO THE CONTRACT.

CONTRACTOR

Community Asphalt Corp.

Address

7795 Hooper Road West Palm Beach, FL 33411

NAME: Paul Suellentrop

TITLE: Executive Vice President

DATE: 06/21/18

ATTACHMENT "A"

Stephen O'Neil

From: Brian Coblentz <bcoblentz@cacorp.net>
Sent: Tuesday, May 02, 2017 5:34 PM
To: Stephen O'Neil
Cc: Scot Grove A.; Robert Niston; Mark Tomlinson
Subject: Old Dixie RFI's 1 and 2
Attachments: Old Dixie Hwy - RFI #1 - 6" Force Main Conflict; Old Dixie Hwy - RFI #2 12" Water Main Deflection

Steve,

Had to come home to gain access to my emails. Please see attached RFI's 1 and 2 for Old Dixie. After today's pre-con I believe we will be seeing a few more soon.

Regards,



Brian Coblentz
Project Manager
Community Asphalt Corp.
Phone: 561-227-5323
Fax: 561-790-1073
Cell: 561-718-4734
Email: bcoblentz@cacorp.net

DISCLAIMER: This e-mail message is intended only for the use of the individual or entity to which it is addressed, and may contain information that is privileged, confidential and exempt from disclosure under applicable law. If you are not the intended recipient, any dissemination, distribution or copying of this communication is strictly prohibited. If you have received this communication in error, please notify us immediately by reply email to bcoblentz@cacorp.net and delete or destroy all copies of the original message and attachments thereto.



Please consider the environment before printing this email.

Stephen O'Neil

From: Mike Griffin <mgriffin@ecunderground.net>
Sent: Monday, May 01, 2017 1:35 PM
To: Brian Coblentz
Cc: Curt Parcels; 'Bobby Burns'
Subject: Old Dixie Hwy - RFI #1 - 6" Force Main Conflict
Attachments: Old Dixie Roadway Plans - RFI #1 FM Conflict.pdf

Good Afternoon Brian,

Please see the attached page 38 that reflects the area where the 6" Force Main is shown in direct conflict with the proposed 42" RCP outfall pipe. Within the Bid Tab item #92 calls out for Adjust 6" DIP Water Main pipe but this would be incorrect as this reflects as a Force Main within the plans. Further pricing would need to be provided if this is an existing Force Main pipe, then different style pipe will be needed as well as methodology of draining the pipe when we perform the deflection. Please get this into Steve for his review and direction on what would need to be done in this area and it appears that the deflection could be accomplished deflecting above the drainage pipe and maintain the 30" to 36" cover for SUA. We will also need the Force Main atlas of this area so that we can see how much Force Main would need to be evacuated in order to accomplish this work as well. If you have any questions on this RFI, please don't hesitate to contact me.

Michael Griffin
Principal / Finances / Estimating



**East Coast Underground &
Construction Corp**
1100 Technology Place, Suite 122
West Palm Beach, Florida 33407
CUC1224751 CGC1514556

Mobile (561) 248-1747
Office (561) 932-1070
Fax (561) 228-8918
E-Mail: mgriffin@ecunderground.net
Visit our website at <http://www.ecunderground.net>

Stephen O'Neil

From: Stephen O'Neil
Sent: Thursday, May 25, 2017 3:49 PM
To: Brian Coblentz
Cc: Scot Grove A.; Robert Niston; Maroun Azzi
Subject: FW: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2
Attachments: 201603091512.pdf; ATT00001.htm

Brian,

Please see responses to RFI's 1 and 2 below and attached SUA plan.

Thanks,
Steve

Stephen O'Neil
Chief Construction Coordinator
Palm Beach County Department of Engineering & Public Works
Construction Coordination Division

Office 561-684-4180
E-Mail soneil@pbcgov.org

From: Maroun Azzi
Sent: Thursday, May 25, 2017 1:22 PM
To: Stephen O'Neil <SOneil@pbcgov.org>
Subject: Fwd: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Maroun Azzi, PE

Begin forwarded message:

From: "O'Reilly, Christopher N." <coreilly@acp-fl.com>
To: "Maroun Azzi" <MAzzi@pbcgov.org>
Subject: RE: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Maroun,

Response for RFI #1:

The pipe in question is a 6" Force main as shown on sheet 38. PIN 52 on sheet 2 and Bid Tab #94 both call out to "Adjust 6" DIP WM" which should have been stated as " Adjust 6" DIP FM".

In discussion with Seacoast we prefer to keep the deflection below the proposed drainage pipe as the detail shows on sheet UTV-2 unless the contractor can show how the minimum cover can be maintained outside of the proposed 42" pipe area.

See attached for Seacoast utilities in this area.

Response for RFI#2:

In discussion with Seacoast we prefer to keep the deflection below the proposed drainage pipe as the detail on sheet UTV-2 shows unless the contractor can show how the minimum cover can be maintained.

Let me know if we need to meet to discuss these issues.

Thanks,
Chris

Christopher N. O'Reilly, PE
American Consulting Professionals, LLC
2000 Palm Beach Lakes Blvd Suite 1000
West Palm Beach, FL 33409
561.253.9563
561.239.6027 (Cell)
coreilly@acp-fl.com

From: Maroun Azzi [<mailto:MAzzi@pbcgov.org>]
Sent: Wednesday, May 03, 2017 7:26 AM
To: O'Reilly, Christopher N.
Subject: Fwd: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Here we go

Maroun Azzi, PE

Begin forwarded message:

From: Stephen O'Neil <SOneil@pbcgov.org>
Date: May 3, 2017 at 6:49:50 AM EDT
To: Maroun Azzi <MAzzi@pbcgov.org>
Cc: Robert Niston <RNiston@pbcgov.org>, Scot Grove A. <SGrove@pbcgov.org>
Subject: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Maroun,

Please see attached RFI's.

Stephen O'Neil
Chief Construction Coordinator
Palm Beach County Department of Engineering & Public Works
Construction Coordination Division

Office 561-684-4180
EMail soneil@pbcgov.org

Under Florida law, e-mail addresses are public records. If you do not want your e-mail address released in response to a public records request, do not send electronic mail to this entity. Instead, contact this office by phone or in writing.

Stephen O'Neil

From: Brian Coblentz <bcoblentz@cacorp.net>
Sent: Thursday, October 26, 2017 12:05 PM
To: Stephen O'Neil
Cc: Scot Grove A.
Subject: FW: [EXTERNAL] RE: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Steve,

Please see below in response to RFI 2. Please advise on how we should proceed. Thank you.

Regards,



Brian Coblentz
 Project Manager
 Community Asphalt Corp.
Phone: 561-227-5323
Fax: 561-790-1073
Cell: 561-718-4734
Email: bcoblentz@cacorp.net

DISCLAIMER: This e-mail message is intended only for the use of the individual or entity to which it is addressed, and may contain information that is privileged, confidential and exempt from disclosure under applicable law. If you are not the intended recipient, any dissemination, distribution or copying of this communication is strictly prohibited. If you have received this communication in error, please notify us immediately by reply email to bcoblentz@cacorp.net and delete or destroy all copies of the original message and attachments thereto.



Please consider the environment before printing this email.

From: Mike Griffin [mailto:mgriffin@ecunderground.net]
Sent: Tuesday, October 24, 2017 6:49 PM
To: Brian Coblentz <bcoblentz@cacorp.net>
Cc: 'Bobby Burns' <bburns@ecunderground.net>
Subject: [EXTERNAL] RE: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Good Afternoon Brian,

In review of the response below from the County this will be a change order for the Force Main as the bid tab clearly called out a water main deflection and there will be different style pipe as well as methodology of this proposed deflection. With this in mind, there are numerous ways to accomplish this deflection and / or conflict area. They are as follows listed from the most expensive route to the most economical route in our opinion:

1. Deflect Force Main above the proposed drainage but 6" line will need to be evacuated, valves placed, temporary stabilized rock road approx. 1400 LF long to get the Vac trucks to the location of the deflection and interrupting service on this line for approx. 6 to 8 hour window.
2. Placement of line stops on each side of the drainage pipe and deflect the pipe over the drainage, evacuation of force main (minimal), temporary road for Vac truck to gain access to the location of the deflection and possible service interruption as were not sure how this line is feed or received.

3. Placement of Conflict Structure with casing pipe for the force main to go thru the drainage manhole which would avoid any service interruption, no deflection nor temporary rock roadway would be necessary.

Please send this into the County and SUA for their direction on this matter so that we can price accordingly depending on the direction they would like us to proceed. If there are any questions that you may have on any of this, please don't hesitate to contact me.

From: Brian Coblentz [<mailto:bcoblentz@cacorp.net>]
Sent: Thursday, May 25, 2017 3:49 PM
To: 'mgriffin@ecunderground.net'
Cc: Curt Parcels (cparcells@ecunderground.net); 'bburns@ecunderground.net'
Subject: FW: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Mike,

See below and attached.

Regards,



Brian Coblentz
Project Manager
Community Asphalt Corp.
Phone: 561-227-5323
Fax: 561-790-1073
Cell: 561-718-4734
Email: bcoblentz@cacorp.net

DISCLAIMER: This e-mail message is intended only for the use of the individual or entity to which it is addressed, and may contain information that is privileged, confidential and exempt from disclosure under applicable law. If you are not the intended recipient, any dissemination, distribution or copying of this communication is strictly prohibited. If you have received this communication in error, please notify us immediately by reply email to bcoblentz@cacorp.net and delete or destroy all copies of the original message and attachments thereto.

 Please consider the environment before printing this email.

From: Stephen O'Neil [<mailto:SOneil@pbcgov.org>]
Sent: Thursday, May 25, 2017 3:48 PM
To: Brian Coblentz
Cc: Scot Grove A.; Robert Niston; Maroun Azzi
Subject: FW: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Brian,

Please see responses to RFI's 1 and 2 below and

Stephen O'Neil
Chief Construction Coordinator
Palm Beach County Department of Engineering & Public Works
Construction Coordination Division

Stephen O'Neil

From: Stephen O'Neil
Sent: Monday, December 04, 2017 1:05 PM
To: Brian Coblentz
Cc: Maroun Azzi; Jim Lance; Scott Serra; Scot Grove A.; Mark Tomlinson
Subject: FW: [EXTERNAL] RE: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Categories: Red Category

Brian,

See email below from Jim Lance.
Assuming Option #3 would be the more economical, please submit a cost proposal for option #3.

Thank you

Stephen O'Neil
Chief Construction Coordinator
Palm Beach County Department of Engineering & Public Works
Construction Coordination Division

Office 561-684-4180
E-Mail soneil@pbcgov.org

From: Jim Lance [<mailto:jlance@sua.com>]
Sent: Monday, December 04, 2017 12:56 PM
To: Stephen O'Neil <SOneil@pbcgov.org>
Cc: Scot Grove A. <SGrove@pbcgov.org>; Maroun Azzi <MAzzi@pbcgov.org>; Scott Serra <sserra@sua.com>
Subject: RE: [EXTERNAL] RE: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

Stephen

Either the first or third option is acceptable to Seacoast. The line stops would not be an option.
If you utilize the conflict box please be sure shop drawings are submitted.
Thank you

Jim Lance
Construction/Development Manager
Seacoast Utility Authority
561-627-2900 extension 1347
jlance@sua.com

From: Stephen O'Neil [<mailto:SOneil@pbcgov.org>]
Sent: Friday, December 01, 2017 8:27 AM
To: Jim Lance <jlance@sua.com>
Cc: Scot Grove A. <SGrove@pbcgov.org>; Maroun Azzi <MAzzi@pbcgov.org>
Subject: FW: [EXTERNAL] RE: Old Dixie Highway, Park Ave. to Northlake Blvd. RFI #1 and #2

REQUEST FOR CHANGE ORDER #4

OLD DIXIE HWY FROM NORTH OF PARK AVE TO NORTHLAKE BLVD
PBC : 2004506
CAC : 7044



Community
Asphalt
OHL Group

DATE: Tuesday, January 02, 2018

DESCRIPTION: Conflict Structure at STA 225 offsite drainage
Request time extension of 30 days for procurement and installation. Time based off of immediate approval of CO to expedite the submittal process for the structure and approval and subject to change

LABOR BREAKDOWN

| DESCRIPTION | U/M | RATE | QTY | EXTENSION | BURDEN | TOTAL COST |
|--------------|-----|------|-----|-----------|--------|------------|
| | | \$ - | - | \$ - | 0.00% | \$ - |
| | | \$ - | - | \$ - | 0.00% | \$ - |
| | | \$ - | - | \$ - | 0.00% | \$ - |
| | | \$ - | - | \$ - | 0.00% | \$ - |
| | | \$ - | - | \$ - | 0.00% | \$ - |
| | | \$ - | - | \$ - | 0.00% | \$ - |
| | | \$ - | - | \$ - | 0.00% | \$ - |
| | | \$ - | - | \$ - | 0.00% | \$ - |
| | | \$ - | - | \$ - | 0.00% | \$ - |
| TOTAL LABOR: | | | | | | \$ - |

EQUIPMENT BREAKDOWN

| DESCRIPTION | U/M | RATE | QTY | EXTENSION |
|------------------|-----|------|-----|-----------|
| | | \$ - | - | \$ - |
| | | \$ - | - | \$ - |
| | | \$ - | - | \$ - |
| | | \$ - | - | \$ - |
| | | \$ - | - | \$ - |
| | | \$ - | - | \$ - |
| | | \$ - | - | \$ - |
| TOTAL EQUIPMENT: | | | | \$ - |

MATERIAL BREAKDOWN

| DESCRIPTION | U/M | RATE | QTY | EXTENSION |
|-----------------|-----|------|-----|-----------|
| | | \$ - | - | \$ - |
| | | | | \$ - |
| | | | | \$ - |
| | | | | \$ - |
| TOTAL MATERIAL: | | | | \$ - |

SUBCONTRACT

| SUBCONTRACTOR | U/M | RATE | QTY | EXTENSION |
|------------------------------|-----|--------------|------|--------------|
| East Coast Const (Utilities) | LS | \$ 14,231.27 | 1.00 | \$ 14,231.27 |
| | | \$ - | - | \$ - |
| | | | | \$ - |
| TOTAL SUBCONTRACT | | | | \$ 14,231.27 |

| | | |
|----------------------------|----|-----------|
| TOTAL LABOR: | \$ | - |
| TOTAL EQPT: | \$ | - |
| TOTAL MATL: | \$ | - |
| (+) 20% | \$ | - |
| TOTAL SUBC: | \$ | 14,231.27 |
| -) 17.5% Allowable Mark-up | \$ | 2,490.47 |
| SUBTOTAL: | \$ | 16,721.74 |
| PER DIEM COSTS | \$ | - |
| LESS CREDIT | \$ | - |
| BOND: | | |
| TOTAL COST: | \$ | 16,721.74 |



1100 Technology Pl., Suite 122
West Palm Beach, FL 33461
Phone: (561) 932-1070
Fax: (561) 228-8918
DBPR License # CUC1224751
DBPR License # CGC1514556

TO: Community Asphalt
ATTN: Brian Coblentz
RE: Old Dixie Hwy - Park Ave. to Northlake Blvd.
DATE: December 29, 2017

PROPOSAL # 16-06202
CHANGE ORDER # 5

| CHANGE ORDER | | | | | |
|------------------------|-------------------------------|-----|------|------------|------------|
| # | SERVICE ITEM | QTY | UNIT | UNIT PRICE | LINE TOTAL |
| 1 | INSTALL CONFLICT STRUCTURE AT | | | | \$ - |
| 2 | FORCE MAIN LOCATION W/ 16" | 1 | LS | 12,937.52 | 12,937.52 |
| 3 | STEEL CASING | | | | - |
| 4 | | | | | - |
| 5 | | | | | - |
| 6 | | | | | - |
| 7 | | | | | - |
| 8 | | | | | - |
| 9 | | | | | - |
| 10 | MARK-UP | 0.1 | % | 12,937.52 | 1,293.75 |
| SUB TOTAL: | | | | | 14,231.27 |
| CHANGE ORDER TOTAL: \$ | | | | | 14,231.27 |

PRICING NOTES:

- 1. Change Order is based upon directive given by Palm Baech County to provide a confclit structure at the discharge area of the 42" RCP drainage run at STA 225+00.
- 2. Split Casing will be placed around the existing 6" Force Main and all items will adhere to SUA specs.
- 3. Welder will be utilized to weld horizontal seams and bitumis will be placed over welded seams.
- 3. Daily rate back up sheets has been provided.

Submitted By:
EAST COAST UNDERGROUND & CONSTRUCTION CORP.

Accepted By:

Signed:

Signed: _____

By: Michael Griffin

By: _____

Date: 29-Dec-17

Date: _____

AMERICAN CONCRETE INDUSTRIES, Inc.

350 NORTH ROCK ROAD
FORT PIERCE, FLORIDA 34945
772-464-1187 · FAX (772) 595-9050

DATE: DECEMBER 27, 2017

TO: EAST COAST UNDERGROUND
1100 TECHNOLOGY PLACE, SUITE 122
WEST PALM BEACH, FLORIDA 33407

ATTENTION: MR, MIKE GRIFFIN

PROJECT: OLD DIXIE HIGHWAY

LOCATION: PALM BEACH COUNTY

ENGINEER: PALM BEACH COUNTY ENGINEERING

QUOTE #: 2017-0752

PLAN DATE: 7-28-11, NO REVISIONS

WE PROPOSE TO SUPPLY THE FOLLOWING MATERIALS:

| QUANTITY | DESCRIPTION | UNIT PRICE | EXTENSION |
|----------|--|------------|-----------|
| 1 | 5 FT. X 5 FT. CONFLICT STRUCTURE #219A W/U.S. FOUNDRY #170-X RING & COVER | 3450.00 | 3450.00 |

| | | |
|-----------|-------|----------|
| SUB TOTAL | \$ | 3,450.00 |
| SALES TAX | 6.00% | 207.00 |
| SUR TAX | 1.00% | 34.50 |
| TOTAL | \$ | 3,691.50 |

ALL MATERIAL SUBJECT TO ENGINEER'S APPROVAL.
QUANTITIES ARE ESTIMATED - UNIT PRICES TO PREVAIL. / F.O.B. JOBSITE.
PAYMENT TO BE MADE AS FOLLOWS: NET 30 DAYS. A FINANCE CHARGE AND/OR SERVICE CHARGE OF 1.5% PER MONTH, 18% PER YEAR WILL BE CHARGED ON ALL ACCOUNTS OVER 30 DAYS. IN THE EVENT THAT IT BECOMES NECESSARY TO INSTITUTE ACTION FOR COLLECTION OF AMOUNT ON ANY UNPAID BALANCE, BUYER AGREES TO PAY ALL COSTS OF COLLECTION, INCLUDING ATTORNEY'S FEES.
THIS PROPOSAL MAY BE WITHDRAWN BY ACI IF NOT ACCEPTED WITHIN 30 DAYS.

AUTHORIZED BY: AMERICAN CONCRETE INDUSTRIES, INC.

ACCEPTED BY: _____

(SIGNATURE) _____ (DATE) _____

ROBERT L. SNOWE, PRESIDENT

(PRINT NAME AND TITLE)

(SIGNATURE) _____ (DATE) _____

(PRINT NAME AND TITLE)



Formerly HD Supply Waterworks

Bid Proposal for OLD DIXIE 6" FM CONFLICT

| | | |
|----------|---|--|
| CUSTOMER | EAST COAST UNDERGROUND STOCK 039 WEST PALM BEACH, FL 33461 | Job OLD DIXIE 6" FM CONFLICT PALM BEACH GARDENS, FL Palm Beach County Bid Date: 12/28/2017 Bid #: 478056 |
| | Sales Representative Jim Amsler (M) 561-513-2028 (T) 561-848-4396 (F) 561-845-7267 jim.amsler@coreandmain.com | Core & Main 1101 W 17th St Riviera Beach, FL 33404 (T) 561-848-4396 |
| CONTACT | | |
| NOTES | | |



Formerly HD Supply Waterworks

Bid Proposal for OLD DIXIE 6" FM CONFLICT

EAST COAST UNDERGROUND
Job Location: PALM BEACH GARDENS, FL
Bid Date: 12/28/2017
Core & Main Bid #: 478056

Core & Main
1101 W 17th St
Riviera Beach, FL 33404
Phone: 561-848-4396
Fax: 561-845-7267

| Seq# | Qty | Description | Units | Price | Ext Price |
|------|-----|---|-------|------------------|-----------------|
| 20 | 10 | 16X.375 WALL STEEL CASING SPLIT | FT | 60.00 | 600.00 |
| 40 | 2 | 6X16 CASING SPACER SS | EA | 70.00 | 140.00 |
| 50 | 2 | 6X16 END SEAL | EA | 65.00 | 130.00 |
| 60 | 4 | UFR1390-C-6-I BELL HARNESS C900/DI PIPE TO PIPE IMP | EA | 45.00 | 180.00 |
| 70 | 1 | 5 GAL #50 BITUMASTIC COATING | EA | 205.00 | 205.00 |
| 80 | 2 | PHD 550-16 RISER CLAMP | EA | 60.00 | 120.00 |
| | | | | SUBTOTAL | 1,375.00 |
| | | | | Sub Total | 1,375.00 |
| | | | | Tax | 82.50 |
| | | | | Total | 1,457.50 |

SCHEDULE 1
LIST OF PROPOSED SBE-M/WBE SUBCONTRACTORS

PROJECT NAME: Old Dixie Hwy - From Park Ave to Northlake Blvd PROJECT NO. 2004506

NAME OF PRIME BIDDER: Community Asphalt Corp ADDRESS:

CONTACT PERSON: Brian Coblentz PHONE NO. 561-790-6467 FAX NO.

BID OPENING DATE: July 6, 2016 DEPARTMENT: Roadway/Construction

PLEASE IDENTIFY ALL APPLICABLE CATEGORIES OF SUBCONTRACTORS

Name, Address and Phone Number Subcontract Amount:

(Check one or both Categories)
Minority Business Small Business Black Hispanic Women Caucasian Other (Please Specify)

| | | | | | |
|-------------------------------|----|----|----|----|----|
| 1. NO SBE SUBCONTRACTORS USED | \$ | \$ | \$ | \$ | \$ |
| 2. | \$ | \$ | \$ | \$ | \$ |
| 3. | \$ | \$ | \$ | \$ | \$ |
| 4. | \$ | \$ | \$ | \$ | \$ |
| 5. | \$ | \$ | \$ | \$ | \$ |

(Please use additional sheets if necessary) Total \$ \$ \$ \$ \$

Total Bid Price: \$ 16,721.24 Total Value of SBE Participation \$ 0.00

- NOTE:
- The amounts listed on this form must be supported by the Subcontractors prices included on Schedule 2 in order to be counted toward goal attainment
 - Firms may be certified by Palm Beach County as an SBE and/or and M/WBE. If firms are certified as both an SBE and M/WBE, please indicate the dollar amount under the appropriate category.
 - M/WBE information is being collected for tracking purposes only.
