

PALM BEACH COUNTY
BOARD OF COUNTY COMMISSIONERS
AGENDA ITEM SUMMARY

Meeting Date: December 18, 2018	<input checked="" type="checkbox"/> Consent	<input type="checkbox"/> Regular
	<input type="checkbox"/> Workshop	<input type="checkbox"/> Public Hearing

Department:	Engineering & Public Works
Submitted By:	Engineering & Public Works
Submitted For:	Construction Coordination Division


I. EXECUTIVE BRIEF

Motion and Title: Staff recommends motion to approve: Change Order No. 1 with Engecon Construction, Inc. (Engecon) in the amount of \$113,188, including a time extension of 14 days, for the additional utility items requested by Palm Beach County (County) Water Utilities Department (WUD) on the Sandalfoot Boulevard/State Road 7 and SW 3rd Street/State Road 7 bridge replacements project R2018-0365. Per PPM CW-F-050, this change order exceeds the \$100,000 threshold relating to staff approvals of change orders to contractors, and requires the Board of County Commissioners' approval.

SUMMARY: Approval of Change Order No. 1 will compensate for additional costs and delays due to upsizing the County WUD existing force main from 8" to 12". During the course of the bridge construction, WUD requested an upgrade of their existing 8" force main. All costs will be paid by WUD. The Small Business Enterprise (SBE) goal for all contracts is 15%. Engecon proposed 25% SBE participation. Their SBE participation for this change order is 100% and their cumulative SBE participation to date including this change order is 66%. District 5 (LBH)

Background and Justification: The upgrade is required in order to accommodate their expanded services to their customers.

- Attachments:**
- 1. Location Map
 - 2. Change Order No. 1 with Exhibits A, B, C, D and Schedules 1 and 2

Recommended by:		4 DEC 2018
	County Engineer	Date

Approved by:		12/4/18
	Assistant County Administrator	Date

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

Fiscal Years	2019	2020	2021	2022	2023
Capital Expenditures	<u>\$113,188</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>
Operating Costs	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>
External Revenues	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>
Program Income (County)	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>
In-Kind Match (County)	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>
NET FISCAL IMPACT	<u>\$113,188</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>	<u>-0-</u>
# ADDITIONAL FTE					
POSITIONS (Cumulative)					

Is Item Included in Current Budget? Yes X No
Does this item include the use of federal funds? Yes No X

Budget Account No:

Fund 4011 Dept 721 Unit W007 Object 6543

Recommended Sources of Funds/Summary of Fiscal Impact:

Capital Improvements
Utility Line Relocations-County Road Projects

Change Order #1 \$113,188.00

C. Departmental Fiscal Review: Aluikovalanen

III. REVIEW COMMENTS

A. OFMB Fiscal and/or Contract Dev. and Control Comments:

Joe Pen 11/24/18
OFMB 11/21/18

A. J. Javelle 11/29/18
Contract Dev. and Control 11/28/18 TW

B. Approved as to Form
and Legal Sufficiency:

JP Herman 12/4/2018
Assistant County Attorney

C. Other Department Review:

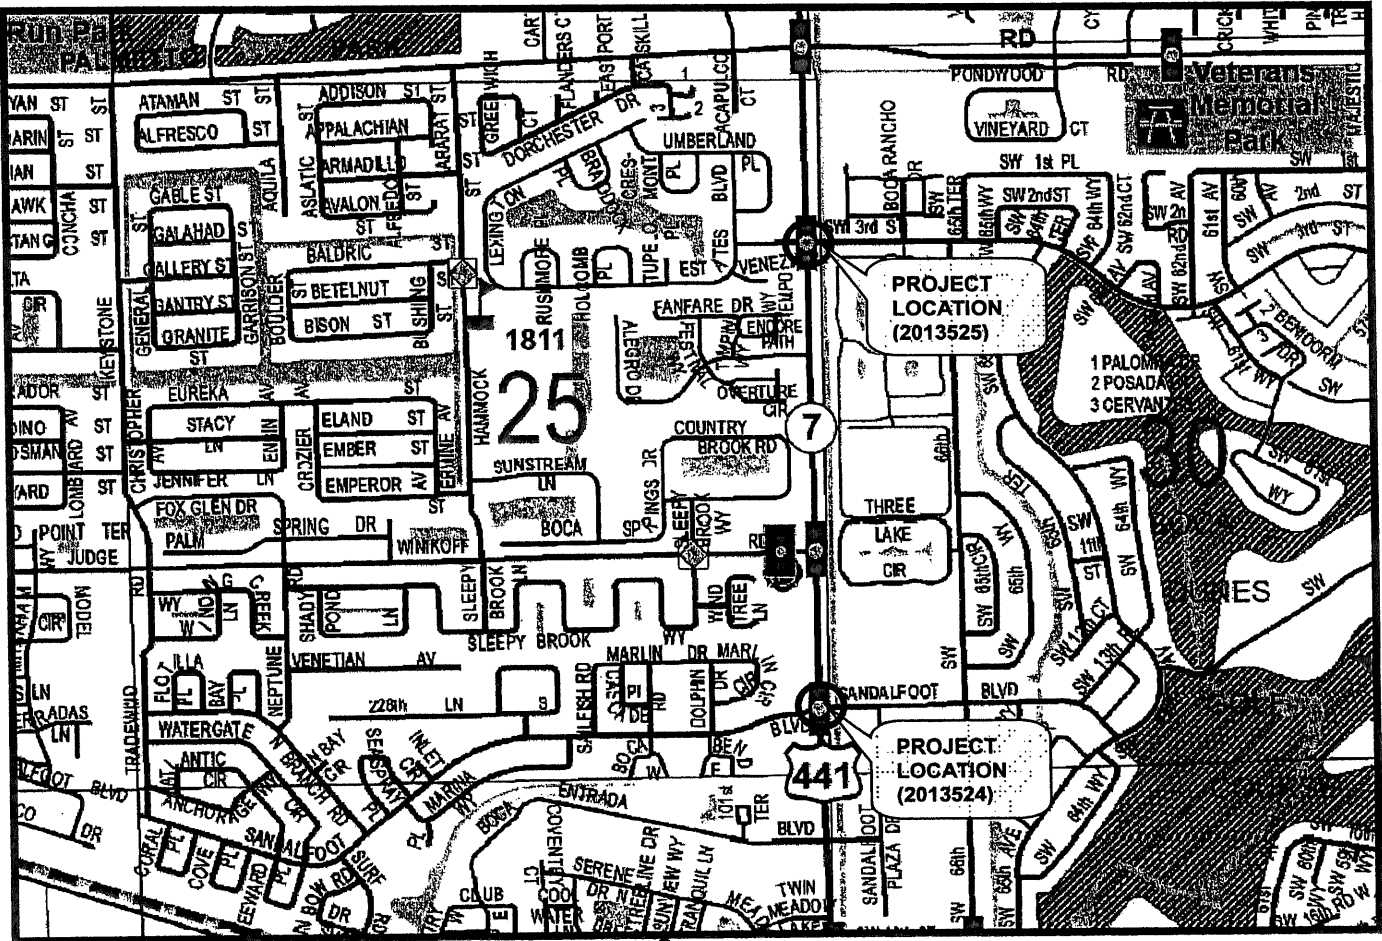
Department Director

This summary is not to be used as a basis for payment.

PROJECT LOCATION

SANDALFOOT BOULEVARD AND STATE ROAD 7
&
SW 3RD STREET AND STATE ROAD 7
BRIDGE REPLACEMENTS

PALM BEACH COUNTY PROJECT NO. 2013524 & 2013525



LOCATION MAP

**PALM BEACH COUNTY BOARD OF COUNTY COMMISSIONERS
ENGINEERING & PUBLIC WORKS DEPARTMENT
P. O. BOX 21229, WEST PALM BEACH, FL 33416-1229**



REQUEST:

___ WORK ORDER NO. _____
___ NEW AUTHORIZATION _____
☒ CHANGE ORDER NO. 1
___ SUPPLEMENTAL NO. _____
___ OTHER: _____

REQUESTING DIVISION:

___ ROAD & BRIDGE
___ TRAFFIC
___ ROADWAY PRODUCTION
☒ CONSTRUCTION COOR.
___ STREETSCAPE

INFORMATION:

DATE 10/22/18
REQUESTOR John Kopelakis
COMMISSION DISTRICT NO: 5
RESOLUTION NO: R2018-0365
PBC PO NUMBER: _____

PROJECT LOCATION/LIMITS: Sandalford Blvd. and State Road 7 and SW 3rd Street and State Road 7 Bridge

Replacements

PROJECT NUMBER: 2013524 & 2013525
CONTRACT NO: _____

BUDGET LINE ITEM: _____
CONTRACT DATE: 4/10/18

CONTRACTOR/CONSULTANT/VENDOR: Engecon Construction, Inc. **VENDOR #** _____
CONTACT: Geoff Waite **CONTACT PHONE NUMBER:** 561-585-1565

Details: Change Order #1 is for additional utility items requested by Palm Beach County Water Utilities Department. Includes contract extension of 14 days.

Exhibit "A" – Change Order Detail
Exhibit "B" – Contractor's Change Order Cost Proposal to upgrade force main
Exhibit "C" – PBCWUD Budget Availability Statement
Exhibit "D" – Bond Rider

The total amount of this request, per the attached documentation, is not to exceed \$113,188.00

The Small Business Enterprise (SBE) goal for this contract is 25 %. The estimated SBE participation for this request is 100 %.
The cumulative SBE participation to date for this Contract including this request is 66 %.

Palm Beach County Engineering and Public Works Contact:

Mark A. Tomlinson	Director, Construction Coordination	561-684-4180
Name	Title	Telephone Number

CONTRACTOR/CONSULTANT/VENDOR APPROVALS

Please indicate your receipt of this request by signing and returning this original document to our office.

[Signature] 11/15/2018
Signature Date

Raque NAM / President
Print Name and Title

Please sign below and submit with invoice at the completion of the project. Project completed in compliance with Contract and Project Specifications.

Signature Date

Print Name and Title

PALM BEACH COUNTY APPROVALS

[Signature] 11-16-18
Division Approval Date

[Signature] 11/16/18
Deputy County Engineer Date

BOARD APPROVAL? YES **Date:** 12/18/18

[Signature] 11/15/18
Budget Approval Date

PBC Board of Co. Commissioner Date

ATTEST: Sharon R. Bock,
Clerk & Comptroller

**Approved as to Form and Legal
Sufficiency:**

(Deputy Clerk) Date

(County Attorney)

CHANGE ORDER

☒ Owner Initiated
☐ Differing Site Conditions
☐ Zoning/Code/Ordinance Changes
☐ Errors/Omissions/In Design

☐ Quantity Overruns/Underruns
☐ Request By Another Agency/Outside Party:
PBCWUD
☒ A. Reimbursable ☐ B. Non-Reimbursable
☐ Other:

PROJECT: Sandalfoot Blvd. and State Road 7 and SW 3rd Street
and State Road 7 Bridge Replacements
(Name)
TO: Engecon Construction, Inc.
(Contractor)

CHANGE ORDER NO: 1 (ONE)
COUNTY PROJECT NO: 2013524/2013525
CONTRACT DATE: 4/10/18
RESOLUTION NO: R2018-0365
DISTRICT NO: 5


You are directed to make the following changes in this Contract:

Additional utility items requested by PBCWUD. Upgrading existing force main from 8" to 12" (See Exhibit "B") - Lump Sum	112,322.00
Bond Rider – Lump Sum	866.00
TOTAL	\$113,188.00

Extend contract time 14 days.

The original Contract Sum was	\$4,413,458.07
Net change by previous Change Orders	\$ -0-
The Contract Sum prior to this Change Order was	\$4,413,458.07
The Contract Sum will be increased by this Change Order	\$ 113,188.00
The new Contract Sum including this Change Order will be	\$4,526,646.07
The Contract Time will be increased by.	(14) Days
The Date of Completion including this Change Order therefore is	September 12, 2019

EXECUTION OF THIS CHANGE ORDER ACKNOWLEDGES FINAL SETTLEMENT OF, AND RELEASES ALL CLAIMS FOR, COSTS AND TIME ASSOCIATED, DIRECTLY OR INDIRECTLY, WITH THE ABOVE-STATED MODIFICATION(S). INCLUDING ALL CLAIMS FOR CUMULATIVE DELAYS OR DISRUPTIONS RESULTING FROM, CAUSED BY, OR INCIDENT TO, SUCH MODIFICATION(S), AND INCLUDING ANY CLAIM THAT THE ABOVE-STATED MODIFICATION(S) CONSTITUTES, IN WHOLE OR PART, A CARDINAL CHANGE TO THE CONTRACT.


CONTRACTOR
2290 10th Ave West #408
Address
Lake Worth FL 33461

NAME: RANA NAIM
TITLE: President
DATE: 11/2/2018

ATTACHMENT "A"



Certified SBE / DBE

PROPOSAL (Rev B)

Phone: (561) 585-1565

Fax: (561)-753-1467

SANDALFOOT BOULEVARD AND STATE ROAD 7, AND SW 3RD STREET AND STATE ROAD 7 PALM BEACH COUNTY PROJECT NO. 2013524 & 2013525					
---	--	--	--	--	--

79A	12" DIP Force Main	72	LF	\$380.00	\$27,360.00
80A	12" Flange DIP Force Main	57	LF	\$550.00	\$31,350.00
81A	12" Gate Valve & Valve Box	2	EA	\$4,040.00	\$8,080.00
83A	F&I DIP Fittings w/Joint Restraint	0.7	TN	\$25,714.29	\$18,000.00
85A	Fan Guard with support struts	2	EA	\$5,766.00	\$11,532.00
86A	Connect to Existing Force Main	2	EA	\$8,000.00	\$16,000.00

\$112,322.00

	Bond Fee	1	EA	\$866.00	\$866.00
--	----------	---	----	----------	----------

TOTAL

\$113,188.00

Request for a 14 Day Time Extension.					
--------------------------------------	--	--	--	--	--

John Kopelakis

From: John Kopelakis
Sent: Monday, July 16, 2018 8:55 AM
To: 'robert waite'
Cc: Christopher Little W.
Subject: FW: Sandalfoot Blvd Water Main and Force Main Relocation Project - PBC 2013-524 & 2013-525
Attachments: Re: 12" Force Main @ Sandalfoot - Revised Pricing

Hello Geoff,
PBCWU has agreed to the revised C.O. please see attached and proceed.
Thank you,

From: Jennifer Prettel <JPrettel@pbcwater.com>
Sent: Monday, July 16, 2018 8:38 AM
To: John Kopelakis <JKopelak@pbcgov.org>; Frantz Fenelon <FFenelon@pbcwater.com>
Cc: Christopher Little W. <CWLittl@pbcgov.org>; Henry Melendez <hmelendez@pbcwater.com>; Gaverio Dixon <GDixon@pbcwater.com>; Vincent Riccobono <VMRiccobono@pbcwater.com>; geoff waite/raquel naim <engeconconstruction@gmail.com>; Frantz Fenelon <FFenelon@pbcwater.com>
Subject: RE: Sandalfoot Blvd Water Main and Force Main Relocation Project - PBC 2013-524 & 2013-525

Good Morning John:

We have agreed to proceed with the change order. See attached e-mail for the proposal that we have agreed to with Engecon. Please go ahead and direct them to proceed.

Thanks,

Jennifer

INTEROFFICE COMMUNICATION
PALM BEACH COUNTY WATER UTILITIES DEPARTMENT
BUDGET AVAILABILITY STATEMENT

DATE: October 19, 2018

TO: John Kopelakis, Chief Construction Coordinator
 Department of Engineering and Public Works

FROM: Guy Eggertsson, Fiscal Manager 1 *Guy Eggertsson*
 Water Utilities Department

RE: Sandalfoot Blvd @ SR 7 Bridge Over LWDD E-1 Canal
 PBC Project #2013-524
 WUD Project #15-054

FISCAL IMPACT ANALYSIS:

Summary of Fiscal Impact:

Is item included in current budget? Yes X No ____

Budget Account Number:

Fund	Agency	Organization	Object	Amount
4011	721	W007	6543	\$112,322.00

Sources of Funds:

Water Utilities Department user fees

**INTEROFFICE COMMUNICATION
PALM BEACH COUNTY WATER UTILITIES DEPARTMENT**

BUDGET AVAILABILITY STATEMENT

DATE: October 31, 2018

TO: John Kopelakis, Chief Construction Coordinator
 Department of Engineering and Public Works

FROM: Guy Eggertsson, Fiscal Manager 1
 Water Utilities Department

Guy Eggertsson

RE: Sandalfoot Blvd @ SR7 Bridge Over LWDD E-1 Canal
 PBC Project #2013-524
 WUD Project #15-054

FISCAL IMPACT ANALYSIS:

Summary of Fiscal Impact:

Is item included in current budget? Yes X No ____

Budget Account Number:

Fund	Agency	Organization	Object	Amount
4011	721	W007	6543	\$866.00

Sources of Funds:

Water Utilities Department user fees

RIDER

TO BE ATTACHED TO AND FORM PART OF

Performance and Payment Bonds NO. 4226349
(Bond Type) *(Bond Number)*
IN FAVOR OF Palm Beach County
(Obligee)
ON BEHALF OF Engecon Construction, Inc.
(Principal)
EFFECTIVE January 17, 2018
(Original Effective Date)

PROJECT: Project Nos. 2013524 & 2013525, Sandalfoot Blvd and State Road 7 & SW 3rd Street & State Road 7 Bridge Replacements, Palm Beach County, FL

IT IS AGREED THAT, in consideration of the original premium charged for this bond, and any additional premium that may be properly chargeable as a result of this rider.

The Surety, Great American Insurance Company,
hereby gives its consent to change;

Bond/Contract Amount

FROM: Old Bond Amount = \$4,413,458.07



TO: New Bond Amount = \$4,526,646.07

REASON: To include changes to contract through and including Proposal (Rev B)

EFFECTIVE: October 29, 2018

PROVIDED, however that the bond shall be subject to all its agreements, limitations, and conditions except as herein expressly modified, and that the liability of the Surety under the bond and under the bond as changed by this rider shall not be cumulative.

SIGNED, AND SEALED this 29th day of October, 2018.

Engecon Construction, Inc.
Principal
By: 
Great American Insurance Company
Surety

April L. Lively, Attorney-in-fact
Inquiries: (407) 834-0022

GREAT AMERICAN INSURANCE COMPANY®

Administrative Office: 301 E 4TH STREET • CINCINNATI, OHIO 45202 • 513-369-5000 • FAX 513-723-2740

The number of persons authorized by
this power of attorney is not more than NINE

No. 0 20715

POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS: That the GREAT AMERICAN INSURANCE COMPANY, a corporation organized and existing under and by virtue of the laws of the State of Ohio, does hereby nominate, constitute and appoint the person or persons named below, each individually if more than one is named, its true and lawful attorney-in-fact, for it and in its name, place and stead to execute on behalf of the said Company, as surety, any and all bonds, undertakings and contracts of suretyship, or other written obligations in the nature thereof; provided that the liability of the said Company on any such bond, undertaking or contract of suretyship executed under this authority shall not exceed the limit stated below

	Name	Address	Limit of Power
J.W. GUIGNARD	CHRISTINE MORTON	ALL OF	ALL
BRYCE R. GUIGNARD	JENNIFER L. HINDLEY	LONGWOOD, FLORIDA	\$100,000,000
PAUL J. CIAMBRIELLO	MARGIE L. MORRIS		
APRIL L. LIVELY	EILEEN C. HEARD		

DEBORAH ANN MURRAY

TAMPA, FLORIDA

This Power of Attorney revokes all previous powers issued on behalf of the attorney(s)-in-fact named above
IN WITNESS WHEREOF the GREAT AMERICAN INSURANCE COMPANY has caused these presents to be signed and attested by its appropriate officers and its corporate seal hereunto affixed this 9TH day of MARCH 2018
Attest
GREAT AMERICAN INSURANCE COMPANY



Atty L C B
Assistant Secretary

David C Kitchen
Divisional Senior Vice President

STATE OF OHIO, COUNTY OF HAMILTON - ss:

DAVID C KITCHIN (877-377-2405)

On this 9TH day of MARCH, 2018, before me personally appeared DAVID C. KITCHIN, to me known, being duly sworn, deposes and says that he resides in Cincinnati, Ohio, that he is a Divisional Senior Vice President of the Bond Division of Great American Insurance Company, the Company described in and which executed the above instrument; that he knows the seal of the said Company; that the seal affixed to the said instrument is such corporate seal; that it was so affixed by authority of his office under the By-Laws of said Company, and that he signed his name thereto by like authority.



Susan A. Kohorst
Notary Public, State of Ohio
My Commission Expires 05-10-2020

Susan A Kohorst

This Power of Attorney is granted by authority of the following resolutions adopted by the Board of Directors of Great American Insurance Company by unanimous written consent dated June 9, 2008.

RESOLVED: That the Divisional President, the several Divisional Senior Vice Presidents, Divisional Vice Presidents and Divisional Assistant Vice Presidents, or any one of them, be and hereby is authorized, from time to time, to appoint one or more Attorneys-in-Fact to execute on behalf of the Company, as surety, any and all bonds, undertakings and contracts of suretyship, or other written obligations in the nature thereof; to prescribe their respective duties and the respective limits of their authority; and to revoke any such appointment at any time.

RESOLVED FURTHER: That the Company seal and the signature of any of the aforesaid officers and any Secretary or Assistant Secretary of the Company may be affixed by facsimile to any power of attorney or certificate of either given for the execution of any bond, undertaking, contract of suretyship, or other written obligation in the nature thereof, such signature and seal when so used being hereby adopted by the Company as the original signature of such officer and the original seal of the Company, to be valid and binding upon the Company with the same force and effect as though manually affixed.

CERTIFICATION

I, STEPHEN C. BERAHA, Assistant Secretary of Great American Insurance Company, do hereby certify that the foregoing Power of Attorney and the Resolutions of the Board of Directors of June 9, 2008 have not been revoked and are now in full force and effect

Signed and sealed this 29th day of October, 2018



Atty L C B
Assistant Secretary

Invoice # 201801599	 GUIGNARD AN UNCOMMON BOND
DATE: 10/29/2018	1904 Boothe Circle, Longwood, FL 32750 407-834-0022 888-220-3780

To: Engecon Construction, Inc. 2290 10th Avenue North #408 Lake Worth, FL 33461	Client No.: 2013010
---	-----------------------------------

Effective Date	Surety	Bond No.
1/17/2018	Great American Insurance Company	4226349

Description				Premium Due	
<div>Obligee:</div> <div>Description:</div> <div>Bond Amount:</div> <div>Fees:</div> <div>Notes:</div>	Palm Beach County			\$866.00	
	Project Nos. 2013524 & 2013525, Sandalfoot Blvd and State Road 7 & SW 3rd Street & State Road 7 Bridge Replacements, Palm Beach County, FL				
	\$4,526,646.07				
	Agent Fees	Agency Fees	Carrier Fees		Total Fees
	\$0.00	\$0.00	\$0.00		\$0.00
Total Due:				\$866.00	

Payment due upon receipt.
Please reference the bond number or invoice number on your check.
If you have any questions, don't hesitate to contact our office.

WE SINCERELY APPRECIATE YOUR BUSINESS!

Bonding Since 1977

SCHEDULE 1

LIST OF PROPOSED SBE/M/WBE PRIME AND/OR SUBCONTRACTOR PARTICIPATION

PROJECT NAME OR BID NAME:	Sandalfoot Blvd. and State Road 7 & SW 3rd	PROJECT NO. OR BID NO.:	2013524 & 2013525
NAME OF PRIME BIDDER:	Engecon Construction, Inc.	ADDRESS:	2290 10th Ave. N, Suite #408, Lake Worth, FL. 33461
CONTACT PERSON:	Raquel Naim	PHONE NO.:	(561) 585-1565
BID OPENING DATE:	12/5/17	FAX NO.:	(561) 585-1565
		USER DEPARTMENT:	

THIS DOCUMENT IS TO BE COMPLETED BY THE PRIME CONTRACTOR AND SUBMITTED WITH BID PACKET. PLEASE LIST THE NAME, CONTACT INFORMATION, AND DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SBE/M/WBE SUBCONTRACTORS ON THIS PROJECT. IF THE PRIME IS AN SBE/M/WBE, PLEASE ALSO LIST THE NAME, CONTACT INFORMATION, AND DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME ON THIS PROJECT. THE PRIME AFFIRMS THAT IT WILL MONITOR THE SBES LISTED TO ENSURE THE SBES PERFORM THE WORK WITH ITS OWN FORCES.

(Check one or both Categories)			DOLLAR AMOUNT OR PERCENTAGE OF WORK				
<u>M/WBE</u> <u>SBE</u>							
Name, Address and Phone Number	Minority Business	Small Business	Black	Hispanic	Women	Caucasian	Other (Please Specify)
1. Engecon Construction, Inc. 2290 10th Ave. N, Suite #408 Lake Worth, FL. 33461 (561) 585-1565	<input type="checkbox"/>	<input checked="" type="checkbox"/>		X	X		
2.	<input type="checkbox"/>	<input type="checkbox"/>					
2.	<input type="checkbox"/>	<input type="checkbox"/>					
3.	<input type="checkbox"/>	<input type="checkbox"/>					
4.	<input type="checkbox"/>	<input type="checkbox"/>					

(Please use additional sheets, if necessary.)

(Please use additional sheets, if necessary.)

Total

Total Bid Price: \$ **\$113,188.00**

Total SBE/M/WBE Participation Dollar Amount or Percentage of Work: **100%**

I hereby certify that the above information accurate to the best of my knowledge:

Raquel Naim
Signature

/ President
Title

- Note:
- The amount listed on this form for a subcontractor must be supported by price or percentage listed on the signed Schedule 2 or signed proposal in order to be counted toward goal attainment.
 - Firms may be certified by Palm Beach County as an SBE and/or M/WBE. If firms are certified as both an SBE and M/WBE, please indicate the dollar amount or percentage under the appropriate category.
 - M/WBE information is being collected for tracking purposes only.

OSBA SCHEDULE 2
LETTER OF INTENT TO PERFORM AS AN SBE-M/WBE SUBCONTRACTOR

This document must be completed by the SBE-M/WBE Subcontractor and submitted with bid packet. Specify in detail the particular work items to be performed and the dollar amount and/or percentage for each work item. SBE credit will only be given for items which the SBE-M/WBE Subcontractor is SBE certified to perform. Failure to properly complete Schedule 2 may result in your SBE participation not being counted.

PROJECT NUMBER: 2013524 & 2013525 PROJECT NAME:
TO: Engecon Construction, Inc.

Sandalford Blvd. and State Road 7 & SW 3rd
Street & State Road 7 Bridge Replacements

(Name of Prime Bidder)

The undersigned is certified by Palm Beach County as a (check one or more, as applicable):

Small Business Enterprise ☒ Minority Business Enterprise
Black ☐ Hispanic ☒ Women ☒ Caucasian ☐ Other (Please Specify)

Date of Palm Beach County Certification: 10/27/18

The undersigned is prepared to perform the following described work in connection with the above project (additional sheets may be used as necessary):

Line Item/ Lot No. Item Description	Qty./Units	Unit Price	Total Price/ Percentage
<u>Upsizing existing force main from 8" to 12"</u>	<u>1/LS</u>	<u>\$113,188.00</u>	<u>\$113,188.00/100%</u>

at the following price or percentage: _____
(Subcontractor's Quote)


and will enter into a formal agreement for work with you conditioned upon your execution of a contract with Palm Beach County.

If undersigned intends to subcontract any portion of this job to a certified SBE or a non-SBE subcontractor, please list the name of the subcontractor and the amount below.


Price and/or Percentage _____
(Name of Subcontractor)

The Prime affirms that it will monitor the SBE's listed to ensure the SBE's perform the work with its own forces. The undersigned subcontractor affirms that it has the resources necessary to perform the work listed without subcontracting to non-certified SBE or any other certified SBE subcontractors except as noted above.

The undersigned subcontractor understands that the provision of this form to Prime Bidder does not prevent Subcontractor from providing quotations to other bidders.

Engecon Construction, Inc.
Print Name of Prime Contractor
By: 
Signature

Raquel Naim/ President
Print Name Title of Person Executing on Behalf of
Prime Contractor

Engecon Construction, Inc.
Print Name of SBE-M/WBE Subcontractor
By: 
Signature

Raquel Naim/ President
Print Name Title of Person Executing on Behalf of
SBE-M/WBE Subcontractor

Revised 10-11-2011

Date: 11/14/18
