

**PALM BEACH COUNTY
BOARD OF COUNTY COMMISSIONERS**

AGENDA ITEM SUMMARY

Meeting Date: **October 7, 2025**

**Consent [X]
Public Hearing []**

Regular []

Department: **Water Utilities Department**

I. EXECUTIVE BRIEF

Motion and Title: **Staff recommends motion to approve:** Change Order (CO) No. 2 to the NW Belle Glade Water Main Improvements, Zone 3 (Project) with Centerline Utilities, Inc. (Contractor) in the amount of \$357,500 and for a Contract project time extension of 30 calendar days.

Summary: On December 19, 2023, the Palm Beach County Board of County Commissioners (BCC) approved the Palm Beach County Water Utilities Department (PBCWUD) Contract (R2023-1865) with Contractor. The Project includes furnishing all materials, labor and equipment necessary to construct approximately 23,000 linear feet of new water main and other appurtenances in the City of Belle Glade. CO No. 2 is to furnish and install 65 water services and relocate the existing water service from the rear of the property to the front of the property and extends the contract duration by 30 days.

The Project is partially funded through the Palm Beach County Department of Housing and Economic Development (DHED) in the amount of \$1,109,605 under the grant from the United States Department of Housing and Urban Development (HUD) to Palm Beach County through the Community Development Block Grant (CDBG) program. Requirements of the Build America, Buy America Act (2CFR Part 184) and Davis-Bacon are applicable. Federally funded projects are subject to the federal Disadvantaged Business Enterprise (DBE) requirements and local governments are precluded from requiring local preferences during the solicitation. Per federal requirements, the Contractor undertook a good faith effort to identify and include DBE participants in this Project. DBE participation will be tracked as part of the Contract. Contractor is headquartered in Palm City, Florida. The funding of this CO No. 2 is included in the FY 2026 budget. (PBCWUD Project 18-002R) District 6 (MWJ)

Background and Justification: Zone 3 of the City of Belle Glade water distribution system experiences issues with leaks, unknown location of facilities, substandard pipe materials, undersized mains and valve isolation. The purpose of this Project is to improve the water distribution infrastructure within the project area including the relocation of water services from the rear to the front of the properties, increase fire protection, replacement of aging water distribution system, restore the service life and increase the efficiency and effectiveness of the distribution system. CO No. 2 will enable ease of access and maintenance by bringing the water services to the front of the properties.

Attachments:

1. Three(3) Originals of Change Order No. 2
2. Location Map
3. Ebix Compliance Summary Report

Recommended By: _____

Department Director

**9/15/25
Date**

Approved By: _____

Deputy County Administrator

**9/21/25
Date**

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

Fiscal Years	2026	2027	2028	2029	2030
Capital Expenditures	\$357,500	0	0	0	0
Operating Costs	0	0	0	0	0
External Revenues	0	0	0	0	0
Program Income (County)	0	0	0	0	0
In-Kind Match County	0	0	0	0	0
NET FISCAL IMPACT	\$357,500	0	0	0	0
# ADDITIONAL FTE POSITIONS (Cumulative)	0	0	0	0	0

Budget Account No.: Fund 4011 Dept 721 Unit W038 Object 6543

Is Item Included in Current Budget? Yes X No

Is this item using Federal Funds? Yes No X

Is this item using State Funds? Yes No X

Reporting Category N/A

B. Recommended Sources of Funds/Summary of Fiscal Impact:

One (1) time expenditure from user fees, connection fees and balance brought forward.

C. Department Fiscal Review:

Joony Foreman

III. REVIEW COMMENTS

A. OFMB Fiscal and/or Contract Development and Control Comments:

Lucy M. 9/11/2025
OFMB 9/11/25
9/11

Frankie Pacheco 9/11/25
Contract Development and Control
26 9.11.25

B. Legal Sufficiency:

9/15/25
Assistant County Attorney

C. Other Department Review:

Department Director

This summary is not to be used as a basis for payment.

CHANGE ORDER NO. 2
Palm Beach County Water Utilities Department
North West Belle Glade
Water Main Improvements, Zone 3
Resolution No. R2023-1865 Contract Dated December 19, 2023

Project Title: North West Belle Glade Water Main Improvements, Zone 3

PBCWUD Project No.: 18-002R

Contractor: Centerline Utilities, Inc.

Address: 2180 SW Poma Drive, Palm City, Florida 34990

Budget Line Item No.: 4011-721- W038 - 6543

District: 6

Notice to Proceed: 06/03/24

The Contract provides for 0% SBE participation. This Change Order includes 0% overall participation. The cumulative SBE participation, including this Change Order is 0%.

The Contract and this Change Order is subject to the County Emergency Ordinance 2025-014, approved by the Board of County Commissioners on June 3, 2025.

You are directed to make the following changes in this contract:

- 1.1 Furnish and Install 65 water services from rear to front yard at \$5,500/each. (30 days) \$357,500.00

Total: \$357,500.00



All Attachments to this Change Order are made a part of this Change Order and incorporated herein.

NOT VALID UNTIL SIGNED BY BOTH OWNER AND ENGINEER. SIGNATURE OF THE CONTRACTOR INDICATES THEIR AGREEMENT HERewith INCLUDING ANY ADJUSTMENT IN THE CONTRACT SUM OR CONTRACT TIME, AND NO ADDITIONAL COST OR TIME INDICATED HEREIN WILL BE RELATED TO THIS CHANGE

The Original Contract Sum was.....	\$7,895,974.70
Net Change by previous Change Order.....	\$0.00
The Contract Sum prior to this Change Order was.....	\$7,895,974.70
The Contract Sum will be increased/decreased by this Change Order.....	\$357,500.00
The New Contract Sum indicating this Change Order will be.....	\$8,253,474.70
The Date of Substantial Completion prior to this Change Order was	08/27/25
The Date of Final Completion prior to this Change Order was	09/26/25
The Contract Time will be increased/decreased by.....	30 Days
The Date of Substantial Completion including this Change Order.....	09/26/25
The Date of Final Completion including this Change Order.....	10/26/25



CHANGE ORDER NO. 2
Palm Beach County Water Utilities Department
North West Belle Glade
Water Main Improvements, Zone 3
Resolution No. R2023-1865 Contract Dated December 19, 2023

Execution of this change order acknowledges final settlement of, and releases, all claims for costs and time associated, directly or indirectly, with the above stated modification(s), including all claims for cumulative delays or disruptions resulting from, caused by, or incident to such modification(s), and including any claim that the above stated modification(s) constitutes, in whole or part, a cardinal change to the contract.

Centerline Utilities, Inc.	Palm Beach County Water Utilities Department	Palm Beach County Board of County Commissioners
CONTRACTOR	ENGINEER	OWNER
2180 SW Poma Drive Palm City, FL 34997	8100 Forest Hill Blvd. West Palm Beach, FL 33413	301 N. Olive Avenue West Palm Beach, FL 33401
ADDRESS	ADDRESS	ADDRESS
 SIGNATURE	 SIGNATURE	 SIGNATURE
Randy Stringer PRINT NAME	Joseph Tracardi PRINT NAME	Maria G. Marino PRINT NAME
Vice President TITLE	Engineer TITLE	Mayor TITLE
7/11/2025 DATE	7-14-25 DATE	DATE


STATE OF FLORIDA
COUNTY OF Martin

The foregoing instrument was acknowledged
before me by means of ☒ physical presence or ☐ online notarization
this 11th day of July, 2025
by Randy Stringer who is ☒ personally known
to me or ☐ has produced _____ as identification.


(Signature of Notary Public – State of Florida)


(Print, Type, or Stamp Commissioned Name of Notary Public)

Approved as to Form and Legal Sufficiency

By: 
County Attorney

Attest: Michael A. Caruso, Clerk of the Circuit Court
& Comptroller, Palm Beach County

By: _____
Deputy Clerk

CHANGE ORDER NO. 2
Palm Beach County Water Utilities Department
North West Belle Glade
Water Main Improvements, Zone 3
Resolution No. R2023-1865 Contract Dated December 19, 2023

LIST OF ATTACHMENTS

ATTACHMENT A	Change Order Summary and Categorization
ATTACHMENT B	Change Order Additions/Deletions Summary
ATTACHMENT C	OEBO Schedule 1 and Schedule 2
ATTACHMENT D	Location Map
ATTACHMENT E	Bond Rider (if applicable)
ATTACHMENT F	Supporting Documentation

ATTACHMENT B

CHANGE ORDER ADDITIONS/DELETIONS SUMMARY

Project Title: North West Belle Glade Water Main Improvements, Zone 3

Contractor: Centerline Utilities, Inc.

PBCWUD Project No.: 18-002R

Resolution No.: R2023-1865

Date Approved: 12/19/23

Contract Amount: \$7,895,974.70

APPROVAL LIMITS:

Department HeadContract Review Committee

Amount/DaysAmount/Days

Individual C.O.Cumulative C.O.\$100,000.00 - 180 Days\$200,000.00 - 180 Days\$375,000.00¹- 180 Days\$375,000.00 - 180 Days

C.O. NO.	DATE APPROVED	NET CHANGE ²	DEPARTMENT HEAD (ADDS PLUS DEDUCTS) ³		CONTRACT REVIEW COMMITTEE (ADDS PLUS DEDUCTS) ³		TOTAL DEPT. HEAD & CONTRACT REVIEW COMM. (ADDS PLUS DEDUCTS) ³		BOARD OF COUNTY COMMISSIONERS (ADDS PLUS DEDUCTS) ³		TOTALS
			AMOUNT	DAYS	AMOUNT	DAYS	AMOUNT	DAYS	AMOUNT	DAYS	
1	5/14/25	0.00	0.00	90	0.00	0	0.00	90	0.00	0	0.00
2	Pending	357,500.00	0.00	0	0	0	0.00	0	357,500.00	30	357,500.00
		357,500.00	0.00	90	0.00	0	0.00	90	357,500.00	30	357,500.00

NOTES:

- Per PPM #CW-F-050, upon approval of the C.O. in the cumulative amount of \$375,000.00 or 10% of the original Contract value must submit a Receive and File to the Board of County Commissioners and the cumulative value is reset.
- Net Change reflects the net amount of additions plus deductions.
- Adds plus Deducts reflects the absolute value of unrelated changes for use in determining the approval authority for the Change Order.

ATTACHMENT C
OEBO SCHEDULE 1

OFFICE OF EQUAL BUSINESS OPPORTUNITY COMPLIANCE PROGRAMS

OEBO SCHEDULE 1*

SOLICITATION/PROJECT/BID NAME: North West Belle Glade Water Main Improvement, Zone 318-002RSOLICITATION/PROJECT/BID NO.:

SOLICITATION OPENING/SUBMITTAL DATE: 08/30/2023COUNTY DEPARTMENT: PBCWUD

Section A PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME CONTRACTOR/CONSULTANT* ON THE PROJECT:

NAME OF PRIME RESPONDENT/BIDDER: Centerline Utilities, Inc. ADDRESS: 2180 SW Poma Drive Palm City, FL 34997

CONTACT PERSON: Spencer Weiner PHONE NO.: 239-247-4882 E-MAIL: Spencer@centerlineinc.com

PRIME'S DOLLAR AMOUNT OR PERCENTAGE OF WORK: \$357,500.00Non-SBE ☒ SBE ☐

SBE Prime's must include their percentage or dollar amount in the Total Participation line under section B.

Section B PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SUBCONTRACTORS/SUBCONSULTANTS ON THE PROJECT BELOW:

Subcontractor/Sub consultant Name	(Check all Applicable Categories)		DOLLAR AMOUNT OR PERCENTAGE OF WORK
	Non-SBE	SBE	
1.	☐	☐	
2.	☐	☐	
3.	☐	☐	
4.	☐	☐	
5.	☐	☐	

(Please use additional sheets if necessary)

Total Bid/Offer Price \$ 357,500.00

Total 0%

Total Certified SBE Participation \$

I hereby certify that the above information is accurate to the best of my knowledge: Randy ShingerVice President

Name & Authorized Signature Title

- Note:
- The amount listed on this form for a Subcontractor/sub consultant must be supported by price or percentage listed on the properly executed Schedule 2 or attached signed proposal.
 - Only those firms certified by Palm Beach County at the time of solicitation due date are eligible to meet the established OEBO Affirmative Procurement Initiative (API). Please check the applicable box and list the dollar amount or percentage under the appropriate demographic category.
 - Modification of this form is not permitted and will be rejected upon submittal.
 - If a Mandatory API goal applies, failure to submit a properly executed Schedule 2 will result in a determination of non-responsiveness to the solicitation.

ATTACHMENT C
OEBO SCHEDULE 2

N/A

OFFICE OF EQUAL BUSINESS OPPORTUNITY COMPLIANCE PROGRAMS

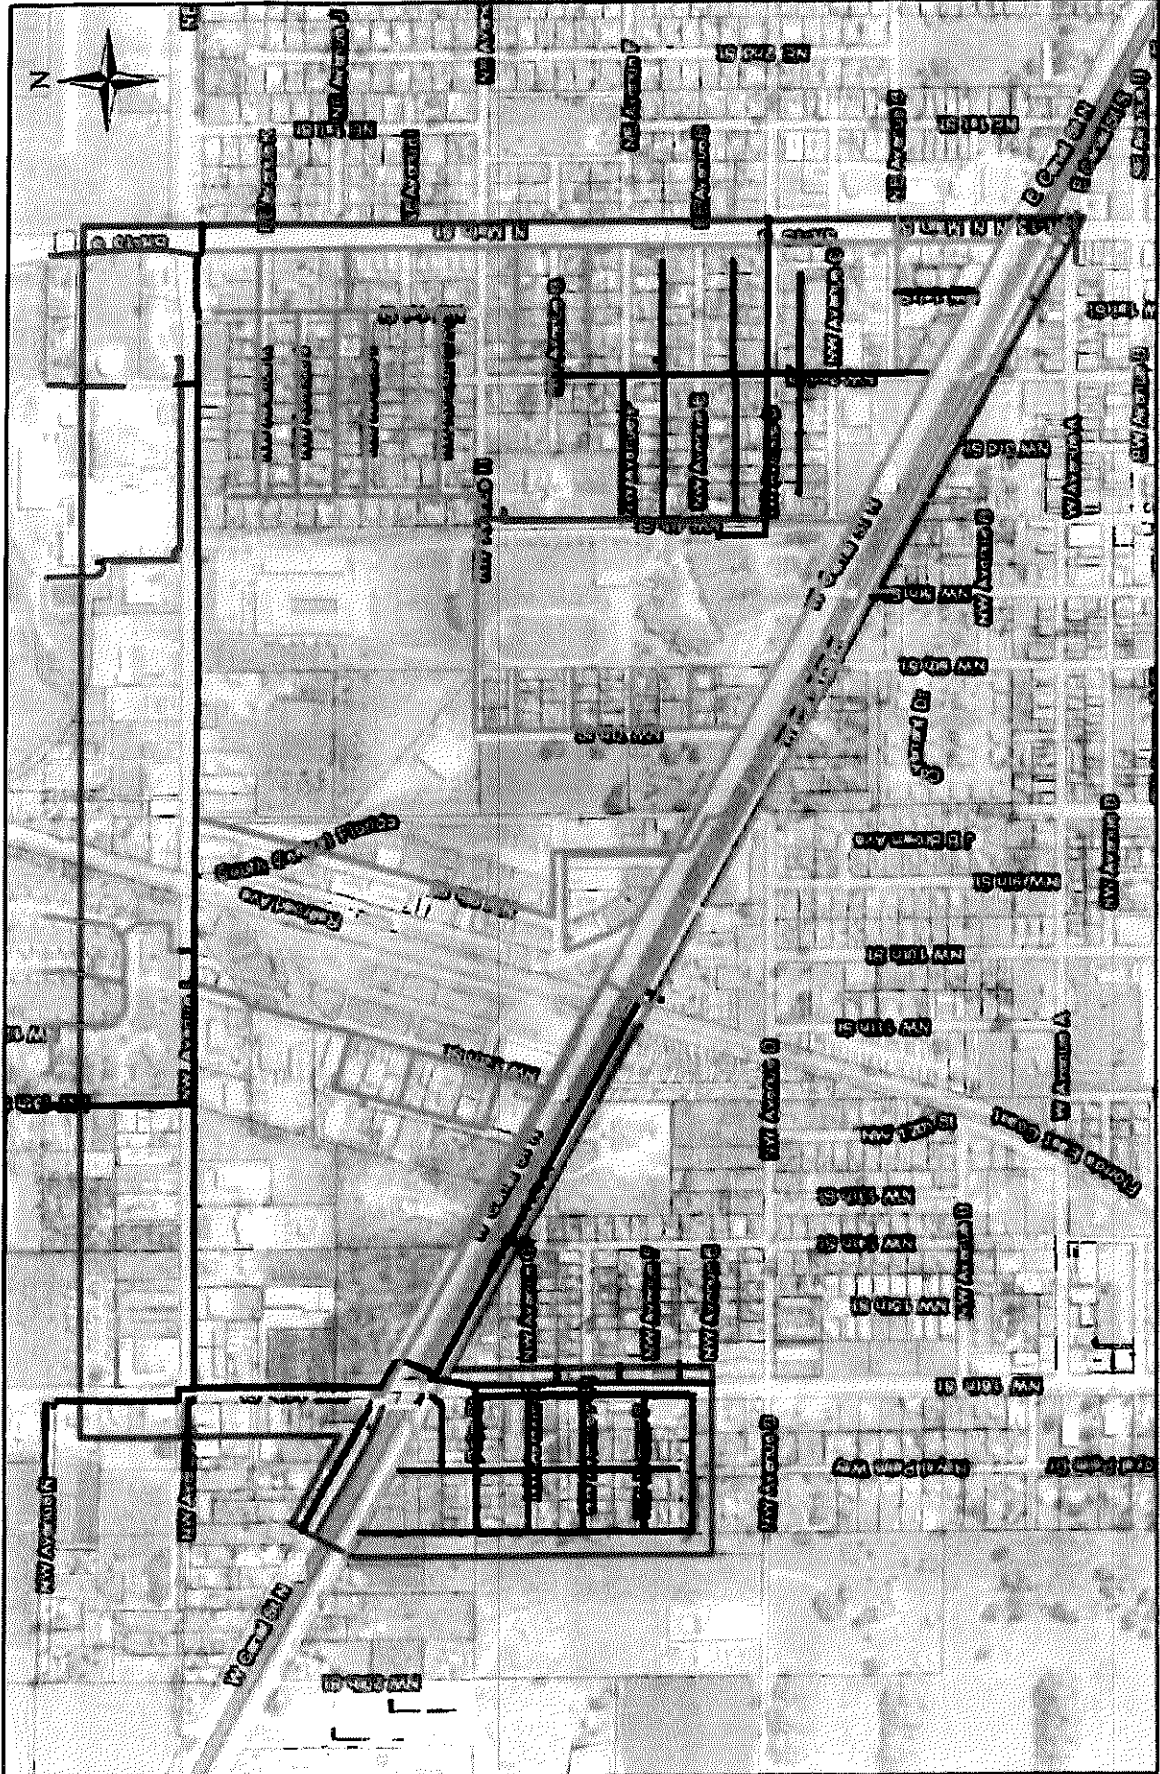
Revised 07-08-25

ATTACHMENT D

LOCATION MAP

PBCWUD Project No. 18-002R

Revised 07-08-25



North West Belle Glade Water Main Improvements, Zone 3
PBCWUD 18-002R



Legend

Pipe Installation

No Data

2000 - 2008

2010 - 2016

1986

1986

1976

1876

1992 - 1998

Project Boundary

0 390 780 1,560 Feet

1 inch = 780 feet

ATTACHMENT E

BOND RIDER
(IF APPLICABLE)

INCREASE RIDER

Rider to be attached to and form a part of Payment & Performance Bond Number 0250327, dated the 10th day of October, 2023 issued by Berkley Insurance Company a corporation organized and existing under the laws of the State of DE, (hereinafter called the "Surety"), on behalf of Centerline Utilities, Inc. dba Centerline, Inc (hereinafter called the "Principal"), in favor of Palm Beach County (hereinafter called the "Obligee").

It is understood and agreed that the penal sum of the attached bond is hereby INCREASED as follows:

From: \$7,895,974.70	Seven Million Eight Hundred Ninety Five Thousand Nine Hundred Seventy Four Dollars and 70/100
To: \$8,253,474.70	Eight Million Two Hundred Fifty Three Thousand Four Hundred Seventy Four Dollars and 70/100

The attached bond shall be subject to all of its terms, conditions and limitations except as herein modified.

IN WITNESS WHEREOF, the above bounden parties have executed this instrument under their several seals this 20th day of May, 2025, the name and corporate seal of each corporate party being hereto affixed and these presents duly signed by its undersigned representative, pursuant to authority of its governing body.

Centerline Utilities, Inc. dba Centerline, Inc
(Principal) (Seal)

2180 SW Poma Drive, Palm City, FL 04990
(Business Address)


Witness: 
Or Secretary's Attest

By 
(Signature) (Title)

Berkley Insurance Company
(Surety) (Seal)

475 Steamboat Road, Greenwich, CT 06830
(Business Address)

Witness: 
Or Secretary's Attest

By 
(Signature) Brett Rosenhaus (Title)
Attorney-in-Fact
Surety Phone No. 973-775-5021

(Seal) _____
Vincent P. Forte

ATTACHMENT F

SUPPORTING DOCUMENTATION

Revised 07-08-25

INTER-OFFICE COMMUNICATION

Palm Beach County

WATER UTILITIES DEPARTMENT

DATE: May 06, 2025

TO: File

FROM: Joseph Tanacredi P.E.



RE: Change order No. 2, WUD 18-002R

North West Belle Glade Water Main Improvements, Zone 3

2.1 Contractor request additional cost and 30 day time extension. The additional cost and time is due to furnishing and installing 65 additional water services from the water meter to the house connection. The contract line item quantity is under the amount needed to complete the project.



CENTERLINE, INC.

Earthwork – Underground Utilities – Roadways
www.centerlineinc.com

State Underground Utility License # CUC032651 State General Contractor License # CGC011107

July 16, 2025

Joseph Tanacredi
Palm Beach County Water Utilities Department
8100 Forest Hill Blvd
West Palm Beach, FL 33413

RE: Project: (WUD#18-002) NORTH WEST BELLE GLADE WATER MAIN IMPROVEMENT,
Zone 3
Rear to Front Service Connection Cost Agreement Letter

Centerline Utilities, Inc. agrees to furnish and install 65 water services from rear to front yard at \$5,500/EA.

Brian Shaw
Secretary
Centerline Inc.
2180 SW Poma Drive
Palm City, FL 34990

2180 SW Poma Drive, Palm City, FL 34990 ~ Phone: (561) 689-3917 Fax: (561) 689-0017



CENTERLINE, INC.

Earthwork – Underground Utilities – Roadways
www.centerlineinc.com

State Underground Utility License # CUC032651 State General Contractor License # CGC011107

June 27, 2025

Joseph Tanacredi
Palm Beach County Water Utilities Department
8100 Forest Hill Blvd
West Palm Beach, FL 33413

RE: Project: (WUD#18-002) NORTH WEST BELLE GLADE WATER MAIN IMPROVEMENT,
Zone 3

30-Day Time Extension Request – New substantial completion date: 9/26/2025

Below are Centerline's reasoning for time extension request:

1. Centerline is seeking additional time for the 65 – rear to front water service connections added to our scope.

Randy Stringer
Vice President
Centerline Inc.
2180 SW Poma Drive
Palm City, FL 34990

ID	Task Name	Duration	Start	Finish	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1	NW Belle Glade WM Improv. Zone 3	365 days	Mon 6/3/24	Sun 10/26/25																		
2	Mobilize	1 day	Mon 6/3/24	Mon 6/3/24																		
3	Avenue E	14 days	Tue 6/4/24	Fri 6/21/24																		
4	School + Avenue NW E, F, G	20 days	Mon 6/24/24	Fri 7/19/24																		
5	Avenue H & North	65 days	Mon 7/22/24	Fri 10/18/24																		
6	South Of Avenue H	80 days	Mon 10/21/24	Fri 2/7/25																		
7	Unexpected Utility Conflicts - Potholing, Hard Pan not on Boring Reports	40 days	Mon 2/10/25	Fri 4/4/25																		
8	NW 9th St + NW 13th St.	14 days	Mon 4/7/25	Thu 4/24/25																		
9	Canal Street (FDOT)	7 days	Thu 2/27/25	Fri 3/7/25																		
10	Unexpected Utility Conflicts	21 days	Mon 3/10/25	Mon 4/7/25																		
11	Canal Street (FDOT)	7 days	Tue 4/8/25	Wed 4/16/25																		
12	Unauthorized Access	238 days	Mon 6/3/24	Wed 4/30/25																		
13	West Canal Street (N) + West Canal Street (S)	13 days	Thu 5/1/25	Sun 5/18/25																		
14	NW 17th St	7 days	Mon 5/19/25	Tue 5/27/25																		
15	Water Service transfer to new main	9 days	Mon 8/4/25	Thu 8/14/25																		
16	Abandon W.M	14 days	Thu 8/14/25	Tue 9/2/25																		
17	Substantial Completion Date	1 day	Tue 6/17/25	Tue 6/17/25																		
18	Testing, Punch Out	7 days	Wed 6/18/25	Thu 6/26/25																		
19	Final Completion Date	1 day	Sat 6/28/25	Sat 6/28/25																		
20	Restoration of ROW & Private W.S	30 days	Mon 8/11/25	Fri 9/19/25																		
21	New Substantial Completion Date - CO#1 Conflicts	1 day	Wed 8/27/25	Wed 8/27/25																		
22	Final Completion With 90 - Day Time Extension CO#1 - Conflicts & Unforseen	1 day	Fri 9/26/25	Fri 9/26/25																		
23	New Substantial Completion Date - CO#2 Added Rear to Front Water Service Connection	1 day	Wed 9/24/25	Wed 9/24/25																		
24	New Final Completion Date - CO#2 Added Rear to Front Water Service Connection	1 day	Sun 10/26/25	Sun 10/26/25																		

Prepared For:
Palm Beach County WUD
Date: Fri 8/1/25





[Department of State](#) / [Division of Corporations](#) / [Search Records](#) / [Search by Entity Name](#) /

Detail by Entity Name

Florida Profit Corporation
CENTERLINE UTILITIES, INC.

Filing Information

Document Number P98000065504
FE/EIN Number 65-0849488
Date Filed 07/23/1998
Effective Date 07/18/1998
State FL
Status ACTIVE
Last Event AMENDMENT
Event Date Filed 12/13/2013
Event Effective Date NONE

Principal Address

2180 SW POMA DRIVE
PALM CITY, FL 34990

Changed: 02/15/2013

Mailing Address

2180 SW POMA DRIVE
PALM CITY, FL 34990

Changed: 02/15/2013

Registered Agent Name & Address

Young Foster, PLLC
Young Foster PLLC
1600 South Federal Highway
Suite 570
Pompano Beach, FL 33062

Name Changed: 03/14/2023

Address Changed: 03/14/2023

Officer/Director Detail

Name & Address

Title VP

Stringer, Randy W
520 SE Meadow Wood Way
Stuart, FL 34997



Title President, Treasurer

Chesney, Frederick H, Jr.
20180 SE Bridgewater Drive
Jupiter, FL 33458

Title Secretary

Shaw, Brian
12850 165th Road North
Jupiter, FL 33478

Annual Reports

Report Year	Filed Date
2023	03/14/2023
2024	03/04/2024
2025	02/05/2025

Document Images

02/05/2025 -- ANNUAL REPORT	View image in PDF format
03/04/2024 -- ANNUAL REPORT	View image in PDF format
03/14/2023 -- ANNUAL REPORT	View image in PDF format
02/18/2022 -- ANNUAL REPORT	View image in PDF format
02/05/2021 -- ANNUAL REPORT	View image in PDF format
03/05/2020 -- ANNUAL REPORT	View image in PDF format
08/06/2019 -- AMENDED ANNUAL REPORT	View image in PDF format
05/06/2019 -- ANNUAL REPORT	View image in PDF format
01/05/2018 -- ANNUAL REPORT	View image in PDF format
07/05/2017 -- AMENDED ANNUAL REPORT	View image in PDF format
02/17/2017 -- ANNUAL REPORT	View image in PDF format
05/18/2016 -- AMENDED ANNUAL REPORT	View image in PDF format
03/31/2016 -- ANNUAL REPORT	View image in PDF format
11/09/2015 -- AMENDED ANNUAL REPORT	View image in PDF format
09/09/2015 -- AMENDED ANNUAL REPORT	View image in PDF format
01/08/2015 -- ANNUAL REPORT	View image in PDF format
02/03/2014 -- ANNUAL REPORT	View image in PDF format
12/13/2013 -- Amendment	View image in PDF format
02/15/2013 -- ANNUAL REPORT	View image in PDF format
01/13/2012 -- ANNUAL REPORT	View image in PDF format
03/08/2011 -- ANNUAL REPORT	View image in PDF format
03/25/2010 -- ANNUAL REPORT	View image in PDF format
04/07/2009 -- ANNUAL REPORT	View image in PDF format



Water Utilities Department
Engineering Division
8100 Forest Hill Blvd
West Palm Beach, FL 33413
(561) 493-6000
Fax: (561) 493-6085
www.pbcwater.com

**Palm Beach County
Board of County
Commissioners**

Maria G. Marino, Mayor
Sara Baxter, Vice Mayor
Gregg K. Weiss
Joel G. Flores
Marc Woodward
Maria Sachs
Bobby Powell Jr.

Interim County Administrator
Todd J. Bonlarron

"An Equal Opportunity Employer"
Official Electronic Letterhead

July 16, 2025

Mr. Randy Stringer, Vice President
Centerline Utilities, Inc.
2180 SW Poma Drive
Palm City, Florida 34990

Re: Project Number: 18-002
North West Belle Glade Water Main Improvements,
Zone 3
Notification of Contract Clauses No Longer Being
Enforced Pursuant to Emergency Ordinance 2025-014

Dear Mr. Stringer,

On June 3, 2025, the Board of County Commissioners (BCC) approved an emergency ordinance to suspend the race and gender conscious provisions of the County's EBO ordinance. The suspension will remain in effect for two years or until further direction by the BCC, whichever comes first. As a result, the provisions relating to minority/women-owned business enterprise (M/WBEs) participation contained in the contract document (R2023-1865) in Instructions to Bidders on section 5.3 **will not be enforced** as of June 3, 2025, only the small business enterprise (SBE) provisions will apply.

Please sign below to acknowledge receipt of this notification. This acknowledgement will be included in, and made part of, the contract file.

Should you require any additional information please contact Ms. Christina Bervin at cbervin@pbcwater.com or at (561) 493 5203.


Cordially,


Jane House, P.E., LEED AP
Director of Engineering Division

Receipt Acknowledged and In Agreement:

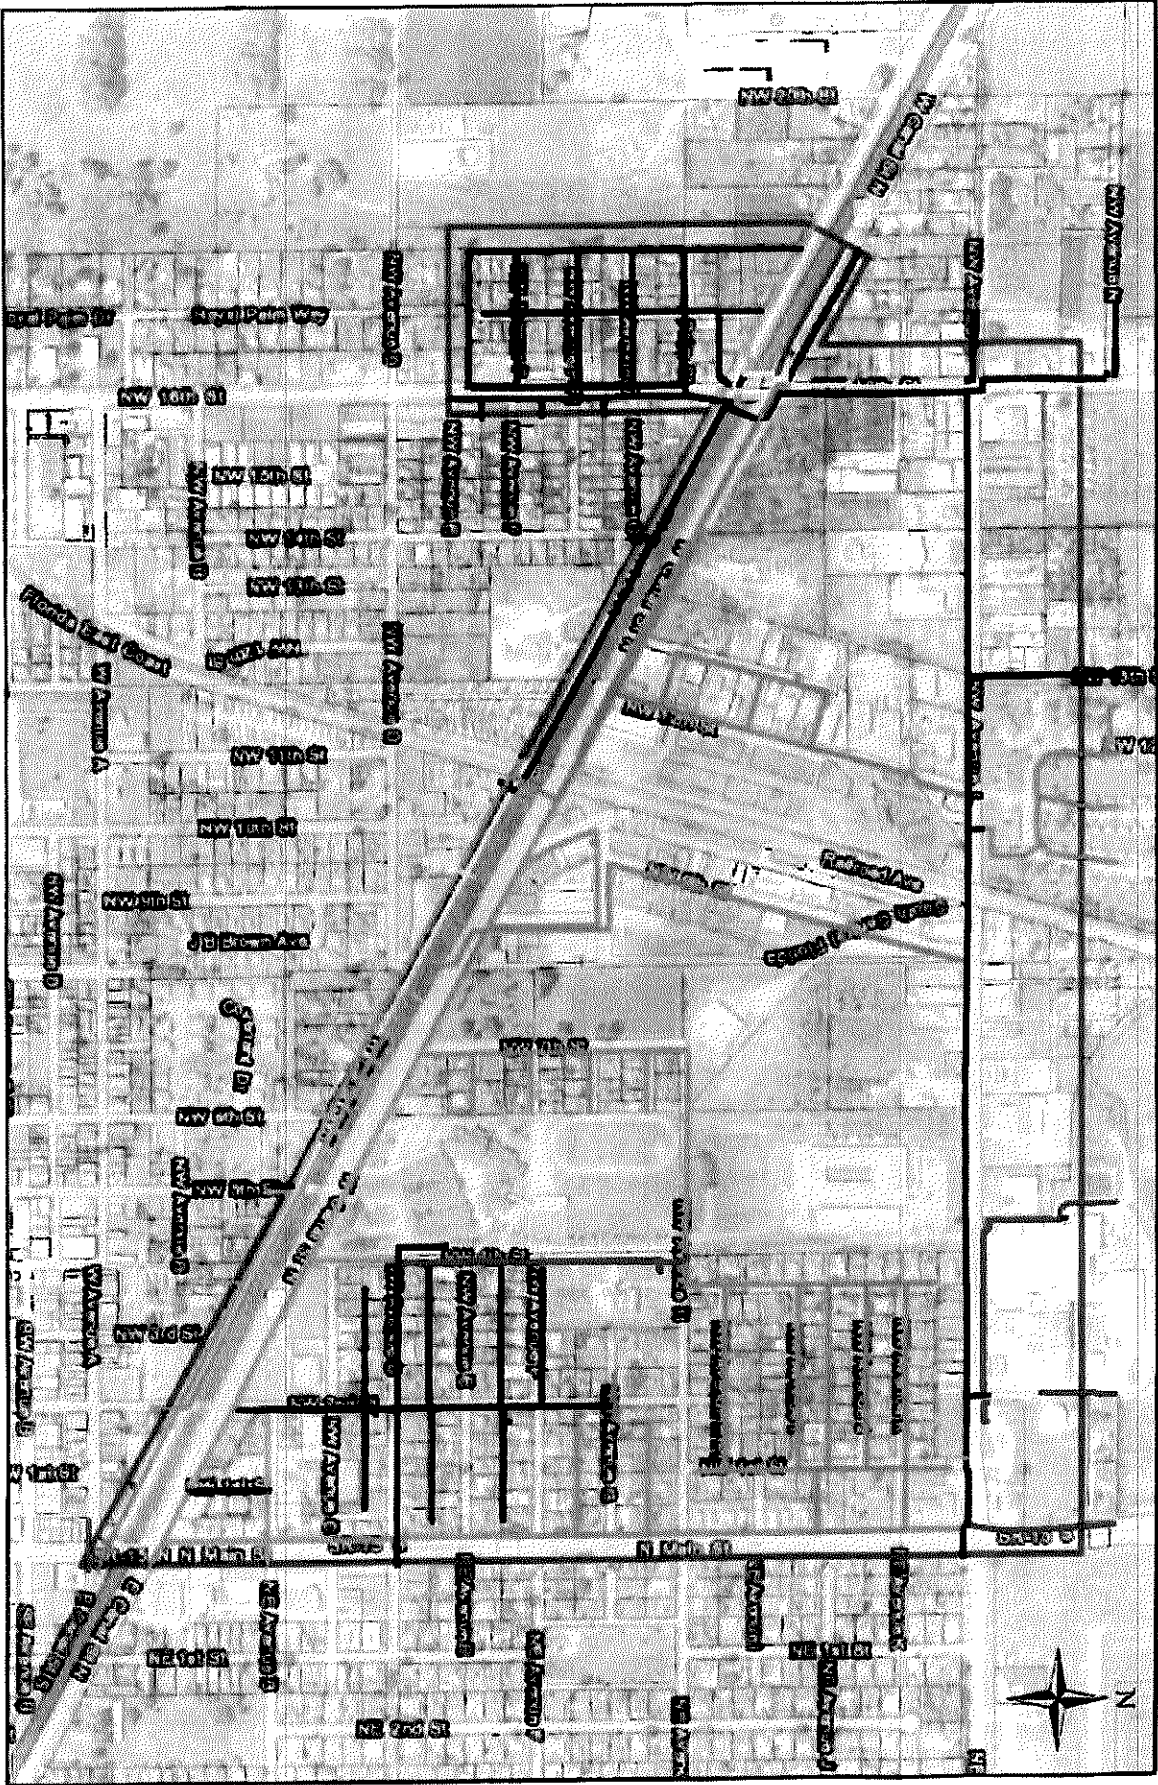
CENTERLINE UTILITIES, INC
(Contractor)

RANDY STRINGER
(Print Name)


(Signature)

07/30/2025
(Date)

ATTACHMENT NO. 2



North West Belle Glade Water Main Improvements, Zone 3

PBCWMD 18-002R

Legend

Pipe Installation

No Data

2000 - 2008

2010 - 2016

1985

1966

0 390 780

1,560

Feet

1992 - 1998

1976

Project Boundary

1 inch = 780 feet



CH2M HILL
HILL ASSOCIATES



ATTACHMENT NO. 3

Palm Beach County Compliance Summary Report

[illegible]
