

PALM BEACH COUNTY
BOARD OF COUNTY COMMISSIONERS
AGENDA ITEM SUMMARY

=====

Meeting Date: May 3, 2022	<input type="checkbox"/> Consent	<input checked="" type="checkbox"/> Regular
	<input type="checkbox"/> Workshop	<input type="checkbox"/> Public Hearing

Submitted By: Department of Airports

=====

I. EXECUTIVE BRIEF

Motion and Title: Staff recommends motion to approve:

- (A) Amendment No. 3 to the Construction Manager (CM) at Risk Contract (Contract) with Lebolo Construction Management, Inc. (LCM) for CM at Risk Services for Miscellaneous Airport Improvements for Palm Beach County Department of Airports (Department) in the amount of \$1,518,790.48 and 290 Calendar Days for Work Order SL 04: Federal Inspection Services (FIS) & Building 846 Storm Resiliency Modifications Package 2 at Palm Beach International Airport (PBI); and
- (B) A Budget Transfer of \$518,791 in the Airport’s Improvement and Development Fund to provide budget for the project; including a transfer from Reserves in the amount of \$518,791.


Summary: The CM at Risk Contract with LCM was approved by the Board on August 20, 2019 (R-2019-1222). The Contract is for two years with three, one-year renewal options for CM at Risk Services for Airport Improvements for the Department. LCM is a Boynton Beach, Florida, based firm. The County has exercised the first one-year renewal option. The contract value to date is \$1,003,615.62. Approval of Amendment No. 3 in the amount of \$1,518,790.48 and 290 Calendar Days will enable LCM to complete Work Order SL 04: FIS & Building 846 Storm Resiliency Modifications Package 2 at PBI. The Department of Airports Administration and Communications Facility (Building 846) is home for essential personnel who remain on Airport property during hurricanes and other emergency events. This project will provide protection to roof top mounted equipment from impact of wind-borne debris and will replace existing HVAC equipment that is nearing its end of service life with new HVAC equipment as well as provide related structural supports for the new HVAC equipment. The project was presented to the Goal Setting Committee on September 9, 2020 and an Affirmative Procurement Initiative (API) of SBE Subcontracting (Minimum of 20%) of which a MBE Segmented Subcontracting Goal of 5% MBEs composed of African American (AA) firms and Hispanic American (HA) firms was applied. The S/MBE subcontracting participation on this work order is 60.6% with 46.8% participation by HA/AA firms. Current cumulative subcontractor S/M/WBE participation for all work orders to-date under this contract including this amendment is 69.6%. Pursuant to changes to Chapter 332, Florida Statutes, effective October 1, 2020, a governing body of a commercial service airport may not approve purchases of contractual services in excess of the Category Five threshold amount of \$325,000 provided in Section 287.017, Florida Statutes, on a consent agenda. This amendment exceeds the threshold amount and must be approved on the regular agenda. Countywide (AH)

Background and Policy Issues: In 2019, the Department procured consultant services to identify improvements needed to facilities housing essential County personnel during hurricane and other emergency events. The improvements were separated into multiple packages due to budget and schedule. Storm Resiliency Modifications Package 1 (Package 1), was completed by LCM in 2020 and included the additional protection of impact-resistant fabric shutters to the exterior side of the impact glazing on Building 846. This work order was under \$200,000 and was approved by Contract Review Committee on June 10, 2020. This project includes implementing the recommended improvements at Building 846 and FIS facility at PBI to meet 2017 Florida Building Codes. Storm Resiliency Modifications Package 2 project will provide protection to roof top mounted equipment from impact of wind-borne debris and will replace existing HVAC equipment that is nearing its end of service life with new HVAC equipment as well as provide related structural supports for the new HVAC equipment. Builder’s Risk Insurance is required for this scope of work and will be provided by the Contractor prior to the start of construction.

Attachments:

- 1. Amendment No. 3 to CM at Risk Contract with LCM (w/Contract History) – (3 originals)
- 2. OEBO Schedules
- 3. Budget Transfer

=====

Recommended By:		
	Department Director	Date
Approved By:		
	County Administrator	Date

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

Fiscal Years	2022	2023	2024	2025	2026
Capital Expenditures	\$1,518,791				
Operating Costs					
External Revenues (Grants)					
Program Income (County)					
In-Kind Match (County)					
NET FISCAL IMPACT	\$1,518,791				
# ADDITIONAL FTE POSITIONS (Cumulative)					

Is Item Included in Current Budget?

Yes _____ No X

Does this item include the use of federal funds?

Yes _____ No X

Budget Account No: Fund 4111 Department 121 Unit A413 Object 6505
Reporting Category _____

B. Recommended Sources of Funds/Summary of Fiscal Impact:

Approval of this item provides budget for Amendment No. 3 to the Contract with LCM in the amount of \$1,518,790.48. Funding sources consist of Local funds of \$1,518,791; including a transfer from Reserves of \$518,791.

C. Departmental Fiscal Review:

III. REVIEW COMMENTS

A. OFMB Fiscal and/or Contract Development and Control Comments:

Lucy Mark 4/15/22
OFMB 4/14/22
4/15/22

Ann J. Jacobson 4/16/22
Contract Dev. and Control
4-6-22

B. Legal Sufficiency:

Anne Delgant 4/16/22
Assistant County Attorney

C. Other Department Review:

Department Director

REVISED 11/17

(THIS SUMMARY IS NOT TO BE USED AS A BASIS FOR PAYMENT)



Risk Profile : Standard - General Services-AOA

Required Additional Insured : Palm Beach County Board of County Commissioners

Ownership Entity :



Detail by Entity Name

Florida Profit Corporation
LEBOLO CONSTRUCTION MANAGEMENT, INC.

Filing Information

Document Number P00000095039
FEI/EIN Number 65-1055266
Date Filed 10/06/2000
State FL
Status ACTIVE

Principal Address

2100 CORPORATE DRIVE
BOYNTON BEACH, FL 33426

Changed: 06/21/2005

Mailing Address

2100 CORPORATE DRIVE
BOYNTON BEACH, FL 33426

Changed: 06/21/2005

Registered Agent Name & Address

LEBOLO, RANDALL E
2100 CORPORATE DRIVE
BOYNTON BEACH, FL 33426

Name Changed: 04/03/2002

Address Changed: 01/14/2008

Officer/Director Detail

Name & Address

Title D

LEBOLO, RANDALL E
2100 CORPORATE DRIVE
BOYNTON BEACH, FL 33426

Annual Reports

Report Year	Filed Date
2020	03/02/2020
2021	03/04/2021
2022	02/24/2022

<u>Document Images</u>	
<u>02/24/2022 -- ANNUAL REPORT</u>	View image in PDF format
<u>03/04/2021 -- ANNUAL REPORT</u>	View image in PDF format
<u>03/02/2020 -- ANNUAL REPORT</u>	View image in PDF format
<u>02/12/2019 -- ANNUAL REPORT</u>	View image in PDF format
<u>01/16/2018 -- ANNUAL REPORT</u>	View image in PDF format
<u>01/18/2017 -- ANNUAL REPORT</u>	View image in PDF format
<u>02/12/2016 -- ANNUAL REPORT</u>	View image in PDF format
<u>01/28/2015 -- ANNUAL REPORT</u>	View image in PDF format
<u>02/26/2014 -- ANNUAL REPORT</u>	View image in PDF format
<u>03/05/2013 -- ANNUAL REPORT</u>	View image in PDF format
<u>01/10/2012 -- ANNUAL REPORT</u>	View image in PDF format
<u>02/16/2011 -- ANNUAL REPORT</u>	View image in PDF format
<u>01/28/2010 -- ANNUAL REPORT</u>	View image in PDF format
<u>03/06/2009 -- ANNUAL REPORT</u>	View image in PDF format
<u>01/14/2008 -- ANNUAL REPORT</u>	View image in PDF format
<u>04/02/2007 -- ANNUAL REPORT</u>	View image in PDF format
<u>04/27/2006 -- ANNUAL REPORT</u>	View image in PDF format
<u>06/21/2005 -- ANNUAL REPORT</u>	View image in PDF format
<u>04/16/2004 -- ANNUAL REPORT</u>	View image in PDF format
<u>03/17/2003 -- ANNUAL REPORT</u>	View image in PDF format
<u>04/03/2002 -- ANNUAL REPORT</u>	View image in PDF format
<u>02/20/2001 -- ANNUAL REPORT</u>	View image in PDF format
<u>10/06/2000 -- Domestic Profit</u>	View image in PDF format

**AMENDMENT NO. 3 TO THE CONTRACT
BETWEEN
PALM BEACH COUNTY DEPARTMENT OF AIRPORTS AND
LEBOLO CONSTRUCTION MANAGEMENT, INC. FOR
CONSTRUCTION MANAGEMENT SERVICES
MISCELLANEOUS AIRPORT IMPROVEMENTS PROJECT NO. DOA 18-13**

This Amendment No. 3 to the Contract is made as of the ____ day of _____, 2022, by and between Palm Beach County, Florida (COUNTY) and **LEBOLO CONSTRUCTION MANAGEMENT, INC.**, a corporation authorized to do business in the State of Florida, hereinafter referred to as the CONSTRUCTION MANAGER, having its office and principal place of business for this Contract at 2100 Corporate Drive, Boynton Beach, Florida 33426.

WHEREAS, the Owner and Construction Manager acknowledge and agree that the Contract between Owner and **LEBOLO CONSTRUCTION MANAGEMENT, INC** dated August 20, 2019 (R-2019-1222) is in full force and effect and that this merely supplements said Contract; and

WHEREAS, on July 13, 2021, the County entered into Amendment #1 (R-2021-0888) with the CONSTRUCTION MANAGER and that this merely supplements said Contract; and

WHEREAS, on February 8, 2022, the County entered into Amendment #2 (R-2022-0135) with the CONSTRUCTION MANAGER and that this merely supplements said Contract; and

WHEREAS, the parties hereto entered into a Contract between Owner and CONSTRUCTION MANAGER whereby the CONSTRUCTION MANAGER has rendered or will render pre-construction services as specified therein; and

WHEREAS, the parties have negotiated a Guaranteed Maximum Price (GMP), including CONSTRUCTION MANAGER's fees for construction and warranty services and other services as set forth herein and in the Contract; and

WHEREAS, the CONSTRUCTION MANAGER represents that the CONSTRUCTION MANAGER, Subcontractors, material and equipment suppliers have compared and reviewed all general and specific details on the Drawings and that all conflicts, discrepancies, errors and omissions, which are within the commonly accepted knowledge based of a licensed general contractor, subcontractor, trades persons, manufacturers or other parties required to carry out the Work involved in this Amendment, have been corrected or clarified prior to execution of this Amendment to the Contract, and therefore CONSTRUCTION MANAGER warrants that the GMP (exclusive of contingency) includes the cost of correcting all conflicts, discrepancies, errors, or omissions which CONSTRUCTION MANAGER identifies, or should have identified through the exercise of reasonable skill and care, during the pre-construction phase of this Contract; and

WHEREAS, the CONSTRUCTION MANAGER's review and comparison of all Drawings has taken into consideration the total and complete functioning of all systems and therefore the CONSTRUCTION MANAGER represents that the GMP represents the total cost for complete and functional systems including Pre-Construction Services.

NOW THEREFORE, in considerations of the mutual covenants herein contained, and such other good and

valuable consideration, the receipt of which the parties hereby acknowledge, the parties agree to the following terms and conditions:

(1) GUARANTEED MAXIMUM PRICE

Pursuant to Article 2.2 and Article 6 of the Contract between Owner and CONSTRUCTION MANAGER, the parties have agreed to the establishment of a Guaranteed Maximum Price of **\$1,518,790.48** for the construction costs for **Work Order SL 04: FIS & Building 846 Storm Resiliency Modifications Package 2 at Palm Beach International Airport.**

(2) SCHEDULE OF TIME FOR COMPLETION

Pursuant to Article 5.3, CONSTRUCTION MANAGER shall complete the project within the milestones noted in the table below or Liquidated Damages for failure to complete within the contract time or approved extension thereof shall be assessed.

Description	Calendar Days from NTP	Liquidated Damages
Substantial Completion	260	\$1,000/ Cal Day
Final Completion	290	\$0/ Cal Day

(3) Except as specifically amended herein, all other terms and conditions of the Contract shall remain in full force and effect.

(4) Attachments Exhibit A

IN WITNESS WHEREOF, the Board of County Commissioners of Palm Beach County, Florida has made and executed this Amendment on behalf of the COUNTY and CONSTRUCTION MANAGER has hereunto set its hand the day and year above written.

ATTEST:

**JOSEPH ABRUZZO, CLERK OF THE
CIRCUIT COURT & COMPTROLLER**

**PALM BEACH COUNTY, FLORIDA
A Political Subdivision of the State of Florida
BOARD OF COUNTY COMMISSIONERS**

By: _____
Deputy Clerk

By: _____
Robert S. Weinroth, Mayor

**APPROVED AS TO FORM
AND LEGAL SUFFICIENCY**


**APPROVED AS TO TERMS
AND CONDITIONS**

By: _____
County Attorney

By:  _____
Director of Airports

WITNESS:

**FOR CONSTRUCTION MANAGER
SIGNATURE**




Signature

Sebastian Fonnegra

Name (type or print)

CONSTRUCTION MANAGER:



Signature

Randall E. Lebolo

President

(Corporate Seal)

Exhibit A

- 1. GMP dated March 21, 2022**
- 2. Public Construction Bond**

GMP



PALM BEACH COUNTY DEPARTMENT OF AIRPORTS

DOA 18-13 CM@RISK SERVICES for
MISCELLANEOUS IMPROVEMENTS PROJECTS
on a CONTINUING CONTRACT BASIS

GMP

SL - 04 FIS \$ BUILDING STORM RESILIENCY MODIFICATIONS PACKAGE 2

WEST PALM BEACH, FL

Monday, March 21 2022
2021-0024

DOA 18 - 2A SL-04
Version 4.0

SAFETY / INTEGRITY

2100 CORPORATE DRIVE
BOYNTON BEACH, FL 33426
LEBOLO.COM | CGC-062151



Table
of
Contents

LETTER

Section A

COST SUMMARY
ASSUMPTIONS & CLARIFICATIONS, ALLOWANCES

Section B

CONSTRUCTION PHASE MANAGEMENT FEE
GENERAL CONDITIONS

Section C

REIMBURSABLE GENERAL CONDITIONS

Section D

MINORITY PARTICIPATION REPORT

Section E

SUBCONTRACTOR BIDDING STATUS REPORT

Section F

SCOPE SHEETS
SUBCONTRACTOR PROPOSALS (See Section F Individual Document)

Section G

PUBLIC AD

Section H

DRAWING LOG

Section I

CONSTRUCTION SCHEDULE

Section J

SITE VISIT ATTENDANCE
BID OPENING LOG

Section K

VALUE ANALYSIS / VALUE ENGINEERING REPORT
CONSTRUCTABILITY REPORT



March 21, 2022

Ms. Cynthia M. Portnoy

PE Project Manager

Palm Beach County Department of Airports

846 Palm Beach International Airport

West Palm Beach, FL 33406-1470

(561) 471-7411 Direct

(954) 242-5181 Mobile

**Ref:DOA 18-2A FIS & Building 846 Storm Resiliency Modifications Package 2
West Palm Beach, FL - SL-04
2020-0024**

Ms. Portnoy,

In accordance with Article 2 - Construction Manager's Basic Services, Article 2.1.
The PreConstruction Phase we are submitting the GMP V.4 required information in
compliance with the 100% CDs requirements for PreConstruction Services.

We look forward, with much enthusiasm to work with you on this project and being
your construction resource and team member in its successful completion.

If you have any questions, please call me at my mobile (561) 632-4894 or email me
at sfonnegra@lebolo.com.

Sincerely,


Sebastian Fonnegra
Pre-Construction Manager
Lebolo Construction Management, Inc.
sfonnegra@lebolo.com

SECTION A

Cost Summary

Assumptions & Clarifications

Allowances

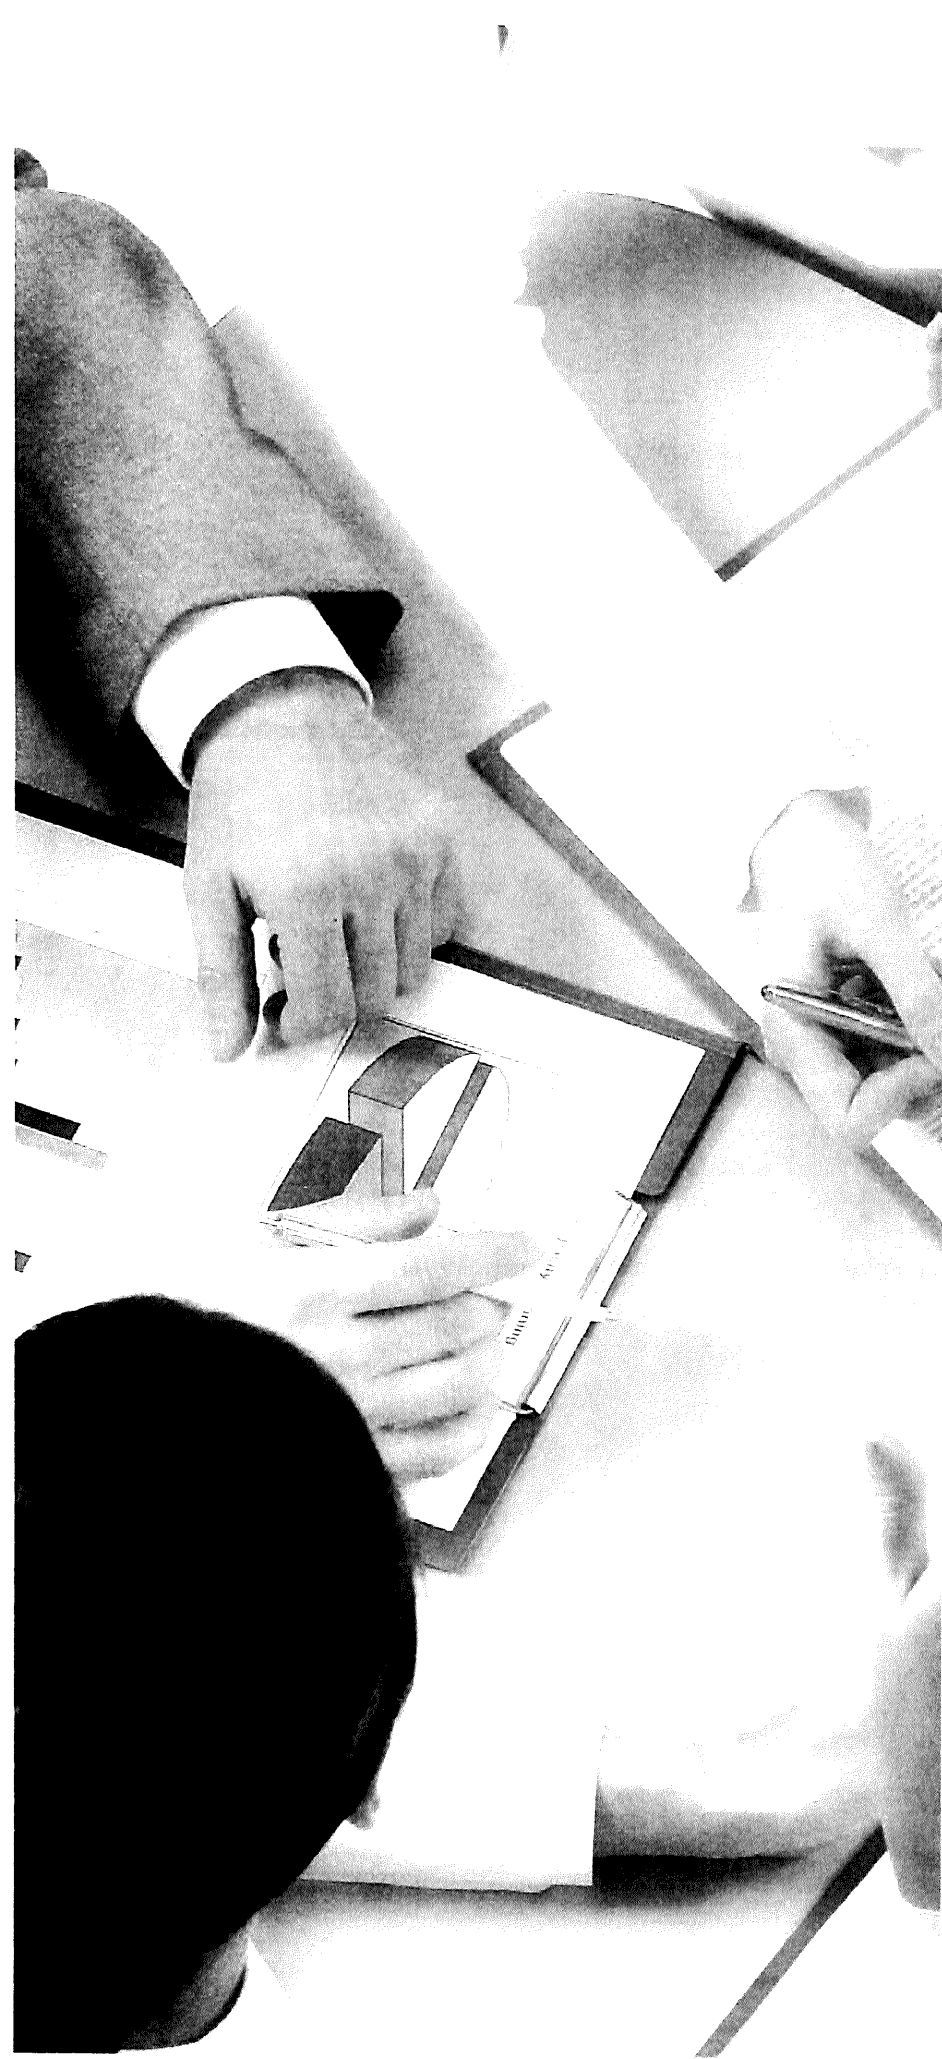

PROJECT NAME:

LEBOLO PROJECT No:

PBIA PROJECT No:

VERSION:

PROPOSAL DATE:

SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
2021-0024
DOA 18-2A SL-04
4.0
Monday, March 21, 2022

FORM LCM-PC-01 | 09/21/2021

SCOPE OF WORK										
2 Roof chiller units replacement New Grating over chillers Interior (35) VAV replacement Interior finishes Interior & Exterior S.Steel										
PALM BEACH COUNTY DEPARTMENT OF AIRPORTS			SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2							
LEBOLO COST CODE	SPEC. COST CODE	DESCRIPTION OF WORK	846 BUILDING	# PROP.	VENDOR	Sub Permit Inc.	BOND REQ.	BOND COST	DEPOSIT	COMMENTS
DIVISION 2		SITE CONSTRUCTION	\$4,594.48							
02-020		Selective Demolition	\$4,594.48	2	All American Ceilings	\$0	N/A	\$0	No	Acoustical Ceiling removal
DIVISION 5		METALS	\$210,788.50							
05-005		Structural Steel Package	\$210,788.50	2	Van Linda Iron		BOND	\$7,423	No	W8 Chiller bench, Joist bottom chord
DIVISION 7		THERMAL /MOISTURE	\$3,000.00							
07-405		Roofing Package	\$3,000.00	0	LEBOLO ESTIMATE	\$0	N/A	\$0	0	Allowance - Patch & Repairs
DIVISION 9		FINISHES	\$67,143.56							
09-105		Drywall & Framing Package	\$30,850.00	1	I.Q. Constructions		N/A	\$0	No	Drywall ceilings
09-205		Acoustical Ceiling Package	\$27,393.56	1	All American Ceilings		N/A	\$0	No	
09-505		Painting Package	\$8,900.00	1	I.Q. Constructions		N/A	\$0	No	Interior drywall ceilings & Steel Patch & Repairs
DIVISION 15		MECHANICAL	\$640,981.83							
15-105		Fire Protection Package	\$3,685.83	1	Johnsons Controls	\$0	N/A	\$0	0	Sprinkler heads relocation
15-205		HVAC Package	\$577,320.00	4	Quantum Mechanical	\$0	BOND	\$11,320	No	(2) Chillers 90T - 35 VAV Boxes
15-235		HVAC Duct Cleaning	\$59,976.00	3	Quantum Mechanical	\$0	BOND	\$1,476	No	
DIVISION 16		ELECTRICAL	\$41,200.00							
16-005		Electrical Package	\$33,600.00	1	Protect Video	\$0	N/A	\$0	No	(2) Chiller Disconnects & 35 VAV connections
16-105		Low Voltage Package	\$2,500.00	0	LEBOLO ESTIMATE	\$0	N/A	\$0	0	Allowance - Antennas service if required
16-020		Lightning Protection	\$5,100.00	2	Bonded Lightning	\$0	N/A	\$0	No	
	2	SUBTOTAL	\$967,708.37			\$0		\$19,624		
90-035	3	Payment & Performance Bond	\$33,869.79							Article 8 Cost of the Work - Bonds
90-025	4	General Liability - On Site	\$5,806.25							Article 8 Cost of the Work - Insurance (Liability, OCP, Hurricane Fund)
90-030	5	Builders Risk Policy	\$7,257.81							Article 8 Cost of the Work - Builders Risk
Div. 17	6	General Requirements (See GR Detail)	\$44,305.40							Article 8 Cost of the Work - Reimbursable General Conditions (labor other than admin and supervision, clean-up, trash removal, tempr power and utilities, surveys, prep shop drawings, as-builts, safety, machinery etc, reproduction, tools)
91-165	6a	Material Cost Escalation Contingency	\$145,156.26							15.0%
17-810		Permits	\$0.00							Building Permit Fee - by owner
Subtotal Cost of the Work-w/o precon (Items 2-6a)			\$1,204,103.89							
Div. 80	7	Construction Managers Fee - Art 6.4.CM Management - Staffing	\$95,062.50							4.5 month(s)
Div. 80	8	Construction Managers Fee - Art 6.4 Site supplies, trailers, furniture, cameras, radios, copiers, vehicles, phone, travel, computers, postage, home office staff	\$33,310.39							4.5 month(s)
91-120	9	Contractor Fee	\$96,328.31							Construction Managers Fee - Art 6 O & P - % of Article 8 Cost of the work items 1-6
91-105	10	Contingency	\$60,205.19							Cost of the work-Owners Contingency
91-145		Pre-Construction Payment	\$29,780.21							Pre-Construction Services
Total Construction Fee based on Contract (Includes Items 7, 8, 9)			\$224,701.20							
Precon+Fee+GC's+Bonds+Insurance (items 3,4,5,6,6a,7,8,9)			\$490,876.92							
TOTAL GMP			\$1,518,790.48							



ASSUMPTIONS & CLARIFICATIONS

PROJECT NAME:	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	4.0
PROPOSAL DATE:	Monday, March 21, 2022

FORM LCM-PC-04 | 08/20/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS	
No.	Work Division
	DIVISION 1 - GENERAL
1	The Contract Sum and the amount of each item are based upon the costs of materials and labor as they exist on the date of the contract. Owner and contractor acknowledge that market conditions are being adversely affected by international market conditions, unusually adverse weather conditions and other not reasonably foreseeable events that are not within the reasonable control of the owner or contractor. Accordingly, in the event that costs for any substantive item or element of materials and/or supplies, shall increase after the date of this contract and during the time of performance of same, and such cost increases are due to the above described events that are beyond the control of the Owner and the Contractor, then the Contractor shall be entitled to an equitable adjustment of the Contract Sum to reasonably compensate the Contractor for these increases.
2	Work to be performed Monday to Friday 7AM to 5PM on rooftop work and after hours for interior work.
3	Temporary power and water being available within 50' of project location.
4	All costs shown to be added are direct costs.
5	Cost is based on plans and specifications provided.
6	Assumed that owner will provide a laydown area for dumpsters, bathrooms, storage, etc. close to 846 Building.
7	All Permits and Permit Fees assumed by owner.
8	Secondary Permit Fees assumed as refundables. Allowance included, see Allowance Exhibit E.
9	Impact fees are excluded.
10	Textura Fees are included.
11	No provision included for special inspections.
12	Rental property for storage of materials and equipment is excluded.
13	Parking Fees are excluded.
14	Removal or studies of hazardous materials are excluded.
15	Work or modifications for the Public Address system are excluded
16	BDA system is not included.
17	Alta Survey is not included.
	DIVISION 5 - METALS
1	Steel - Corrections or repairs to existing to remain not included.
	DIVISION 7 - THERMAL & MOISTURE PROTECTION
1	Roofing - Roofing area will be protected during chiller replacement activity and steel installation. LEBOLO will provide a visual inspection of the roof before to start the work. We suggest for PBIA to do a roof report with the warranty holder vendor before mobilization.
2	Roofing - An allowance for patch and repairs after roof work is included.



ASSUMPTIONS & CLARIFICATIONS

PROJECT NAME:	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	4.0
PROPOSAL DATE:	Monday, March 21, 2022

FORM LCM-PC-04 | 08/20/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS	
No.	Work Division
	DIVISION 9 - FINISHES
1	Acoustical Ceiling - Additional demo and replace grid and removal and reinstall tiles due to actual removal conditions included as allowance.
2	Painting - Paint over steel structure patch and repairs only after welding areas included. Match color is not possible.
	DIVISION 15 - MECHANICAL WORK
1	HVAC - Filters for existing equipment's required for T&B assumed by owner.
2	HVAC - Excluded motor starters and VFD's other than what is supplied by HVAC vendors shown on Mechanical drawings and in the specifications.
3	HVAC - Duct cleaning is included.
4	HVAC - 12 Month warranty starting at equipment startup included. 5 year parts & labor warranty on new chillers.
5	HVAC - If two (2) 1.5 Ton temporary spot coolers to be included add \$3,000 per week.
6	HVAC - One (1) 100 Ton temporary chiller with hoses included.
7	HVAC - Removal of existing EMS/BAS controls, wiring, conduit and devices other than what is required to tie in new EMS controls is excluded.
8	Fire Protection - Fire Protection to provide labor and material to disconnect an existing 1 1/4" BL because is in conflict with the New Structural Member to be installed. This relocation is up to 10 Ft over. This proposal is also including pluggin a total of 6 Hds. in the area of work to prevent any water damage during the installation of the New Structural Member. Once the new Structural member is installed we will come back and re-install the hds (New Sprinkler Hds) in this area. NO Sprinkler relocation is included in this proposal as this could affect the Layout/proper coverage of the space (Area of Work).
	DIVISION 16 - ELECTRICAL WORK
1	Lightning Protection - Any needed repairs to the existing lightning protection system are excluded. UL Recertification included.
2	Low Voltage - Allowance for Antennas service if required is included.
3	Electrical - Switchboard specs are unknown, breakers cost is included as allowance for \$3,000ea.



ALLOWANCES

PROJECT NAME:	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	4.0
PROPOSAL DATE:	Monday, March 21, 2022

FORM LCM-PC-05 | 08/20/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS		
No.	Description	Cost \$
	DIVISION 1 - GENERAL	
1	Secondary Permit Fees (Subcontractors)	\$0.00
2	Subcontractor's Bond Cost over \$100,000	\$19,624.11
	DIVISION 7 - THERMAL & MOISTURE PROTECTION	
1	Roofing - Patch & repairs	\$3,000.00
	DIVISION 9 - FINISHES	
1	Acoustical Ceiling - Additional repairs due to actual removal conditions	\$5,000.00
	DIVISION 16 - ELECTRICAL WORK	
1	Low Voltage - Antennas service if required - add	\$2,500.00
2	Electrical - Disconnects	\$6,000.00

SECTION B

Construction Phase Management Fee

General Conditions





CONSTRUCTION PHASE MANAGEMENT FEE

PROJECT NAME: SL-04 FIS & BUILDING 846 STORM
RESILIENCY MODIFICATIONS PACKAGE 2

LEBOLO PROJECT No: 2021-0024

PBIA PROJECT No: DOA 18-2A SL-04

VERSION: 4.0

PROPOSAL DATE: Monday, March 21, 2022

Project Estimate Duration - On Site 140.0 days
20.0 week(s)
4.5 month(s)

FORM LCM-PC-03 | 08/20/2021

GENERAL CONDITIONS DIV.80									
LEBOLO COST CODE	SPEC. COST CODE	PERSONNEL	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total
		FIELD SUPERVISION							\$95,063
80-120		Superintendent	4.50	mth	\$13,500	\$60,750		\$0	\$60,750
		PROJECT MANAGEMENT							\$34,313
80-215		Senior Project Manager	0.23	mth	\$14,500	\$3,263		\$0	\$3,263
80-220		Project Manager	1.80	mth	\$13,500	\$24,300		\$0	\$24,300
80-285		Project Coordinator	0.90	mth	\$7,500	\$6,750		\$0	\$6,750
GENERAL CONDITIONS TOTAL			.			\$95,062.50		\$0.00	\$95,062.50
									OK



GENERAL CONDITIONS

PROJECT NAME: SL-04 FIS & BUILDING 846 STORM
RESILIENCY MODIFICATIONS PACKAGE
2

LEBOLO PROJECT No: 2021-0024

PBIA PROJECT No: DOA 18-2A SL-04

VERSION: 4.0

PROPOSAL DATE: Monday, March 21, 2022


Project Estimate Duration - On Site 140.0 days
20.0 week(s)
4.5 month(s)

FORM LCM-PC-03 | 08/20/2021

GENERAL CONDITIONS DIV.80										
LEBOLO COST CODE	SPEC. COST CODE	TEMPORARY TRAILER & STORAGE	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$17,050
80-410		Trailer/Office Buildout & Setup	1.00	ea		\$0	\$2,200	\$2,200	\$2,200	
80-405		Office Trailer and Related Expenses	4.50	mth		\$0	\$3,300	\$14,850	\$14,850	
80-441		Ground Level Storage Container Setup	2.00	ea		\$0	\$335	\$670	\$670	
80-440		Ground Level Storage Container	2.25	mth		\$0	\$198	\$445	\$445	
LEBOLO COST CODE	SPEC. COST CODE	SAFETY	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$11,720
80-540		Safety/Protection	1.00	ls		\$0	\$11,720.00	\$11,720	\$11,720	
LEBOLO COST CODE	SPEC. COST CODE	PROJECT CLOSEOUT	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$500
80-270		Close Out Administrator	1.00	ls		\$0	\$500	\$500	\$500	
LEBOLO COST CODE	SPEC. COST CODE	LISS	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$2,925
80-045		LISS - Lebolo Integrated Software Solutions	4.50	month	\$650	\$2,925		\$0	\$2,925	
GENERAL CONDITIONS TOTAL			.			\$2,925.00		\$30,385.39	\$33,310.39	OK

SECTION C

Reimbursable General Conditions

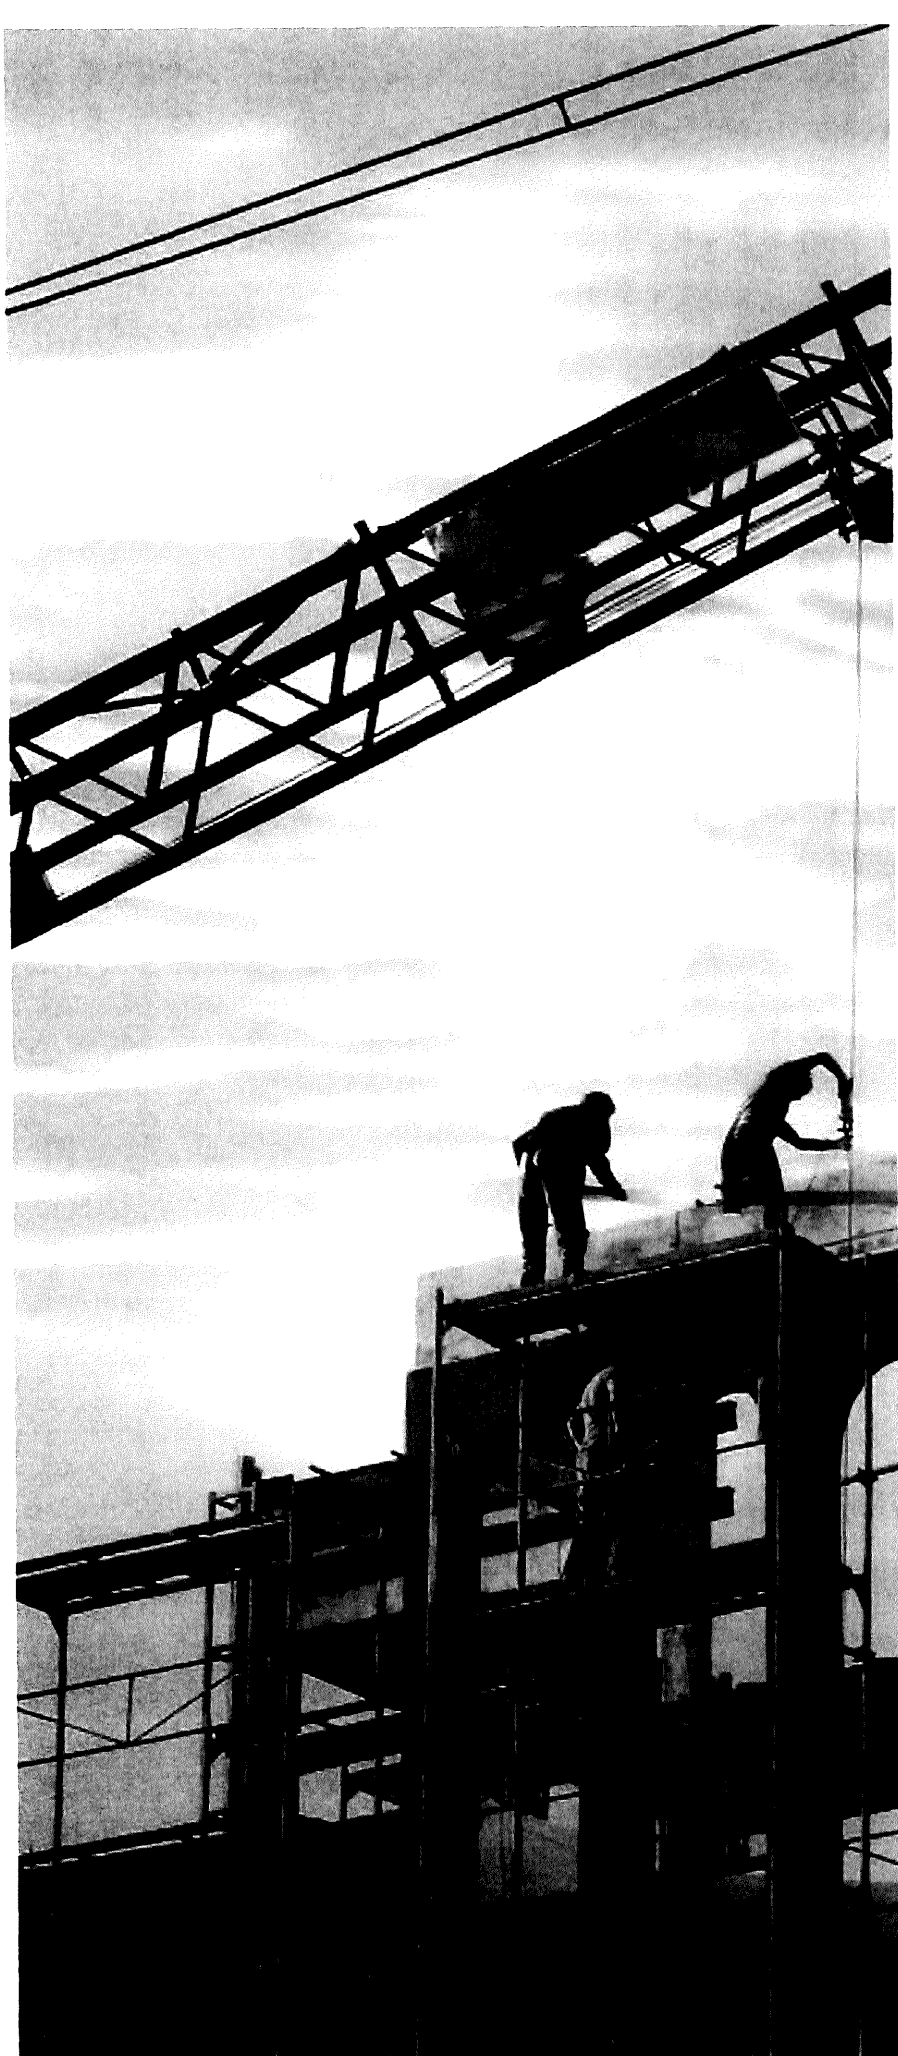



GENERAL REQUIREMENTS

PROJECT NAME: SL-04 FIS & BUILDING 846 STORM
RESILIENCY MODIFICATIONS PACKAGE
2

LEBOLO PROJECT No: 2021-0024

PBIA PROJECT No: DOA 18-2A SL-04

VERSION: 4.0


PROPOSAL DATE: Monday, March 21, 2022

Project Estimate Duration - On Site 140.0 days
20.0 week(s)
4.5 month(s)

GENERAL REQUIREMENTS DIV.17										
LEBOLO COST CODE	SPEC. COST CODE	SAFETY	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$4,275
17-110		Safety Inspections/Misc.	4.50	mth		\$0	\$950	\$4,275	\$4,275	
LEBOLO COST CODE	SPEC. COST CODE	CLEANING	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$23,850
17-205		Clean-up	80.00	hr	\$55	\$4,400		\$0	\$4,400	
17-210		Final Cleaning	1.00	ls	\$1,750	\$1,750		\$0	\$1,750	
17-220		Dumpsters	10.0	ea	\$1,500	\$15,000		\$0	\$15,000	
17-225		Temporary Toilets	4.50	2*mth	\$100	\$450	\$250	\$2,250	\$2,700	
LEBOLO COST CODE	SPEC. COST CODE	TEMPORARY SERVICES	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$7,000
17-305		Temporary Fence	1.00	ls	\$2,000	\$2,000		\$0	\$2,000	
17-310		Temporary Power	1.00	ls		\$0	\$5,000	\$5,000	\$5,000	
LEBOLO COST CODE	SPEC. COST CODE	TEMPORARY OFFICE	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$180
17-665		Plans & Documents	4.50	set*pg*mth		\$0	\$40	\$180	\$180	
LEBOLO COST CODE	SPEC. COST CODE	OTHER GENERAL REQUIREMENTS	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	\$9,000
17-950		Textura	1.00	ls	\$9,000	\$9,000		\$0	\$9,000	
GENERAL REQUIREMENTS TOTAL						\$32,600.40		\$11,705.00	\$44,305.40	OK

SECTION D

Minority Participation Report

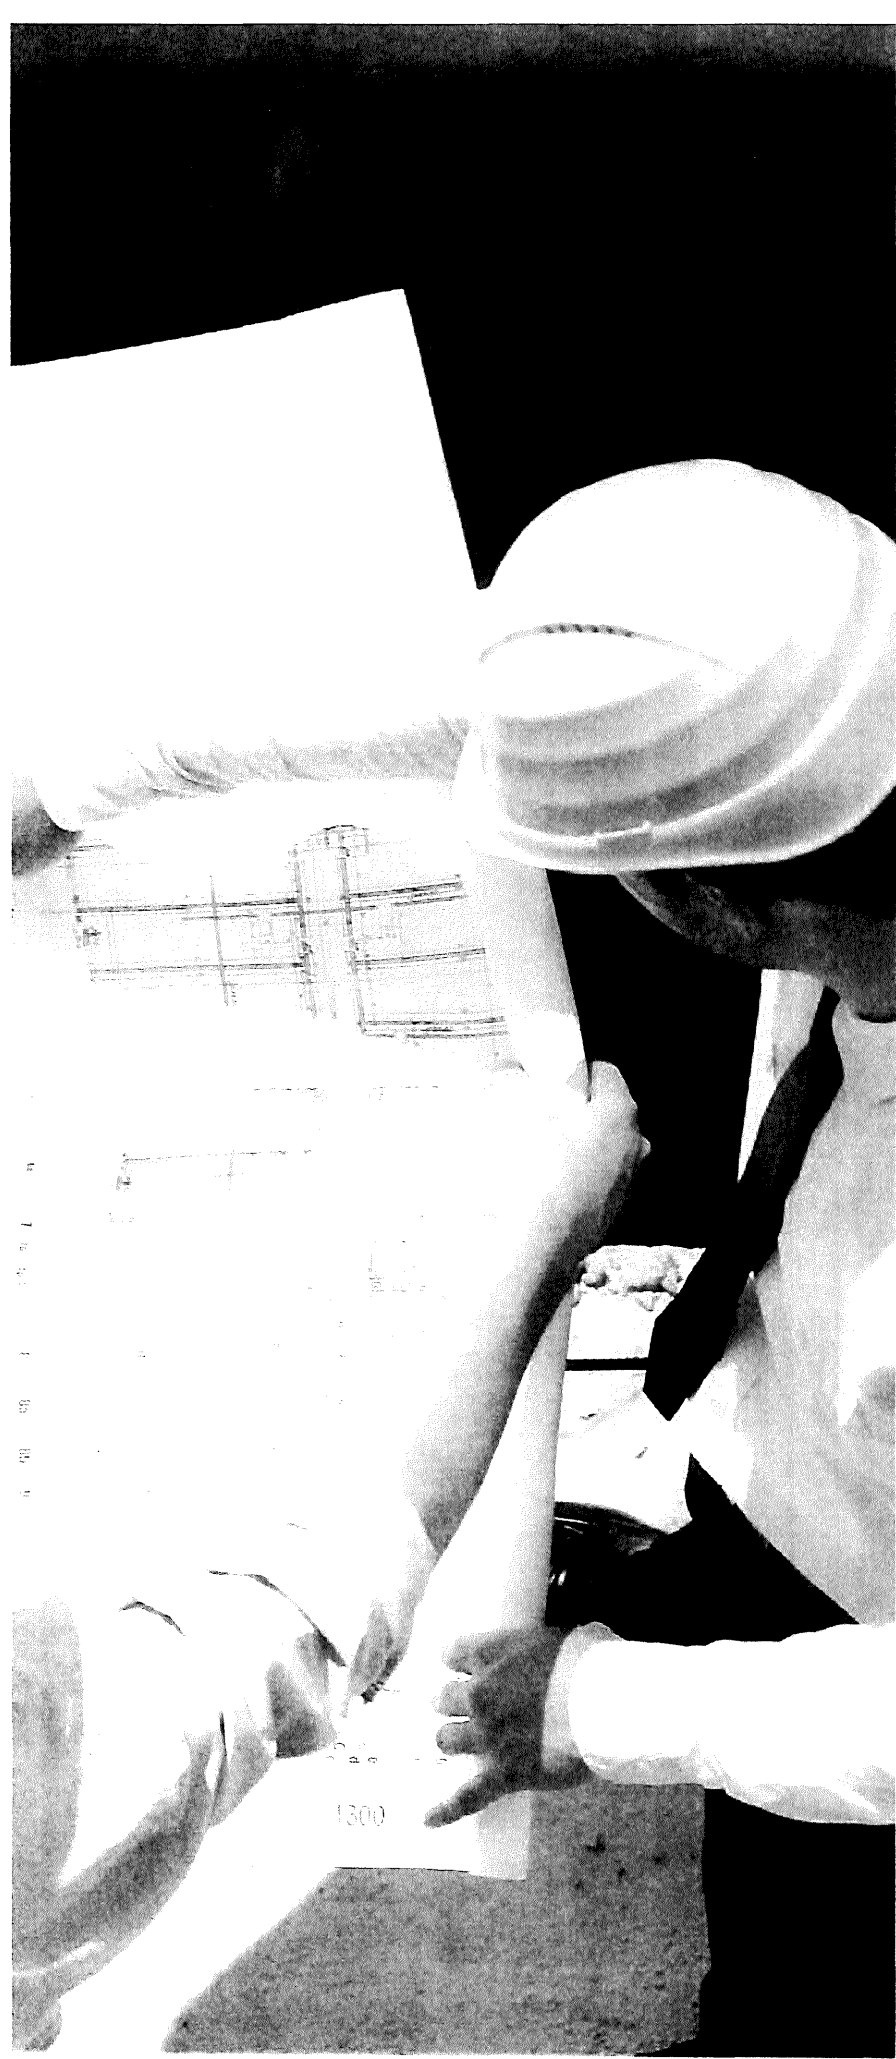



MINORITY PARTICIPATION REPORT
PALM BEACH COUNTY DEPARTMENT OF AIRPORTS
DOA 18-13 CM@RISK SERVICES for MISCELLANEOUS
IMPROVEMENTS PROJECTS on a CONTINUING CONTRACT BASIS

PBI Project No.	LEBOLO Project No.	Project Name	GMP BASE BID	DIRECT COST	EBO CERTIFICATION	SBE	MBE	WBE	OTHER MINORITY	TOTAL MINORITY PARTICIPATION	%	Status
SL-04	2020-0024	Storm Resiliency Package Phase 2	\$ 1,518,790.48	\$ 967,708.37								
		SUBCONTRACTORS										
SL-04	2020-0024	All American Ceilings		\$ 31,988.04	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
SL-04	2020-0024	Van Linda Iron		\$ 210,788.50	Yes	\$ 210,789	\$ -	\$ -	\$ -	\$ 210,789	22%	
SL-04	2020-0024	Roofing Package LEBOLO Allowance		\$ 3,000.00	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
SL-04	2020-0024	I.Q. Constructions		\$ 39,750.00	Yes	\$ 39,750	\$ -	\$ -	\$ -	\$ 39,750	4%	
SL-04	2020-0024	Johnsons Controls		\$ 3,685.83	No		\$ -	\$ -	\$ -	\$ -	0%	
SL-04	2020-0024	Quantum Mechanical		\$ 637,296.00	Yes	\$ 637,296	\$ -	\$ -	\$ -	\$ 637,296	66%	
SL-04	2020-0024	Protect Video		\$ 33,600.00	Yes	\$ 33,600	\$ -	\$ -	\$ -	\$ 33,600	3%	
SL-04	2020-0024	Bonded Lightning		\$ 5,100.00	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
SL-04	2020-0024	Low Voltage Package LEBOLO Allowance		\$ 2,500.00	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
TOTAL			\$ 1,518,790.48	\$ 967,708.37		\$ 921,435	\$ -	\$ -	\$ -	\$ 921,435	95%	
						95.22%	0.00%	0.00%	0.00%		95.22%	*Based on Direct Cost
						60.67%	0.00%	0.00%	0.00%		60.67%	*Based on Total Cost
						SBE	MBE	WBE	OTHER MINORITY			

SECTION E

Subcontractor Bidding Status Report



Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
02020 - Selective Demolition					
	Bader Demolition	Declined			
	Cushing Demolition	Declined			
	Demton Group	Declined	NONE, N/A Cert		
	I.Q. Constructions, Inc	Proposed	SBE, M/WBE, N/A Cert	02/21/2022 16:14	01-05-2022 11:32 AM Juna Hagaman said: Bidding, 02-10-2022 2:57 PM Sebastian Fonnegra said: final request sent
	J Sterling Services	Declined			
	Midway Corp.	Declined			
					01-12-2022 7:47 AM Sub Tony Piedra said: Good morning! Thank you for the invitation. I'll be at the site visit. My name is Tony Piedra (561) 644-2443. Thank you,
	N & P Construction and Development	Proposed	MWBE	02/07/2022 11:01	
	North Star Contractors	Declined	SWBE, ESBE, NRCA		01-09-2022 11:21 AM Juna Hagaman said: Not Bidding
	Others Construction	Declined			
	Pronto Construction Developers	Declined	SBE, MBE, MBE-DBE, DBE/MBE, DBE, DBE-MBE, CBE, ACI		
	Rapid Removal	Declined	SBE		02-10-2022 2:55 PM Sebastian Fonnegra said: Resent for demo, 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
05005 - Structural Steel Package	The BG Group	Declined	WBE, N/A Cert	01/11/2022 13:40	
	Wildcat Demolition	Declined	SBE		
	Ultimate Fabrication & Welding Services	Declined	NONE, AISC		01-04-2022 11:06 AM Juna Hagaman said: Did receive email and will review., 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
	AAA Steel Fabricators Inc	Declined			01-04-2022 11:08 AM Juna Hagaman said: Will review., 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
					01-04-2022 11:09 AM Juna Hagaman said: Accent welding@gmail.com, 01-04-2022 11:11 AM Juna Hagaman said: Accentwelding@gmail.com Added and resent, 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
	Accent Welding	Declined			
	ADF International Inc.	Declined	NONE, AISC FAB	01/05/2022 09:34	02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
					01-04-2022 11:15 AM Juna Hagaman said: Will review and will visit site visit if decide to bid., 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
	America CMS	Declined			
	Arriaga Steel	Declined			01-04-2022 11:17 AM Juna Hagaman said: VM Full, 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
	Associated Steel & Aluminum	Declined			01-04-2022 11:19 AM Juna Hagaman said: VM, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	Associated Steel & Aluminum Ltd Inc	Declined			01-04-2022 11:20 AM Juna Hagaman said: Not Bidding
	Bandy Universal Inc	Declined			01-04-2022 11:21 AM Juna Hagaman said: Not Bidding
	Buck Steel	Declined			01-04-2022 11:23 AM Juna Hagaman said: Not Bidding Not profitable for them.
	Camuke Enterprises	Declined			01-04-2022 11:25 AM Juna Hagaman said: Review, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	Castle Welding Inc dba J & R Welding	Declined			01-04-2022 11:26 AM Juna Hagaman said: VM, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	CBR Steel Fabricators & Erectors	Declined			01-04-2022 11:28 AM Juna Hagaman said: Review, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	Coastal Welding & Fabrications	Declined			01-04-2022 11:29 AM Juna Hagaman said: No Airport projects. Not Bidding
					01-04-2022 11:33 AM Juna Hagaman said: He will respond to email, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	Commercial Metal Buildings (CMB)	Declined			01-04-2022 11:35 AM Juna Hagaman said: Will remind Dom., 02-25-2022 9:15 AM Sebastian Fonnegra said: No answer - Not interested
	Composite Systems Inc.	Declined			
					01-04-2022 11:36 AM Juna Hagaman said: Call after Jan 4th., 01-04-2022 11:36 AM Juna Hagaman said: Call after Jan 4th. Return from vacation., 02-25-2022 9:15 AM Sebastian Fonnegra said: No answer - Not interested
	Custom Welding Diversified, Inc	Declined			01-04-2022 11:38 AM Juna Hagaman said: VM, 02-25-2022 9:15 AM Sebastian Fonnegra said: No answer - Not interested
	D & D Welding and Fabrication, LLC	Declined			01-04-2022 11:39 AM Juna Hagaman said: Not Bidding
	D W RECREATION SERVICES INC	Declined	DBE		01-04-2022 11:40 AM Juna Hagaman said: VM, 02-25-2022 9:15 AM Sebastian Fonnegra said: No answer - Not interested
	DBK Construction	Declined			
	Dordourian Enterprises Inc	Declined			
	Durabuilt Construction LLC	Declined			01-04-2022 11:43 AM Juna Hagaman said: Steel pilings
					01-04-2022 11:44 AM Juna Hagaman said: Review, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Dynamic Contractor Services LLC	Declined			01-04-2022 11:45 AM Juna Hagaman said: Review, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Eagle Metal Products Inc.	Declined		01/20/2022 14:53	
					01-04-2022 11:47 AM Juna Hagaman said: Review, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	East Coast Metal Structures	Declined	WBE/MBE, ABC, AGC, AISC	02/07/2022 10:16	01-04-2022 11:49 AM Juna Hagaman said: Copied info., 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Evans Roofing	Declined			
					01-04-2022 11:54 AM Juna Hagaman said: He is interested. Will review today., 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Florida Steel Buildings System	Declined			01-04-2022 11:55 AM Juna Hagaman said: Closed after 48 Years.
	Florida Welding Fabricators & Erectors	Declined			01-04-2022 11:56 AM Juna Hagaman said: Not Bidding
	Hofmann Investments	Declined			
	Hollywood Iron Works	Declined			01-04-2022 11:57 AM Juna Hagaman said: Incorrect phone number. Private #!, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Hollywood Ironworks	Declined			01-04-2022 11:57 AM Juna Hagaman said: Duplicate, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Jacob Erecting & Construction	Declined			01-05-2022 8:44 AM Juna Hagaman said: Call cannot be completed at this time.
	Jupiter Welding	Declined	N/A, N/A Cert		01-05-2022 8:45 AM Juna Hagaman said: VM, 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Limitless Contractors Corp	Declined			01-05-2022 8:46 AM Juna Hagaman said: Wireless caller is unavailable., 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
					01-05-2022 8:53 AM Juna Hagaman said: Anthony will review., 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Metal Supply	Declined	NONE, N/A Cert		
	Metal Tech Design Inc	Declined			01-05-2022 8:53 AM Juna Hagaman said: Disconnected, 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Palm Beach Iron Works	Declined	SBE	02/07/2022 11:41	01-05-2022 8:59 AM Juna Hagaman said: Will attend site visit., 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Sembco, Inc.	Declined			01-05-2022 9:01 AM Juna Hagaman said: She will remind them of site visit., 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
					01-05-2022 9:03 AM Juna Hagaman said: She will remind them to review., 01-05-2022 9:34 AM Juna Hagaman said: She will remind them to review. Added and resent: estimating@skylintsteel.com, 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Skyline Steel Inc	Declined		01/05/2022 10:05	01-05-2022 9:08 AM Juna Hagaman said: VM, 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Southern Custom Iron & Art	Declined	SBE		01-05-2022 9:11 AM Juna Hagaman said: VM, 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Sparks Metalworks	Declined		01/10/2022 10:34	

Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	Steel Fabricators	Declined	N/A, ABC, AGC, AISC ERE, AISC FAB		01-05-2022 9:13 AM Juna Hagaman said: Not Bidding
	Steel Fabricators and Welding, Inc.	Declined			01-05-2022 9:14 AM Juna Hagaman said: Not Bidding
	SteelCast Builders	Declined			01-05-2022 9:15 AM Juna Hagaman said: Fax number, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	STERLING STEEL FABRICATIONS, INC	Declined	SBE, DBE/MBE		01-05-2022 9:16 AM Juna Hagaman said: Gates, Railings, stairs No Structural work. Not Bidding. 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Structural And Metal Services LLC	Declined		01/05/2022 15:35	01-05-2022 9:23 AM Juna Hagaman said: Will attend site visit. 01-05-2022 9:31 AM Juna Hagaman said: Will attend site visit. Added and resent : structuralmetal@outlook.com. 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Suntor	Declined	NONE, AISC FAB		01-05-2022 9:38 AM Juna Hagaman said: Scott will look at it.. 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Tan Construction Services	Declined			01-05-2022 9:41 AM Juna Hagaman said: Wrong number as of 3 years ago., 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Treasure Coast Ornamental Iron	Declined			01-05-2022 9:43 AM Juna Hagaman said: VM, 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Tru-Steel Corp.	Declined			01-05-2022 9:45 AM Juna Hagaman said: Took our phone number., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	TWS Fabricators	Proposed	SBE	02/10/2022 08:56	01-05-2022 9:40 AM Juna Hagaman said: She will remind Bill.
	Valencia Welding	Declined			01-05-2022 9:46 AM Juna Hagaman said: Review. 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Van Linda Iron Works, Inc.	Proposed	SBE, AISC FAB	02/10/2022 07:40	
	VM Iron Works & Stuctural Steel Co	Declined		02/10/2022 13:49	01-05-2022 9:48 AM Juna Hagaman said: On their list to bid., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Walker Design & Construction	Declined	SBE, ABC	01/04/2022 21:14	02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Wallabys Fabrications LLC	Declined			01-05-2022 9:50 AM Juna Hagaman said: Took info., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Wentworth Construction	Declined			01-05-2022 9:51 AM Juna Hagaman said: Out of service., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	West Palm Machining & Welding, In	Declined		02/07/2022 11:45	01-05-2022 9:54 AM Juna Hagaman said: He will discuss with partners., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	West Point Industries	Declined			01-05-2022 9:55 AM Juna Hagaman said: Out of service, 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	WG Fabricators, LLC	Declined			01-05-2022 9:56 AM Juna Hagaman said: Out of service, 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	YATS Construction	Declined			01-05-2022 9:58 AM Juna Hagaman said: Will attend site visit. Sending name of rep to our email., 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	Yukon Construction, Inc.	Declined			01-05-2022 10:04 AM Juna Hagaman said: No VM, 01-05-2022 11:07 AM Juna Hagaman said: Shell contractor
09105 - Drywall & Framing Package					
	ACA CONTRACTORS, INC.	Declined	MWBE, DBE		01-05-2022 10:10 AM Juna Hagaman said: VM, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	Acousti Engineering Company of Flo	Declined	N/A, N/A Cert	01/06/2022 08:57	01-05-2022 10:34 AM Juna Hagaman said: Bidding and will remind , 01-05-2022 10:34 AM Juna Hagaman said: Bidding and will remind estimator of site visit., 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	Alen Construction Group	Declined	SBE, SBE-E, FED SBA 6A, DBE/MBE, DBE, DBE-MBE, CBE, ABC, ACI, AGC, SMACNA, NAWIC, CSI, ASPE		01-05-2022 10:38 AM Juna Hagaman said: VM for Angelina, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	ALLENMICHE' DEVELOPMENT & CO	Declined	DBE/MBE		01-05-2022 10:43 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	Applegate Interiors	Declined	SBE, MWBE		01-05-2022 10:46 AM Juna Hagaman said: She suggested an email be sent to remind him., 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	Arco & Associates	Declined			01-05-2022 10:48 AM Juna Hagaman said: Not Bidding
	Atlantic Interior Services	Declined	SBE, SBE-E, N/A Cert	01/03/2022 14:55	01-05-2022 10:51 AM Juna Hagaman said: Not Bidding
	Best Build	Declined	SBE, DBE/MBE		01-05-2022 10:52 AM Juna Hagaman said: VM, 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	CI Painting	Declined			02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	CREATIVE CONTRACTING GROUP	Declined	MWBE		01-05-2022 10:58 AM Juna Hagaman said: Suggested a reminder email., 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CRITICAL PATH CONSTRUCTION (PA	Declined	MWBE, DBE/MBE		01-05-2022 11:01 AM Juna Hagaman said: Will review., 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	FMA CONSTRUCTION	Declined	MBE, DBE/MBE, AWCI		02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	GAST CONSTRUCTION GROUP, INC.	Declined	SBE		01-05-2022 11:09 AM Juna Hagaman said: No VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	I.Q. Constructions, Inc.	Proposed	SBE, M/WBE, N/A Cert	02/21/2022 16:14	01-05-2022 11:32 AM Juna Hagaman said: Bidding, 02-10-2022 2:57 PM Sebastian Fonnegra said: final request sent
	Interior Textures	Declined			01-05-2022 11:34 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	MLS CONSTRUCTION, LLC.	Declined	MWBE		01-05-2022 11:21 AM Juna Hagaman said: VM, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	North Star Contractors	Declined	SWBE, ESBE, NRCA		01-05-2022 11:21 AM Juna Hagaman said: Not Bidding
	Precision Interiors, Inc.	Declined	NONE, N/A Cert		01-05-2022 11:36 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	Reynolds Construction Services	Declined	SBE, PDCA		01-05-2022 11:37 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	S3S CONSTRUCTION INC	Declined	DBE/MBE		01-05-2022 11:26 AM Juna Hagaman said: General Contractor
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Scott Murphy Plastering Inc.	Declined			01-05-2022 11:38 AM Juna Hagaman said: Out of service, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Walker Gerri's Construction	Declined	DBE/MBE		01-05-2022 11:30 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
09205 - Acoustical Ceiling Package					
	A Beautiful Ceiling	Declined			01-05-2022 10:06 AM Juna Hagaman said: Not Bidding
	A Ceiling Contractors, Inc.	Declined			01-05-2022 10:07 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	ABURI LLC	Declined			01-05-2022 10:08 AM Juna Hagaman said: Not Bidding
	ACA CONTRACTORS, INC.	Declined	MWBE, DBE		01-05-2022 10:10 AM Juna Hagaman said: VM, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	ACCEL Construction	Declined	DBE/MBE		01-05-2022 10:28 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Acousti Engineerng Company of Flo	Declined	N/A, N/A Cert	01/05/2022 08:57	01-05-2022 10:34 AM Juna Hagaman said: Bidding and will remind , 01-05-2022 10:34 AM Juna Hagaman said: Bidding and will remind estimator of site visit., 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested

Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	ACP CONSTRUCTION INC	Declined	DBE		01-05-2022 10:35 AM Juna Hagaman said: Silence on phone, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Alen Construction Group	Declined	SBE, SBE-E, FED SBA BA, DBE/MBE, DBE, DBE-MBE, CBE, ABC, ACI, AGC, SMACNA, NAWIC, CSI, ASPE		01-05-2022 10:38 AM Juna Hagaman said: VM for Angelina, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	All American Ceilings Inc	Proposed	ABE, ABC		01-05-2022 10:41 AM Juna Hagaman said: Bidding, 02-10-2022 2:59 PM Sebastian Fonnegra said: Not for pricing
	ALLENMICHE' DEVELOPMENT & CO	Declined	DBE/MBE		01-05-2022 10:43 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	American Construction Services	Declined	N/A, ABC		01-05-2022 10:45 AM Juna Hagaman said: She will remind Wagner., 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	Applegate Interiors	Declined	SBE, MWBE		01-05-2022 10:46 AM Juna Hagaman said: She suggested an email be sent to remind him., 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	Aron & Associates	Declined			01-05-2022 10:48 AM Juna Hagaman said: Not Bidding
	Assured Contracting, LLC	Declined			01-05-2022 10:49 AM Juna Hagaman said: Impact Windows and doors, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	Atlantic Interior Services	Declined	SBE, SBE-E, N/A Cert	01/03/2022 14:55	01-05-2022 10:51 AM Juna Hagaman said: Not Bidding
	Best Build	Declined	SBE, DBE/MBE		01-05-2022 10:52 AM Juna Hagaman said: VM, 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	C. SQUARE DEVELOPMENT CO.	Declined	MWBE		01-05-2022 10:53 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CCGC, INC.	Declined	MWBE		01-05-2022 10:55 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CONTRACTORS SUPPORT SERVICES	Declined	MWBE		01-05-2022 10:56 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CREATIVE CONTRACTING GROUP	Declined	MWBE		01-05-2022 10:58 AM Juna Hagaman said: Suggested a reminder email., 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CRITICAL PATH CONSTRUCTION (PA	Declined	MWBE, DBE/MBE		01-05-2022 11:01 AM Juna Hagaman said: Will review., 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	DORSAINVIL CONSTRUCTION LLC (P	Declined	DBE/MBE		01-05-2022 11:03 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	FMA CONSTRUCTION	Declined	MBE, DBE/MBE, AWC		02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	GAST CONSTRUCTION GROUP, INC.	Declined	SBE		01-05-2022 11:09 AM Juna Hagaman said: No VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	JAX CONSTRUCTION & DEVELOPME	Declined	DBE/MBE		01-05-2022 11:10 AM Juna Hagaman said: VM Full, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	JU CONSTRUCTION CORP	Declined	DBE/MBE		01-05-2022 11:11 AM Juna Hagaman said: VM Full No accepto mensaje!, 01-05-2022 11:18 AM Juna Hagaman said: VM Full No accepto mensaje!, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	Martin Acoustic, LLC	Declined		01/18/2022 13:20	01-05-2022 11:18 AM Juna Hagaman said: Bidding, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	MLS CONSTRUCTION, LLC	Declined	MWBE		01-05-2022 11:21 AM Juna Hagaman said: VM, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	North Star Contractors	Declined	SWBE, ESBE, NRCA		01-05-2022 11:21 AM Juna Hagaman said: Not Bidding
	R2T, INC	Declined	MWBE		01-05-2022 11:24 AM Juna Hagaman said: Estimator out sick., 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	S3S CONSTRUCTION INC	Declined	DBE/MBE		01-05-2022 11:26 AM Juna Hagaman said: General Contractor
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Superior Interior Systems Inc	Declined	NONE, N/A Cert		01-05-2022 11:28 AM Juna Hagaman said: Not Bidding
	TOTAL SOLUTION CONTRACTORS	Declined	SBE		01-05-2022 11:29 AM Juna Hagaman said: Not in service., 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	Walker Gerrits Construction	Declined	DBE/MBE		01-05-2022 11:30 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
09505 - Painting Package	A to Z Paint Contracting	Declined	SWBE, SBE		01-05-2022 11:43 AM Juna Hagaman said: Not Bidding
	A1 Paint, Inc of Palm Beach	Declined	SBE, SBE-E, MBE, NAWIC		02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	ACA CONTRACTORS, INC.	Declined	MWBE, DBE		01-05-2022 10:10 AM Juna Hagaman said: VM, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	Advanced Painting Contractors	Declined	N/A, N/A Cert	01/03/2022 15:28	02-25-2022 9:26 AM Sebastian Fonnegra said: Not interested
	Advantage Painting LLC	Declined			02-25-2022 9:37 AM Sebastian Fonnegra said: No answer - Not interested
	Alen Construction Group	Declined	SBE, SBE-E, FED SBA BA, DBE/MBE, DBE, DBE-MBE, CBE, ABC, ACI, AGC, SMACNA, NAWIC, CSI, ASPE		01-05-2022 10:38 AM Juna Hagaman said: VM for Angelina, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	ALLENMICHE' DEVELOPMENT & CO	Declined	DBE/MBE		01-05-2022 10:43 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	Best Build	Declined	SBE, DBE/MBE		01-05-2022 10:52 AM Juna Hagaman said: VM, 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	Brookley Wallcoverings	Declined	SBE		01-05-2022 11:44 AM Juna Hagaman said: VM, 02-25-2022 9:26 AM Sebastian Fonnegra said: No answer - Not interested
	Campbell Painting, Inc.	Declined	SBE-E, MBE-E		01-05-2022 11:45 AM Juna Hagaman said: Closing the business.
	CCGC, INC.	Declined	MWBE		01-05-2022 10:55 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CHAMPION PAINTING SPECIALTY SE	Declined	DBE/MBE		01-05-2022 11:47 AM Juna Hagaman said: Gave me options for NYC and Alaska. Not for Florida, 02-25-2022 9:26 AM Sebastian Fonnegra said: No answer - Not interested
	Copax LLC	Declined	WOSB, WCOE		01-05-2022 11:50 AM Juna Hagaman said: Will attend site visit., 01-05-2022 11:52 AM Juna Hagaman said: Will attend site visit. Added and resent: bids@copaxpainting.com, 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	CREATIVE CONTRACTING GROUP	Declined	MWBE		01-05-2022 10:58 AM Juna Hagaman said: Suggested a reminder email., 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CRITICAL PATH CONSTRUCTION (PA	Declined	MWBE, DBE/MBE		01-05-2022 11:01 AM Juna Hagaman said: Will review., 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	Dynamic Painting	Declined	WMBE, SBE, DBE/MBE		01-05-2022 11:54 AM Juna Hagaman said: VM 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	Eagle Painting (U&J Inc)	Declined	MWBE		01-05-2022 11:55 AM Juna Hagaman said: Suggested an email reminder be sent., 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	G.P.S. Painting Group	Declined	SBE		01-05-2022 11:57 AM Juna Hagaman said: Review, 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	GAST CONSTRUCTION GROUP, INC.	Declined	SBE		01-05-2022 11:09 AM Juna Hagaman said: No VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	Interior Textures	Declined			01-05-2022 11:34 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	MLS CONSTRUCTION, LLC	Declined	MWBE		01-05-2022 11:21 AM Juna Hagaman said: VM, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested

Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	North Star Contractors	Declined	SWBE, ESBE, NRCA		01-05-2022 11:21 AM Juna Hagaman said: Not Bidding
	QUALITY PAINTING & MORE	Declined	HUD SECTION 3		01-05-2022 11:59 AM Juna Hagaman said: Phone went to fax sound., 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	R2T, INC	Declined	MWBE		01-05-2022 11:24 AM Juna Hagaman said: Estimator out sick., 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	Reynolds Construction Services	Declined	SBE, PDCA		01-05-2022 11:37 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	S3S CONSTRUCTION INC	Declined	DBE/MBE		01-05-2022 11:26 AM Juna Hagaman said: General Contractor
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Scott Murphy Plastering Inc.	Declined			01-05-2022 11:38 AM Juna Hagaman said: Out of service, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	SELECT COATINGS, INC.	Declined	SBE, MBE-E, ASC		01-05-2022 12:01 PM Juna Hagaman said: Concrete resurfacing only.
	Sun Art Painting	Declined	SBE		01-05-2022 12:03 PM Juna Hagaman said: Resent email, 02-25-2022 9:28 AM Sebastian Fonnegra said: No answer - Not interested
	Talbot Painting	Declined	SBE		01-05-2022 12:06 PM Juna Hagaman said: Don looked at plans but no decision., 02-25-2022 9:28 AM Sebastian Fonnegra said: No answer - Not interested
	TOTAL SOLUTION CONTRACTORS	Declined	SBE		01-05-2022 11:29 AM Juna Hagaman said: Not in service., 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	Walker Gerrits Construction	Declined	DBE/MBE		01-05-2022 11:30 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
13100 - Lightning Protection	All South Lightning Protection	Proposed	NONE, N/A Cert		
	Bonded Lightning Protection	Proposed			
15105 - Fire Protection Package					
	A.B. Fire Equipment	Declined	SBE		01-05-2022 9:41 AM Juna Hagaman said: Resent., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Alliance Automatic Fire Sprinklers	Declined	SMBE, SBE		01-06-2022 9:42 AM Juna Hagaman said: Phone not in service, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	American Eagle Fire Protection Inc	Declined			01-06-2022 9:45 AM Juna Hagaman said: Rick will look at plans., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Brigade Fire Protection	Declined			01-06-2022 9:45 AM Juna Hagaman said: Not Bidding
	Caribbean Fire	Declined			01-06-2022 9:51 AM Juna Hagaman said: Added and resent: Michael Vidal mvidal@caribbeanfire.com, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Farmer & Irwin	Declined	N/A, N/A Cert	02/07/2022 10:05	01-04-2022 9:49 AM Juna Hagaman said: No VM, 01-04-2022 12:17 PM Sebastian Fonnegra said: Jeff will be the SR PM on this Project., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Harpers Fire Sprinkler	Declined	SBE, MWBE		01-06-2022 9:53 AM Juna Hagaman said: VM, 01-06-2022 9:55 AM Juna Hagaman said: Frank called and said he would look at plans., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Johnson Controls Fire Protection	Proposed			02-25-2022 9:10 AM Sebastian Fonnegra said: Proposed
	Metro Fire Protection Services, Inc.	Declined			01-06-2022 9:59 AM Juna Hagaman said: VM, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	National Fire Protection	Declined			01-06-2022 10:01 AM Juna Hagaman said: Answering service, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Sprinklermatic	Declined	NONE, ABC		01-05-2022 10:07 AM Juna Hagaman said: Under Review, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Total Life Safety Corporation	Declined			01-06-2022 10:08 AM Juna Hagaman said: Respond to email, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Wiginton Fire Systems	Declined			01-06-2022 10:09 AM Juna Hagaman said: Scott's VM, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
15205 - HVAC Package					
	Phoenix Air Conditioning, Inc.	Declined			01-04-2022 10:14 AM Juna Hagaman said: She will ask Chris., 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	AC Power & Comfort	Declined	SBE-E, N/A Cert		01-04-2022 9:25 AM Juna Hagaman said: VM, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Air Handlers of the Palm Beaches	Declined	SBE		01-04-2022 8:35 AM Juna Hagaman said: Out of service.
	Air South Mechanical	Declined	NONE, PHCC		01-04-2022 9:28 AM Juna Hagaman said: VM, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	All Year Cooling	Declined			01-04-2022 9:27 AM Juna Hagaman said: If they are interested they will respond., 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Altman Air Conditioning	Declined		01/05/2022 08:10	01-04-2022 8:37 AM Juna Hagaman said: Will remind estimator., 01-04-2022 10:11 AM Sebastian Fonnegra said: Contacted - Will review drawings, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Aspen	Declined	EB0, ACCA	01/03/2022 14:55	02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Big Air Mechanical	Declined	SBE	02/21/2022 16:39	01-04-2022 9:23 AM Juna Hagaman said: Will be at site visit., 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Bradley Heating & Air Conditioning	Declined	SBE		01-04-2022 9:34 AM Juna Hagaman said: Will review today and respond to email., 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Cal's Mechanical Group	Declined			01-04-2022 9:36 AM Juna Hagaman said: Not Bidding
	Cedars Electro-Mechanical Inc.	Proposed	WBE, SBE	01/04/2022 14:19	01-04-2022 9:43 AM Juna Hagaman said: Review today,
	Climax Mechanical Corp	Declined	NONE, N/A Cert	01/20/2022 12:22	01-04-2022 9:43 AM Juna Hagaman said: Review, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Commercial Cooling	Declined			01-04-2022 9:44 AM Juna Hagaman said: Not Bidding
	Cool Solutions A/C	Declined			01-04-2022 9:45 AM Juna Hagaman said: VM, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	EDS Air Conditioning	Declined			01-04-2022 9:48 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Farmer & Irwin	Proposed	N/A, N/A Cert	02/07/2022 10:05	01-04-2022 9:49 AM Juna Hagaman said: No VM, 01-04-2022 12:17 PM Sebastian Fonnegra said: Jeff will be the SR PM on this Project., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Florida Mechanical LLC	Proposed	SBE	02/08/2022 08:38	01-04-2022 9:52 AM Juna Hagaman said: They are interested and will call Sebastian.
	Flowmaster	Declined	SBE		01-04-2022 9:54 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	General Mechanical Corporation	Declined	SCSDB, SBE, NABE, DBE-MBE, N/A Cert		01-05-2022 10:00 AM Juna Hagaman said: Added and resent: David Cannon dcannon@oescgroup.com, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	H. Lamm Industries	Declined	NONE, ABC	02/07/2022 12:45	01-04-2022 10:03 AM Juna Hagaman said: Jeff is reviewing and will respond to email., 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	HS Hoffman	Declined	MWBE		01-04-2022 10:03 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested

Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	INTEG MIAMI LLC	Declined	SBE		01-04-2022 10:09 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Matrix Air, LLC	Declined			01-04-2022 10:12 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Natal Air Conditioning	Declined	SBE-F, ABC		01-04-2022 10:12 AM Juna Hagaman said: It was passed to owner., 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Precision Air Systems	Declined	SBE		01-04-2022 10:15 AM Juna Hagaman said: She suggested we send a follow-up email., 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Quantum Mechanical	Proposed	SBE, SBE-E, MWSBE, MWBE, MSBE, DBE/MBE, DBE, N/A Cert	02/10/2022 11:35	01-04-2022 10:18 AM Juna Hagaman said: Review.
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Sequil Systems Inc.	Declined	SBE, SBE-E, USGBC		01-04-2022 10:23 AM Juna Hagaman said: The menu kept sending me back to menu!, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Smithco Service	Declined	SBE		01-04-2022 10:25 AM Juna Hagaman said: Rikch, 01-04-2022 10:27 AM Juna Hagaman said: Resent and added: Richard@smithcoservices.com, 01-11-2022 9:21 PM This contact has unsubscribed from receiving: - communications on this project only - all project communications - all general communications - all prequal communications Contact said: Not interested ., 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Southeast Mechanical	Declined	BEP, ABC	01/04/2022 08:06	02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Southern Mechanical	Declined		01/03/2022 14:52	02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Stokes Mechanical	Declined	WBE		01-04-2022 10:29 AM Juna Hagaman said: Jane's VM , 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Sunshine State	Declined	SBE, MWBE		01-04-2022 10:32 AM Juna Hagaman said: Will be at site visit., 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	The Airtex Corp.	Declined	SBE		01-04-2022 10:34 AM Juna Hagaman said: She will remind them., 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	The True-Pros	Declined	SBE		01-04-2022 10:36 AM Juna Hagaman said: First day back after Holidays., 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Thermal Concepts	Declined	NONE, ABC		01-05-2022 10:39 AM Juna Hagaman said: Mike VM, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	TOTAL SYSTEMS, INC.	Declined	MWBE, DBE		01-04-2022 10:40 AM Juna Hagaman said: Phone just rings busy., 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Wright Brothers Contracting Service	Declined			01-04-2022 10:53 AM Juna Hagaman said: Resent to : Vishal Singh vsingh@wrightbrotherscs.com, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
16005 - Electrical Package	Albert Electric	Declined	SBE		01-06-2022 10:23 AM Juna Hagaman said: VM, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Ali Lake Electrical	Declined	SBE		01-06-2022 10:24 AM Juna Hagaman said: VM, 01-06-2022 10:26 AM Juna Hagaman said: Not Bidding
	Arlington Electric	Declined			01-06-2022 10:28 AM Juna Hagaman said: Not Bidding
	Bosco Electric	Declined			01-06-2022 10:30 AM Juna Hagaman said: Not bidding
	Bradford Electric	Declined	SBE		01-06-2022 10:33 AM Juna Hagaman said: VM, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	BROWN & BROWN ELECTRIC INC	Declined	SBE, MWBE, DBE		01-06-2022 10:33 AM Juna Hagaman said: Not in Service
	C.R. DUNN	Declined	HUD SECTION 3		01-06-2022 10:35 AM Juna Hagaman said: Resent., 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Construct Connect	Declined		02/07/2022 11:36	02-25-2022 9:37 AM Sebastian Fonnegra said: No answer - Not interested
	Construction Journal	Declined			02-25-2022 9:37 AM Sebastian Fonnegra said: No answer - Not interested
	Design Electrical	Declined			01-05-2022 10:38 AM Juna Hagaman said: Review, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Electrical Consulting Services	Declined	SBE		01-06-2022 10:40 AM Juna Hagaman said: She will check with Ken., 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	ELECTRON PLUS OF FLORIDA, LLC	Declined	SBE		01-06-2022 10:42 AM Juna Hagaman said: Not Bidding
	Ellington Electrical Inc	Declined			01-06-2022 10:46 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Everton Electric LLC	Declined			01-06-2022 10:45 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Fine Line Electric, Inc.	Declined	NONE, ABC		01-06-2022 10:47 AM Juna Hagaman said: Not Bidding
	Firecomm Services LLC	Declined	CMBE, IEC		01-06-2022 10:48 AM Juna Hagaman said: Review, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	FLORIDA METRO CONSTRUCTION CO	Declined	SBE, DBE/MBE		01-06-2022 10:51 AM Juna Hagaman said: Added and resent: Sommer Russell s.russell@floridametro.com, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Gilmore Electric Company	Declined	SBE		01-06-2022 11:04 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Godfrey Electric	Declined	SBE, IEC		01-06-2022 11:07 AM Juna Hagaman said: Tad VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Grid-One Electrical Construction	Declined	SBE		01-06-2022 11:08 AM Juna Hagaman said: Not Bidding
	Guthart Electric	Declined	WOSB, IEC		01-06-2022 11:09 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Intercoastal Electric	Declined	NONE, N/A Cert	01/03/2022 15:21	01-06-2022 11:13 AM Juna Hagamah said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	JAG ELECTRICAL ENTERPRISES INC	Declined	MWBE, DBE		01-06-2022 11:15 AM Juna Hagaman said: Added and resent: kgordonjag@icloud.com, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	JMA Electric	Declined	SBE, MBE, DBE/MBE		01-06-2022 11:17 AM Juna Hagaman said: Will respond to email, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Metro Electric	Declined			01-06-2022 11:19 AM Juna Hagaman said: Recep thought they would bid., 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Mr. Wireman (Arbor Electrical Serv	Declined	SWBE, SBE, DBE/MBE		01-06-2022 11:21 AM Juna Hagaman said: Resent to Magaret, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	OHMS Electrical Corp.	Declined	SBE, MWBE	01/21/2022 10:32	01-06-2022 11:23 AM Juna Hagaman said: Gabriela, 01-06-2022 11:24 AM Juna Hagaman said: Gabriela, 01-06-2022 11:24 AM Juna Hagaman said: Gabriela Coordinator., 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Protect Video	Proposed	WOSB, WBE/MBE, WBE-MBE, SBE, IEC		01-06-2022 11:26 AM Juna Hagaman said: VM, 02-25-2022 9:06 AM Sebastian Fonnegra said: Proposed

Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	Proton Electric Service Llc	Declined			01-06-2022 11:27 AM Juna Hagaman said: VM, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	PVM Electric	Declined	SBE		01-05-2022 11:29 AM Juna Hagaman said: Suggested we call back tomorrow., 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Pyke Electric	Declined	SBE, DBE/MBE	02/21/2022 09:28	01-05-2022 11:30 AM Juna Hagaman said: Will respond to email., 01-06-2022 11:31 AM Juna Hagaman said: Will respond to email., 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	The Blue Book	Declined		01/19/2022 12:08	02-25-2022 9:37 AM Sebastian Fonnegra said: No answer - Not interested
	TNA Electric	Declined	SBE-E, DISABLED/SVC DISABLED VET, NECA	01/06/2022 20:54	01-06-2022 11:32 AM Juna Hagaman said: VM, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Triton Electric Company	Declined	SBE		01-06-2022 11:34 AM Juna Hagaman said: Resent to admin., 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Universal Electric of Florida	Declined	SBE	01/07/2022 08:21	01-06-2022 11:37 AM Juna Hagaman said: Resent, 01-06-2022 11:38 AM Juna Hagaman said: Resent to Phil, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Valor Construction Management	Declined	SDVOSB, SBA 8(a), FED HUB ZONE		01-06-2022 11:38 AM Juna Hagaman said: VM, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Wright Brothers Contracting Service	Declined			01-04-2022 10:53 AM Juna Hagaman said: Resent to Vishal Singh vsingh@wrightbrotherscs.com, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested

SECTION F

Scope Sheets

Subcontractor Proposals

See Individual Document

SECTION G

Public Ad

The Palm Beach Post


Palm Beach Daily News | **LOCALiQ**

PROOF OF PUBLICATION STATE OF FLORIDA PUBLIC NOTICE

Before the undersigned authority, personally appeared Teal Pontarelli, who on oath, says that he/she is a Legal Advertising Representative of The Palm Beach Post, a daily and Sunday newspaper, published in West Palm Beach and distributed in Palm Beach County, Martin County, and St. Lucie County, Florida; that the attached copy of advertising for a Legal - NoticetoBid was published in said newspaper in issues dated: first date of Publication 01/05/2022 and last date of Publication 02/04/2022. or by publication on the newspaper's website. Affiant further says that the said The Palm Beach Post is a newspaper published in West Palm Beach, in said Palm Beach County, Florida and that the said newspaper has heretofore been continuously published in said Palm Beach County, Florida, daily and Sunday and has been entered as second class mail matter at the post office in West Palm Beach, in said Palm Beach County, Florida, for a period of one year next preceding the first publication of the attached copy of advertisement; and affiant further says that he/she has neither paid nor promised any person, firm or corporation any discount, rebate, commission or refund for the purpose of securing this advertisement for publication in said newspaper.

LEBOLO CONSTRUCTION MANAGEMENT
2100 CORPORATE DRIVE
BOYNTON BEACH, FL 33426


Invoice/Order Number:	0000678868
Ad Cost:	\$3,467.52
Paid:	\$3,467.52
Balance Due:	\$0.00

Signed 

(Legal Advertising Agent)

Sworn or affirmed to, and subscribed before me, this 9th day of February, 2022 in Testimony whereof, I have hereunto set my hand and affixed my official seal, the day and year aforesaid.

Signed 



Please see Ad on following page(s).

Invoice/Order Number:	0000678868
Ad Cost:	\$3,467.52
Paid:	\$3,467.52
Balance Due:	\$0.00

ADVERTISEMENT FOR BID 2020-0024-S104 - LEBOLO CONSTRUCTION MANAGEMENT, INC. for Palm Beach County - Department of Airports (Owner) is seeking bids for the project: FIS & Building 846 Storm Resiliency Modifications - Package 2 at Palm Beach International Airport. The overall scope of the project involves rooftop new metal grating and structural steel frame over existing screen wall to protect two (2) new replacement chiller units, chiller V8 bench beams replacement, lightning system and antennas temporary relocation, interior structural steel deck reinforcement, VAV boxes replacement, new and repairs of acoustical and hard ceilings. Project bid documents are available via SmartBid. The Pre-Bid Conference and Site Visit are scheduled for 01/12/22 at 1:00 PM at 846 Palm Beach International Airport - West Palm Beach, FL 33406 for all interested subcontractors. Must be limited to one (1) representative per company and must comply with COVID protocols; interested participants are required to wear a face mask at all times, participants will need to undergo a Temperature Screening and Questionnaire before entering the building. Palm Beach County, in accordance with the provisions of Title VI of the Civil Rights Act of 1964 (78 Stat. 252, 42 USC §§ 2000d to 2000d-4) and the Regulations, hereby notifies all bidders or offerors that it will affirmatively ensure that any contract entered into pursuant to this advertisement, disadvantaged business enterprises will be afforded full and fair opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, or national origin in consideration for an award. Preference will be given to firms having a permanent place of business in Palm Beach County as per Local Preferences (Article 2-2.1.13.2). Sealed Bids must be submitted on or before February 8, 2022, 02:00 PM at 846 Palm Beach International Airport, West Palm Beach, FL 33406 on a sealed envelope with your Company Name, Date, and Name of the Project. Electronic mail proposals are not accepted for this solicitation. No bid may be withdrawn after the bid due date & time for a period of 90 days. LEBOLO reserves the right to reject any or all bids & waive any informalities or irregularities in the bids, & to re-advertise for bids for any reason. All costs incurred by bidders in preparing a proposal shall be the sole responsibility of the bidder. For help contact LEBOLO Pre-Construction Office (bids@lebolo.com) 561-742-7644 for access to SmartBid to complete prequal info & access bid docs.
1-5, 1-7, 1-10, 1-12, 1-14, 1-17, 1-19, 1-21, 1-24, 1-26, 1-28, 1-31, 2-2, 2-4/2022
0000678868-01

SECTION H

Drawing Log





Lebolo Construction Management, Inc.

Printed on Wed Mar 9, 2022 at 09:26 am EST

Job #: 2020-0024 PBIA - Storm Resilience Phase 2
846 846, Palm Beach International Airport
West Palm Beach, Florida 33406

100% CD's Storm Resilience Pck. (10/08/21)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
Cover Sheet					
Cover Sheet	COVER SHEET	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
General					
G001	GENERAL NOTES, ABBREVIATIONS AND SYMBOLS & SHEET INDEX	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
G002	GENERAL CONTRACT NOTES & SAFETY AND SECURITY NOTES	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
G003	WORK AREA & ACCESS ROUTE	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
G004	CONSTRUCTION SCHEDULE	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
G100	CONTRACT LAYOUT PLAN AND GENERAL NOTES	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
Architectural					
A131	OVERALL FIRST LEVEL REFLECTED CEILING PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
A131	OVERALL FIRST LEVEL REFLECTED CEILING PLAN	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
A132	OVERALL SECOND LEVEL REFLECTED CEILING PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
A132	OVERALL SECOND LEVEL REFLECTED CEILING PLAN	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
A132A	PARTIAL SECOND LEVEL REFLECTED CEILING PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
A132A	PARTIAL SECOND LEVEL REFLECTED CEILING PLAN	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
Electrical					
E001	ELECTRICAL GENERAL NOTES, SYMBOLS, AND ABBREVIATIONS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E101	OVERALL FIRST FLOOR POWER PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E102	OVERALL SECOND FLOOR POWER PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E103	OVERALL ROOF LEVEL POWER PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E801	PARTIAL ELECTRICAL ONE-LINE DIAGRAM	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E901	EXISTING PANELBOARD SCHEDULES	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)



Lebolo Construction Management, Inc.


Printed on Wed Mar 9, 2022 at 09:26 am EST

Job #: 2020-0024 PBIA - Storm Resilience Phase 2
846 846, Palm Beach International Airport
West Palm Beach, Florida 33406

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
ED101	OVERALL FIRST FLOOR ELECTRICAL DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
ED102	OVERALL SECOND FLOOR ELECTRICAL DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
ED103	OVERALL ROOF LEVEL ELECTRICAL DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
ED103	OVERALL ROOF LEVEL ELECTRICAL DEMOLITION PLAN	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
Mechanical					
M001	LEGEND AND GENERAL NOTES	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M101	OVERALL FIRST FLOOR HVAC PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M102	OVERALL SECOND FLOOR HVAC PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M103A	PARTIAL ROOF HVAC PLAN - AREA A	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M103A	PARTIAL ROOF HVAC PLAN - AREA A	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
M201	CHILLER PIPING SCHEMATIC	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M501	MECHANICAL DETAILS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M601	MECHANICAL HVAC SCHEDULE	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M701	MECHANICAL CONTROLS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M702	MECHANICAL CONTROLS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M703	MECHANICAL CONTROLS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
MD101	OVERALL FIRST FLOOR HVAC DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
MD102	OVERALL SECOND FLOOR HVAC DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
MD103A	PARTIAL ROOF HVAC DEMOLITION PLAN - AREA A	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
MD103A	PARTIAL ROOF HVAC DEMOLITION PLAN - AREA A	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
Structural					
S101	STRUCTURAL NOTES, PLANS, AND DETAILS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)

SECTION I

Construction Schedule

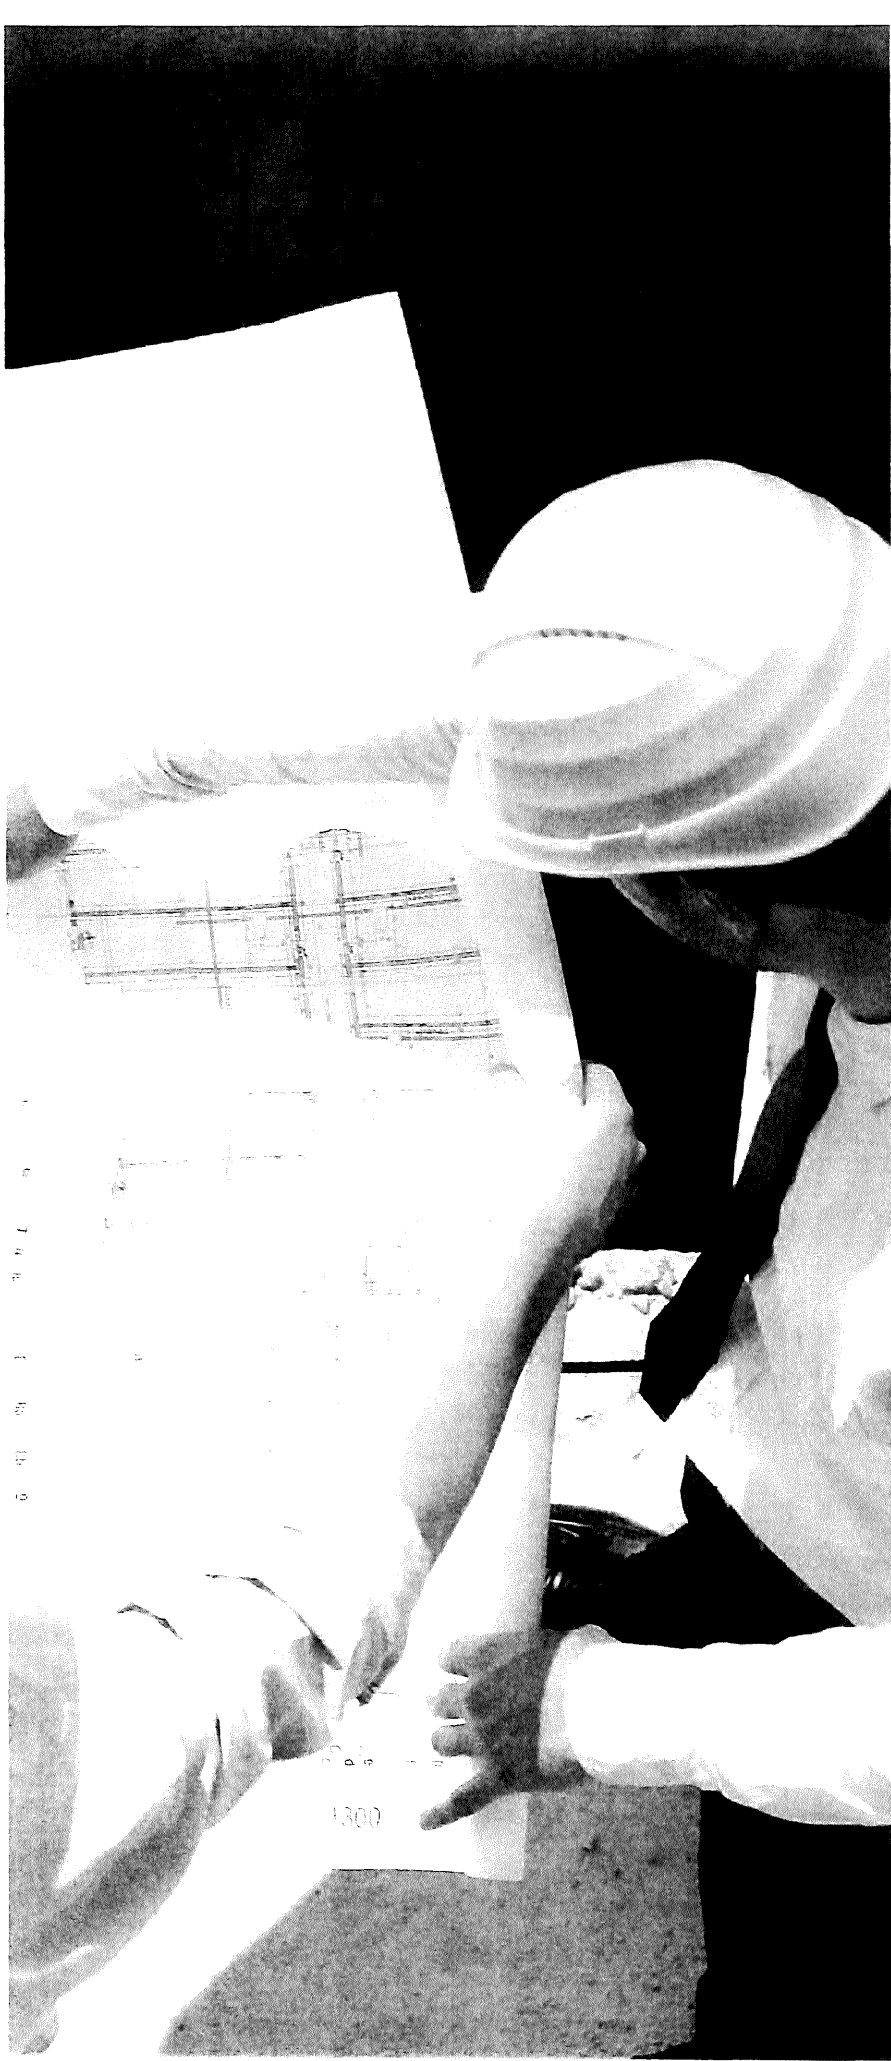


ID	Task Mode	Task Name	Duration	Start	Finish	Task Summary
1	☐	Storm Resilience Package - PRELIMINARY SCHEDULE	265 days	Sat 1/15/22	Fri 1/20/23	Task Summary
2	☐	Preliminars	81 days	Sat 1/15/22	Mon 5/9/22	Inactive Task
3	☐	Bid Process	39 edays	Sat 1/15/22	Wed 2/23/22	Inactive Milestone
4	☐	NTP	10 days	Fri 4/15/22	Thu 4/28/22	Inactive Milestone
5	☐	Contract Execution	7 days	Fri 4/29/22	Mon 5/9/22	Inactive Summary
6	☐	Permit - BY OWNER	60 edays	Sat 1/15/22	Wed 3/16/22	Manual Summary
7	☐	Procurement	131 days	Thu 4/28/22	Sun 10/30/22	Manual Summary
8	☐	Buy-Out & Execution of Subcontracts Agreements	10 edays	Thu 4/28/22	Sun 5/8/22	Manual Summary
9	☐	Submittals (Prepare, Review & Approve)	15 edays	Fri 5/13/22	Sat 5/28/22	Manual Summary
10	☐	Long-Leads Items (Order, Fabrication & Delivery)	155 edays	Sat 5/28/22	Sun 10/30/22	Manual Summary
11	☐	Construction	90 days	Mon 9/19/22	Fri 1/20/23	Manual Summary
12	☐	Mobilization	10 days	Mon 9/19/22	Fri 9/30/22	Manual Summary
13	☐	Interior Work (First and Second Floor)	65 days	Mon 10/3/22	Fri 12/30/22	Manual Summary
14	☐	Demolition/ Removals (Includes Protection & Salvage)	7 days	Mon 10/3/22	Tue 10/11/22	Manual Summary
15	☐	VAV Boxes Replacement	35 days	Wed 10/12/22	Tue 11/29/22	Manual Summary
16	☐	Relocate Fire Sprinkler Heads	2 days	Wed 10/12/22	Thu 10/13/22	Manual Summary
17	☐	Relocate Electrical conduits	2 days	Wed 10/12/22	Thu 10/13/22	Manual Summary
18	☐	W8 Beam Joist Bottom Chord	3 days	Fri 10/14/22	Tue 10/18/22	Manual Summary
19	☐	Drywall Ceilings	35 days	Fri 11/4/22	Thu 12/22/22	Manual Summary
20	☐	ACT Ceilings	35 days	Fri 11/4/22	Thu 12/22/22	Manual Summary
21	☐	Painting	3 days	Fri 12/23/22	Tue 12/27/22	Manual Summary
22	☐	Punch-List	3 days	Wed 12/28/22	Fri 12/30/22	Manual Summary
23	☐	Roof framing & Chiller Replacement	20 days	Mon 10/31/22	Fri 11/25/22	Manual Summary
24	☐	Remove Chiller CH-1	1 day	Mon 10/31/22	Mon 10/31/22	Manual Summary
25	☐	Remove and install W8 chiller bench beams	1 day	Tue 11/1/22	Tue 11/1/22	Manual Summary
26	☐	Install new CH-1 with fittings and piping	1 day	Wed 11/2/22	Wed 11/2/22	Manual Summary
27	☐	Provide new 3P/200A/460V Disconnect and circuit breaker	1 day	Thu 11/3/22	Thu 11/3/22	Manual Summary
28	☐	Remove Chiller CH-2	1 day	Fri 11/4/22	Fri 11/4/22	Manual Summary
29	☐	Remove and install W8 chiller bench beams	1 day	Mon 11/7/22	Mon 11/7/22	Manual Summary
30	☐	Install new CH-2 with fittings and piping	1 day	Tue 11/8/22	Tue 11/8/22	Manual Summary
31	☐	Provide new 3P/200A/460V Disconnect and circuit breaker	1 day	Wed 11/9/22	Wed 11/9/22	Manual Summary
32	☐	Framing and metal grating installation	10 days	Wed 11/9/22	Tue 11/22/22	Manual Summary
33	☐	Hatch handrail replacement	1 day	Wed 11/9/22	Wed 11/9/22	Manual Summary
34	☐	Punch-List	3 days	Wed 11/23/22	Fri 11/25/22	Manual Summary
35	☐	Project Close-Out	15 days	Mon 1/2/23	Fri 1/20/23	Manual Summary
36	☐	Documents (As-Built's, Manuals, Releases)	15 days	Mon 1/2/23	Fri 1/20/23	Manual Summary
37	☐	Final Completion	0 days	Fri 1/20/23	Fri 1/20/23	Manual Summary

SECTION J

Site Visit Attendance

Bid Opening Log

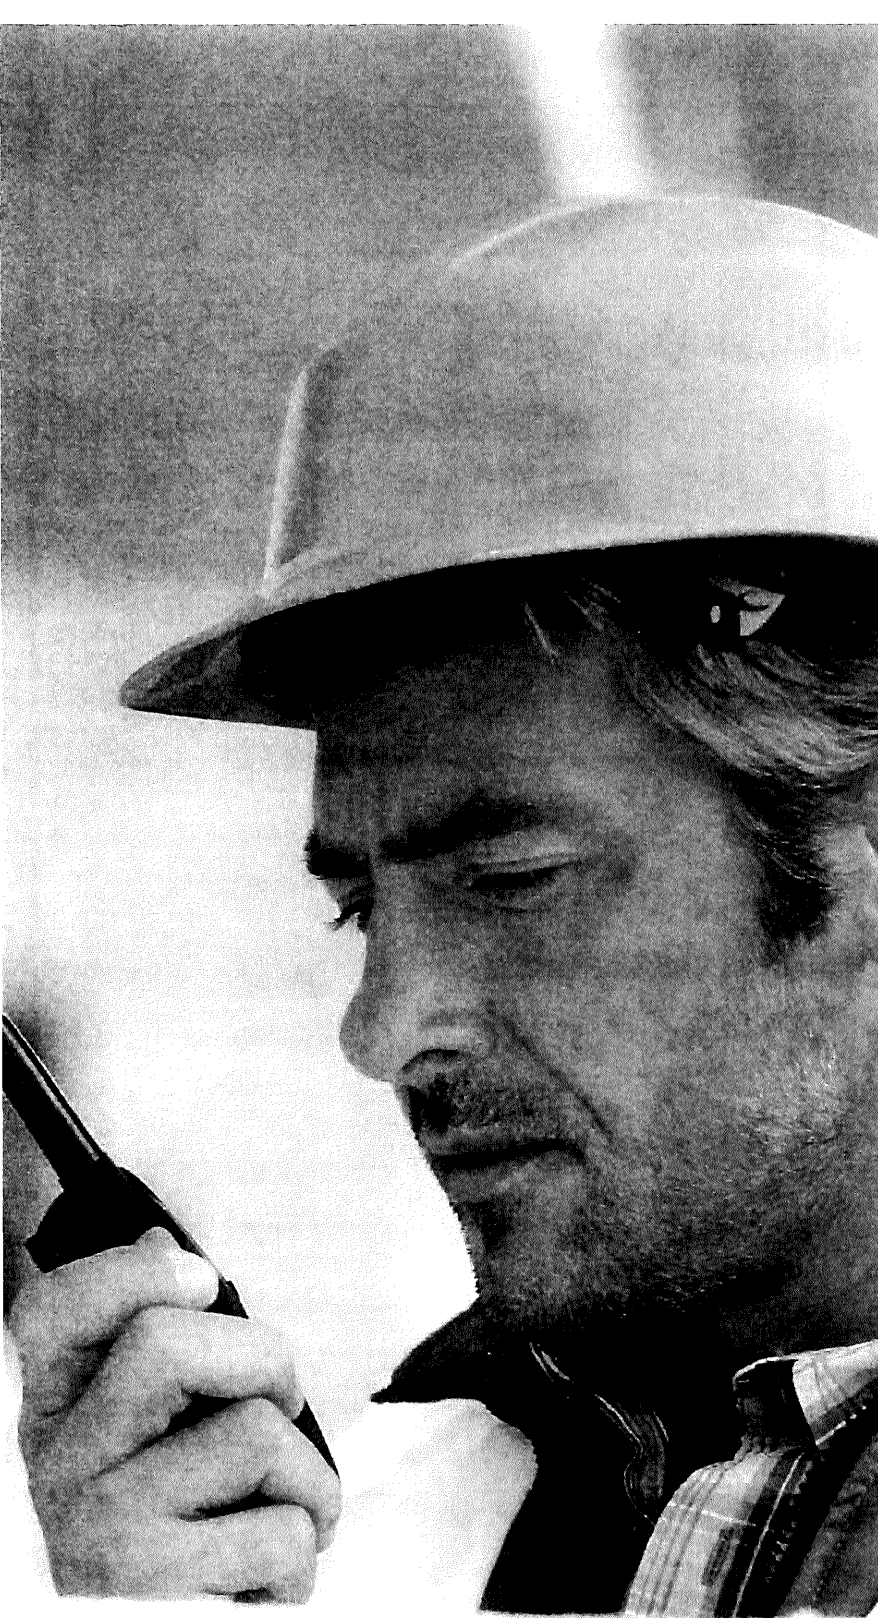



Subcontractors
PreBid Meeting & Site Visit Attendance

PROJECT NAME :	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	1.0
SITE VISIT DATE:	Wednesday, January 12, 2022

FORM LCM-PC-17 | 08/20/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS		
Name	Company	Signature
WARD HOPE	Big Air Mechanical	[Signature]
	Sunshine State	[Signature]
Timothy Sullivan	Palm Beach Iron	[Signature]
	Structural & Metal Services	
	Yats Construction	
	I.Q. Constructions	
Tom, Mike	N & P Construction and Development, Inc.	[Signature]
Motaberi Majidolahi	Cedars Electro-Mechanical	[Signature]
Edens Vilmar	Van Linda Iron Works	[Signature]
PATRICK GORDON	QUANTUM MECHANICAL	[Signature]
Daren Gordon	Quantum Mechanical	[Signature]
GEORGE SANTOS	PBCDOA	[Signature]
im CH	Florida Tech	[Signature]
SEBASTIAN FERRER	LEBOLO	[Signature]
Everton White	Everton Electric	[Signature]

GOOD
DRAWINGS



BID OPENING LOG

PROJECT NAME :	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
OPENING DATE:	Tuesday, February 8, 2022
OPENING TIME:	2:00 PM

FORM LCM-PC-21 | 10/19/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS

Company Name	Trade (s)	Bid Form (Yes/No)	Amount USD
CEDARS ELECTRO MECHANICAL HVAC	HVAC	YES	\$ 681,315 HVAC \$ 12,500 TEMP HVAC BOLD \$ 14,160. WORTH
VAN LINDA IRON WORKS, S STEEL	S STEEL	YES	\$ 176,191.16
CRADCOM MECHANICAL HVAC	HVAC	YES.	\$ 569,000.00.
FLORIDA MECHANICAL HVAC	HVAC	YES	\$ 702.485.00
T.W.S. FABRICATORS S. STEEL	S. STEEL	NO	\$ 174,000.00
FARMER S IRVING HVAC	HVAC	YES	\$ 566,673 (1 WORK) \$ 563,658 (1 MONTH) BOLD \$ 7277.00
N & P CONSTRUCTION SELECTIVE DEMO	SELECTIVE DEMO	YES	\$ 73,700.00.

<div>PALM BEACH COUNTY DEPARTMENT OF AIRPORTS</div> <div>By: </div> <div>Print Name: GEORGE SANTOS</div> <div>Title: PROJECT ENGINEER Date: 2/8/2022</div>	<div>LEBOLO CONSTRUCTION MANAGEMENT, INC.</div> <div>By: </div> <div>Print Name: SEBASTIAN FOULGER</div> <div>Title: Proj COO MANAGER Date: 2/8/22.</div>
--	---

SECTION K

Constructability Report

VA/VE Report



LEBOLO PROJECT No: 2021-0024
PBIA PROJECT No: DOA 18-2A SL-04
VERSION: 1.0
DATE: Wednesday, December 15, 2021

CONSTRUCTABILITY LOG

PRE-CONSTRUCTION

FORM LCMP-C-20 | 09/21/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS SL-04 FIS & BUILDING 040 STORM RESILIENCY MODIFICATIONS PACKAGE 2

REVIEWER NAME	REVIEWER FIRM	SPEC. SECTION & DWG #	TRADE	ACTIVITY	SITUATION	RECOMMENDATION	COST IMPACT	RESPONSE FROM	RESPONSE	ACTION	IMPACT DRAWINGS	IMPACT SPECS
Sebastian Fonnegra	LEBOLO	N/A	Mechanical	Replace chiller units CH-1 & CH-2	The area around Adm. Bldg. does not allow sufficient space to stage the crane without impacting vehicular traffic	Crane can be staged SW of Adm. Bldg. inside airport area. Special permission may be required	N/A	Aaron Jackson	Accepted	Included in 100% CDs	Yes	No
Sebastian Fonnegra	LEBOLO	N/A	Mechanical	Replace chiller units CH-1 & CH-2	Height of boom crane must be verified due to the possibility of airport restrictions	During the Precon phase request input from the supplier	N/A	Sunshine State and Farmer & Irwin	Use a 150Ton crane to be on the safe loading zone. Boom lift was verified	Crane can be used without interfering airport operations	No	No
Sebastian Fonnegra	LEBOLO	N/A	S. Steel Misc. Metals	Chiller bench W8 beams replacement and new metal grating installation	Material size must be verified to allow access through the existing roof hatch	Field coordination will be implemented to use same crane for chiller and metals	No Impact	Sunshine State and Farmer & Irwin	Field coordination to use same crane is possible	HVAC crane will bring materials to rooftop	No	No
Sebastian Fonnegra	LEBOLO	024119 - Selective Demolition A131, A132	Selective Demolition Acoustical Ceiling	Acoustical ceiling removal for VAV Replacement	On previous projects we had to partially remove AC grid with the inconvenience of having the existing remaining grid damaged on the edges causing additional cost to replace the entire areas to comply with QC	Remove complete AC grid in each room to avoid future cost implications or include an allowance for additional repairs if needed	TBD	Nicholas Hopkins	REMOVE AND REPLACE: Demolish entire existing ACT ceiling and grid in full room. Provide all new framing system and tiles. Rooms: 108 - Multi-Purpose Room, 113 - Employee Break Room, 116 - Emergency Supply Storage, 141 - Plans Review, 144 - I.T. Mgr., 147 - Laboratory, 148 - Server, 203 - Fiscal Spec II, 213 - Conference Rm., 217 - Conference Rm., 235 - Data, 240 - Plan Storage, & 241 - File Storage REMOVE AND REINSTALL: Demolish main and secondary framing to limits shown in plans. Provide new main and secondary framing tying into existing to remain. Re-install existing tiles to maintain color consistency in the corridor. Rooms: All Corridors, 219 - Central Storage	Included in Addendum 1	YES	NO
Sebastian Fonnegra	LEBOLO	055313 S-101	S. Steel	New W8 bellow joist bottom chord	There is an access restriction to get the proposed 22ft long W8 into the second floor of the building	Design W8 as two components to be mechanically attached for final installation	TBD	Aaron Jackson	Agreed. Note on 7/S101 indicates for the beam to be spliced mid-span between joists (approx 13'-3" / 8'-9" split). Note indicates splice shall be fully bolted and designed for full shear and moment capacity.	Included in 100% CDs		
Sebastian Fonnegra	LEBOLO	MD101, MD102, M101, M102	Selective Demolition Acoustical Ceiling Mechanical Electrical	VAV replacement	The work requires to install new VAV units in occupied space	Coordinate with PBIA Adm. to relocate personnel or plan for afterhours & weekends work to avoid conflicts	N/A	Aaron Jackson	No exception taken to recommendation. Note that demolition is required to be completed at nighttime per General Contract Note #22 on G002. New installation work shall be coordinated with airport staff.	Included in 100% CDs		



LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	1.0
DATE:	Wednesday, December 15, 2021

VA/VE LOG

PRE-CONSTRUCTION

FORM LCM-PG-19 | 09/21/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS										
SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2										
REVIEWER NAME	REVIEWER FIRM	SPEC. SECTION & DWG #	VA/VE COMMENT	DISCIPLINES IMPACTED	COST IMPACT	RESPONSE FROM	RESPONSE	ACTION	CHANGE IMPACT DRAWINGS	CHANGE IMPACT SPECS
Sebastian Fonnegra	LEBOLO	055313 S-101	Existing supports for antennas are located on the interior of the enclosure. If new metal grating has a detail to surround each support, this should be considered as an alternate to leave antenna's supports were they exist and reduce the cost associated with this relocation	Misc. Metals Communications	TBD	Aaron R Jackson	Agreed. See Note on photo near Section 3 of S101. Note states that horizontal leg of L3x3 of 3/S101 and grating shall be coped at existing antenna support posts and to provide 1" clearance. Note on 6/S101 indicates that Antenna's are to remain active while installation occurs but can be relocated at Contractor's option.	None needed. Info included on 100% CD's.	YES	NO
Sebastian Fonnegra	LEBOLO	M-601	VAV and Chiller Units are specified by Trane. Considering alternate manufacturers may result in savings	Mechanical	TBD	Kevin Gomez	Chillers and VAV boxes equal to those specified will be considered; however, any and all costs required due to alternates shall be included. This includes but not limited to controls integration to the existing system and any electrical modifications necessary. The controls shall remain on the native Trane controls network including compatible hardware and software & matching protocol.		YES	NO

Public Construction Bond



March 29, 2022

Palm Beach County Board of County Commissioners
c/o Dept. of Airports
846 Palm Beach International Airport
West Palm Beach, FL 33406-1470

**RE: *Authority to Insert Contract Date and Date Bond(s) and
Power(s) of Attorney
Principal: Lebolo Construction Management, Inc.
Bond No. 6021361629
Project: SL 04 FIS & Building 846 Storm Resiliency Modifications Package 2 - SL 04***

To Whom It May Concern:

Please be advised that this letter serves as our authorization for Palm Beach County Board of County Commissioners c/o Dept. of Airports to do the following:

- *Once the Contract is signed, insert the date of the contract to the bond(s);*
- *Date the bond(s) and Power(s) of Attorney the date of the contract; and*

Please provide us with a copy for our files.

If you have any questions, please do not hesitate to contact this office.

Sincerely yours,

NIELSON, HOOVER & ASSOCIATES


Charles J. Nielson
President of Nielson, Hoover & Associates and,
Attorney-In-Fact of United States Fire Insurance Company

Attachments

15050 NW 79th Court
Suite 200
Miami Lakes, FL 33016
P: 305.722.2663
F: 305.558.9650
W: nielsonbonds.com

PUBLIC CONSTRUCTION BOND

BOND NUMBER	<u>6021361629</u>
BOND AMOUNT	<u>One Million Five Hundred Eighteen Thousand Seven Hundred Ninety and 48/100 Dollars (\$1,518,790.48)</u>

CONTRACT AMOUNT One Million Five Hundred Eighteen Thousand Seven Hundred Ninety and 48/100 Dollars (\$1,518,790.48)

CONTRACTOR'S NAME: Lebolo Construction Management, Inc.

CONTRACTOR'S ADDRESS: 2100 Corporate Drive, Boynton Beach, FL, 33426

CONTRACTOR'S PHONE: (561) 742-7644

SURETY COMPANY: United States Fire Insurance Company

SURETY'S ADDRESS: 305 Madison Avenue, Morristown, NJ 07960

SURETY'S PHONE: (973) 490-6600

OWNER'S NAME: PALM BEACH COUNTY BOARD OF COUNTY COMMISSIONERS

OWNER'S ADDRESS: c/o Department of Airports
846 Palm Beach International Airport
West Palm Beach, Florida 33406-1470

OWNER'S PHONE: (561) 471-7462

PROJECT NAME: SL 04 FIS & Building 846 Storm Resiliency Modifications Package 2

PROJECT NUMBER: SL 04

CONTRACT NUMBER (to be provided after Contract award):

DESCRIPTION OF WORK: 2 Rooftop Chiller units replacement, new grating over chillers, replace chiller support beams, Interior (35) VAV replacements, Acoustical Ceiling replacement, Interior W8 Steel Beam installation.

PROJECT ADDRESS, PCN, or LEGAL DESCRIPTION: _____

846 Palm Beach International Airport, West Palm Beach, FL 33406

Legal Description: PCN 00-43-43-31-01-001-0010

This Bond is issued in favor of the County conditioned on the full and faithful performance of the Contract.

KNOW ALL MEN BY THESE PRESENTS: that Contractor and Surety, are held and firmly bound unto

Palm Beach County Board of County Commissioners
301 N. Olive Avenue
West Palm Beach, Florida 33401

as Oblige, herein called County, for the use and benefit of claimant as herein below defined, in the amount of

One Million Five Hundred Eighteen Thousand Seven Hundred Ninety and 48/100 Dollars (\$1,518,790.48)
(Here insert a sum equal to the Contract Price)

for the payment whereof Principal and Surety bind themselves, their heirs, personal representatives, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

WHEREAS,

Principal has by written agreement entered into a contract with the County for

Project Name: FIS & Building 846 Storm Resiliency Modifications Package 2
Project No.: SL 04
Project Description: 2 Rooftop Chiller units replacement, new grating over chillers, replace chiller support beams, Interior (35) VAV replacements, Acoustical Ceiling replacement, Interior W8 Steel Beam installation.
Project Location: 846 Palm Beach International Airport, West Palm Beach, FL 33406

in accordance with Drawings and Specifications prepared by

NAME OF ARCHITECTURAL FIRM: RS&H
LOCATION OF FIRM: 3125 West Commercial Blvd, Suite 130, Fort Lauderdale, FL, 33309.
PHONE: (954) 474-3005

NAME OF ARCHITECTURAL FIRM: JLRD Consulting Engineers
LOCATION OF FIRM: 1450 Centrepark Boulevard, Suite 350, West Palm Beach, FL, 33401
PHONE: (561) 689-2303

which contract is by reference made a part hereof in its entirety and is hereinafter referred to as the Contract.

THE CONDITION OF THIS BOND is that if Principal:

1. Performs the contract between Principal and County for the construction of SL 04 FIS & Building 846 Storm Resiliency Modifications Package 2, the contract being made a part of this bond by reference, at the times and in the manner prescribed in the contract; and
2. Promptly makes payments to all claimants, as defined in Section 255.05, Florida Statutes, supplying Principal with labor, materials, or supplies, used directly or indirectly by Principal in the prosecution of the work provided for in the contract; and
3. Pays County all losses, damages (including liquidated damages), expenses, costs, and attorneys' fees, including appellate proceedings, that County sustains because of a default by Principal under the contract; and
4. Performs the guarantee of all work and materials furnished under the contract for the time specified in the contract, then this bond is void; otherwise it remains in full force.
5. Any changes in or under the contract documents and compliance or noncompliance with any formalities connected with the contract or the changes does not affect Surety's obligation under this bond and Surety waives notice of such changes.
6. The amount of this bond shall be reduced by and to the extent of any payment or payments made in good faith hereunder, inclusive of the payment by Surety of construction liens which may be filed of record against said improvement, whether or not claim for the amount of such lien be presented under and against the bond.
7. Principal and Surety expressly acknowledge that any and all provisions relating to consequential, delay and liquidated damages contained in the contract are expressly covered by and made a part of this Performance, Labor and Material Payment Bond. Principal and Surety acknowledge that any such provisions lie within their obligations and within the policy coverages and limitations of this instrument.

Section 255.05, Florida Statutes, as amended, together with all notice and time provisions contained therein, is incorporated herein, by reference, in its entirety. Any action instituted by a claimant under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2), Florida Statutes. This instrument regardless of its form, shall be construed and deemed a statutory bond issued in accordance with Section 255.05, Florida Statutes.

Any action brought under this instrument shall be brought in the court of competent jurisdiction in Palm Beach County and not elsewhere.

Dated: _____

Witness

Lebolo Construction Management, Inc.

Principal (Seal)

Andrie Powell
Print Name

PRINCIPAL
Title

Witness

United States Fire Insurance Company
Surety (Seal)

Charles D. Nielson
Print Name

Charles D. Nielson
Title – Attorney-In-Fact

***Bond Must Contain Original Signatures.
No Copies Will Be Accepted***

IMPORTANT: Surety companies executing bonds must appear and remain on the U.S. Treasury Department’s most current list (Federal Register) during construction, guarantee and warranty periods, and be authorized to transact business in the State of Florida.

The provisions and limitations of Section 255.05 Florida Statutes, including but not limited to the notice and time limitations in Sections 255.05(2) and 255.05(10), are incorporated in this bond by reference.

POWER OF ATTORNEY
UNITED STATES FIRE INSURANCE COMPANY
PRINCIPAL OFFICE - MORRISTOWN, NEW JERSEY

0092722

KNOW ALL MEN BY THESE PRESENTS: That United States Fire Insurance Company, a corporation duly organized and existing under the laws of the state of Delaware, has made, constituted and appointed, and does hereby make, constitute and appoint:

*Ian A. Nipper, David Russell Hoover, Joseph Penichet Nielson,
Charles David Nielson, Charles Jackson Nielson, Shawn Alan Burton, Jarrett Merlucci*

each, its true and lawful Attorney(s)-In-Fact, with full power and authority hereby conferred in its name, place and stead, to execute, acknowledge and deliver: Any and all bonds and undertakings of surety and other documents that the ordinary course of surety business may require, and to bind United States Fire Insurance Company thereby as fully and to the same extent as if such bonds or undertakings had been duly executed and acknowledged by the regularly elected officers of United States Fire Insurance Company at its principal office, in amounts or penalties not exceeding: **Seven Million, Five Hundred Thousand Dollars (\$7,500,000).**

This Power of Attorney limits the act of those named therein to the bonds and undertakings specifically named therein, and they have no authority to bind United States Fire Insurance Company except in the manner and to the extent therein stated.

This Power of Attorney revokes all previous Powers of Attorney issued on behalf of the Attorneys-In-Fact named above and expires on January 31, 2023.

This Power of Attorney is granted pursuant to Article IV of the By-Laws of United States Fire Insurance Company as now in full force and effect, and consistent with Article III thereof, which Articles provide, in pertinent part:

Article IV, Execution of Instruments - Except as the Board of Directors may authorize by resolution, the Chairman of the Board, President, any Vice-President, any Assistant Vice President, the Secretary, or any Assistant Secretary shall have power on behalf of the Corporation:

(a) to execute, affix the corporate seal manually or by facsimile to, acknowledge, verify and deliver any contracts, obligations, instruments and documents whatsoever in connection with its business including, without limiting the foregoing, any bonds, guarantees, undertakings, recognizances, powers of attorney or revocations of any powers of attorney, stipulations, policies of insurance, deeds, leases, mortgages, releases, satisfactions and agency agreements;

(b) to appoint, in writing, one or more persons for any or all of the purposes mentioned in the preceding paragraph (a), including affixing the seal of the Corporation.

Article III, Officers, Section 3.11, Facsimile Signatures. The signature of any officer authorized by the Corporation to sign any bonds, guarantees, undertakings, recognizances, stipulations, powers of attorney or revocations of any powers of attorney and policies of insurance issued by the Corporation may be printed, facsimile, lithographed or otherwise produced. In addition, if and as authorized by the Board of Directors, dividend warrants or checks, or other numerous instruments similar to one another in form, may be signed by the facsimile signature or signatures, lithographed or otherwise produced, of such officer or officers of the Corporation as from time to time may be authorized to sign such instruments on behalf of the Corporation. The Corporation may continue to use for the purposes herein stated the facsimile signature of any person or persons who shall have been such officer or officers of the Corporation, notwithstanding the fact that he may have ceased to be such at the time when such instruments shall be issued.

IN WITNESS WHEREOF, United States Fire Insurance Company has caused these presents to be signed and attested by its appropriate officer and its corporate seal hereunto affixed this 28th day of September, 2021


UNITED STATES FIRE INSURANCE COMPANY



Matthew E. Lubin, President

State of New Jersey }
County of Morris }

On this 28th day of September, 2021, before me, a Notary public of the State of New Jersey, came the above named officer of United States Fire Insurance Company, to me personally known to be the individual and officer described herein, and acknowledged that he executed the foregoing instrument and affixed the seal of United States Fire Insurance Company thereto by the authority of his office.



Melissa H. D'Alessio

(Notary Public)

I, the undersigned officer of United States Fire Insurance Company, a Delaware corporation, do hereby certify that the original Power of Attorney of which the foregoing is a full, true and correct copy is still in force and effect and has not been revoked.

IN WITNESS WHEREOF, I have hereunto set my hand and affixed the corporate seal of United States Fire Insurance Company on the _____ day
of _____ 20____

UNITED STATES FIRE INSURANCE COMPANY



Alfred N. Wright, Senior Vice President

Contract History

DEPARTMENT OF AIRPORTS
MISCELLANEOUS AIRPORT IMPROVEMENTS - CMAR (LOCAL OEBO PROGRAM)
LEBOLO CONSTRUCTION MANAGEMENT INC.
PB NO: DOA 18-13
CONTRACT HISTORY

ORIGINAL CONTRACT RESOLUTION NO DATE APPROVED SBE Goal EXPIRATION		YEAR 1-2 R-2019-1222 8/20/2019 15.00% 8/20/2021		1 st EXT YR 3 R2021-0888 7/13/21		2 nd EXT YR 4 8/20/2022		3 rd EXT YR 5 8/20/2023		8/20/2024							
API-GSC	REF DOC	SBE/WMBE PARTICIPATION		DESCRIPTION	TIME(Cal Days) for Substantial	NTP	Substantial Completion Date	Final Completion Date	AMOUNT	CHANGE ORDER OR ADJUSTMENT	CHANGE ORDER VALUE PLUS TIME	REVISED AMOUNT	LEAD DEPT APPROVAL	CRC APPROVAL	BCC APPROVAL	STATUS	TOWO CLOSED
		Total SBE/WBE (%)	% SBE														
N/A Under \$100k	Task Order SL -01		0%	Precon for New Noise Monitoring Station at PBI	30	11/28/19			\$1,500.00			\$1,500.00	\$ 1,500.00			Approved 11/26/19	
N/A Under \$100k	Work Order SL -02		0%	Noise Monitor - GMP	60	3/10/20	5/8/20	6/7/20	\$18,160.00				\$ 18,160.00				
				GMP Adjustments						(\$1,881.90)		\$16,278.04					Approved Close-out by DOA on 5/19/2020
Waiver - 0%	Work Order SL -03		Waiver	Storm Resiliency-Package 1	90	6/10/20	9/7/20	10/7/20	\$168,328.00							Approved by CRC on 6/10/2020	
				CO No 1	46		10/23/20	11/23/20		\$0.00				0.00		Approved 9/9/2020	
				GMP Adjustments						(\$8,377.92)		\$159,947.08					Approved by CRC 2/24/2021
	Amendment 1 Time Extension														7/13/21 Board Meeting	Approved R2021-0888	
N/A Under \$100k	Task Order SL -06		16%	Preconstruction Services for Terminal Building 4th Level Exterior Wall Repairs					\$14,644.92			\$14,644.92	\$14,644.92			Approved 9/21/21	
20% SBE Goal	Amendment 2: SL 07	\$248,297.60	32%	Construction Services for Terminal Building 4th Level Exterior Wall Repairs	211	2/14/22	9/12/22	10/12/22	\$777,546.69						\$777,546.69	Approved R-2022-0135	
				CO No 1	0					\$33,698.89			\$33,698.89				
				GMP Adjustments								\$811,245.58					
20% w 5% AAHA	Amendmet 3: SL 04	\$921,435.00	60%	PreCon & Construction Services for Storm Resiliency Package 2	260				\$1,518,790.48						\$1,518,790.48	Going to May 3rd Board Meeting	
Total									\$2,498,987.09	\$23,439.01		\$1,003,615.62	\$68,003.81	\$0.00	\$2,296,337.17		

Notes:

Items in Blue are draft

Approval Authority for Task Authorizations (CM @ Risk) - No cumulative tracking

Document

Task Order

Task Order

Amendment

Authority

Lead Dept

CRC

BCC

less than \$100,000

\$100,000 <\$200,000

≥ \$200,000

Approval Authority

CO Value

\$0-\$0,000

\$50,001-\$100,000

>\$100,001

Cumulative CO Value

See Note 1

See Note 1

See Note 1

Authority

Lead Dept

CRC

BCC

Days

0-30 Days

31-90

120

Authority

Lead Dept

CRC

BCC

Cumulative Days up to 30

Individual Days up to 90

See Note 2

Time Extensions in excess of 90 Days must be approved by the Board and does not count towards the

- 1 When the cumulative value of changes or additional work approved by the Lead or CRC exceeds the greater of \$250,000 or 5% of the original contract an agenda item notifying the board that the item puts it in the excess category must be prepared and forwarded as a Receive and File item
- 2 When the cumulative time extensions approved by a combination of the Lead Dept and the CRC exceeds 120 Cal Days then an agenda item notifying the board that the item puts it in the excess category must be prepared and forwarded as a Receive and File item

*Time must also be evaluated based on value of LD's for projects over \$1,000,000. The value of the time extension is not included when calc the cumulative value

Attachment No. 2

OEBO Schedules

OEBO SCHEDULE 1

LIST OF PROPOSED CONTRACTOR/CONSULTANT AND SUBCONTRACTOR/SUBCONSULTANT PARTICIPATION
FIS & Building 846 Storm Resiliency Modifications Package 2


SOLICITATION/PROJECT/BID NAME: _____
NAME OF PRIME RESPONDENT/BIDDER: Lebolo Construction Management, Inc
CONTACT PERSON: Sebastian Fonnegra
SOLICITATION OPENING/SUBMITTAL DATE: N/A

SOLICITATION/PROJECT/BID No.: DOA 18-13 (SL-04)
ADDRESS: 2100 Corporate Drive, Boynton Beach, FL 33426
PHONE NO.: (561) 742 7644 E-MAIL: sfonnegra@lebolo.com
DEPARTMENT: PreConstruction

PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME CONTRACTOR/CONSULTANT ON THIS PROJECT.
PLEASE ALSO LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SUBCONTRACTORS/SUBCONSULTANTS ON THE PROJECT.

Name, Address and Phone Number	(Check all Applicable Categories)			DOLLAR AMOUNT OR PERCENTAGE OF WORK				
	Non-SBE	M/WBE	SBE	Black	Hispanic	Women	Caucasian	Other (Please Specify)
		Minority/Women Business	Small Business					
1. <u>All American Ceilings</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____	_____	_____	<u>\$31,988.04</u>	_____
2. <u>Van Linda Iron</u>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	_____	_____	_____	<u>\$210,788.54</u>	_____
3. <u>I.Q. Constructions</u>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	_____	_____	<u>\$39,750.00</u>	_____	_____
4. <u>Johnson's Controls</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____	_____	_____	<u>\$3,685.83</u>	_____
5. <u>Quantum Mechanical</u>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<u>\$637,296.40</u>	_____	_____	_____	_____
(Please use additional sheets if necessary)				Total	<u>see P.2</u>	<u>see P.2</u>	<u>see P.2</u>	_____
Total Bid Price \$ <u>\$1,518,790.48</u>				Total SBE - M/WBE Participation <u>see P.2</u>				

I hereby certify that the above information is accurate to the best of my knowledge:


Signature

PreConstruction Manager
Title

- Note:
- The amount listed on this form for a Subcontractor/subconsultant must be supported by price or percentage listed on the properly executed Schedule 2 or attached signed proposal.
 - Firms may be certified by Palm Beach County as an SBE and/or an M/WBE. If firms are certified as both an SBE and/or M/WBE, please indicate the dollar amount under the appropriate category.
 - Modification of this form is not permitted and will be rejected upon submittal.

OEBO SCHEDULE 1

LIST OF PROPOSED CONTRACTOR/CONSULTANT AND SUBCONTRACTOR/SUBCONSULTANT PARTICIPATION
FIS & Building 846 Storm Resiliency Modifications Package 2

SOLICITATION/PROJECT/BID NAME: _____
NAME OF PRIME RESPONDENT/BIDDER: Lebolo Construction Management, Inc
CONTACT PERSON: Sebastian Fonnegra
SOLICITATION OPENING/SUBMITTAL DATE: N/A

SOLICITATION/PROJECT/BID No.: DOA 18-13 (SL-04)
ADDRESS: 2100 Corporate Drive, Boynton Beach, FL 33426
PHONE NO.: (561) 742 7644 E-MAIL: sfonnegra@lebolo.com
DEPARTMENT: PreConstruction

PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME CONTRACTOR/CONSULTANT ON THIS PROJECT.
PLEASE ALSO LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SUBCONTRACTORS/SUBCONSULTANTS ON THE PROJECT.

Name, Address and Phone Number	(Check all Applicable Categories)			DOLLAR AMOUNT OR PERCENTAGE OF WORK				
	Non-SBE	M/WBE	SBE	Black	Hispanic	Women	Caucasian	Other (Please Specify)
		Minority/Women Business	Small Business					
1. <u>Protect Video</u>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<u> </u>	<u>\$33,600.00</u>	<u> </u>	<u> </u>	<u> </u>
2. <u>Bonded Lightning</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u> </u>	<u> </u>	<u> </u>	<u>\$5,100.00</u>	<u> </u>
3. <u> </u>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u> </u>	<u> </u>	<u> </u>	<u> </u>	<u> </u>
4. <u> </u>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u> </u>	<u> </u>	<u> </u>	<u> </u>	<u> </u>
5. <u> </u>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u> </u>	<u> </u>	<u> </u>	<u> </u>	<u> </u>
(Please use additional sheets if necessary)				Total	<u>\$637,296.00</u>	<u>\$33,600.00</u>	<u>\$39,750.00</u>	<u>\$251,562.00</u>
Total Bid Price \$ <u>\$1,518,790.48</u>				Total SBE - M/WBE Participation <u>\$921,435</u>				

I hereby certify that the above information is accurate to the best of my knowledge: _____
Signature _____ Title PreConstruction Manager

Note: 1. The amount listed on this form for a Subcontractor/subconsultant must be supported by price or percentage listed on the properly executed Schedule 2 or attached signed proposal.
2. Firms may be certified by Palm Beach County as an SBE and/or an M/WBE. If firms are certified as both an SBE and/or M/WBE, please indicate the dollar amount under the appropriate category.
3. Modification of this form is not permitted and will be rejected upon submittal.

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)
SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☐SBE ☐ WBE ☐MBE ☐M/WBE ☒Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1 Column 2
☒Male ☐Female ☐African-American/Black ☐Asian American ☒Caucasian American
☐Hispanic American ☐Native American


S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.


Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Remove and Replace Acoustical Ceilings	\$31,988.04	1	\$ 0.00	\$31,988.04

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$31,988.04

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant Price or Percentage:

Lebolo Construction Management, Inc
Print name of Prime
By: 
Authorized Signature
Sebastian Fonnegra
Print name
PreConstruction Manager
Title
Date: March 21, 2022

All American Ceilings
Print name of Subcontractor/subconsultant
By: 
Authorized Signature
Robert Rawiszer
Print name
President
Title
Date: March 21, 2022

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☒SBE ☐ WBE ☐ MBE ☐ M/WBE ☐ Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☒Male ☐Female ☐African-American/Black ☐Asian American ☒Caucasian American ☐Hispanic American ☐Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Structural Steel & Misc. Metals Package	\$210,788.50	1	\$ 0.00	\$210,788.50


The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$210,788.50

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc
Print name of Prime

By: 
Authorized Signature

Sebastian Fonnegra
Print name

PreConstruction Manager
Title

Date: 03/21/2022

Van Linda Iron Works, Inc.
Print name of Subcontractor/subconsultant

By: 
Authorized Signature

Steven McBriarty
Print name

Director of Estimating and Project Management
Title

Date: 03/21/2022

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☒SBE ☐WBE ☐MBE ☒M/WBE ☐Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☐Male ☒Female ☐African-American/Black ☐Asian American ☐Caucasian American ☒Hispanic American ☐Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Drywall Ceilings & Painting Package	\$39,750.00	1	\$ 0.00	\$39,750.00

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$39,750.00

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc

Print name of Prime

By: Authorized Signature

Sebastian Fonnegra

Print name

PreConstruction Manager

Title

Date: 3/21/22

I.Q. Constructions

Print name of Subcontractor/subconsultant

By: Authorized Signature

Print name

Owner - Qualifier

Title

Date: 3.21.22

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

SBE WBE MBE M/WBE Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

Male Female African-American/Black Asian American Caucasian American Hispanic American Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Fire Protection Package	\$3,685.83	1	\$ 0.00	\$3,685.83

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$3,685.83

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc
Print name of Prime

By: Sebastian Fonnegra
Authorized Signature

Sebastian Fonnegra
Print name

PreConstruction Manager
Title

Date: 03/21/22

Johnson's Controls
Print name of Subcontractor/subconsultant

By: Brian J. Grabenhorst
Digitally signed by Brian J. Grabenhorst
Date: 2022.03.22 14:44:51 -04'00'
Authorized Signature

Brian Grabenhorst
Print name

Sprinkler Install Manager
Title

Date: March 22nd, 2022

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)
SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☒SBE ☐ WBE ☒MBE ☐M/WBE ☐Non-S/M/WBE Date of Palm Beach County Certification (if applicable): 09/30/2020

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☒Male ☐Female ☒African-American/Black ☐Asian American ☐Caucasian American
☐Hispanic American ☐Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	HVAC Package	\$577,320.00	1	\$ 0.00	\$577,320.00
2.0	HVAC Duct Cleaning	\$59,976.00	1	\$0.00	\$59,976.00

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$637,296.00

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc

Print name of Prime

By:

Authorized Signature

Sebastian Fonnegra

Print name

PreConstruction Manager

Title

Date: 03/21/22

Quantum Mechanical

Print name of Subcontractor/subconsultant

By:

Authorized Signature

Patrick N. Gordon

Print name

President

Title

Date: 03/22/22

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☒SBE ☐ WBE ☐ MBE ☒M/WBE ☐Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☐Male ☒Female ☐African-American/Black ☐Asian American ☐Caucasian American ☒Hispanic American ☐Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Electrical Package	\$33,600.00	1	\$ 0.00	\$33,600.00

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$33,600.00

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc

Print name of Prime

By:

Authorized Signature

Sebastian Fonnegra

Print name

PreConstruction Manager

Title

Date: 03/21/22

Protect Video

Print name of Subcontractor/subconsultant

By:

Authorized Signature

Shad DiMaria

Print name

President

Title

Date: 03/21/22

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☐SBE ☐ WBE ☐MBE ☐M/WBE ☒Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☒Male ☐Female ☐African-American/Black ☐Asian American ☒Caucasian American ☐Hispanic American ☐Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Lightning Package	\$5,100.00	1	\$ 0.00	\$5,100.00

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$5,100.00

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2nd/3rd tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc

Print name of Prime

By: Authorized Signature

Sebastian Fonnegra

Print name

PreConstruction Manager

Title

Date: 03/21/22

Bonded Lightning

Print name of Subcontractor/subconsultant

By: Authorized Signature

Patrick Dillon

Print name

President

Title

Date: 03/21/22


BUDGET TRANSFER
BOARD OF COUNTY COMMISSIONERS
PALM BEACH COUNTY, FLORIDA

Fund 4111 Airport Passenger Improvement and Development Fund

Advantage Document Numbers:
BGEX 032822/1111

Use this form to provide budget for items not anticipated in the budget.

ACCT.NUMBER	ACCOUNT NAME	ADOPTED BUDGET	CURRENT BUDGET	INCREASE	DECREASE	ADJUSTED BUDGET	EXPENDED/ ENCUMBERED AS OF 03/28/2022	REMAINING BALANCE
<u>Expenditures</u>								
121-A413-6505	lotb Non Infrastructure	1,000,000	1,000,000	518,791		1,518,791	0	1,518,791
121-A900-9909	Reserves Improvement Program	19,773,212	9,174,926		518,791	8,656,135	0	8,656,135
Total Appropriations & Expenditures				518,791	518,791	0		

OFMB	Signatures	Date	By Board of County Commissioners
INITIATING DEPARTMENT/DIVISION		3/31/20	At Meeting of
Administration/Budget Department Approval			May 3, 2022
OFMB Department - Posted			Deputy Clerk to the Board of County Commissioners
