

Date \_\_\_\_\_

## **II. FISCAL IMPACT ANALYSIS**

**A. Five Year Summary of Fiscal Impact:**

Fiscal Years	2019	2020	2021	2022	2023
Capital Expenditures	<u>\$1,264,999</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
Operating Costs	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
External Revenues	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
Program Income (County)	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
In-Kind Match County	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
NET FISCAL IMPACT	<u>\$1,264,999</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
# ADDITIONAL FTE					
POSITIONS (Cumulative)	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
Budget Account No.:	Fund 4011	Dept 721	Unit W031	Object	6543

Is Item Included in Current Budget? Yes   X   No       

Does this item include the use of federal funds?      Yes      No      X

Reporting Category **N/A**

**B. Recommended Sources of Funds/Summary of Fiscal Impact:**

One (1) time expenditure from user fees, connection fees and balance brought forward.

C. Department Fiscal Review: \_\_\_\_\_

### III. REVIEW COMMENTS

**A. OFMB Fiscal and/or Contract Development and Control Comments:**

Robert Lawrence 9/7/18  
OFMB 5/9/17

*A. J. Jacoby*  
Contract Development and Control  
9/13/18 *TJ*

### B. Legal Sufficiency:

9/18/18  
Assistant County Attorney

**C. Other Department Review:**

Department Director

This summary is not to be used as a basis for payment.

WORK AUTHORIZATION NO. 11

**Palm Beach County Water Utilities Department**  
Pipeline Continuing Construction Contract 2017 – WUD 16-077  
Resolution # R2017-0072 Contract Dated Jan. 10, 2017

**Project Title:** CD01- Water Main Improvements Zones 2,3 & 4

**WUD Project No.** WUD 15-013

**Contractor:** Hinterland Group, Inc.

**Address:** 2051 W Blue Heron, Blvd, Riviera Beach, FL 33404

**Budget Line Item No.** 4011 - 721 - W031 - 6543

**District:** 4,5,6

This Work Authorization provides for: The construction scope of services as described  
herein; which includes approximately 5,500 LF of new C-900 and DIP water main in varying  
sizes from 4" to 12" with valves, associated appurtenances and site restoration.

See **ATTACHMENT A** for detailed scope of services.

The Contract provides for 15 % SBE participation. This Work Authorization includes 100 % participation. The cumulative proposed SBE participation, including this authorization is 100 %.

1. Services completed by the Contractor to date:

See **ATTACHMENT B**.

2. Contractor shall begin work within ten (10) calendar days from the issuance of Notice to Proceed (NTP). Execution of the Project will be accomplished as follows from the issuance of the NTP:

Substantial Completion	<u>240</u>	Calendar Days
Final Construction Completion	<u>270</u>	Calendar Days

Liquidated damages will apply as follows:

\$ 500.00 per day past substantial completion date.

\$ 250.00 per day past final completion date.

Revised 4-12-18

3. The compensation to be paid to the Contractor for providing the requested services in accordance with the Contract Bid Prices is \$1,264,998.80.
4. This Work Authorization does not amend, change, or modify the Contract which remains in full force and effect.
5. All Attachments to this Authorization are incorporated herein and made a part of this Work Authorization.

**Revised 4-12-18**

**Palm Beach County Water Utilities Department**  
Pipeline Continuing Construction Contract 2017 – WUD 16-077  
Resolution # R2017-0072 Contract Dated Jan. 10, 2017

**Project Title:** CD01 Water Main Improvements Zones 2,3 & 4

**WUD Project No.:** WUD 15-013

IN WITNESS WHEREOF, this Work Authorization is accepted, subject to the terms, conditions and obligations of the aforementioned Contract.

PALM BEACH COUNTY, A POLITICAL SUBDIVISION OF THE STATE OF FLORIDA

Sharon R. Bock, Clerk & Comptroller,  
Palm Beach County

Palm Beach County,  
Board of County Commissioners

ATTEST:

Signed: \_\_\_\_\_

Signed: \_\_\_\_\_  
Melissa McKinlay, Mayor

Typed Name: \_\_\_\_\_  
**Deputy Clerk**

\_\_\_\_\_  
Date

Approved as to Form and Legal  
Sufficiency

**CONTRACTOR:** Hinterland Group, Inc.


Signed: \_\_\_\_\_

\_\_\_\_\_  
(Signature)

Typed Name: \_\_\_\_\_  
**County Attorney**


Daniel Duke III, President  
(Name and Title)

7/12/2018  
Date



STATE OF FLORIDA  
COUNTY OF Palm Beach

The foregoing instrument was acknowledged before me this 12th day of July, 2018,  
by Daniel Duke III as President  
for Hinterland Group, Inc.



\_\_\_\_\_  
(Signature of Notary Public - State of Florida)  
Chase Rogers  
(Print, Type, or Stamp Commissioned Name of Notary Public)

Personally Known X OR Produced Identification \_\_\_\_\_ Type of Identification Produced \_\_\_\_\_

## LIST OF ATTACHMENTS

WORK AUTHORIZATION NO. 11

**Palm Beach County Water Utilities Department**  
Pipeline Continuing Construction Contract 2017 – WUD 16-077  
Resolution # R2017-0072      Contract Dated Jan. 10, 2017

ATTACHMENT	A	Scope of Work
ATTACHMENT	B	Summary and Status of Work Authorizations
ATTACHMENT	C	Public Construction Bond
ATTACHMENT	D	Form of Guarantee
ATTACHMENT	E	Work Authorization Schedule of Bid Items
ATTACHMENT	F	SBE Schedule 1 and Schedule 2
ATTACHMENT	G	Summary of SBE/Minority Business Tracking
ATTACHMENT	H	Location Map

Revised 4-12-18

**ATTACHMENT A**

**SCOPE OF WORK AUTHORIZATION # 11**

**PROJECT NO.** WUD 15-013

**PROJECT TITLE:** CD01 Water Main Improvements Zones 2, 3 & 4

Contractor shall perform:  
Furnish and install all materials necessary to complete the Water Main Improvements on  
CD01 Water Main Improvements Zones 2, 3 & 4 (Project), including but not limited to:  
furnish material, labor supervision, equipment, supplies, fees, expertise and services  
necessary to fully complete work in accordances with construction documents and governing  
regulations. This work includes approximately 5,500 LF of new C-900 and DIP water main in  
varying sizes from 4" to 12" with valves, associated appurtenances and site restoration.

**ATTACHMENT B**

## SUMMARY AND STATUS OF WORK AUTHORIZATIONS

[illegible]



**ATTACHMENT C**

**PUBLIC CONSTRUCTION BOND – WORK AUTHORIZATION NO. 11 TO  
CONTINUING CONSTRUCTION CONTRACT  
RESOLUTION NO. R2017-0072    Contract Dated Jan10,2017**

PROJECT TITLE: CD01 Water Main Improvements Zones 2, 3 & 4

WUD PROJECT NO.: WUD 15-013

BOND NUMBER: 0219056

WORK AUTHORIZATION/BOND AMOUNT: \$1,264,998.80

CONTRACTOR'S NAME: Hinterland Group, Inc.

CONTRACTOR'S ADDRESS: 2051 W. Blue Heron Blvd. Riviera Beach, FL 33404

CONTRACTOR'S PHONE: (561)640-3503

SURETY COMPANY: Berkley Insurance Company

SURETY'S ADDRESS: 475 Steamboat Road

Greenwich, CT 06830

OWNER'S NAME: PALM BEACH COUNTY

OWNER'S ADDRESS: 8100 Forest Hill Boulevard  
West Palm Beach, FL 33413

OWNER'S PHONE: (561) 493-6000

DESCRIPTION OF WORK: The construction scope of services as described herein; which includes approximately 5,500LF of new C-900 and DIP water main in varying sizes from 4" to 12" with valves, associated appurtenances and site restoration.

PROJECT LOCATION: District 4,5,6

LEGAL DESCRIPTION: \*Site 9- Section 30, Township 44, Range 42  
Section 31, Township 44, Range 42  
\*Site 10- Section 31, Township 46 S, Range 43 E  
\*Site 11- Section 3, Township 47, Range 42  
Section 5, Township 47, Range 42  
\*Site 12- Section 5, Township 47, Range 42

**Revised 4-12-18**

**PUBLIC CONSTRUCTION BOND**

This Bond is issued in favor of the County conditioned on the full and faithful performance of the Work Authorization No. 11 to Continuing Construction Contract Resolution No. R-2017-0072 dated on January 10, 2017.

KNOW ALL MEN BY THESE PRESENTS: that Contractor and Surety, are held and firmly bound unto

Palm Beach County Board of County Commissioners  
301 N. Olive Avenue  
West Palm Beach, Florida 33401

as Obligee, herein called County, for the use and benefit of claimant as herein below defined, in the amount of One Million Two Hundred Sixty-Four Thousand, Nine Hundred Ninety-Eight Dollars and Eighty Cents. \$1,264,998.80

for the payment whereof Principal and Surety bind themselves, their heirs, personal representatives, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

WHEREAS,

Principal has by written agreement dated \_\_\_\_\_, 20\_\_\_\_, entered into Work Authorization No. 11 to Continuing Construction Contract Resolution No. R-2017-0072 with the County for

Work Authorization Project Name: CD01 Water Main Improvments Zones 2,3 & 4  
Work Authorization Project No.: WUD 15-013  
Project Description: The construction scope of services as described herin; which includes approximately 5,500 LF of new C-900 and DIP water main varying sizes from 4" to 12" with valves, associated appurtenances and site restoration.  
Project Location: District 4, 5, 6

in accordance with Design Criteria Drawings and Specifications prepared by

Name of Design Firm: CES Conslutants, Inc  
Location of Firm: 3300 PGA Blvd, Suite 780, Palm Beach Gardens, FL 33410  
Phone: 561-227-6862  
Fax: N/A

which Work Authorization No. 11 to Continuing Construction Contract Resolution No. R-2017-0072 is by reference made a part hereof in its entirety, and is hereinafter referred to as the Work Authorization.

1. THE CONDITION OF THIS BOND is that if Principal:
- a. Performs the Work Authorization dated \_\_\_\_\_, 20\_\_\_\_, between Principal and County for the construction of the above project, the Work Authorization being made a part of this bond by reference, at the times and in the manner prescribed in the Work Authorization; and
  - b. Promptly makes payments to all claimants, as defined in Section 255.05, Florida Statutes, supplying Principal with labor, materials, or supplies, used directly or indirectly by Principal in the prosecution of the work provided for in the Work Authorization; and

c. Pays County all losses, damages (including liquidated damages), expenses, costs, and attorneys' fees, including appellate proceedings, that County sustains because of a default by Principal under the Work Authorization; and

d. Performs the guarantee of all work and materials furnished under the Work Authorization for the time specified in the Work Authorization; then this bond is void; otherwise it remains in full force.

2. Any changes in or under the contract documents and compliance or noncompliance with any formalities connected with the Work Authorization or the changes does not affect Surety's obligation under this bond and Surety waives notice of such changes.

3. The amount of this bond shall be reduced by and to the extent of any payment or payments made in good faith hereunder, inclusive of the payment by Surety of construction liens which may be filed of record against said improvement, whether or not claim for the amount of such lien be presented under and against the bond.

4. Principal and Surety expressly acknowledge that any and all provisions relating to consequential, delay and liquidated damages contained in the Work Authorization are expressly covered by and made a part of this Performance, Labor and Material Payment Bond. Principal and Surety acknowledge that any such provisions lie within their obligations and within the policy coverage's and limitations of this instrument.


5. Section 255.05, Florida Statutes, as amended, together with all notice and time provisions contained therein, is incorporated herein, by reference, in its entirety. Any action instituted by a claimant under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2), Florida Statutes. This instrument regardless of its form, shall be construed and deemed a statutory bond issued in accordance with Section 255.05, Florida Statutes.

6. Any action brought under this instrument shall be brought in the state court of competent jurisdiction in Palm Beach County, Florida and not elsewhere.

\_\_\_\_\_  
Witness  
Chase Rogers  
\_\_\_\_\_  
Print name

\_\_\_\_\_  
Witness  
Candy Wagner  
\_\_\_\_\_  
Print name

\_\_\_\_\_  
Principal  
Daniel Duke III  
\_\_\_\_\_  
Print name  
President  
\_\_\_\_\_  
Title  
\_\_\_\_\_  
Surety  
Taylor D. Wagner  
\_\_\_\_\_  
Print name  
\_\_\_\_\_  
Attorney-in-Fact  
\_\_\_\_\_  
Title



**ATTACHMENT D**  
**FORM OF GUARANTEE**

GUARANTEE FOR (Contractor and Surety Name) Hinterland Group, Inc. and Berkley Insurance Company

We the undersigned hereby guarantee that the **Pipeline Continuing Construction Contract 2017, Resolution No. R2017-0072, Contract Dated Jan 10, 2017, WUD Project No. WUD 15-013, Work Authorization No. 11, Project Title: CD01 Water main Improvements Zones 2,3 & 4**, Palm Beach County, Florida, which we have constructed and bonded, has been done in accordance with the plans and specifications; that the work constructed will fulfill the requirements of the guaranties included in the Contract Documents. We agree to repair or replace any or all of our work, together with any work of others which may be damaged in so doing, that may prove to be defective in the workmanship or materials within a period of one year from the date of Final Completion of all of the above named work by the County of Palm Beach, State of Florida, without any expense whatsoever to said County of Palm Beach, ordinary wear and tear and unusual abuse or neglect excepted by the County. When correction work is started, it shall be carried through to completion.

In the event of our failure to acknowledge notice, and commence corrections of defective work within five (5) calendar days after being notified in writing by the Board of County Commissioners, Palm Beach County, Florida, we, collectively or separately, do hereby authorize Palm Beach County to proceed to have said defects repaired and made good at our expense and we will honor and pay the costs and charges therefore upon demand.

County and (contractor, engineer, architect as applicable) agree that the provisions of Florida Statute Chapter 558 shall not apply to this (contract, agreement as applicable).

DATED \_\_\_\_\_  
(notice of completion filing date)

**SEAL AND NOTARIAL ACKNOWLEDGMENT OF SURETY**

Hinterland Group, Inc (Seal)  
(Contractor)

By: \_\_\_\_\_  
(Signature)

Daniel Duke III

\_\_\_\_\_  
(Printed Name)

Berkley Insurance Company (Seal)  
(Surety)

By: \_\_\_\_\_  
(Signature)

Taylor D. Wagner

\_\_\_\_\_  
(Printed Name)

**Revised 4-12-18**

POWER OF ATTORNEY  
BERKLEY INSURANCE COMPANY  
WILMINGTON, DELAWARE

NOTICE: The warning found elsewhere in this Power of Attorney affects the validity thereof. Please review carefully.

KNOW ALL MEN BY THESE PRESENTS, that BERKLEY INSURANCE COMPANY (the "Company"), a corporation duly organized and existing under the laws of the State of Delaware, having its principal office in Greenwich, CT, has made, constituted and appointed, and does by these presents make, constitute and appoint: *Daniel F. Wagner or Taylor D. Wagner of Wagner Bonding & Insurance, Inc. of Lakeland, FL* its true and lawful Attorney-in-Fact, to sign its name as surety only as delineated below and to execute, seal, acknowledge and deliver any and all bonds and undertakings, with the exception of Financial Guaranty Insurance, providing that no single obligation shall exceed Fifty Million and 00/100 U.S. Dollars (U.S.\$50,000,000.00), to the same extent as if such bonds had been duly executed and acknowledged by the regularly elected officers of the Company at its principal office in their own proper persons.

This Power of Attorney shall be construed and enforced in accordance with, and governed by, the laws of the State of Delaware, without giving effect to the principles of conflicts of laws thereof. This Power of Attorney is granted pursuant to the following resolutions which were duly and validly adopted at a meeting of the Board of Directors of the Company held on January 25, 2010:

RESOLVED, that, with respect to the Surety business written by Berkley Surety, the Chairman of the Board, Chief Executive Officer, President or any Vice President of the Company, in conjunction with the Secretary or any Assistant Secretary are hereby authorized to execute powers of attorney authorizing and qualifying the attorney-in-fact named therein to execute bonds, undertakings, recognizances, or other suretyship obligations on behalf of the Company, and to affix the corporate seal of the Company to powers of attorney executed pursuant hereto; and said officers may remove any such attorney-in-fact and revoke any power of attorney previously granted; and further  
RESOLVED, that such power of attorney limits the acts of those named therein to the bonds, undertakings, recognizances, or other suretyship obligations specifically named therein, and they have no authority to bind the Company except in the manner and to the extent therein stated; and further  
RESOLVED, that such power of attorney revokes all previous powers issued on behalf of the attorney-in-fact named; and further  
RESOLVED, that the signature of any authorized officer and the seal of the Company may be affixed by facsimile to any power of attorney or certification thereof authorizing the execution and delivery of any bond, undertaking, recognizance, or other suretyship obligation of the Company; and such signature and seal when so used shall have the same force and effect as though manually affixed. The Company may continue to use for the purposes herein stated the facsimile signature of any person or persons who shall have been such officer or officers of the Company, notwithstanding the fact that they may have ceased to be such at the time when such instruments shall be issued.

IN WITNESS WHEREOF, the Company has caused these presents to be signed and attested by its appropriate officers and its corporate seal hereunto affixed this 12<sup>th</sup> day of January, 2018.

Attest:  
  
(Seal) By Ira S. Lederman  
Executive Vice President & Secretary

Berkley Insurance Company  
By Jeffrey M. Hafter  
Senior Vice President

WARNING: THIS POWER INVALID IF NOT PRINTED ON BLUE "BERKLEY" SECURITY PAPER.

STATE OF CONNECTICUT )  
 ) ss:  
COUNTY OF FAIRFIELD )

Sworn to before me, a Notary Public in the State of Connecticut, this 12<sup>th</sup> day of January, 2018, by Ira S. Lederman and Jeffrey M. Hafter who are sworn to me to be the Executive Vice President and Secretary and the Senior Vice President, respectively, of Berkley Insurance Company.

MARIA C. RUNDBAKEN  
NOTARY PUBLIC  
MY COMMISSION EXPIRES  
APRIL 30, 2019

Maria C. Rundbaken  
Notary Public, State of Connecticut

CERTIFICATE

I, the undersigned, Assistant Secretary of BERKLEY INSURANCE COMPANY, DO HEREBY CERTIFY that the foregoing is a true, correct and complete copy of the original Power of Attorney; that said Power of Attorney has not been revoked or rescinded and that the authority of the Attorney-in-Fact set forth therein, who executed the bond or undertaking to which this Power of Attorney is attached, is in full force and effect as of this date.

Given under my hand and seal of the Company, this \_\_\_\_\_ day of \_\_\_\_\_

(Seal) Vincent P. Forte  
Vincent P. Forte

WARNING - Any unauthorized reproduction or alteration of this document is prohibited. This power of attorney is void unless seals are readable and the certification seal at the bottom is embossed. The background imprint, warning and verification instructions (on reverse) must be in blue ink.

Please **verify the authenticity** of the instrument attached to this Power by:

Toll-Free Telephone: (800) 456-5486; or

Electronic Mail: [BSGInquiry@berkleysurety.com](mailto:BSGInquiry@berkleysurety.com)

---

Any written notices, inquiries, claims or demands to the Surety on the bond attached to this Power should be directed to:

Berkley Surety  
412 Mount Kemble Ave.  
Suite 310N  
Morristown, NJ 07960  
Attention: Surety Claims Department

Or

Email: [BSGClaim@berkleysurety.com](mailto:BSGClaim@berkleysurety.com)

---

Please include with all communications the bond number and the name of the principal on the bond. Where a claim is being asserted, please set forth generally the basis of the claim. In the case of a payment or performance bond, please also identify the project to which the bond pertains.

Berkley Surety is a member company of W. R. Berkley Corporation that underwrites surety business on behalf of Berkley Insurance Company, Berkley Regional Insurance Company and Carolina Casualty Insurance Company.

**ATTACHMENT E**

**SCHEDULE OF BID ITEMS**

**Palm Beach County Water Utility Department  
Pipeline Continuing Construction Contract WUD 16-077**

**Work Authorization No.: 11  
Contractor Name: Hinterland Group, Inc.  
Project Name: **CD01 Water Main Improvements - Site 9**  
Project No.: WUD 15-013**

<u>NO.</u>	<u>BID ITEM</u>	<u>QTY</u>	<u>UNIT</u>	<u>UNIT PRICE</u>	<u>TOTAL</u>
2	4" DIP Push-On Joint Water Main	130	LF	\$35.00	\$4,550.00
5	6" DIP Push-On Joint Water Main	1,295	LF	\$32.00	\$41,440.00
8	8" DIP Push-On Joint Water Main	2,005	LF	\$32.00	\$64,160.00
29	Ductile Iron Fittings for Water Main	4.00	TON	\$8,000.00	\$32,000.00
58	4" Mechanical Joint Restraint for DIP	39	EA	\$300.00	\$11,700.00
59	6" Mechanical Joint Restraint for DIP	107	EA	\$325.00	\$34,775.00
60	8" Mechanical Joint Restraint for DIP	42	EA	\$350.00	\$14,700.00
84	6" Pressure Pipe Restraint	34	EA	\$110.00	\$3,740.00
85	8" Pressure Pipe Restraint Harness	49	EA	\$150.00	\$7,350.00
98	Restrain existing 4" Pressure Pipe	13	EA	\$350.00	\$4,550.00
102	4" Gate Valve & Valve Box	-	EA	\$820.00	\$0.00
103	6" Gate Valve & Valve Box	18	EA	\$950.00	\$17,100.00
104	8" Gate Valve & Valve Box	10	EA	\$1,380.00	\$13,800.00
118	8"x6" Tapping Sleeve w/Valve & Valve Box	2	EA	\$4,100.00	\$8,200.00
121	12"X8" Tapping Sleeve w/ Valve and Valve Box	2	EA	\$5,900.00	\$11,800.00
153	Fire Hydrant Assembly	13	EA	\$6,000.00	\$78,000.00
155	Relocation of Existing Hydrant	1	EA	\$1,200.00	\$1,200.00
157	Sample Points W/Double Strap Saddle & Corp. Stop	8	EA	\$1,000.00	\$8,000.00
158	Sample Points on Fire Hydrant	11	EA	\$500.00	\$5,500.00
166	Short Single 5/8" Meter Service (1-1/2" PVC) (Up to 10' Long)	2	EA	\$1,250.00	\$2,500.00
187	4" to 12" Diameter connection to Existing Water Main/Reclaimed Water Main or Force Main (Joint Restraint for existing pipe to be included)	18	EA	\$2,800.00	\$50,400.00
195	Milling of Asphalt	2,250	SY	\$15.00	\$33,750.00
197	Asphalt Overlay, Type S-III	140	TON	\$245.00	\$34,300.00
198	Asphalt Roadway Removal and Restoration	1,205	SY	\$65.00	\$78,325.00
205	Limerock/Shell Driveway or Roadway Removal and Restoration	100	TON	\$30.00	\$3,000.00
207	Concrete Sidewalk Removal & Restoration	30	SY	\$50.00	\$1,500.00
211	Bahia Sod	3,800	SY	\$3.00	\$11,400.00

212	Root Barrier	40	LF	\$22.00	\$880.00
213	Remove Trees up to 4" diameter or Palm Trees up to 12" diameter	60	EA	\$350.00	\$21,000.00
214	Record Drawing	3,430	LF	\$2.00	\$6,860.00
215	Construction Survey	3,430	LF	\$2.00	\$6,860.00
216	Preconstruction Video Taping	3,500	LF	\$1.00	\$3,500.00
217	Mail Box Removal and Reinstallation	8	EA	\$175.00	\$1,400.00
218	Maintenance of Traffic Residential Street	3,500	LF	\$1.50	\$5,250.00
221	Density Tests	66	EA	\$30.00	\$1,980.00
222	Proctor Tests	3	EA	\$90.00	\$270.00
223	Concrete 12"x6" Cylinder Tests	4	EA	\$100.00	\$400.00
224	4-ft to 5-ft High Chain Link Fence Removal and Reinstallation	100	LF	\$40.00	\$4,000.00
233	Guardrail Removal and Restoration	200	LF	\$50.00	\$10,000.00
277	4" Single Line Stop	13	EA	\$3,500.00	\$45,500.00
		Subtotal			\$685,640.00
287	Additional Work Not Included (15%)	1	LS	0.00%	\$0.00
288	Mobilization (2.5% Subtotal Price)	1	LS	2.50%	\$17,141.00
289	Demobilization (1% of Subtotal Price)	1	LS	1.00%	\$6,856.40
		Total			\$709,637.40



**ATTACHMENT E**

**SCHEDULE OF BID ITEMS**

**Palm Beach County Water Utility Department**  
**Pipeline Continuing Construction Contract WUD 16-077**

**Work Authorization No.: 11**  
**Contractor Name: Hinterland Group, Inc.**  
**Project Name: CD01 Water Main Improvements - Site 10**  
**Project No.: WUD 15-013**

<u>NO.</u>	<u>BID ITEM</u>	<u>QTY</u>	<u>UNIT</u>	<u>UNIT PRICE</u>	<u>TOTAL</u>
7	8" PVC Push-On Joint Water Main	410	LF	\$ 24.00	\$ 9,840.00
8	8" DIP Push-On Joint Water Main	150	LF	\$ 32.00	\$ 4,800.00
29	Ductile Iron Fitting for Water Main	0.9	Tons	\$ 8,000.00	\$ 7,200.00
60	8" Mechanical Joint Restraint for DIP	12	EACH	\$ 350.00	\$ 4,200.00
62	12" Mechanical Joint Restraint for DIP	2	EACH	\$ 450.00	\$ 900.00
67	6" Mechanical Joint Restraint for PVC	3	EACH	\$ 325.00	\$ 975.00
68	8" Mechanical Joint Restraint for PVC	14	EACH	\$ 350.00	\$ 4,900.00
85	8" PVC Pressure Pipe Restraint Harness	14	EACH	\$ 150.00	\$ 2,100.00
103	6" Gate Valve & Valve Box	1	EACH	\$ 950.00	\$ 950.00
104	8" Gate Valve & Valve Box	1	EACH	\$ 1,380.00	\$ 1,380.00
157	Sample Points W/Double Strap Saddle & Corp. Stop	2	EACH	\$ 1,000.00	\$ 2,000.00
187	4" to 12" Diameter Connection to Existing Water Main/Reclaimed Water Main or Force Main(Joint Restraint for existing pipe to be included)	2	EACH	\$ 2,800.00	\$ 5,600.00
193	Deactivation of Existing 12" Pipe	150	LF	\$ 18.00	\$ 2,700.00
195	Milling of asphalt(Minimum 220 Sq. Yd. per mobilization - 1.5" thick)	1540	SY	\$ 15.00	\$ 23,100.00
197	Asphalt Overlay, Type S-III	125	Tons	\$ 245.00	\$ 30,625.00
198	Asphalt roadway removal and restoration(2.5" thick)	160	SY	\$ 65.00	\$ 10,400.00
203	Concrete Paver Brick Driveway Removal and Restoration	20	SY	\$ 75.00	\$ 1,500.00
207	Concrete Sidewalk Removal & Restoration	95	SY	\$ 50.00	\$ 4,750.00
208	Concrete Curb & Gutter Removal & Restoration	40	LF	\$ 40.00	\$ 1,600.00
210	Floritam Sod	220	SY	\$ 4.00	\$ 880.00
212	Root Barrier	120	LF	\$ 22.00	\$ 2,640.00
213	Remove Trees up to 4" Diameter or Palm Trees up to 12" Diameter	10	EACH	\$ 350.00	\$ 3,500.00
214	Record Drawing	560	LF	\$ 2.00	\$ 1,120.00
215	Construction Survey	560	LF	\$ 2.00	\$ 1,120.00
216	Preconstruction Video Taping	650	LF	\$ 1.00	\$ 650.00
219	Maintenance of Traffic Arterial Roadway	1000	LF	\$ 2.00	\$ 2,000.00
220	Maintenance of Traffic FDOT Roadway	2000	LF	\$ 4.00	\$ 8,000.00

Palm Beach County Water Utility Department  
Pipeline Continuing Construction Contract WUD 16-077

Work Authorization No.: 11  
Contractor Name: Hinterland Group, Inc.  
Project Name: CD01 Water Main Improvements - Site 10  
Project No.: WUD 15-013

<u>NO.</u>	<u>BID ITEM</u>	<u>QTY</u>	<u>UNIT</u>	<u>UNIT PRICE</u>	<u>TOTAL</u>
221	Density Tests	16	EACH	\$ 30.00	\$ 480.00
222	Proctor Tests	1	EACH	\$ 90.00	\$ 90.00
223	Concrete Cylinder Tests	4	EACH	\$ 100.00	\$ 400.00
234	ADA Concrete Ramps	1	EACH	\$ 1,800.00	\$ 1,800.00
269	Silt Fence	500	LF	\$ 2.00	\$ 1,000.00
279	6" Single Line Stop	1	EACH	\$ 4,500.00	\$ 4,500.00
		Subtotal			\$147,700.00
287	Additional work not included in Bid Items(Max 15% of Subtotal Bas Bid Price.(0.15xA)	1	LS	0%	\$0.00
	Additional Cost Items:				
	Additional Depth for WM Installation Under Congress Ave	55	LF	\$ 200.00	\$11,000.00
	Excavation Near or Under Conflicts	2	EACH	\$ 3,500.00	\$7,000.00
	Soft Dig and Utility Locates	0	HR	\$ 350.00	\$0.00
	Night Work	0	EACH	\$ 3,500.00	\$0.00
288	Mobilization(2.5% of Subtotal Base Bid Price.(0.25xA)	1	LS	2.50%	\$3,692.50
289	Demobilization(1.0% of Subtotal Base Bid Price.(0.01xA)	1	LS	1.00%	\$1,477.00
		Totals			\$170,869.50

## ATTACHMENT E

### SCHEDULE OF BID ITEMS

Palm Beach County Water Utility Department  
Pipeline Continuing Construction Contract WUD 16-077

Work Authorization No.: \_\_11\_\_

Contractor Name: \_\_Hinterland Group, Inc.

Project Name: CD01 Water Main Improvements - Site 11

Project No.: WUD \_15-013\_\_\_\_\_

<u>NO.</u>	<u>BID ITEM</u>	<u>QTY</u>	<u>UNIT</u>	<u>UNIT PRICE</u>	<u>TOTAL</u>
7	8" PVC Push-On Joint Water Main	615	LF	\$ 24.00	\$ 14,760.00
8	8" DIP Push-On Joint Water Main	130	LF	\$ 32.00	\$ 4,160.00
10	10" DIP Push-On Joint Water Main	10	LF	\$ 30.00	\$ 300.00
29	Ductile Iron Fitting for Water Main	1.5	TON	\$ 8,000.00	\$ 12,000.00
60	8" Mechanical Joint Restraint for DIP	12	EACH	\$ 350.00	\$ 4,200.00
67	6" Mechanical Joint Restraint for PVC	5	EACH	\$ 325.00	\$ 1,625.00
68	8" Mechanical Joint Restraint for PVC	28	EACH	\$ 350.00	\$ 9,800.00
69	10" Mechanical Joint Restraint for PVC	2	EACH	\$ 425.00	\$ 850.00
85	8" PVC Pressure Pipe Restraint Harness	6	EACH	\$ 150.00	\$ 900.00
94	Restrain Existing 6" PVC Pressure Pipe	2	EACH	\$ 500.00	\$ 1,000.00
103	6" Gate Valve & Valve Box	1	EACH	\$ 950.00	\$ 950.00
104	8" Gate Valve & Valve Box	1	EACH	\$ 1,380.00	\$ 1,380.00
153	Fire Hydrant Assembly with Captivator Caps, 6" Gate Valve & Anchor Tee Assembly & 10-ft of 6" P.J. DIP	1	EACH	\$ 6,000.00	\$ 6,000.00
157	Sample Points W/Double Strap Saddle & Corp. Stop	2	EACH	\$ 1,000.00	\$ 2,000.00
158	Sample Points on Fire Hydrants	0	EACH	\$ 500.00	\$ -
167	Short Single 5/8" Meter Service(1-1/2" Polyethylene)(up to 10' long)	2	EACH	\$ 1,200.00	\$ 2,400.00
187	4" to 12" Diameter Connection to Existing Water Main/Reclaimed Water Main or Force Main(Joint Restraint for existing pipe to be included)	2	EACH	\$ 2,800.00	\$ 5,600.00
190	Deactivation of Existing 4" Pipe	320	LF	\$ 12.00	\$ 3,840.00
195	Milling of asphalt(Minimum 220 Sq. Yd. per mobilization - 1.5" thick)	1100	SY	\$ 15.00	\$ 16,500.00
197	Asphalt Overlay, Type S-III	100	TON	\$ 245.00	\$ 24,500.00
198	Asphalt roadway removal and restoration(2.5" thick)	80	SY	\$ 65.00	\$ 5,200.00
202	Stamped Concrete Driveway Removal and Restoration	60	SY	\$ 80.00	\$ 4,800.00

203	Concrete Paver Brick Driveway Removal and Restoration	100	SY	\$ 75.00	\$ 7,500.00
207	Concrete Sidewalk Removal & Restoration	60	SY	\$ 50.00	\$ 3,000.00
208	Concrete Curb & Gutter Removal & Restoration	40	LF	\$ 40.00	\$ 1,600.00
210	Floritam Sod	690	SY	\$ 4.00	\$ 2,760.00
212	Root Barrier	100	LF	\$ 22.00	\$ 2,200.00
213	Remove Trees up to 4" Diameter or Palm Trees up to 12" Diameter	20	EACH	\$ 350.00	\$ 7,000.00
214	Record Drawing	750	LF	\$ 2.00	\$ 1,500.00
215	Construction Survey	750	LF	\$ 2.00	\$ 1,500.00
216	Preconstruction Video Taping	1000	LF	\$ 1.00	\$ 1,000.00
217	Mail Box Removal and Reinstallation	3	EACH	\$ 175.00	\$ 525.00
218	Maintenance of Traffic Residential Street	400	LF	\$ 1.50	\$ 600.00
220	Maintenance of Traffic FDOT Street	2000	LF	\$ 4.00	\$ 8,000.00
221	Density Tests	16	EACH	\$ 30.00	\$ 480.00
222	Proctor Test	1	EACH	\$ 90.00	\$ 90.00
269	Silt Fence	750	LF	\$ 2.00	\$ 1,500.00
279	6" Single Line Stop(for PVC/DIP/CIP/AC)	1	EACH	\$ 4,500.00	\$ 4,500.00
		Subtotal			\$166,520.00
287	Additional work not included in Bid Items(Max 15% of Subtotal Bas Bid Price.(0.15xA)	1	LS	0.00%	\$0.00
	Additional Work Items:				
	Additional Depth for WM Installation	70	LF	\$ 200.00	\$14,000.00
	Excavation Near or Under Conflicts	1	EACH	\$ 3,500.00	\$3,500.00
	Soft Dig and Utility Locates	0	HR	\$ 350.00	\$0.00
	Night Work	0	EACH	\$ 3,500.00	\$0.00
	Remove and Replace Metal Fence	1	LS	\$ 2,500.00	\$2,500.00
288	Mobilization(2.5% of Subtotal Base Bid Price.(0.25xA)	1	LS	2.50%	\$4,163.00
289	Demobilization(1.0% of Subtotal Base Bid Price.(0.01xA)	1	LS	1.00%	\$1,665.20
		Totals			\$192,348.20

## ATTACHMENT E

### SCHEDULE OF BID ITEMS

Palm Beach County Water Utility Department  
Pipeline Continuing Construction Contract WUD 16-077

Work Authorization No.: \_\_11\_\_

Contractor Name: \_\_Hinterland Group, Inc.

Project Name: CD01 Water Main Improvements - Site 12

Project No.: WUD \_15-013\_\_\_\_\_

<u>NO.</u>	<u>BID ITEM</u>	<u>QTY</u>	<u>UNIT</u>	<u>UNIT PRICE</u>	<u>TOTAL</u>
7	8" PVC Push-On Joint Water Main	10	LF	\$ 24.00	\$ 240.00
8	8" DIP Push-On Joint Water Main	330	LF	\$ 32.00	\$ 10,560.00
29	Ductile Iron Fitting for Water Main	1.5	TON	\$ 8,000.00	\$ 12,000.00
33	8" HDPE Directional Drill Water Main	400	LF	\$ 65.00	\$ 26,000.00
52	8" DIP/PVC x HDPE Adapter	2	EACH	\$ 600.00	\$ 1,200.00
60	8" Mechanical Joint Restraint for DIP	31	EACH	\$ 350.00	\$ 10,850.00
68	8" Mechanical Joint Restraint for PVC	2	EACH	\$ 350.00	\$ 700.00
95	Restrain Existing 8" PVC Pressure Pipe	0	EACH	\$ 650.00	\$ -
104	8" Gate Valve & Valve Box	2	EACH	\$ 1,380.00	\$ 2,760.00
134	Aerial Crossing Complete(8" Water/Reclaimed Water main, 31' to 50' Long)	1	LS	\$ 45,000.00	\$ 45,000.00
157	Sample Points W/Double Strap Saddle & Corp. Stop	2	EACH	\$ 1,000.00	\$ 2,000.00
167	Short Single Service	2	EACH	\$ 1,200.00	\$ 2,400.00
187	4" to 12" Diameter Connection to Existing Water Main/Reclaimed Water Main or Force Main(Joint Restraint for existing pipe to be included)	2	EACH	\$ 2,800.00	\$ 5,600.00
190	Deactivation of Existing 4" Pipe	60	LF	\$ 12.00	\$ 720.00
195	Milling of asphalt(Minimum 220 Sq. Yd. per mobilization - 1.5" thick)	160	SY	\$ 15.00	\$ 2,400.00
197	Asphalt Overlay, Type S-III	10	TON	\$ 245.00	\$ 2,450.00
198	Asphalt roadway removal and restoration(2.5" thick)	28	SY	\$ 65.00	\$ 1,820.00
208	Concrete Curb & Gutter Removal & Restoration	20	LF	\$ 40.00	\$ 800.00
210	Floritam Sod	340	SY	\$ 4.00	\$ 1,360.00
212	Root Barrier	120	LF	\$ 22.00	\$ 2,640.00
213	Remove Trees up to 4" Diameter or Palm Trees up to 12" Diameter	1	EACH	\$ 350.00	\$ 350.00
214	Record Drawing	750	LF	\$ 2.00	\$ 1,500.00

215	Construction Survey	750	LF	\$ 2.00	\$ 1,500.00
216	Preconstruction Video Taping	1000	LF	\$ 1.00	\$ 1,000.00
217	Mail Box Removal and Reinstallation	2	EACH	\$ 175.00	\$ 350.00
218	Maintenance of Traffic Residential Street	300	LF	\$ 1.50	\$ 450.00
221	Density Tests	16	EACH	\$ 30.00	\$ 480.00
222	Proctor Test	1	EACH	\$ 90.00	\$ 90.00
223	Concrete Cylinder Tests	4	EACH	\$ 100.00	\$ 400.00
224	4-ft to 5-ft High Chain Link Fence Removal and Reinstallation	60	LF	\$ 40.00	\$ 2,400.00
232	Remove & Replace Signs	2	EACH	\$ 350.00	\$ 700.00
266	Aerial Pipe Coatings/Paints	1	EACH	\$ 5,000.00	\$ 5,000.00
267	Fan Guard with Support Struts	2	EACH	\$ 5,200.00	\$ 10,400.00
268	Aerial Crossing Automatic Air Release Valve, pressure gauge with double strap saddle and corporation stop welded on outlet	1	EACH	\$ 3,800.00	\$ 3,800.00
269	Silt Fence	750	LF	\$ 2.00	\$ 1,500.00
270	Canal Bank Grade and Place Rip-Rap Revetment	2	EACH	\$ 3,200.00	\$ 6,400.00
281	8" Single Line Stop	2	EACH	\$ 5,000.00	\$ 10,000.00
		Subtotal			\$177,820.00
287	Additional work not included in Bid Items(Max 15% of Subtotal Bas Bid Price.(0.15xA)	1	LS	0.00%	\$0.00
	Additional Work Items:				
	Excavation Near or Under Conflicts	1	EACH	\$ 3,500.00	\$3,500.00
	Soft Dig and Utility Locates	0	HR	\$ 350.00	\$0.00
	8" x 8" Tapping Sleeve w/ Valve	1	LS	\$ 4,600.00	\$4,600.00
288	Mobilization(2.5% of Subtotal Base Bid Price.(0.25xA)	1	LS	2.50%	\$4,445.50
289	Demobilization(1.0% of Subtotal Base Bid Price.(0.01xA)	1	LS	1.00%	\$1,778.20
		Totals			\$192,143.70

ATTACHMENT F  
SCHEDULE 1  
LIST OF PROPOSED SBE-M/WBE PARTICIPATION

PROJECT NAME OR BID NAME: CD01 Water Main Improvements Zones 2, 3 & 4

NAME OF PRIME BIDDER: Hinterland Group, Inc.

CONTACT PERSON: Chase Rogers

BID OPENING DATE: N/A

Project No. or Bid No.: CD01-WUD 15-013

ADDRESS: 2051 W Blue Heron, Blvd Riviera Beach FL 33404

PHONE NO.: (561)-640-3503 FAX NO.: (561)640-3504

USER DEPARTMENT: WUD

THIS DOCUMENT IS TO BE COMPLETED BY THE PRIME CONTRACTOR AND SUBMITTED WITH BID PACKET. PLEASE LIST THE NAME, CONTACT INFORMATION AND DOLLAR AMOUNT AND/OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SBE -M/WBE's ON THIS PROJECT. IF THE PRIME IS AN SBE-M/WBE, PLEASE ALSO LIST THE NAME, CONTACT INFORMATION AND DOLLAR AMOUNT AND/OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME ON THIS PROJECT. THE PRIME AFFIRMS THAT IT WILL MONITOR THE SBES LISTED TO ENSURE THE SBES PERFORM THE WORK WITH ITS OWN WORKFORCE.

(Check one or both Categories)			DOLLAR AMOUNT AND/OR PERCENTAGE OF WORK				
Name, Address and Phone Number	M/WBE	SBE	Black	Hispanic	Women	Caucasian	Other (Please Specify)
	Minority Business	Small Business					
1. Hinterland Group, Inc. 2051 W. Blue Heron Blvd. Riviera Beach, FL 33404 (561)640-3503	<input type="checkbox"/>	<input checked="" type="checkbox"/>				\$1,264,998.80	
2.	<input type="checkbox"/>	<input type="checkbox"/>					
3.	<input type="checkbox"/>	<input type="checkbox"/>					
4.	<input type="checkbox"/>	<input type="checkbox"/>					
5.	<input type="checkbox"/>	<input type="checkbox"/>					
(Please use additional sheets if necessary)	Total					\$1,264,998.80	
Total Bid Price \$ 1,264,998.80			Total SBE-M/WBE Participation Dollar Amount and/or Percentage of Work \$1,264,998.80				

I hereby certify that the above information accurate to the best of my knowledge:

Signature

Title

NOTE:

1.

2.

3.

The amount listed on this form for a SBE-M/WBE Prime or Subcontractor must be supported by price or percentage listed on the signed Schedule 2 or signed proposal in order to be counted toward goal attainment.

Firms may be certified by Palm Beach County as an SBE and/or M/WBE. If firms are certified as both an SBE and M/WBE, please indicate the dollar amount and/or percentage under the appropriate category.

M/WBE information is being collected for tracking purposes only

REVISED 07-02-13

ATTACHMENT F

OSBA SCHEDULE 2  
LETTER OF INTENT TO PERFORM AS AN SBE-M/WBE

This document must be completed by ALL SBE-M/WBE's and submitted with this bid packet. Specify in detail, the particular work items to be performed and the dollar amount and/or percentage for each work item. SBE credit will only be given for items which the SBE-M/WBE's is certified to perform. Failure to properly complete Schedule 2 will result in your SBE participation not being counted.

PROJECT NUMBER: WUD 15-013 PROJECT NAME: CD01 Water Main Improvements Zones 2,3 & 4  
TO: Hinterland Group, Inc.  
(Name of Prime Bidder)

The undersigned is certified by Palm Beach County as a - (check one or more, as applicable):

Small Business Enterprise X Minority Business Enterprise \_\_\_\_\_  
Black \_\_\_\_\_ Hispanic \_\_\_\_\_ Women \_\_\_\_\_ Caucasian X Other (Please Specify) \_\_\_\_\_

Date of Palm Beach County Certification: Dec 10, 2018

The undersigned is prepared to perform the following described work in connection with the above project. Additional Sheets May Be Used As Necessary

Line Item/ Lot No.	Item Description	Qty/Units	Unit Price	Total Price/ Percentage
All	Per Bid Schedule			

at the following price or percentage 100%  
(SBE Prime or Subcontractor's Quote)

and will enter into a formal agreement for work with you contingent upon your execution of a contract with Palm Beach County.

If undersigned intends to sub-subcontract any portion of this job to a certified SBE-M/WBE or a non-SBE subcontractor, please list the name of that subcontractor and the amount below.

Price or Percentage \_\_\_\_\_  
(Name of Subcontractor)

The Prime affirms that it will monitor the SBE-M/WBE listed to ensure the SBE-M/WBE perform the work with their own work force. The undersigned SBE-M/WBE Prime or SBE-M/WBE subcontractor affirms that it has the resources necessary to perform the work listed without subcontracting to a non-certified SBE or any other certified SBE subcontractors except as noted above.

The undersigned subcontractor understands that the provision of this form to Prime Bidder does not prevent Subcontractor from providing quotations to other bidders.

Hinterland Group, Inc.  
\_\_\_\_\_  
Print name of  
SBE-M/WBE Company  
By: \_\_\_\_\_  
(Signature)  
Daniel Duke III, President  
\_\_\_\_\_  
Print name/title of person executing on behalf  
of SBE-M/WBE

Revised 7/2/2013 Date: 7/12/2018





**ATTACHMENT G**

**Palm Beach County Water Utilities Department  
Pipeline Continuing Construction Contract 2017 – WUD16-077  
Resolution # R2017-0072 Contract Dated Jan10, 2017**

**SUMMARY OF  
SBE-M/WBE MINORITY BUSINESS TRACKING**

<b>Master Contract Goal</b>	<u>15%</u>	<b>SBE</b>
<b>Current Proposal</b>		
Value of Authorization No. 11		\$1,264,998.80
Value of SBE-M/WBE Letters of Intent		\$1,264,998.80
Actual Percentage		<u>100%</u>
<b>Signed/Approved Authorizations</b>		
Total Value of Authorizations		\$3,870,704.20
Total Value of SBE-M/WBE Signed Subcontracts		\$3,870,704.20
Actual Percentage		<u>100%</u>
<b>Signed/Approved Authorizations Plus Current Proposal</b>		
Total Value of Authorization		\$5,135,703.00
Total Value of Subcontracts & Letters of Intent		\$5,135,703.00
Actual Percentage		<u>100%</u>

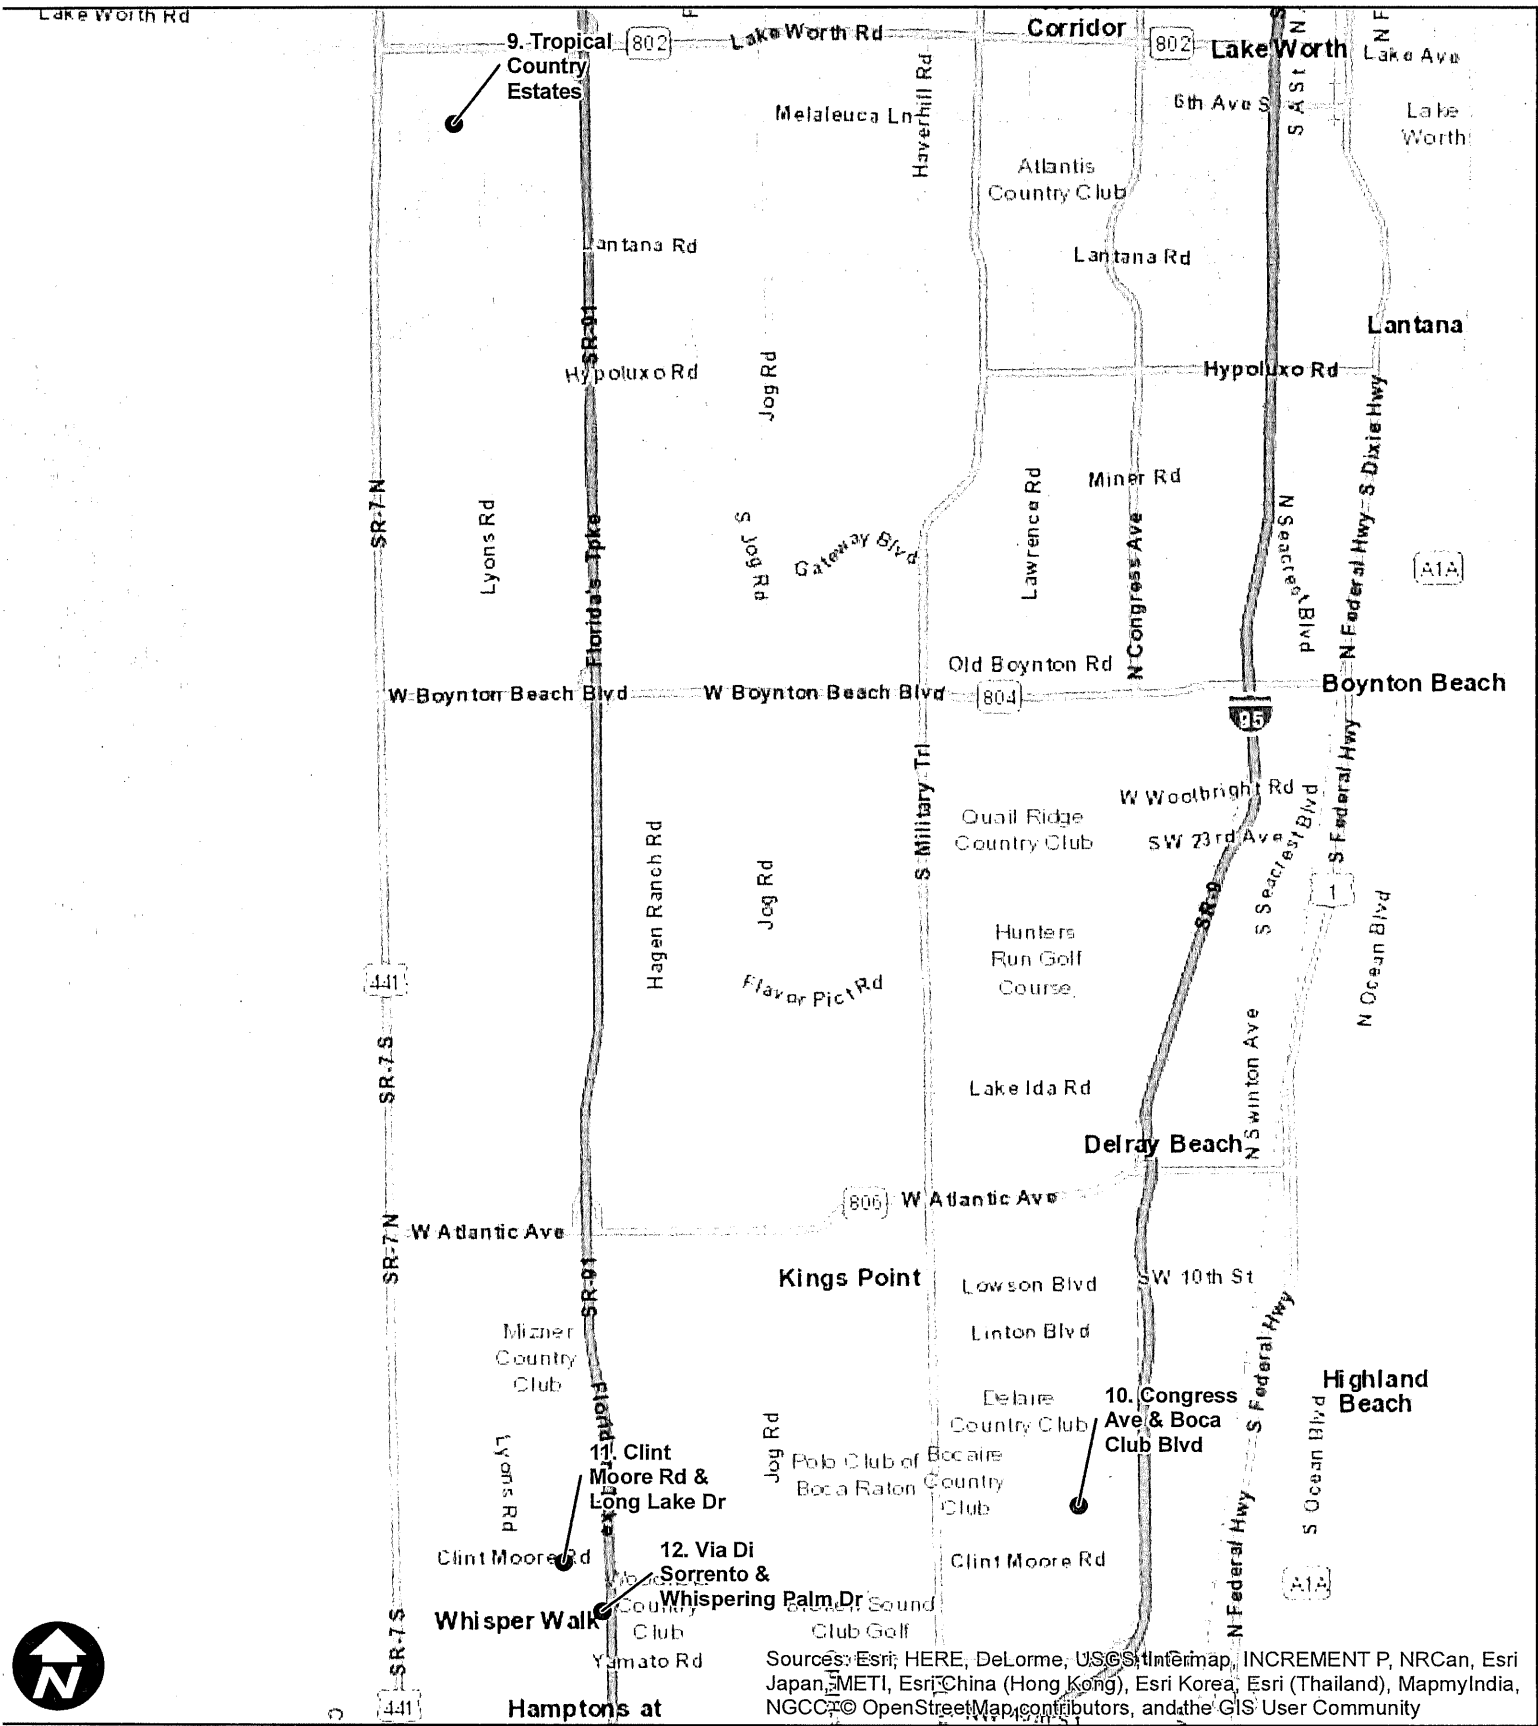



**Palm Beach County**  
**Water Utilities**  
**Department**

8100 Forest Hill Blvd.  
West Palm Beach, FL 33416  
(561) 740-4600

### Project Location Map

#### PBCWUD CD01 Water Main Improvements

#### WUD Zones 2, 3 & 4 - WUD No. 15-013

**Legend**

● Looping Project Sites

# WAGNER BONDING & *INSURANCE, INC.*

August 9, 2018

Palm Beach County  
8100 Forest Hill Blvd.  
West Palm Beach, FL 33413

**Re: Hinterland Group, Inc.**

To whom it may concern,

We are the bonding agent for Hinterland Group, Inc.. They are bonded by Berkley Insurance Company, an "AXV" rated surety in the AM Best Guide. Please be advised that we authorize you to date powers of attorney, form of guarantee and bonds for Pipeline Continuing Construction Contract 2017, Resolution No. R2017-0072, Contract Dated Jan 10, 2017, WUD Project No. 15-013, Work Authorization No. 11, Project Title: CD01 Water main improvements zone 2, 3, & 4.

Should you have any questions or concerns, please do not hesitate to call.

Sincerely,  
Wagner Bonding & Insurance, Inc



Taylor D. Wagner  
Resident Florida Licensed Agent  
Attorney-In-Fact

**P.O. Box 91147 Lakeland, FL. 33804  
Phone 863-859-9823  
Fax 863-815-1864**



Summary of Certificates

This report displays detailed Certificate of Insurance information for a selected Insured. Any items shown in red are deficient.

Tuesday, September 04, 2018

Simple View

Certificate Images

Documents

Insured:	Hinterland Group, Inc.	Insured ID:	16-077-PBC
Status:	Compliant		
ITS Account Number:	PLC2296		
Project(s):	Palm Beach County - Water Utilities - (Active)		
Insurance Policy	Required	Provided	Override
<u>General Liability</u>			
Expiration: 1/31/2019			
General Aggregate:	\$1,000,000	\$2,000,000	
Products - Completed Operations Aggregate:	\$1,000,000	\$2,000,000	
Personal And Advertising Injury:	\$0	\$1,000,000	
Each Occurrence:	\$1,000,000	\$1,000,000	
Fire Damage:	\$0	\$0	
Medical Expense:	\$0	\$0	
<u>Automobile Liability</u>		Any Auto	
Expiration: 1/31/2019	All Owned Autos	not provided	X
	Hired Autos	not provided	X
	Non-Owned Autos	not provided	X
Combined Single Limit:	\$1,000,000	\$1,000,000	
<u>Excess/Umbrella Liability</u>			
Expiration: 1/31/2019			
Each Occurrence:	\$0	\$10,000,000	
Aggregate Limit:	\$0	\$10,000,000	
<u>Workers Compensation/Employers Liability</u>	WC Stat. Limits	WC Stat. Limits	
Expiration: 1/31/2019			
Each Accident:	\$100,000	\$1,000,000	
Disease - Policy Limit:	\$500,000	\$1,000,000	
Disease - Each Employee:	\$100,000	\$1,000,000	
<u>Inland Marine/Transit Insurance</u>	Loss Payee Endorsement	Loss Payee Endorsement	
Expiration: 1/31/2019			

Notifications (Show All)

There were no deficiency letters issued.
