

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

Fiscal Years	2020	2021	2022	2023	2024
Capital Expenditures	\$238,216	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
Operating Costs	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
External Revenues	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
Program Income (County)	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
In-Kind Match County	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
NET FISCAL IMPACT	\$238,216	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>
# ADDITIONAL FTE POSITIONS (Cumulative)	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>

Budget Account No.: Fund 4011 Dept 721 Unit W019 Object 6547

Is Item Included in Current Budget? Yes X No
 Does this item include the use of federal funds? Yes No X

Reporting Category N/A

B. Recommended Sources of Funds/Summary of Fiscal Impact:

One (1) time expenditure from user fees, connection fees and balance brought forward.



C. Department Fiscal Review: _____

III. REVIEW COMMENTS

A. OFMB Fiscal and/or Contract Development and Control Comments:

Lucas 10/24/19
OFMB 10/23

Janey [Signature] for Mark [Signature]
Contract Development and Control
10/24/19 Tu

B. Legal Sufficiency:

[Signature] 10/28/19
Assistant County Attorney

C. Other Department Review:

Department Director

This summary is not to be used as a basis for payment.

WORK AUTHORIZATION NO. 22

**Palm Beach County Water Utilities Department
Pipeline Continuing Construction Contract 2017
Resolution #R2017-0072 Contract Dated January 10, 2017**

Project Title: 12-inch Force Main on Sandalfoot Blvd.

WUD Project No.: 18-063

Contractor: Hinterland Group Inc.

Address: 2051 W Blue Heron Blvd, Riviera Beach, FL 33404

Budget Line Item No. 4011-721-W019-6547

District: 5

This Work Authorization provides for: The installation of approximately 1,000 linear feet of 12-inch force main along the north side of Sandalfoot Blvd from the Lake Worth Drainage District (LWDD) E-1 Canal to east of SW 66th Ave, Boca Raton. The new force main will parallel an existing 8-inch force main which is over capacity, especially in wet weather. This new force main will connect to an existing force main on the east side of LWDD E-1 canal crossing and to a force main north of Lift Station No. 0981.

See **ATTACHMENT A** for detailed scope of services.

The Contract provides for 15.00% SBE participation. This Work Authorization includes 100.00% participation. The cumulative proposed SBE participation, including this authorization is 100.00%.

1. Services completed by the Contractor to date:

See **ATTACHMENT B**.

2. Contractor shall begin work within ten (10) calendar days from the issuance of Notice to Proceed (NTP). Execution of the Project will be accomplished as follows from the issuance of the NTP:

Substantial Completion	<u>90</u>	Calendar Days
Final Construction Completion	<u>120</u>	Calendar Days

Liquidated damages will apply as follows:

\$500.00 per day past substantial completion date.

\$250.00 per day past final completion date.

WORK AUTHORIZATION NO. 22

Palm Beach County Water Utilities Department
Pipeline Continuing Construction Contract 2017
Resolution #R2017-0072 Contract Dated January 10, 2017

3. The compensation to be paid to the Contractor for providing the requested services in accordance with the Contract Bid Prices is \$238,215.60.
4. This Work Authorization does not amend, change, or modify the Contract which remains in full force and effect.
5. All Attachments to this Authorization are incorporated herein and made a part of this Work Authorization.

WORK AUTHORIZATION NO. 22

Palm Beach County Water Utilities Department
Pipeline Continuing Construction Contract 2017
Resolution #R2017-0072 Contract Dated January 10, 2017

Project Title: 12-inch Force Main on Sandalfoot Blvd.

WUD Project No.: 18-063

IN WITNESS WHEREOF, this Work Authorization is accepted, subject to the terms, conditions and obligations of the aforementioned Contract.

PALM BEACH COUNTY, A POLITICAL SUBDIVISION OF THE STATE OF FLORIDA

Sharon R. Bock, Clerk & Comptroller,
Palm Beach County

Palm Beach County,
Board of County Commissioners

ATTEST:

Signed: _____

Sharon Bock
Signed: _____
_____, Mayor *CEI*

Typed Name: _____
Deputy Clerk

Date

Approved as to Form and Legal
Sufficiency

CONTRACTOR: Hinterland Group Inc.

Signed: _____

Chase R. Rogers


(Signature)

Typed Name: _____
County Attorney

Chase R. Rogers, Project Director
(Name and Title)


09/12/2019

Date



STATE OF FLORIDA
COUNTY OF Palm Beach

The foregoing instrument was acknowledged before me this 12 day of September, 2019,
by Chase R. Rogers as Project Director
for Hinterland Group Inc.



Emily Meng

(Signature of Notary Public - State of Florida)

Emily Meng

(Print, Type, or Stamp Commissioned Name of Notary Public)

Personally Known OR Produced Identification _____ Type of Identification Produced _____

LIST OF ATTACHMENTS
WORK AUTHORIZATION NO. 22

Palm Beach County Water Utilities Department
Pipeline Continuing Construction Contract 2017
Resolution #R2017-0072 Contract Dated January 10, 2017

ATTACHMENT A	Scope of Work
ATTACHMENT B	Summary and Status of Work Authorizations
ATTACHMENT C	Public Construction Bond
ATTACHMENT D	Form of Guarantee
ATTACHMENT E	Work Authorization Schedule of Bid Items
ATTACHMENT F	OEBO Schedule 1 and Schedule 2
ATTACHMENT G	Summary of SBE/Minority Business Tracking
ATTACHMENT H	Location Map

Revised 8-29-19

ATTACHMENT A

SCOPE OF WORK AUTHORIZATION # 22

WUD PROJECT NO.: 18-063

PROJECT TITLE: 12-inch Force Main on Sandalfoot Blvd.

Contractor shall perform: The installation of approximately 1,000 linear feet of 12-inch force main along the north side of Sandalfoot Blvd from the Lake Worth Drainage District (LWDD) E-1 Canal to east of SW 66th Ave, Boca Raton. The new force main will parallel an existing 8-inch force main which is over capacity, especially in wet weather. This new force main will connect to an existing force main on the east side of LWDD E-1 canal crossing and to a force main north of Lift Station No. 0981.

Revised 8-29-19

ATTACHMENT B

SUMMARY AND STATUS OF WORK AUTHORIZATIONS

Work Auth. No.	WUD Project No.	Title	Status	Project Total Amount	SBE Total Amount	SBE Participation %	Approved	
							By	Date
1	16-014	Water and Force Main Replacement at Dr. Martin Luther King Jr. Blvd. and SW 10th St	Closed	\$324,736.43	\$324,736.43	100.00%	BCC	5/16/2017
2	16-046	Palm Beach Colony Water Main Extension South	Closed	\$113,277.28	\$113,277.28	100.00%	CRC	4/12/2017
3	16-037	GL06; Gator Blvd Water Main Extension; E Sugarhouse Rd to Duda Rd	Closed	\$792,003.03	\$792,003.03	100.00%	BCC	9/26/2017
3.1	16-037	GL06; Gator Blvd Water Main Extension; E Sugarhouse Rd to Duda Rd	Closed	\$1,541.00	\$1,541.00	100.00%	WUD	5/21/2018
4	17-052	Emergency Repair at E 1 st St and Barfield Highway	Closed	\$88,720.93	\$88,720.93	100.00%	WUD	6/16/2017
5	17-053	Military Trail, Appaloosa St to Wadita Ka Way; Water Main Replacement	Closed	\$108,234.78	\$108,234.78	100.00%	CRC	8/23/2017
6	16-067	Priority Aerial Canal Crossing Improvements	Closed	\$765,220.20	\$765,220.20	100.00%	BCC	9/26/2017
7	16-053	GL06; SW Belle Glade Water Main Improvements; SW 8th St; SW 9th St & SW 4th St. From SW Ave F to Dr. Martin Luther King Jr. Blvd.	Closed	\$1,389,257.38	\$1,389,257.38	100.00%	BCC	12/5/2017
7.1	16-053	GL06; SW Belle Glade Water Main Improvements; SW 8th St; SW 9th St & SW 4th St. From SW Ave F to Dr. Martin Luther King Jr. Blvd.	Closed	\$67,509.60	\$67,509.60	100.00%	WUD	12/6/2018
8	15-013	Water Main Improvements	Closed	\$54,503.10	\$54,503.10	100.00%	WUD	8/15/2017
9	17-061	Pahokee PBC Airport & Pee Hokey Dr. Fire Hydrant Replacements	Closed	\$88,716.40	\$88,716.40	100.00%	WUD	11/7/2017
10	17-058	Force Main Improvements to Lift Station 8105	Closed	\$144,493.67	\$144,493.67	100.00%	CRC	12/20/2017
11	15-013	Water Main Improvements	Open	\$1,264,998.80	\$1,264,998.80	100.00%	BCC	10/2/2018
11.1	15-013	Water Main Improvements	Open	\$46,719.38	\$46,719.38	100.00%	WUD	7/29/2019
12	14-064	Water Main Stub-Outs & Fire Hydrant Installations along 60th Place North (From 110th Avenue North to 180th Avenue North)	Open	\$401,253.98	\$401,253.98	100.00%	BCC	7/2/2019
13	19-003	Installation of Water Services along 60th Place North and 61st Street North	Open	\$43,130.30	\$43,130.30	100.00%	WUD	4/26/2019
14	19-031	Fire Hydrant Relocation on Chickasaw Road	Closed	\$33,885.03	\$33,885.03	100.00%	WUD	5/30/2019
15	17-060	Barfield Highway from Pelican River to East 7th Street, Pahokee; Water Main Replacement	Pending	\$262,482.02	\$262,482.02	100.00%	BCC	Pending
16	17-077	Priority Aerial Canal Crossing Improvements Phase 2	Pending	\$1,819,104.20	\$1,819,104.20	100.00%	BCC	Pending
17	18-070	Water Main Replacement within Sandpiper Avenue, Meadowlark Drive & Oriole Court	Open	\$1,754,414.58	\$1,754,414.58	100.00%	BCC	8/20/2019
18	19-013	Utility Relocations for Belle Glade Citywide Sidewalk Improvements	Open	\$160,937.95	\$160,937.95	100.00%	CRC	8/14/2019
19	19-013	Utility Relocations for Belle Glade Citywide Sidewalk Improvements	Open	\$625,761.75	\$625,761.75	100.00%	BCC	9/10/2019
20	19-064	Loxahatchee Groves Park Lift Station and Force Main	Open	\$38,824.55	\$38,824.55	100.00%	WUD	9/20/2019
21	19-075	Utility Relocation along Hamlin Blvd; Indian Trail Culvert Improvement Project	Pending	\$242,699.20	\$242,699.20	100.00%	BCC	Pending
22	18-063	12-inch Force Main on Sandalfoot Blvd.	Pending	\$238,215.60	\$238,215.60	100.00%	BCC	Pending

ATTACHMENT C

**PUBLIC CONSTRUCTION BOND – WORK AUTHORIZATION NO. 22
TO Pipeline Continuing Construction Contract 2017
RESOLUTION NO. R2017-0072 Contract Dated January 10, 2017**

PROJECT TITLE: 12-inch Force Main on Sandalfoot Blvd.

WUD PROJECT NO.: 18-063

BOND NUMBER: 21BCSIE4088

WORK AUTHORIZATION/BOND AMOUNT: \$238,215.60

CONTRACTOR'S NAME: Hinterland Group Inc.

CONTRACTOR'S ADDRESS: 2051 W Blue Heron Blvd.
Riviera Beach, FL 33404

CONTRACTOR'S PHONE: 561 640-3503

SURETY COMPANY: Hartford Accident & Indemnity Company

SURETY'S ADDRESS: One Hartford Plaza,
Hartford, CT 06155

OWNER'S NAME: PALM BEACH COUNTY

OWNER'S ADDRESS: 8100 Forest Hill Boulevard
West Palm Beach, FL 33413

OWNER'S PHONE: (561) 493-6000

DESCRIPTION OF WORK: Installation of a 12-inch force main along Sandalfoot Blvd
between LWDD E-1 Canal and east of SW 66th Ave in Boca
Raton.

PROJECT LOCATION: Sandalfoot Blvd, between LWDD E-1 Canal and east of SW 66th
Ave in Boca Raton.

LEGAL DESCRIPTION: Section 30; Township 47; Range 42

Revised 8-29-19

PUBLIC CONSTRUCTION BOND

This Bond is issued in favor of the County conditioned on the full and faithful performance of the Work Authorization No. 22 to Pipeline Continuing Construction Contract 2017 Resolution No. R2017-0072 dated on January 10, 2017.

KNOW ALL MEN BY THESE PRESENTS: that Contractor and Surety, are held and firmly bound unto

Palm Beach County Board of County Commissioners
301 N. Olive Avenue
West Palm Beach, Florida 33401

as Obligee, herein called County, for the use and benefit of claimant as herein below defined, in the amount of Two Hundred Thirty-Eight Thousand Two Hundred Fifteen Dollars and 60/100 Cents, \$238,215.60,

(Here insert a sum equal to the Work Authorization/Bond Amount from page 1)

for the payment whereof Principal and Surety bind themselves, their heirs, personal representatives, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

WHEREAS,

Principal has by written agreement dated _____, 20____, entered into Work Authorization No. 22 to Pipeline Continuing Construction Contract 2017 Resolution No. R2017-0072 with the County for

Work Authorization Project Name: 12-inch Force Main on Sandalfoot Blvd.
Work Authorization Project No.: 18-063
Project Description: Installation of a 12-inch force main along Sandalfoot Blvd between LWDD E-1 Canal and east of SW 66th Ave in Boca Raton.
Project Location: Sandalfoot Blvd, between LWDD E-1 Canal and east of SW 66th Ave in Boca Raton.

in accordance with Design Criteria Drawings and Specifications prepared by

Name of Design Firm: Mock, Roos & Associates, Inc.
Location of Firm: 5720 Corporate Way, West Palm Beach, FL 33407
Phone: (561) 683-3113
Fax: (561) 478-7248

which Work Authorization No. 22 to Pipeline Continuing Construction Contract 2017 Resolution No. R2017-0072 is by reference made a part hereof in its entirety, and is hereinafter referred to as the Work Authorization.

1. THE CONDITION OF THIS BOND is that if Principal:
 - a. Performs the Work Authorization dated _____, 20____, between Principal and County for the construction of the above project, the Work Authorization being made a part of this bond by reference, at the times and in the manner prescribed in the Work Authorization; and

Revised 8-29-19

b. Promptly makes payments to all claimants, as defined in Section 255.05, Florida Statutes, supplying Principal with labor, materials, or supplies, used directly or indirectly by Principal in the prosecution of the work provided for in the Work Authorization; and

c. Pays County all losses, damages (including liquidated damages), expenses, costs, and attorneys' fees, including appellate proceedings, that County sustains because of a default by Principal under the Work Authorization; and

d. Performs the guarantee of all work and materials furnished under the Work Authorization for the time specified in the Work Authorization; then this bond is void; otherwise it remains in full force.

2. Any changes in or under the contract documents and compliance or noncompliance with any formalities connected with the Work Authorization or the changes does not affect Surety's obligation under this bond and Surety waives notice of such changes.

3. The amount of this bond shall be reduced by and to the extent of any payment or payments made in good faith hereunder, inclusive of the payment by Surety of construction liens which may be filed of record against said improvement, whether or not claim for the amount of such lien be presented under and against the bond.

4. Principal and Surety expressly acknowledge that any and all provisions relating to consequential, delay and liquidated damages contained in the Work Authorization are expressly covered by and made a part of this Performance, Labor and Material Payment Bond. Principal and Surety acknowledge that any such provisions lie within their obligations and within the policy coverage's and limitations of this instrument.

5. Section 255.05, Florida Statutes, as amended, together with all notice and time provisions contained therein, is incorporated herein, by reference, in its entirety. Any action instituted by a claimant under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2), Florida Statutes. This instrument regardless of its form, shall be construed and deemed a statutory bond issued in accordance with Section 255.05, Florida Statutes.

6. Any action brought under this instrument shall be brought in the state court of competent jurisdiction in Palm Beach County, Florida and not elsewhere.

Emily Meng
Witness

Emily Meng
Print name

Juliana Losardo
Witness

Juliana Losardo
Print name

[Signature]
Principal

Chase R. Rogers
Print name

Project Director
Title

[Signature]
Surety (Seal)



Augusta M. Godinho
Print name

Attorney in Fact
Title



HALCYON UNDERWRITERS

YOUR PARTNER IN PRODUCTION. MAKING THE DIFFERENCE

2301 Lucien Way, Suite 360
Maitland, FL 32751

September 11, 2019

To: Palm Beach County
8100 Forest Hill Boulevard
West Palm Beach, FL 33413

Re: Hinterland Group Inc.
Bond No: 21BCSIE4088
WUD: 18-063/ Work Authorization No. 22
Resolution #: R2017-0072

To Whom It May Concern

Please allow this letter to serve as formal authorization for Palm Beach County Water Utilities Department to date the captioned Construction Bond and power of attorney to coincide with the Contract Date. Please advise our office once dated. We are the bonding agent for Hinterland Group, Inc. They are bonded by Hartford Accident and Indemnity Company, an A+ rated surety in the AM Best Guide. Please be advised that we authorize you to date powers of attorney, form of guarantee and bonds for WUD: 18-063 / Work Authorization No. 22. 12-inch Force Main on Sandalfoot Blvd. Thank you and please call me if you have any questions.

Attorney-in-Fact

Augusta M. Godinho

Print Name

ATTACHMENT D

FORM OF GUARANTEE

GUARANTEE FOR (Contractor and Surety Name) Hinterland Group Inc. and Hartford Accident & Indemnity Company

We the undersigned hereby guarantee that the **Pipeline Continuing Construction Contract 2017, Contract Resolution No. R2017-0072, Contract Dated January 10, 2017, WUD Project No. 18-063, Work Authorization No. 22, Project Title: 12-inch Force Main on Sandalfoot Blvd., Palm Beach County, Florida**, which we have constructed and bonded, has been done in accordance with the plans and specifications; that the work constructed will fulfill the requirements of the guaranties included in the Contract Documents. We agree to repair or replace any or all of our work, together with any work of others which may be damaged in so doing, that may prove to be defective in the workmanship or materials within a period of one year from the date of Final Completion of all of the above named work by the County of Palm Beach, State of Florida, without any expense whatsoever to said County of Palm Beach, ordinary wear and tear and unusual abuse or neglect excepted by the County. The date of Final Completion shall be the date set forth on the fully executed and acknowledged Contractor's Certification of Final Completion form. When correction work is started, it shall be carried through to completion.

In the event of our failure to acknowledge notice, and commence corrections of defective work within five (5) calendar days after being notified in writing by the Board of County Commissioners, Palm Beach County, Florida, we, collectively or separately, do hereby authorize Palm Beach County to proceed to have said defects repaired and made good at our expense and we will honor and pay the costs and charges therefore upon demand.

County and Contractor agree that the provisions of Florida Statute Chapter 558 shall not apply to this Contract/Agreement.

SEAL AND NOTARIAL ACKNOWLEDGMENT OF SURETY

Hinterland Group Inc. (Seal)
(Contractor)

By: _____
(Signature)

Chase R. Rogers
(Printed Name)

Hartford Accident & Indemnity Company (Seal)
(Surety)

By: _____
(Signature)

Augusta M. Godinho
(Printed Name)

POWER OF ATTORNEY

Direct Inquiries/Claims to:

THE HARTFORD
 BOND, T-12
 One Hartford Plaza
 Hartford, Connecticut 06155
 Bond.Claims@thehartford.com

call: 888-266-3488 or fax: 860-757-5835

KNOW ALL PERSONS BY THESE PRESENTS THAT:

Agency Name: HALCYON UNDERWRITERS
 Agency Code: 21-224119

- Hartford Fire Insurance Company, a corporation duly organized under the laws of the State of Connecticut
- Hartford Casualty Insurance Company, a corporation duly organized under the laws of the State of Indiana
- Hartford Accident and Indemnity Company, a corporation duly organized under the laws of the State of Connecticut
- Hartford Underwriters Insurance Company, a corporation duly organized under the laws of the State of Connecticut
- Twin City Fire Insurance Company, a corporation duly organized under the laws of the State of Indiana
- Hartford Insurance Company of Illinois, a corporation duly organized under the laws of the State of Illinois
- Hartford Insurance Company of the Midwest, a corporation duly organized under the laws of the State of Indiana
- Hartford Insurance Company of the Southeast, a corporation duly organized under the laws of the State of Florida

having their home office in Hartford, Connecticut, (hereinafter collectively referred to as the "Companies") do hereby make, constitute and appoint, **up to the amount of** Unlimited :

Paul C. Lyons III, Katherine A. Lee, Augusta M. Godinho of MAITLAND, Florida

their true and lawful Attorney(s)-in-Fact, each in their separate capacity if more than one is named above, to sign its name as surety(ies) only as delineated above by , and to execute, seal and acknowledge any and all bonds, undertakings, contracts and other written instruments in the nature thereof, on behalf of the Companies in their business of guaranteeing the fidelity of persons, guaranteeing the performance of contracts and executing or guaranteeing bonds and undertakings required or permitted in any actions or proceedings allowed by law.

In Witness Whereof, and as authorized by a Resolution of the Board of Directors of the Companies on May 6, 2015 the Companies have caused these presents to be signed by its Senior Vice President and its corporate seals to be hereto affixed, duly attested by its Assistant Secretary. Further, pursuant to Resolution of the Board of Directors of the Companies, the Companies hereby unambiguously affirm that they are and will be bound by any mechanically applied signatures applied to this Power of Attorney.



John Gray

John Gray, Assistant Secretary

M. Ross Fisher

M. Ross Fisher, Senior Vice President

STATE OF CONNECTICUT }
 COUNTY OF HARTFORD } ss. Hartford

On this 5th day of January, 2018, before me personally came M. Ross Fisher, to me known, who being by me duly sworn, did depose and say: that he resides in the County of Hartford, State of Connecticut; that he is the Senior Vice President of the Companies, the corporations described in and which executed the above instrument; that he knows the seals of the said corporations; that the seals affixed to the said instrument are such corporate seals; that they were so affixed by authority of the Boards of Directors of said corporations and that he signed his name thereto by like authority.



CERTIFICATE

Kathleen T. Maynard

Kathleen T. Maynard
 Notary Public

My Commission Expires July 31, 2021

I, the undersigned, Assistant Vice President of the Companies, DO HEREBY CERTIFY that the above and foregoing is a true and correct copy of the Power of Attorney executed by said Companies, which is still in full force effective as of September 11th, 2019
 Signed and sealed at the City of Hartford.



Kevin Heckman

Kevin Heckman, Assistant Vice President

ATTACHMENT E

SCHEDULE OF BID ITEMS

Palm Beach County Water Utilities Department
Pipeline Continuing Construction Contract 2017 – Resolution R2017-0072 Contract Dated January 10, 2017

Work Authorization No.: 22
Contractor Name: Hinterland Group Inc.
Project Name: 12-inch Force Main on Sandalfoot Blvd.
WUD Project No.: 18-063

NO.	BID ITEM (Furnish and Install with Appurtenances)	TOTAL QUANTITIES	UNIT	UNIT PRICE	TOTAL
13	12" PVC Push-On Joint Water Main/Wastewater Force Main/Reclaimed Water Main	940.00	L.F.	\$40.00	\$37,600.00
15	12" DIP Push-On Joint Wastewater Force Main	135.00	L.F.	\$75.00	\$10,125.00
30	Ductile Iron Fittings for Wastewater Force Main	2.10	Tons	\$11,000.00	\$23,100.00
62	12" Mechanical Joint Restraint for DIP	12.00	Each	\$450.00	\$5,400.00
70	12" Mechanical Joint Restraint for PVC	30.00	Each	\$450.00	\$13,500.00
87	12" PVC Pressure Pipe Restraint Harness	14.00	Each	\$290.00	\$4,060.00
97	Restrain existing 12" PVC Pressure Pipe	6.00	Each	\$1,200.00	\$7,200.00
106	12" Gate Valve & Valve Box	1.00	Each	\$2,200.00	\$2,200.00
187	4" to 12" Diameter Connection to Existing Water Main/Reclaimed Water Main or Force Main (Joint Restraint for existing pipe to be included)	2.00	Each	\$2,800.00	\$5,600.00
195	Milling of Asphalt (Minimum 220 Sq. Yd. per mobilization - 1.5" thick)	1867.00	Sq. Yd.	\$15.00	\$28,005.00
197	Asphalt Overlay, Type S-III (20 to 150 tons per work area)	108.00	Tons	\$245.00	\$26,460.00
198	Asphalt Roadway Removal and Restoration (2.5" thick)	340.00	Sq. Yd.	\$65.00	\$22,100.00
200	Asphalt Driveway Removal and Restoration (1.5" thick)	36.00	Sq. Yd.	\$65.00	\$2,340.00
205	Limerock/Shell Driveway or Roadway Removal and Restoration	40.000	Tons	\$30.00	\$1,200.00
207	Concrete Sidewalk Removal & Restoration	322.00	Sq. Yd.	\$50.00	\$16,100.00
208	Concrete Curb & Gutter Removal & Restoration	100.00	L.F.	\$40.00	\$4,000.00
210	Floratom Sod	700.00	Sq. Yd.	\$4.00	\$2,800.00
214	Record Drawing	1060.00	L.F.	\$2.00	\$2,120.00
215	Construction Survey	1060.00	L.F.	\$2.00	\$2,120.00
216	Preconstruction Video Taping	1200.00	L.F.	\$1.00	\$1,200.00
218	Maintenance of Traffic Residential Street	1200.00	L.F.	\$1.50	\$1,800.00
221	Density Tests	25.00	Each	\$30.00	\$750.00
222	Proctor Tests	2.00	Each	\$90.00	\$180.00
223	Concrete 12"x6" Cylinder Tests	6.00	Each	\$100.00	\$600.00
234	ADA Concrete Ramps per FDOT Index 304 (Include Ramp, Curb and Detectable Warning)	4.00	Each	\$1,800.00	\$7,200.00
269	Silt Fence	1200.00	L.F.	\$2.00	\$2,400.00
SUBTOTAL BASE BID PRICE (Item 1-269)					\$230,160.00

NO.	ADDITIONAL WORK/MOBILIZATION/DEMOLITION	TOTAL QUANTITIES	UNIT	UNIT PRICE	TOTAL
287	Additional work not included in Bid Items (Max 15% of Subtotal Base Bid Price)	1.00	Lump Sum	\$0.00	\$0.00
288	Mobilization (2.5% of Subtotal Base Bid Price)	1	Lump Sum	2.5%	\$5,754.00
289	Demobilization (1.0% of Subtotal Base Bid Price)	1	Lump Sum	1.0%	\$2,301.60
SUBTOTAL ADDITIONAL WORK/MOBILIZATION/DEMOLITION BID PRICE (Item 287-289)					\$8,055.60
TOTAL BID PRICE					\$238,215.60

Revised 8-29-19

ATTACHMENT F

OEBO SCHEDULE 1

Office of Equal Business Opportunity Compliance Programs

Revised 8-29-19

ATTACHMENT F
OEBO SCHEDULE 2

Office of Equal Business Opportunity Compliance Programs

Revised 8-29-19

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All Subcontractors/subconsultants, including any tiered Subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: 18-063

SOLICITATION/PROJECT NAME: 12-inch Force Main on Sandalfoot Blvd.

Name of Prime: Hinterland Group Inc.

(Check box(s) that apply)

SBE WBE MBE M/WBE Non-S/M/WBE Date of Palm Beach County Certification (if applicable): 12/10/15-12/9/18

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

Male Female African-American/Black Asian American Caucasian American
 Hispanic American Native American


S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.


Line Item	Item Description	Unit Price	Quantity/ Units	Contingencies/ Allowances	Total Price/Percentage
	See Attachment E				\$238,215.60 / 100.00%

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$238,215.60 / 100.00%

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

N/A Price or Percentage: _____
 Name of 2nd/3rd tier Subcontractor/subconsultant

Hinterland Group Inc.
 Print Name of Prime
 By: 
 Authorized Signature
Chase R. Rogers
 Print Name
Project Director
 Title
 Date: 9/13/19

Hinterland Group Inc.
 Print Name of Subcontractor/subconsultant
 By: 
 Authorized Signature
Chase R. Rogers
 Print Name
Project Director
 Title
 Date: 9/13/19

ATTACHMENT E

SCHEDULE OF BID ITEMS

Palm Beach County Water Utilities Department

Pipeline Continuing Construction Contract 2017 – Resolution R2017-0072 Contract Dated January 10, 2017

Work Authorization No.: 22

Contractor Name: Hinterland Group Inc.

Project Name: 12-inch Force Main on Sandalfoot Blvd.

WUD Project No.: 18-063

<u>NO.</u>	<u>BID ITEM (Furnish and Install with Appurtenances)</u>	<u>TOTAL QUANTITIES</u>	<u>UNIT</u>	<u>UNIT PRICE</u>	<u>TOTAL</u>
13	12" PVC Push-On Joint Water Main/Wastewater Force Main/Reclaimed Water Main	940.00	L.F.	\$40.00	\$37,600.00
15	12" DIP Push-On Joint Wastewater Force Main	135.00	L.F.	\$75.00	\$10,125.00
30	Ductile Iron Fittings for Wastewater Force Main	2.10	Tons	\$11,000.00	\$23,100.00
62	12" Mechanical Joint Restraint for DIP	12.00	Each	\$450.00	\$5,400.00
70	12" Mechanical Joint Restraint for PVC	30.00	Each	\$450.00	\$13,500.00
87	12" PVC Pressure Pipe Restraint Harness	14.00	Each	\$290.00	\$4,060.00
97	Restrain existing 12" PVC Pressure Pipe	6.00	Each	\$1,200.00	\$7,200.00
106	12" Gate Valve & Valve Box	1.00	Each	\$2,200.00	\$2,200.00
187	4" to 12" Diameter Connection to Existing Water Main/Reclaimed Water Main or Force Main (Joint Restraint for existing pipe to be included)	2.00	Each	\$2,800.00	\$5,600.00
195	Milling of Asphalt (Minimum 220 Sq. Yd. per mobilization - 1.5" thick)	1867.00	Sq. Yd.	\$15.00	\$28,005.00
197	Asphalt Overlay, Type S-III (20 to 150 tons per work area)	108.00	Tons	\$245.00	\$26,460.00
198	Asphalt Roadway Removal and Restoration (2.5" thick)	340.00	Sq. Yd.	\$65.00	\$22,100.00
200	Asphalt Driveway Removal and Restoration (1.5" thick)	36.00	Sq. Yd.	\$65.00	\$2,340.00
205	Limerock/Shell Driveway or Roadway Removal and Restoration	40.000	Tons	\$30.00	\$1,200.00
207	Concrete Sidewalk Removal & Restoration	322.00	Sq. Yd.	\$50.00	\$16,100.00
208	Concrete Curb & Gutter Removal & Restoration	100.00	L.F.	\$40.00	\$4,000.00
210	Floratom Sod	700.00	Sq. Yd.	\$4.00	\$2,800.00
214	Record Drawing	1060.00	L.F.	\$2.00	\$2,120.00
215	Construction Survey	1060.00	L.F.	\$2.00	\$2,120.00
216	Preconstruction Video Taping	1200.00	L.F.	\$1.00	\$1,200.00
218	Maintenance of Traffic Residential Street	1200.00	L.F.	\$1.50	\$1,800.00
221	Density Tests	25.00	Each	\$30.00	\$750.00
222	Proctor Tests	2.00	Each	\$90.00	\$180.00
223	Concrete 12"x6" Cylinder Tests	6.00	Each	\$100.00	\$600.00
234	ADA Concrete Ramps per FDOT Index 304 (Include Ramp, Curb and Detectable Warning)	4.00	Each	\$1,800.00	\$7,200.00
269	Silt Fence	1200.00	L.F.	\$2.00	\$2,400.00
SUBTOTAL BASE BID PRICE (Item 1-269)					\$230,160.00

<u>NO.</u>	<u>ADDITIONAL WORK/MOBILIZATION/DEMOBILIZATION</u>	<u>TOTAL QUANTITIES</u>	<u>UNIT</u>	<u>UNIT PRICE</u>	<u>TOTAL</u>
287	Additional work not included in Bid Items (Max 15% of Subtotal Base Bid Price)	1.00	Lump Sum	\$0.00	<u>\$0.00</u>
288	Mobilization (2.5% of Subtotal Base Bid Price)	1	Lump Sum	2.5%	\$5,754.00
289	Demobilization (1.0% of Subtotal Base Bid Price)	1	Lump Sum	1.0%	\$2,301.60
SUBTOTAL ADDITIONAL WORK/MOBILIZATION/DEMOBILIZATION BID PRICE (Item 287-289)					\$8,055.60
TOTAL BID PRICE					\$238,215.60

Revised 8-29-19

ATTACHMENT G


**Palm Beach County Water Utilities Department
Pipeline Continuing Construction Contract 2017
Resolution #R2017-0072 Contract Dated January 10, 2017**

**SUMMARY OF
SBE-M/WBE MINORITY BUSINESS TRACKING**

Master Contract Goal <u>15.00%</u>	SBE
Current Proposal	
Value of Authorization No. <u>22</u>	\$238,215.60
Value of SBE-M/WBE Letters of Intent	\$238,215.60
Actual Percentage	<u>100.00%</u>
Signed/Approved Authorizations	
Total Value of Authorizations	\$8,308,140.12
Total Value of SBE-M/WBE Signed Subcontracts	\$8,308,140.12
Actual Percentage	<u>100.00%</u>
Signed/Approved Authorizations Plus Current Proposal	
Total Value of Authorization	\$8,546,355.72
Total Value of Subcontracts & Letters of Intent	\$8,546,355.72
Actual Percentage	<u>100.00%</u>

Revised 8-29-19



ATTACHMENT H
Project Location
 WORK AUTHORIZATION NO. 22
 HINTERLAND GROUP INC.
 WUD PROJECT NO. 18-063

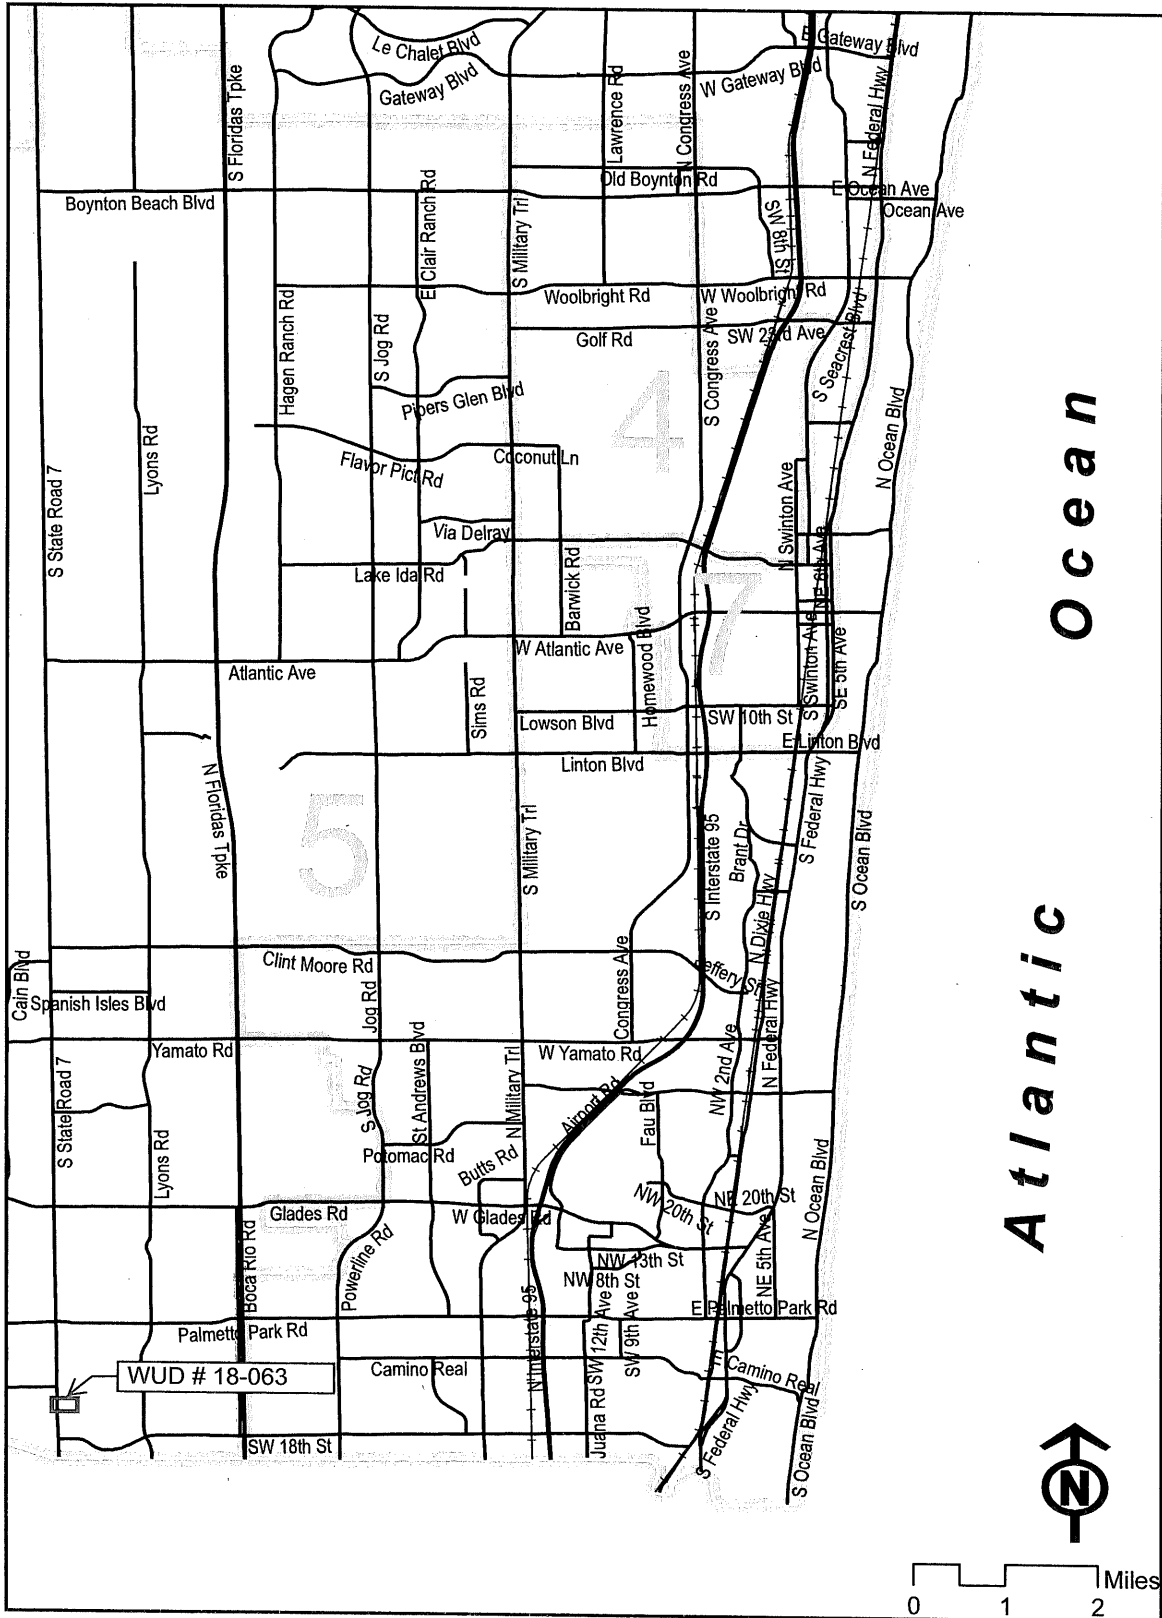

Location Sketch

Project Location

WORK AUTHORIZATION NO. 22
HINTERLAND GROUP INC.
WUD PROJECT NO. 18-063

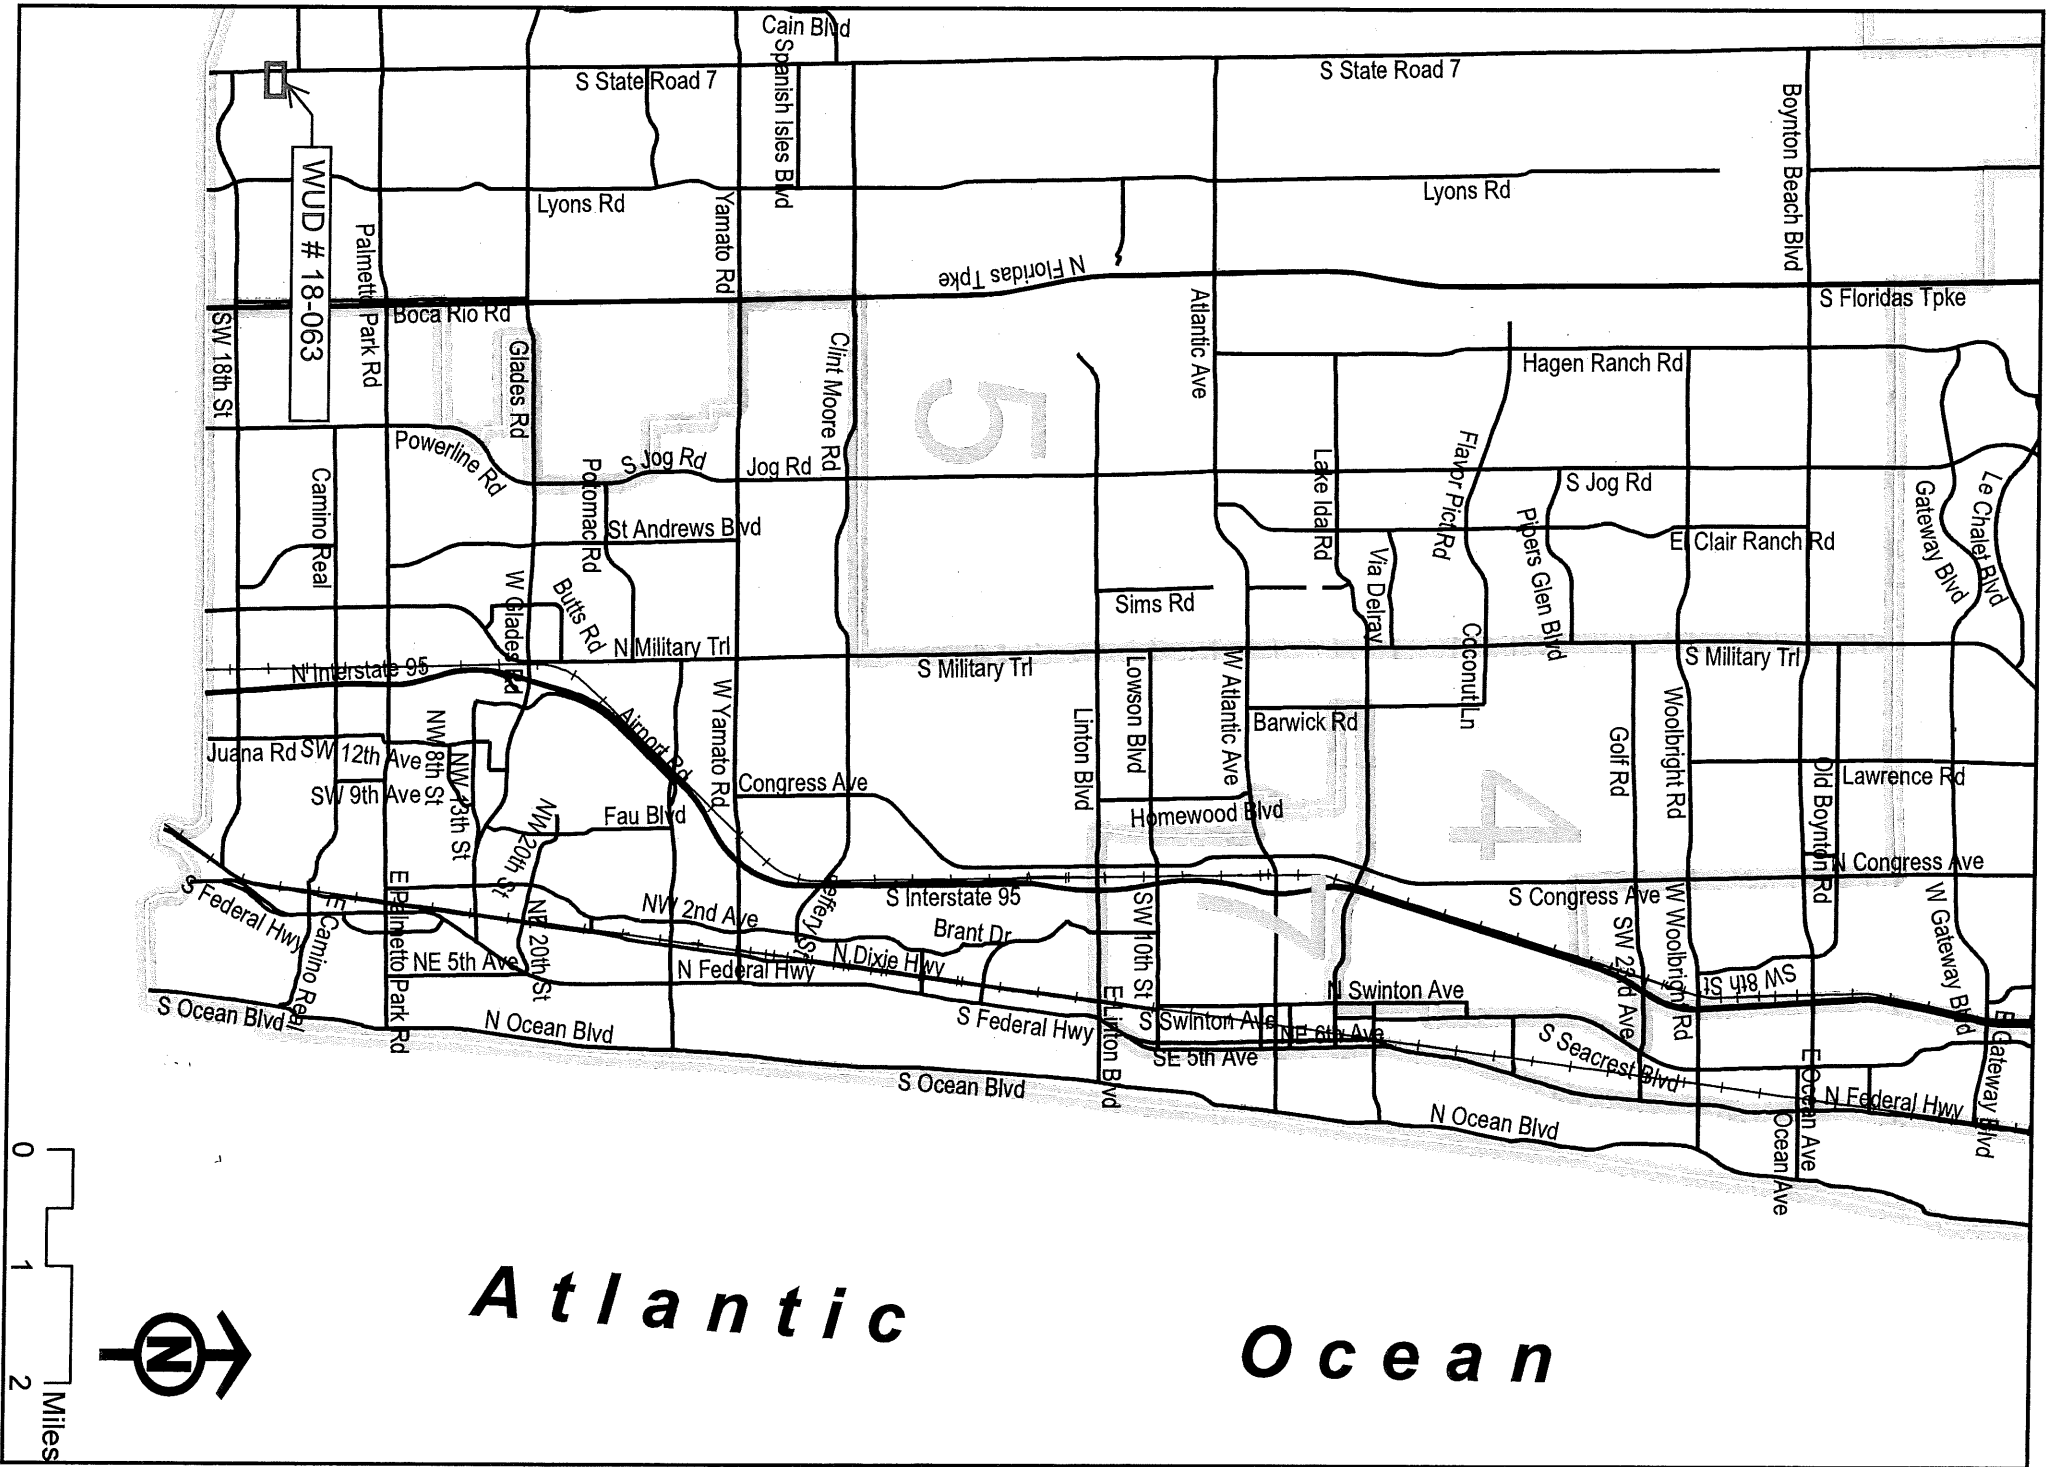

Location Sketch

ATTACHMENT 3



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
01/30/2019

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER South Shore Insurance Inc. 955 SE Central Parkway Stuart, FL 34994		CONTACT NAME: Jennie Lanman PHONE (A/C, No, Ext): (772) 426-9973 FAX (A/C, No): (772) 221-1960 E-MAIL ADDRESS: jennie@southshore-insurance.com	
INSURED		INSURER(S) AFFORDING COVERAGE	
Hinterland Group Inc. 2051 W Blue Heron Blvd Riviera Beach, FL 33404		INSURER A : Hartford Casualty Insurance Company INSURER B : Property & Casualty Ins Comp of The Hartford INSURER C : Sentinel Insurance Compsny INSURER D : Hartford Fire Insurance Company INSURER E : The North River Insurance Company INSURER F :	NAIC # 29424 34690 11000 19682 21105

COVERAGES **CERTIFICATE NUMBER:** **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSTR	TYPE OF INSURANCE	ADDL INSD	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<input checked="checked" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="checked" type="checkbox"/> OCCUR <input checked="checked" type="checkbox"/> XCU Coverage Included GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="checked" type="checkbox"/> PROJECT <input type="checkbox"/> LOC OTHER:	Y	Y	21 UEA HF5360	01/31/2019	01/31/2020	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Per occurrence) \$ 50,000 MED EXP (Any one person) \$ 5,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COMP/OP AGG \$ 2,000,000 \$
B	AUTOMOBILE LIABILITY <input checked="checked" type="checkbox"/> ANY AUTO ALL OWNED AUTOS <input checked="checked" type="checkbox"/> HIRED AUTOS <input checked="checked" type="checkbox"/> SCHEDULED AUTOS NON-OWNED AUTOS	Y	Y	21 UEA HF5507	01/31/2019	01/31/2020	COMBINED SINGLE LIMIT (Per accident) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ \$
E	<input checked="checked" type="checkbox"/> UMBRELLA LIAB <input checked="checked" type="checkbox"/> OCCUR <input checked="checked" type="checkbox"/> EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED RETENTION \$			582-109804-8	01/31/2019	01/31/2020	EACH OCCURRENCE \$ 10,000,000 AGGREGATE \$ 10,000,000 \$
C	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below	Y	N/A	21 WBA AB0MTJ	01/31/2019	01/31/2020	<input checked="checked" type="checkbox"/> PER STATUTE <input type="checkbox"/> OTHER E.L. EACH ACCIDENT \$ 1,000,000 E.L. DISEASE - EA EMPLOYEE \$ 1,000,000 E.L. DISEASE - POLICY LIMIT \$ 1,000,000
D	Inland Marine	Y		21UUMHF5845	01/31/2019	01/31/2020	Transit Coverage \$2,000,000 Rented/Leased Equi \$300,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)
 The Board of County Commissioners, Palm Beach County, Florida (a political subdivision of the State of Florida) is hereby named as additional insured under the terms of the policy on blanket form when required by written contract/agreement with the insured executed prior to injury or damage. Palm Beach County Water Utilities Department, its officers, directors, agents and employees are hereby named as additional insured on blanket form under the terms of this policy when required by written contract/agreement with the insured executed prior to injury or damage. The engineer, its officers, agents, and employees are hereby named as additional insured under the terms of this policy when required by written contract/agreement with the insured executed prior to injury or damage. A Waiver of subrogation on blanket form is also provided when required by written contract/agreement with the insured executed prior to injury or damage. Certificate holder is also listed as additional insured/loss payee with respect to inland marine transit coverage on blanket form when required by written contract/agreement with the insured executed prior to injury or damage. (Additional insured and waiver of subrogation in accordance with policy form HCG00010916). WUD Contract #: 16-077

CERTIFICATE HOLDER		CANCELLATION	
Palm Beach County Water Utilities Dept Director Utilities Engineering 8100 Forest Hill Blvd West Palm Beach, FL 33413		SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.	
		AUTHORIZED REPRESENTATIVE 	



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
09/23/2019

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER South Shore Insurance Inc. 955 SE Central Parkway Stuart FL 34994	CONTACT NAME: Jennie Lanman
	PHONE (A/C, No, Ext): (772) 426-9973 FAX (A/C, No): 772-872-5870 E-MAIL ADDRESS: jennie@southshore-insurance.com
INSURED Hinterland Group Inc. 2051 W Blue Heron Blvd Riviera Beach, FL 33404	INSURER(S) AFFORDING COVERAGE
	INSURER A : The Hartford NAIC # 29424
	INSURER B :
	INSURER C :
	INSURER E :

COVERAGES CERTIFICATE NUMBER: REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSD	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
	COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC OTHER:						EACH OCCURRENCE \$ DAMAGE TO RENTED PREMISES (Ea occurrence) \$ MED EXP (Any one person) \$ PERSONAL & ADV INJURY \$ GENERAL AGGREGATE \$ PRODUCTS - COMP/OP AGG \$
	AUTOMOBILE LIABILITY <input type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> HIRED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> NON-OWNED AUTOS						COMBINED SINGLE LIMIT (Ea accident) \$ BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$
	UMBRELLA LIAB <input type="checkbox"/> OCCUR EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED RETENTION \$						EACH OCCURRENCE \$ AGGREGATE \$
	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) <input type="checkbox"/> Y/N N/A If yes, describe under DESCRIPTION OF OPERATIONS below						PER STATUTE <input type="checkbox"/> OTH-ER <input type="checkbox"/> E.L. EACH ACCIDENT \$ E.L. DISEASE - EA EMPLOYEE \$ E.L. DISEASE - POLICY LIMIT \$
A	Builders Risk	Y		21MSJA9457	07/14/2019	07/14/2020	Blanket Limit \$10,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Palm Beach County, its officers, directors, agents and employees are hereby named as additional insured on blanket form under the terms of this policy when required by written contract/agreement with the insured executed prior to injury or damage

Project: 16-077

5% wind/hail and \$5,000 all other deductible. This policy is on an All Risk form with 100% replacement cost.

CERTIFICATE HOLDER Palm Beach County / Water Utilities Dept. Director Utilities Engineering 8100 Forest Hill Blvd West Palm Beach, FL 33413	CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
	AUTHORIZED REPRESENTATIVE <i>Jennie Lanman</i> <JNL>
