

WORK AUTHORIZATION NO. 7
Palm Beach County Water Utilities Department
Lift Station Rehabilitation Continuing Construction Contract 2020
Resolution No. R2020-1379 Contract Dated September 15, 2020

Project Title: Finrock Lift Station and Force Main Rehabilitation

PBCWUD Project No.: 22-002

Contractor: Hinterland Group Inc.

Address: 2051 West Blue Heron Blvd., Riviera Beach, FL 33404

Budget Line Item No.: 4011-721-W031-6546

District No.: 6

This Work Authorization provides for: Construction Services for the replacement of 2,800 linear feet of 8-inch force main from the connection point at the new Finrock force main aerial crossing to the existing 10-inch ductile iron force main on the west side of SR 715 in Belle Glade.

(See ATTACHMENT A for detailed scope of services)

The Contract provides for 26.87% SBE participation, which includes 3.47% M/WBE participation, 3.18% MBE (H), and 0.29% WBE.

This Work Authorization includes 13.04% overall participation which includes, 4.22% M/WBE participation, 4.22% MBE (H), and 0.00% WBE.

The cumulative SBE participation, including this Work Authorization is 11.09%, which includes 5.64% M/WBE participation, 5.56% MBE (H), and 0.07% WBE.

1. Services completed by the Contractor to date :

See ATTACHMENT B.

2. Contractor shall begin work within ten (10) calendar days from the issuance of Notice to Proceed (NTP). Execution of the Project will be accomplished as follows from the issuance of the NTP:

Substantial Completion 180 Calendar Days

Final Completion 210 Calendar Days

Liquidated damages will apply as follows:

\$500.00 per day past substantial completion date.

\$250.00 per day past final completion date.

WORK AUTHORIZATION NO. 7
Palm Beach County Water Utilities Department
Lift Station Rehabilitation Continuing Construction Contract 2020
Resolution No. R2020-1379 Contract Dated September 15, 2020

Project Title: Finrock Lift Station and Force Main Rehabilitation

PBCWUD Project No.: 22-002

3. The compensation to be paid to the Contractor for providing the requested services in accordance with the Contract Bid Prices is \$493,128.25.

4. The Work Authorization does not amend, change, or modify the Contract which remains in full force and effect.

5. All Attachments to this Authorization are incorporated herein and made a part of this Work Authorization.

--	--	--

WORK AUTHORIZATION NO. 7
Palm Beach County Water Utilities Department
Lift Station Rehabilitation Continuing Construction Contract 2020
Resolution No. R2020-1379 Contract Dated September 15, 2020

Project Title: Finrock Lift Station and Force Main Rehabilitation

PBCWUD Project No.: 22-002

IN WITNESS WHEREOF, this Work Authorization is accepted, subject to the terms, conditions and obligations of the aforementioned Contract.

PALM BEACH COUNTY, A POLITICAL SUBDIVISION OF THE STATE OF FLORIDA

Joseph Abruzzo, Clerk of the Circuit Court
& Comptroller, Palm Beach County

Palm Beach County, Board
of County Commissioners

ATTEST:

Signed: _____

HW

Signed: _____
Robert S. Weinroth, Mayor

A13

Typed Name: _____
Deputy Clerk

(Date)

Approved as to Form and Legal
Sufficiency

Hinterland Group Inc.
(Contractor)

Signed: _____

Chase Rogers
(Print Name)

Typed Name: Michael W. Jones
County Attorney

(Signature)

Project Director
(Title)

3/22/2022
(Date)



STATE OF FLORIDA
COUNTY OF Palm Beach

The foregoing instrument was acknowledged before me by means of physical presence or online notarization, this 22 day of March, 2022, by Chase Rogers who is personally known to me or has produced N/A as identification.



GEANA M. STEWART
Commission # HH 015896
Expires June 29, 2024
Bonded Thru Budget Notary Services

Geana M. Stewart
(Signature of Notary Public - State of Florida)

Geana M. Stewart
(Print, Type, or Stamp Commissioned Name of Notary Public)



January 26, 2022

To whom it may concern:

I, Daniel Duke, III, President of Hinterland Group Inc., do hereby authorize Chase Rogers and Jay Breig to sign any and all project related documents on behalf of Hinterland Group Inc.

In addition, and until further notice, the following personnel are authorized to sign pay applications and supporting documentation relating to Palm Beach County pay applications. This does not authorize the signing of change orders, supplements, lien releases, notice to proceed, warranties of title or Final pay applications or relating documents.

Authorized to Sign Pay Applications and Supporting Documentation for Pay Applications:

- Butch Forrester
- Jacob Crowe
- Kervin Flores-Garcia
- Nelson Bello

Daniel Duke, III – President

Dated: January 26, 2022

State of Florida
County of Palm Beach

The foregoing instrument was acknowledged before me by means of [] physical presence or [] online notarization this 26 day of January, 2022 by Daniel Duke, III who is personally known to me [] or had produced a [] n/a as identification.

Notary Public Geana M. Stewart

My Commission Expires 06/29/2024



GEANA M. STEWART
Commission # HH 015896
Expires June 29, 2024
Bonded Thru Budget Notary Service

Hinterland Group Inc. Corporate Office

2051 W Blue Heron Blvd. Riviera Beach, FL 33404 • Ph 561-640-3503 • Fax 561-640-3504

--	--	--	--

LIST OF ATTACHMENTS

ATTACHMENT A	Scope of Work
ATTACHMENT B	Summary and Status of Work Authorizations
ATTACHMENT C	Public Construction Bond
ATTACHMENT D	Form of Guarantee
ATTACHMENT E	Schedule of Bid Items
ATTACHMENT F	OEBO Schedule 1 and 2
ATTACHMENT G	Summary of SBE-M/WBE Business Tracking
ATTACHMENT H	Location Map

--	--	--	--

ATTACHMENT C

PUBLIC CONSTRUCTION BOND – WORK AUTHORIZATION NO. 7
Lift Station Rehabilitation Continuing Construction Contract 2020
Resolution No. R2020-1379 Contract Dated September 15, 2020

PROJECT TITLE: Finfrock Lift Station and Force Main Rehabilitation

PBCWUD PROJECT NO.: 22-002

BOND NUMBER: 21BCSIU2276

WORK AUTHORIZATION/BOND AMOUNT: \$493,128.25

CONTRACTOR'S NAME: Hinterland Group Inc.

CONTRACTOR'S ADDRESS: 2051 West Blue Heron Blvd., Riviera Beach, FL 33404

CONTRACTOR'S PHONE: (561) 640-3503

SURETY COMPANY: Hartford Accident and Indemnity Company

SURETY'S ADDRESS: 2301 Lucien Way, #360, Maitland, FL 32751

OWNER'S NAME: PALM BEACH COUNTY

OWNER'S ADDRESS: 8100 Forest Hill Boulevard
West Palm Beach, FL 33413

OWNER'S PHONE: (561) 493-6000

DESCRIPTION OF WORK: Installation of force main pipe

PROJECT LOCATION: Orange Ave Circle.

LEGAL DESCRIPTION: S19-T43-R37

Revised 12/06/2021

PUBLIC CONSTRUCTION BOND

This Bond is issued in favor of the County conditioned on the full and faithful performance of the Work Authorization No. 7 to Lift Station Rehabilitation Continuing Construction Contract 2020 Contract Resolution No. R2020-1379 dated on September 15, 2020.

KNOW ALL MEN BY THESE PRESENTS: that Contractor and Surety, are held and firmly bound unto

Palm Beach County Board of County Commissioners
301 N. Olive Avenue
West Palm Beach, Florida 33401

as Obligee, herein called County, for the use and benefit of claimant as herein below defined, in the amount of

Four Hundred Ninety-Three Thousand One Hundred Twenty-Eight Dollars and Twenty-Five Cents, \$493,128.25.

for the payment whereof Principal and Surety bind themselves, their heirs, personal representatives, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

WHEREAS,

Principal has by written agreement dated _____, 20____, entered into Work Authorization No. 7 to Lift Station Rehabilitation Continuing Construction Contract 2020 Contract Resolution No. R2020-1379 with the County for

Work Authorization Project Name: Finrock Lift Station and Force Main Rehabilitation

Work Authorization Project No.: 22-002

Project Description: Installation of force main pipe

Project Location: Orange Ave Circle.

in accordance with Design Criteria Drawings and Specifications prepared by

Name of Design Firm: Holtz Consulting Engineers, Inc.

Location of Firm: 270 South Central Blvd., Suite 207, Jupiter, FL 33458

Phone: (561) 575-2005

Fax: (561) 575-2009


which Work Authorization No. 7 to Lift Station Rehabilitation Continuing Construction Contract 2020 Contract Resolution No. R2020-1379 is by reference made a part hereof in its entirety, and is hereinafter referred to as the Work Authorization.

- 1. THE CONDITION OF THIS BOND is that if Principal:
 - a. Performs the Work Authorization dated _____, 20____, between Principal and County for the construction of the above project, the Work Authorization being made a part of this bond by reference, at the times and in the manner prescribed in the Work Authorization; and


Revised 12/06/2021



- b. Promptly makes payments to all claimants, as defined in Section 255.05, Florida Statutes, supplying Principal with labor, materials, or supplies, used directly or indirectly by Principal in the prosecution of the work provided for in the Work Authorization; and
 - c. Pays County all losses, damages (including liquidated damages), expenses, costs, and attorneys' fees, including appellate proceedings, that County sustains because of a default by Principal under the Work Authorization; and
 - d. Performs the guarantee of all work and materials furnished under the Work Authorization for the time specified in the Work Authorization; then this bond is void; otherwise it remains in full force.
2. Any changes in or under the contract documents and compliance or noncompliance with any formalities connected with the Work Authorization or the changes does not affect Surety's obligation under this bond and Surety waives notice of such changes.
 3. The amount of this bond shall be reduced by and to the extent of any payment or payments made in good faith hereunder, inclusive of the payment by Surety of construction liens which may be filed of record against said improvement, whether or not claim for the amount of such lien be presented under and against the bond.
 4. Principal and Surety expressly acknowledge that any and all provisions relating to consequential, delay and liquidated damages contained in the Work Authorization are expressly covered by and made a part of this Performance, Labor and Material Payment Bond. Principal and Surety acknowledge that any such provisions lie within their obligations and within the policy coverage's and limitations of this instrument.
 5. Section 255.05, Florida Statutes, as amended, together with all notice and time provisions contained therein, is incorporated herein, by reference, in its entirety. Any action instituted by a claimant under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2), Florida Statutes. This instrument regardless of its form, shall be construed and deemed a statutory bond issued in accordance with Section 255.05, Florida Statutes.
 6. Any action brought under this instrument shall be brought in the state court of competent jurisdiction in Palm Beach County, Florida and not elsewhere.




 (Witness)
 Daniel Duke III

 (Print Name)


 (Witness)
 Jay Breig


 (Print Name)

Hinterland Group Inc.



 (Principal)
 Chase Rogers

 (Print Name)
 Project Director

 (Title)



Hartford Accident and Indemnity Company

 (Surety) (seal)


 (Print Name) Jennie N. Lanman
 Attorney - in - Fact

 (Title)

ATTACHMENT D

FORM OF GUARANTEE

GUARANTEE FOR (Contractor and Surety Name) Hinterland Group Inc. and Hartford Accident and Indemnity Company


We the undersigned hereby guarantee that the Lift Station Rehabilitation Continuing Construction Contract 2020 Contract, Resolution No. R2020-1379, Contract Dated September 15, 2020, PBCWUD Project No. 22-002, Work Authorization No. 7, Project Title: Finfrack Lift Station and Force Main Rehabilitation, Palm Beach County, Florida, which we have constructed and bonded, has been done in accordance with the plans and specifications; that the work constructed will fulfill the requirements of the guaranties included in the Contract Documents. We agree to repair or replace any or all of our work, together with any work of others which may be damaged in so doing, that may prove to be defective in the workmanship or materials within a period of one year from the date of Final Completion of all of the above named work by the County of Palm Beach, State of Florida, without any expense whatsoever to said County of Palm Beach, ordinary wear and tear and unusual abuse or neglect excepted by the County. The date of Final Completion shall be the date set forth on the fully executed and acknowledged Contractor's Certification of Final Completion form. When correction work is started, it shall be carried through to completion.


In the event of our failure to acknowledge notice, and commence corrections of defective work within five (5) calendar days after being notified in writing by the Board of County Commissioners, Palm Beach County, Florida, we, collectively or separately, do hereby authorize Palm Beach County to proceed to have said defects repaired and made good at our expense and we will honor and pay the costs and charges therefore upon demand.

County and Contractor agree that the provisions of Florida Statute Chapter 558 shall not apply to this Contract/Agreement.

SEAL AND NOTARIAL ACKNOWLEDGMENT OF SURETY.


Hinterland Group Inc.
(Contractor)

By: 
(Signature)



Chase Rogers
(Print Name)

Hartford Accident and Indemnity Company
(Surety)

By: 
(Signature)

Jennie N. Lanman, Attorney-In-Fact
(Print Name)



HALCYON UNDERWRITERS

YOUR PARTNER IN PRODUCTION, MAKING THE DIFFERENCE

555 Winderley Place, Suite 420
Maitland, Florida 32751

March 22, 2022


To: Palm Beach County Water Utilities
8100 Forest Hill Blvd
West Palm Beach, FL 33413

Re: Hinterland Group Inc.
Bond No: 21BCSIU2276
WUD 22-002
Finrock Lift Station and Force Main Rehabilitation

To Whom It May Concern

Please allow this letter to serve as formal authorization for Palm Beach County to date the captioned Construction Bond to coincide with the Contract Date. Please advise our office once dated. We are the bonding agent for Hinterland Group, Inc. They are bonded by Hartford Accident and Indemnity Company, an A+ rated surety in the AM Best Guide. Please be advised that we authorize you to date the form of guarantee and bonds for Bond No: 21BCSIU2276 ;
WUD 22-002 Finrock Lift Station and Force Main Rehabilitation

Thank you and please call me if you have any questions.



Jennie N. Lanman, Attorney-in-Fact



POWER OF ATTORNEY

Direct Inquiries/Claims to:

THE HARTFORD
BOND, T-12
One Hartford Plaza
Hartford, Connecticut 06155
bond.claims@thehartford.com

call: 888-266-3488 or fax: 860-757-5835

Agency Code: HALCYON UNDERWRITERS
Agency Code: 21-224119

KNOW ALL PERSONS BY THESE PRESENTS THAT:

- Hartford Fire Insurance Company, a corporation duly organized under the laws of the State of Connecticut
- Hartford Casualty Insurance Company, a corporation duly organized under the laws of the State of Indiana
- Hartford Accident and Indemnity Company, a corporation duly organized under the laws of the State of Connecticut
- Hartford Underwriters Insurance Company, a corporation duly organized under the laws of the State of Connecticut
- Twin City Fire Insurance Company, a corporation duly organized under the laws of the State of Indiana
- Hartford Insurance Company of Illinois, a corporation duly organized under the laws of the State of Illinois
- Hartford Insurance Company of the Midwest, a corporation duly organized under the laws of the State of Indiana
- Hartford Insurance Company of the Southeast, a corporation duly organized under the laws of the State of Florida

having their home office in Hartford, Connecticut, (hereinafter collectively referred to as the "Companies") do hereby make, constitute and appoint, **up to the amount of \$15,000,000:**

Jennie N. Lanman
Of
Maitland, FL

their true and lawful Attorney(s)-in-Fact, each in their separate capacity if more than one is named above, to sign its name as surety(ies) only as delineated above by , and to execute, seal and acknowledge any and all bonds, undertakings, contracts and other written instruments in the nature thereof, on behalf of the Companies in their business of guaranteeing the fidelity of persons, guaranteeing the performance of contracts and executing or guaranteeing bonds and undertakings required or permitted in any actions or proceedings allowed by law.

In Witness Whereof, and as authorized by a Resolution of the Board of Directors of the Companies on May 23, 2016 the Companies have caused these presents to be signed by its Assistant Vice President and its corporate seals to be hereto affixed, duly attested by its Assistant Secretary. Further, pursuant to Resolution of the Board of Directors of the Companies, the Companies hereby unambiguously affirm that they are and will be bound by any mechanically applied signatures applied to this Power of Attorney.



Shelby Wiggins

Shelby Wiggins, Assistant Secretary

Joelle L. LaPierre

Joelle L. LaPierre, Assistant Vice President

STATE OF FLORIDA

COUNTY OF SEMINOLE

ss. Lake Mary

On this 20th day of May, 2021, before me personally came Joelle L. LaPierre to me known, who being by me duly sworn, did depose and say: that she resides in Seminole County, State of Florida; that she is the Assistant Vice President of the Companies, the corporations described in and which executed the above instrument; that she knows the seals of the said corporations; that the seals affixed to the said instrument are such corporate seals; that they were so affixed by authority of the Boards of Directors of said corporations and that she signed her name thereto by like authority.



Jessica Ciccone

Jessica Ciccone
My Commission HH 122280
Expires June 20, 2025

I, the undersigned, Assistant Vice President of the Companies, DO HEREBY CERTIFY that the above and foregoing is a true and correct copy of the Power of Attorney executed by said Companies, which is still in full force effective as of March 22, 2022

Signed and sealed in Lake Mary, Florida.



Keith Dozois

Keith Dozois, Assistant Vice President

ATTACHMENT E SCHEDULE OF BID ITEMS

Palm Beach County Water Utilities Department

Lift Station Rehabilitation Continuing Construction Contract 2020

Contract Resolution No.: R2020-1379

Contract Dated September 15, 2020

Work Authorization No.: 7

Contractor Name: Hinterland Group Inc.

Project Name: Finfrock Lift Station and Force Main Rehabilitation

PBCWUD Project No.: 22-002

Bid Item No.	Item (Furnish and Install with Appurtenances)	Quantity	Units	Unit Price	Total
8	New Concrete Valve Vault (Interior Dimension 4'Lx6"Wx4'D)	1	EA	\$10,000.00	\$10,000.00
27	4" Mechanical Joint Restraint for DIP/PVC/HDPE	12	EA	\$150.00	\$1,800.00
29	8" Mechanical Joint Restraint for DIP/PVC/HDPE	42	EA	\$200.00	\$8,400.00
31	12" Mechanical Joint Restraint for DIP/PVC/HDPE	2	EA	\$400.00	\$800.00
33	Ductile Iron Fittings for Wastewater Force Main	2.5	Tons	\$6,500.00	\$16,250.00
34	4" PVC C-900 Push-On Joint Force Main (36"-60" Cover)	40	LF	\$35.00	\$1,400.00
36	8" PVC C-900 Push-On Joint Force Main (36"-60" Cover)	2760	LF	\$50.00	\$138,000.00
43	Pressure Pipe Bell Restraint For 8" DIP/PVC (split design)	14	EA	\$200.00	\$2,800.00
48	8" to 10" Diameter Connection to Existing Wastewater Force Main (Joint Restraint for existing pipe to be included if required)	2	EA	\$3,500.00	\$7,000.00
53	Deactivation, Flush and Grouting of Exist. Pipe 10" to 16"	2700	LF	\$20.00	\$54,000.00
101	4" Gate Valve (FL or MJ)	1	EA	\$700.00	\$700.00
103	8" Gate Valve (FL or MJ)	5	EA	\$1,300.00	\$6,500.00
106	Gate Valve Box (H-20 Load Rated)	6	EA	\$450.00	\$2,700.00
107	Concrete Collar for Valve Box	6	EA	\$200.00	\$1,200.00
108	4" Swing Check Valve w/ Outside Lever and Weight	1	EA	\$1,600.00	\$1,600.00
128	Remove and Reinstall or Replace Trees up to 4" diameter or Palm Trees up to 12" diameter	30	EA	\$850.00	\$25,500.00
129	Asphalt Driveway Removal & Restoration (up to 2.5" thick)	100	SY	\$70.00	\$7,000.00
133	Asphalt Pavement Overlay (1.5" thick, Asphalt Type S-III: 20 to 100 tons per work area) Including Milling and Resurfacing	50	Tons	\$300.00	\$15,000.00
134	Concrete Sidewalk Removal & Restoration (up to 4.0" thick)	20	SY	\$45.00	\$900.00
137	Density Test	30	EA	\$100.00	\$3,000.00
138	Proctor Test	4	EA	\$150.00	\$600.00
139	Sod Replacement (St Augustine or Bahia)	1,000	SY	\$5.00	\$5,000.00
140	Demucking and Backfill with Imported Clean Fill	800	CY	\$30.00	\$24,000.00
141	Maintenance of Traffic	3,000	LF	\$1.00	\$3,000.00
143	Record Drawings (Force Main/Gravity Pipe)	3,000	LF	\$3.00	\$9,000.00
151	Pre-Construction Video (per Project Location)	3	LS	\$600.00	\$1,800.00
(A) SUBTOTAL BASE BID (Bid Items 1-256)					\$347,950.00
159	Mobilization (2.5% of Subtotal Bid Price [A])	1	LS	2.5%	\$8,698.75
160	Demobilization (1% of Subtotal Bid Price [A])	1	LS	1%	\$3,479.50
161	Additional Work not included in Bid Items (See Items 161A - 161C Below)	1	LS	\$133,000.00	\$133,000.00
(B) SUBTOTAL ADDITIONAL WORK BID PRICE (Bid Items 159-161)					\$145,178.25
TOTAL BID PRICE (A + B)					\$493,128.25

Additional Work not included in Bid Items (See Items 161 Above):

161C	Gravel Road Restoration	1300.00	S.Y.	\$25.00	\$32,500.00
161B	8" Aerial Crossing	1	Lump Sum	\$92,000.00	\$92,000.00
161A	12" x 8" Tapping Connection	1	Each	\$8,500.00	\$8,500.00

Revised 12/06/2021

ATTACHMENT F

OEBO SCHEDULE 1

Office of Equal Business Opportunity Compliance Programs

**OEBO SCHEDULE 1
LIST OF PROPOSED CONTRACTOR/CONSULTANT AND
SUBCONTRACTOR/SUBCONSULTANT PARTICIPATION**

SOLICITATION/PROJECT/BID NAME: Finrock Lift Station and Force Main Rehabilitation
 NAME OF PRIME RESPONDENT/BIDDER: Hinterland Group Inc.
 CONTACT PERSON: Chase Roberts
 SOLICITATION OPENING/SUBMITTAL DATE: September 15, 2020

SOLICITATION/PROJECT/BID No.: 22-002
 ADDRESS: 2051 West Blue Heron Blvd., Riviera Beach, FL 33404
 PHONE NO.: (561) 640-3503 E-MAIL: crogers@hinterlandgroup.com
 DEPARTMENT: Palm Beach County Water Utilities Department


**PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME CONTRACTOR/CONSULTANT ON THIS PROJECT.
 PLEASE ALSO LIST THE
 DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SUBCONTRACTORS/SUBCONSULTANTS ON THE PROJECT.**

Name, Address and Phone Number	(Check all Applicable Categories)			DOLLAR AMOUNT OR PERCENTAGE OF WORK					Other (Please Specify)
	Non-SBE	M/WBE Minority/Woman Business	SBE Small Business	Black	Hispanic	Women	Caucasian		
1. <u>Hinterland Group Inc.</u> <u>2051 West Blue Heron Blvd., Riviera Beach, FL 33404</u> <u>(561) 640-3503</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____	_____	_____	_____	<u>\$399,836.75</u> (Non a SBE)	
2. <u>Almazan Construction LLC</u> <u>2771 Vista Parkway, St F6, West Palm Beach, FL 33411</u> <u>(561) 812-3672</u>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	_____	<u>\$20,840.00</u>	_____	_____	_____	
3. <u>Utility Supply Associates, Inc.</u> <u>721 Aspen Rd, West Palm Beach, FL 33409</u> <u>(561) 723-2401</u>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	_____	_____	_____	<u>\$72,451.50x60%=</u> <u>\$43,470.90</u>	_____	
4.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____	_____	_____	_____	_____	
5.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____	_____	_____	_____	_____	
6.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____	_____	_____	_____	_____	

(Please use additional sheets if necessary)

Total Bid Price			<u>\$493,128.25</u>	Total	<u>\$0.00</u> (0.00%)	<u>\$20,840.00</u> (4.22%)	<u>\$0.00</u> (0.00%)	<u>\$43,470.90</u> (8.82%)	<u>\$0.00</u>
				Total SBE – MWBE Participation	<u>\$64,310.90 (13.04%)</u>				

I hereby certify that the above information is accurate to the best of my knowledge


 Signature Chase Rogers

Project Director _____
 Title

- Note:**
- The amount listed on this form for a Subcontractor/subconsultant must be supported by price or percentage listed on the properly executed Schedule 2 or attached signed proposal.
 - Firms may be certified by Palm Beach County as an SBE and/or an M/WBE. If firms are certified as both an SBE and/or M/WBE, please indicate the dollar amount under the appropriate category.
 - Modification of this form is not permitted and will be rejected upon submittal.

ATTACHMENT F

OEBO SCHEDULE 2

Office of Equal Business Opportunity Compliance Programs

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All Subcontractors/subconsultants, including any tiered Subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: 22-002

SOLICITATION/PROJECT NAME: Finrock Lift Station and Force Main Rehabilitation

Prime Contractor: Hinterland Group Inc. Subcontractor: Utility Supply Associates, Inc.

(Check box(s) that apply)

SBE WBE MBE M/WBE Non-S/M/WBE Date of Palm Beach County Certification (if applicable): 8/22/19-8/21/22

The undersigned affirms they are the following (select one from each column if applicable):

Column 1	Column 2	Column 3
<input checked="" type="checkbox"/> Male <input type="checkbox"/> Female	<input type="checkbox"/> African-American/Black <input type="checkbox"/> Hispanic American	<input checked="" type="checkbox"/> Supplier
	<input type="checkbox"/> Asian American <input type="checkbox"/> Native American	
	<input type="checkbox"/> Caucasian American	

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Quantity/ Units	Contingencies/ Allowances	Total Price/Percentage
	Supplier	\$72,451.50		60% of Price	\$72,451.50x0.6=\$43,470.90 / 8.82%


The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$72,451.50x0.6=\$43,470.90 / 8.82%

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

 Name of 2nd/3rd tier

Price or Percentage: _____

Hinterland Group Inc.
 Print Name of Prime


By: 
 Authorized Signature

Chase Rogers
 Print Name

Project Director
 Title

Date: 3/22/2022

Utility Supply Associates, Inc.
 Print Name of Subcontractor/subconsultant

By: 
 Authorized Signature

William Potts
 Print Name

SECRETARY TREASURER DIRECTOR
 Title

Date: 3-22-2022

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All Subcontractors/subconsultants, including any tiered Subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: 22-002

SOLICITATION/PROJECT NAME: Finrock Lift Station and Force Main Rehabilitation

Prime Contractor: Hinterland Group Inc. Subcontractor: Almazan Construction LLC

(Check box(s) that apply)

SBE WBE MBE M/WBE Non-S/M/WBE Date of Palm Beach County Certification (if applicable): 8/3/19-8/2/22

The undersigned affirms they are the following (select one from each column if applicable):

Column 1	Column 2	Column 3
<input checked="" type="checkbox"/> Male	<input type="checkbox"/> African-American/Black	<input type="checkbox"/> Asian American
<input type="checkbox"/> Female	<input checked="" type="checkbox"/> Hispanic American	<input type="checkbox"/> Caucasian American
	<input type="checkbox"/> Native American	<input type="checkbox"/> Supplier

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Quantity/ Units	Contingencies/ Allowances	Total Price/Percentage
	Asphalt and/or Concrete Work	\$20,840.00	LS	\$0.00	\$20,840.00 / 4.23%


If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

_____ Price or Percentage: _____

Name of 2nd/3rd tier

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$20,840.00 / 4.23%

Hinterland Group Inc.
 Print Name of Prime


By: 
 Authorized Signature

Chase Rogers
 Print Name

Project Director
 Title

Date: 3/22/2022

Almazan Construction LLC
 Print Name of Subcontractor/subconsultant

By: 
 Authorized Signature

SAMUEL ALMAZAN
 Print Name

AMBR (Authorized Member)
 Title

Date: 3/22/22

ATTACHMENT G

Palm Beach County Water Utilities Department
 Lift Station Rehabilitation Continuing Construction Contract 2020
 Resolution No. R2020-1379 Contract Dated September 15, 2020

SUMMARY OF SBE-M/WBE BUSINESS TRACKING



Master Contract Goals	SBE: <u>26.87%</u>	M/WBE: <u>3.47%</u>	MBE (Hispanic): <u>3.18%</u>	WBE (Women): <u>0.29%</u>
Current Proposal				
Value of Authorization No. <u>7</u>	\$493,128.25			
Value of SBE-M/WBE Letters of Intent	\$64,310.90	\$20,840.00	\$20,840.00	\$0.00
Actual Percentage	13.04%	4.22%	4.22%	0.00%
Signed/Approved Authorizations				
Total Value of Authorizations	\$2,167,587.76			
Total Value of SBE-M/WBE Signed Subcontractors	\$230,882.89	\$129,389.00	\$127,314.00	\$2,075.00
Actual Percentage	10.65%	5.96%	5.87%	0.09%
Signed/Approved Authorizations Plus Current Proposal				
Total Value of Authorization	\$2,660,716.01			
Total Value of Subcontractors & Letters of Intent	\$295,193.79	\$150,229.00	\$148,154.00	\$2,075.00
Actual Percentage	11.09%	5.64%	5.56%	0.07%

ATTACHMENT H

Location Map

Revised 12/06/2021

ATTACHMENT H
LOCATION MAP
WORK AUTHORIZATION No. 7
HINTERLAND GROUP, INC.
PBCWUD PROJECT No. 22-002

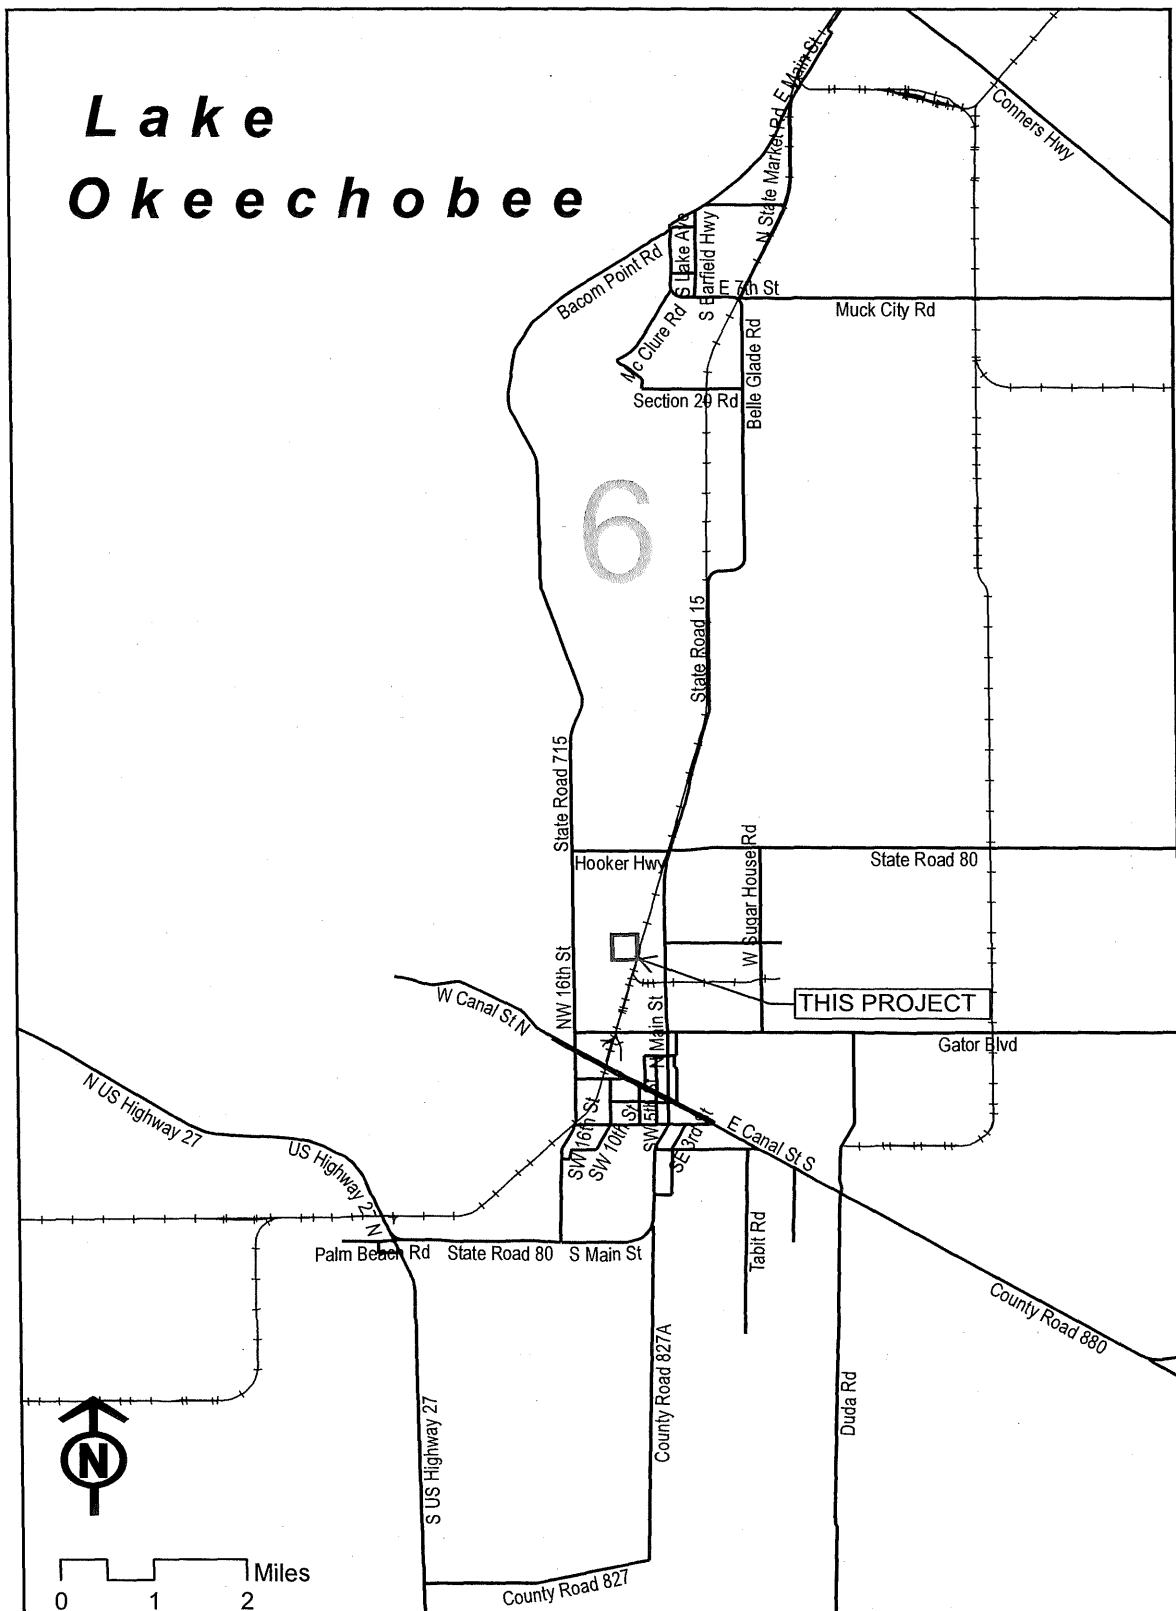

ATTACHMENT 2
LOCATION MAP
AGENDA ITEM
WORK AUTHORIZATION No. 7
HINTERLAND GROUP INC.
WUD PROJECT No. 22-002

Lake Okeechobee

6

THIS PROJECT

